



15- 41463


COG Operating LLC

Eddy County, New Mexico (NAD 27 NME)

Lee 3 Fee

#6H

WB2/Job #1311177



Survey: Phoenix MWD Survey

Phoenix Final Survey Report

03 October, 2013



PHOENIX
TECHNOLOGY SERVICES



Phoenix Technology Services
Phoenix Final Survey Report



Company:	COG Operating LLC	Local Co-ordinate Reference:	Well #6H
Project:	Eddy County, New Mexico (NAD 27 NME)	TVD Reference:	KB @ 3359.00usft (Silver Oak 3)
Site:	Lee 3 Fee	MD Reference:	KB @ 3359.00usft (Silver Oak 3)
Well:	#6H	North Reference:	Grid
Wellbore:	WB2/Job #1311177	Survey Calculation Method:	Minimum Curvature
Design:	Surveys (Silver Oak 3)	Database:	GCR DB

Project:	Eddy County, New Mexico (NAD 27 NME)		
Map System:	US State Plane 1927 (Exact solution)	System Datum:	Mean Sea Level
Geo Datum:	NAD 1927 (NADCON CONUS)		
Map Zone:	New Mexico East 3001		

Site:		Lee 3 Fee			
Site Position:		Northing:	612,139.80 usft	Latitude:	32° 40' 58.31847 N
From:	Map	Easting:	488,590.40 usft	Longitude:	104° 22' 13.49969 W
Position Uncertainty:	0.00 usft	Slot Radius:	13-3/16"	Grid Convergence:	-0.02 °

Well:	#6H					
Well Position	+N-S	0.00 usft	Northing:	612,139.80 usft	Latitude:	32° 40' 58.31847 N
	+E-W	0.00 usft	Easting:	488,590.40 usft	Longitude:	104° 22' 13.49969 W
Position Uncertainty	0.00 usft	Wellhead Elevation:	usft	Ground Level:	3,341.00 usft	

Wellbore	WB2/Job #1311177				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	IGRF2010_14	09/18/13	7.71	60.42	48,578

Design:	Surveys (Silver Oak 3)				
Audit Notes:					
Version:	1.0	Phase:	ACTUAL	Tie On Depth:	2,800.00
Vertical Section:	Depth From (TVD)	+N-S	+E-W	Direction	
	(usft)	(usft)	(usft)	(°)	
	0.00	0.00	0.00	359.55	

Survey Program		Date	10/03/13		
From (usft)	To (usft)	Survey (Wellbore)	Tool Name	Description	
100.00	2,800.00	VES Gyro/Pilot Hole (WB1/Job #1311177)	VES-ISCWSA-GYRO-3	Biaxial Semi-Cont. Gyro	
2,800.00	7,903.00	Phoenix MWD Survey (WB2/Job #1311177)	MWD	MWD - Standard	

Survey	MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	V. Sec (usft)	DLeg (°/100usft)
	2,800.00	0.69	232.74	2,799.09	-48.19	-35.86	-47.90	0.00
Tie-on to Gyro	2,815.00	0.60	247.50	2,814.09	-48.27	-36.01	-47.99	1.25
First Phoenix MWD Survey	2,846.00	0.60	298.50	2,845.09	-48.26	-36.30	-47.97	1.67
	2,877.00	3.90	347.10	2,876.06	-47.15	-36.68	-46.86	11.39
	2,908.00	9.10	355.70	2,906.85	-43.68	-37.10	-43.38	17.02
	2,939.00	15.10	359.40	2,937.15	-37.19	-37.32	-36.89	19.51
	2,970.00	21.20	0.40	2,966.59	-27.54	-37.33	-27.24	19.70
	3,002.00	26.00	0.70	2,995.91	-14.73	-37.20	-14.44	15.00
	3,033.00	30.40	0.70	3,023.22	-0.09	-37.02	0.20	14.19



Phoenix Technology Services
Phoenix Final Survey Report



Company:	COG Operating LLC	Local Co-ordinate Reference:	Well #6H
Project:	Eddy County, New Mexico (NAD 27 NME)	TVD Reference:	KB @ 3359.00usft (Silver Oak 3)
Site:	Lee 3 Fee	MD Reference:	KB @ 3359.00usft (Silver Oak 3)
Well:	#6H	North Reference:	Grid
Wellbore:	WB2/Job #1311177	Survey Calculation Method:	Minimum Curvature
Design:	Surveys (Silver Oak 3)	Database:	GCR/DB

MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	V. Sec (usft)	DLeg (°/100usft)
3,064.00	35.00	359.60	3,049.30	16.66	-36.99	16.95	14.96
3,095.00	37.30	0.10	3,074.33	34.94	-37.03	35.23	7.48
3,126.00	40.60	0.80	3,098.44	54.43	-36.87	54.71	10.74
3,158.00	43.90	0.60	3,122.12	75.94	-36.61	76.22	10.32
3,189.00	47.70	0.20	3,143.73	98.16	-36.46	98.44	12.29
3,220.00	51.30	0.50	3,163.86	121.72	-36.32	122.01	11.64
3,251.00	54.40	1.40	3,182.58	146.43	-35.90	146.70	10.26
3,282.00	57.50	2.10	3,199.93	172.10	-35.11	172.37	10.17
3,313.00	60.70	1.70	3,215.85	198.68	-34.23	198.94	10.38
3,344.00	64.80	0.60	3,230.04	226.23	-33.69	226.48	13.60
3,375.00	67.30	0.30	3,242.62	254.55	-33.46	254.81	8.11
3,406.00	69.90	0.30	3,253.93	283.41	-33.31	283.67	8.39
3,437.00	70.90	0.20	3,264.33	312.62	-33.19	312.87	3.24
3,468.00	72.00	359.40	3,274.20	342.00	-33.29	342.26	4.31
3,499.00	73.70	358.60	3,283.34	371.62	-33.81	371.87	6.01
3,530.00	76.30	358.00	3,291.36	401.55	-34.70	401.81	8.59
3,561.00	77.80	357.30	3,298.31	431.73	-35.94	432.00	5.32
3,592.00	78.30	355.80	3,304.73	462.01	-37.76	462.29	5.00
3,624.00	80.80	355.30	3,310.53	493.38	-40.20	493.68	7.96
3,655.00	84.00	355.10	3,314.63	523.99	-42.77	524.31	10.34
3,686.00	86.60	355.40	3,317.17	554.78	-45.33	555.12	8.44
3,718.00	88.80	356.60	3,318.45	586.67	-47.56	587.03	7.83
3,749.00	89.90	357.60	3,318.80	617.63	-49.13	618.00	4.80
3,780.00	89.80	358.10	3,318.89	648.81	-50.29	648.98	1.64
3,873.00	90.90	358.90	3,318.32	741.57	-52.73	741.96	1.46
3,967.00	90.10	359.50	3,317.50	835.56	-54.04	835.96	1.06
4,061.00	91.30	359.90	3,316.35	929.55	-54.53	929.95	1.35
4,155.00	91.00	0.30	3,314.46	1,023.53	-54.37	1,023.93	0.53
4,248.00	90.30	0.90	3,313.41	1,116.52	-53.39	1,116.90	0.99
4,342.00	90.70	359.80	3,312.59	1,210.51	-52.82	1,210.89	1.25
4,435.00	90.20	359.10	3,311.86	1,303.50	-53.71	1,303.88	0.92
4,529.00	91.70	359.50	3,310.30	1,397.48	-54.86	1,397.87	1.65
4,623.00	91.50	1.20	3,307.67	1,491.44	-54.29	1,491.82	1.82
4,717.00	91.50	0.80	3,305.21	1,585.39	-52.65	1,585.76	0.43
4,810.00	91.30	0.60	3,302.94	1,678.36	-51.51	1,678.71	0.30
4,904.00	91.40	1.10	3,300.73	1,772.32	-50.12	1,772.66	0.54
5,002.00	91.70	0.70	3,298.07	1,870.27	-48.58	1,870.60	0.51
5,095.00	90.80	0.20	3,296.05	1,963.25	-47.85	1,963.56	1.11
5,190.00	90.80	0.00	3,294.72	2,058.24	-47.68	2,058.55	0.21
5,283.00	92.00	359.50	3,292.45	2,151.21	-48.09	2,151.52	1.40
5,377.00	92.00	358.90	3,289.17	2,245.14	-49.40	2,245.46	0.64
5,472.00	90.70	358.70	3,286.93	2,340.09	-51.39	2,340.42	1.38
5,565.00	91.90	358.90	3,284.82	2,433.04	-53.34	2,433.39	1.31
5,659.00	92.10	359.60	3,281.54	2,526.98	-54.57	2,527.33	0.77



Phoenix Technology Services
Phoenix Final Survey Report




Company:	COG Operating LLC	Local Co-ordinate Reference:	Well #6H
Project:	Eddy County, New Mexico (NAD 27 NME)	TVD Reference:	KB @ 3359.00usft (Silver Oak 3)
Sta:	Lee 3 Fee	MD Reference:	KB @ 3359.00usft (Silver Oak 3)
Well:	#6H	North Reference:	Grid
Wellbore:	WB2/Job #131177	Survey Calculation Method:	Minimum Curvature
Design:	Surveys (Silver Oak 3)	Database:	GCRIDB

Survey								
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	V/Sec (usft)	DLeg (°/100usft)	
5,753.00	91.00	0.00	3,279.00	2,620.94	-54.89	2,621.29	1.25	
5,846.00	91.30	359.70	3,277.13	2,713.92	-55.14	2,714.27	0.46	
5,940.00	91.20	0.40	3,275.08	2,807.90	-55.05	2,808.24	0.75	
6,031.00	90.90	1.10	3,273.41	2,898.87	-53.86	2,899.21	0.84	
6,123.00	91.50	0.90	3,271.48	2,990.84	-52.26	2,991.16	0.69	
6,214.00	92.30	0.80	3,268.47	3,081.78	-50.91	3,082.08	0.89	
6,350.00	91.10	0.90	3,264.43	3,217.70	-48.89	3,217.99	0.89	
6,442.00	90.80	0.70	3,262.91	3,309.68	-47.61	3,309.95	0.39	
6,533.00	90.50	0.80	3,261.87	3,400.67	-46.42	3,400.93	0.35	
6,626.00	90.30	0.50	3,261.23	3,493.66	-45.36	3,493.91	0.39	
6,719.00	91.40	0.50	3,259.85	3,586.64	-44.55	3,586.88	1.18	
6,814.00	91.30	0.90	3,257.81	3,681.61	-43.39	3,681.84	0.43	
6,909.00	91.30	0.20	3,255.45	3,776.58	-42.48	3,776.80	0.74	
7,002.00	91.20	359.80	3,253.42	3,869.56	-42.48	3,869.77	0.44	
7,096.00	90.80	359.00	3,251.78	3,963.54	-43.46	3,963.76	0.95	
7,190.00	90.20	358.60	3,250.96	4,057.51	-45.43	4,057.74	0.77	
7,284.00	90.00	357.90	3,250.80	4,151.47	-48.30	4,151.72	0.77	
7,377.00	90.60	359.00	3,250.31	4,244.43	-50.82	4,244.70	1.35	
7,471.00	92.20	0.10	3,248.01	4,338.39	-51.56	4,338.67	2.07	
7,565.00	92.70	359.50	3,244.00	4,432.31	-51.88	4,432.58	0.83	
7,658.00	92.30	359.90	3,239.94	4,525.22	-52.37	4,525.49	0.61	
7,753.00	90.80	0.20	3,237.37	4,620.18	-52.29	4,620.45	1.61	
7,847.00	91.20	0.00	3,235.73	4,714.17	-52.12	4,714.43	0.48	
Last Phoenix MWD Survey								
7,903.00	91.20	0.00	3,234.56	4,770.15	-52.12	4,770.42	0.00	
Projection to TD								

Survey Annotations				
Measured Depth (usft)	Vertical Depth (usft)	Local Coordinates		Comment
		N/S (usft)	E/W (usft)	
2,800.00	2,799.09	-48.19	-35.86	Tie-on to Gyro
2,815.00	2,814.09	-48.27	-36.01	First Phoenix MWD Survey
7,847.00	3,235.73	4,714.17	-52.12	Last Phoenix MWD Survey
7,903.00	3,234.56	4,770.15	-52.12	Projection to TD

Checked By: _____ Approved By: _____ Date: _____




A GYRO TECHNOLOGIES INC. COMPANY

P.O. Box 261021
Corpus Christi, Texas 78426
(361) 767-0602 • (800) 606-GYRO • Fax (361) 767-0612

September 19, 2013

COG Operating LLC (Concho)
One Concho Center
600 W. Illinois Avenue
Midland, TX 79701



Attn: Kanicia Castillo

Re: Lee 3 Fee No 006H

Please find enclosed a copy of the survey from 0' to 4,610' ran on the above referenced well.


If I can be of any further service, please do not hesitate to call me at 800-606-4976.

Sincerely,


Keith Havelka
Operations

STATE OF TEXAS §
COUNTY OF NUECES §

This instrument was acknowledged before me on the 19th day of September A.D., 2013, by Keith Havelka.




Meredith Darden
Notary Public, State of Texas

Company: COG Operating-Concho

Lease/Well: Lee 3 Fee/No 006H




Rig Name: Silveroak 3

State/County: New Mexico/Eddy

Latitude: 32.68, Longitude: -104.37

GRID North is 0.02 Degrees West of True North

VS-Azi: 0.00 Degrees



Depth Reference : RKB = 18 Feet

DRILLOG HA GYRO SURVEY CALCULATIONS

Filename: lee 3 fee 6h-de_gyro survey.ut

Minimum Curvature Method

Report Date/Time: 9/19/2013 / 14:24

Vaughn Energy Services

Midland, Texas

432-563-5444

Surveyor: Gene Heiss

Lee 3 Fee No 006H / API 03-015-41463

Measured Depth FT	Incl Angle Deg	Drift Direction Deg	TVD FT	+N/-S FT	+E/-W FT	Vertical Section FT	Closure Distance FT	Closure Direction Deg	Dogleg Severity Deg/100
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	****
100.00	0.36	172.95	100.00	-0.31	0.04	-0.31	0.32	172.95	0.36
200.00	0.51	156.97	200.00	-1.04	0.25	-1.04	1.07	166.36	0.19
300.00	0.57	158.50	299.99	-1.92	0.61	-1.92	2.01	162.33	0.06
400.00	0.89	175.47	399.98	-3.16	0.86	-3.16	3.27	164.84	0.38
500.00	1.77	180.23	499.96	-5.47	0.91	-5.47	5.55	170.55	0.36
600.00	1.70	182.64	599.91	-8.49	0.84	-8.49	8.53	174.38	0.36
700.00	1.93	192.13	699.86	-11.62	0.41	-11.62	11.62	177.96	0.38
800.00	2.22	196.60	799.79	-15.12	-0.49	-15.12	15.13	181.87	0.33
900.00	2.41	206.39	899.71	-18.86	-1.98	-18.86	18.96	186.00	0.44
1000.00	2.23	214.22	999.63	-22.35	-4.01	-22.35	22.71	190.17	0.36
1100.00	2.14	220.71	1099.56	-25.38	-6.32	-25.38	26.16	193.99	0.27
1200.00	1.90	230.13	1199.50	-27.86	-8.81	-27.86	29.22	197.56	0.41
1300.00	1.73	227.76	1299.45	-29.93	-11.20	-29.93	31.96	200.52	0.19
1400.00	1.77	234.57	1399.40	-31.84	-13.58	-31.84	34.62	203.09	0.21
1500.00	1.66	234.91	1499.36	-33.57	-16.02	-33.57	37.20	205.51	0.12
1600.00	1.52	227.54	1599.32	-35.30	-18.18	-35.30	39.71	207.26	0.25
1700.00	1.62	229.96	1699.28	-37.10	-20.25	-37.10	42.27	208.62	0.12
1800.00	1.53	232.87	1799.24	-38.82	-22.39	-38.82	44.81	209.98	0.12


Measured Depth FT	Incl Angle Deg	Drift Direction Deg	TVD FT	+N/-S FT	+E/-W FT	Vertical Section FT	Closure Distance FT	Closure Direction Deg	Dogleg Severity Deg/100
1900.00	1.52	233.17	1899.21	-40.42	-24.51	-40.42	47.27	211.24	0.01
2000.00	1.19	235.05	1999.18	-41.81	-26.43	-41.81	49.46	212.30	0.34
2100.00	1.05	232.24	2099.16	-42.96	-28.00	-42.96	51.28	213.09	0.15
2200.00	1.15	231.99	2199.14	-44.14	-29.52	-44.14	53.10	213.77	0.10
2300.00	1.06	233.34	2299.12	-45.31	-31.05	-45.31	54.93	214.42	0.09
2400.00	0.74	235.55	2399.11	-46.23	-32.33	-46.23	56.41	214.96	0.32
2500.00	0.56	253.85	2499.10	-46.73	-33.33	-46.73	57.40	215.49	0.27
2600.00	0.46	242.92	2599.10	-47.05	-34.15	-47.05	58.14	215.97	0.14
2700.00	0.60	235.54	2699.10	-47.53	-34.94	-47.53	58.99	216.32	0.16
2800.00	0.69	232.74	2799.09	-48.19	-35.85	-48.19	60.06	216.65	0.09
2900.00	0.77	241.46	2899.08	-48.87	-36.91	-48.87	61.25	217.07	0.14
3000.00	0.69	239.67	2999.07	-49.49	-38.02	-49.49	62.41	217.53	0.01
3100.00	0.71	225.27	3099.07	-50.23	-38.98	-50.23	63.59	217.81	0.18
3200.00	0.81	216.78	3199.06	-51.23	-39.84	-51.23	64.90	217.87	0.15
3300.00	0.82	233.89	3299.05	-52.22	-40.84	-52.22	66.29	218.03	0.24
3400.00	0.76	250.59	3399.04	-52.86	-42.05	-52.86	67.55	218.50	0.24
3500.00	0.69	248.05	3499.03	-53.31	-43.23	-53.31	68.63	219.04	0.08
3600.00	0.82	250.77	3599.02	-53.77	-44.46	-53.77	69.77	219.59	0.14
3700.00	1.23	266.24	3699.00	-54.07	-46.21	-54.07	71.13	220.52	0.49
3800.00	1.73	284.69	3798.97	-53.76	-48.73	-53.76	72.56	222.19	0.68
3900.00	1.53	281.56	3898.93	-53.11	-51.50	-53.11	73.98	224.12	0.21
4000.00	1.51	289.31	3998.90	-52.41	-54.05	-52.41	75.29	225.88	0.21
4100.00	1.41	285.28	4098.86	-51.65	-56.48	-51.65	76.53	227.56	0.14
4200.00	1.37	292.67	4198.83	-50.87	-58.77	-50.87	77.72	229.12	0.18
4300.00	1.29	294.76	4298.81	-49.93	-60.89	-49.93	78.75	230.65	0.09
4400.00	1.14	298.27	4398.79	-48.99	-62.79	-48.99	79.64	232.04	0.16
4500.00	1.66	293.22	4498.75	-47.95	-65.00	-47.95	80.77	233.59	0.33
4610.00	1.89	296.06	4608.70	-46.52	-68.10	-46.52	82.47	235.66	0.23




Vaughn Energy Services
Midland, Texas
432-563-5444
Surveyor: Gene Heiss
Lee 3 Fee No 006H / API 03-015-41463



Depth=0.0, Inc=0.0, AzG=0.0

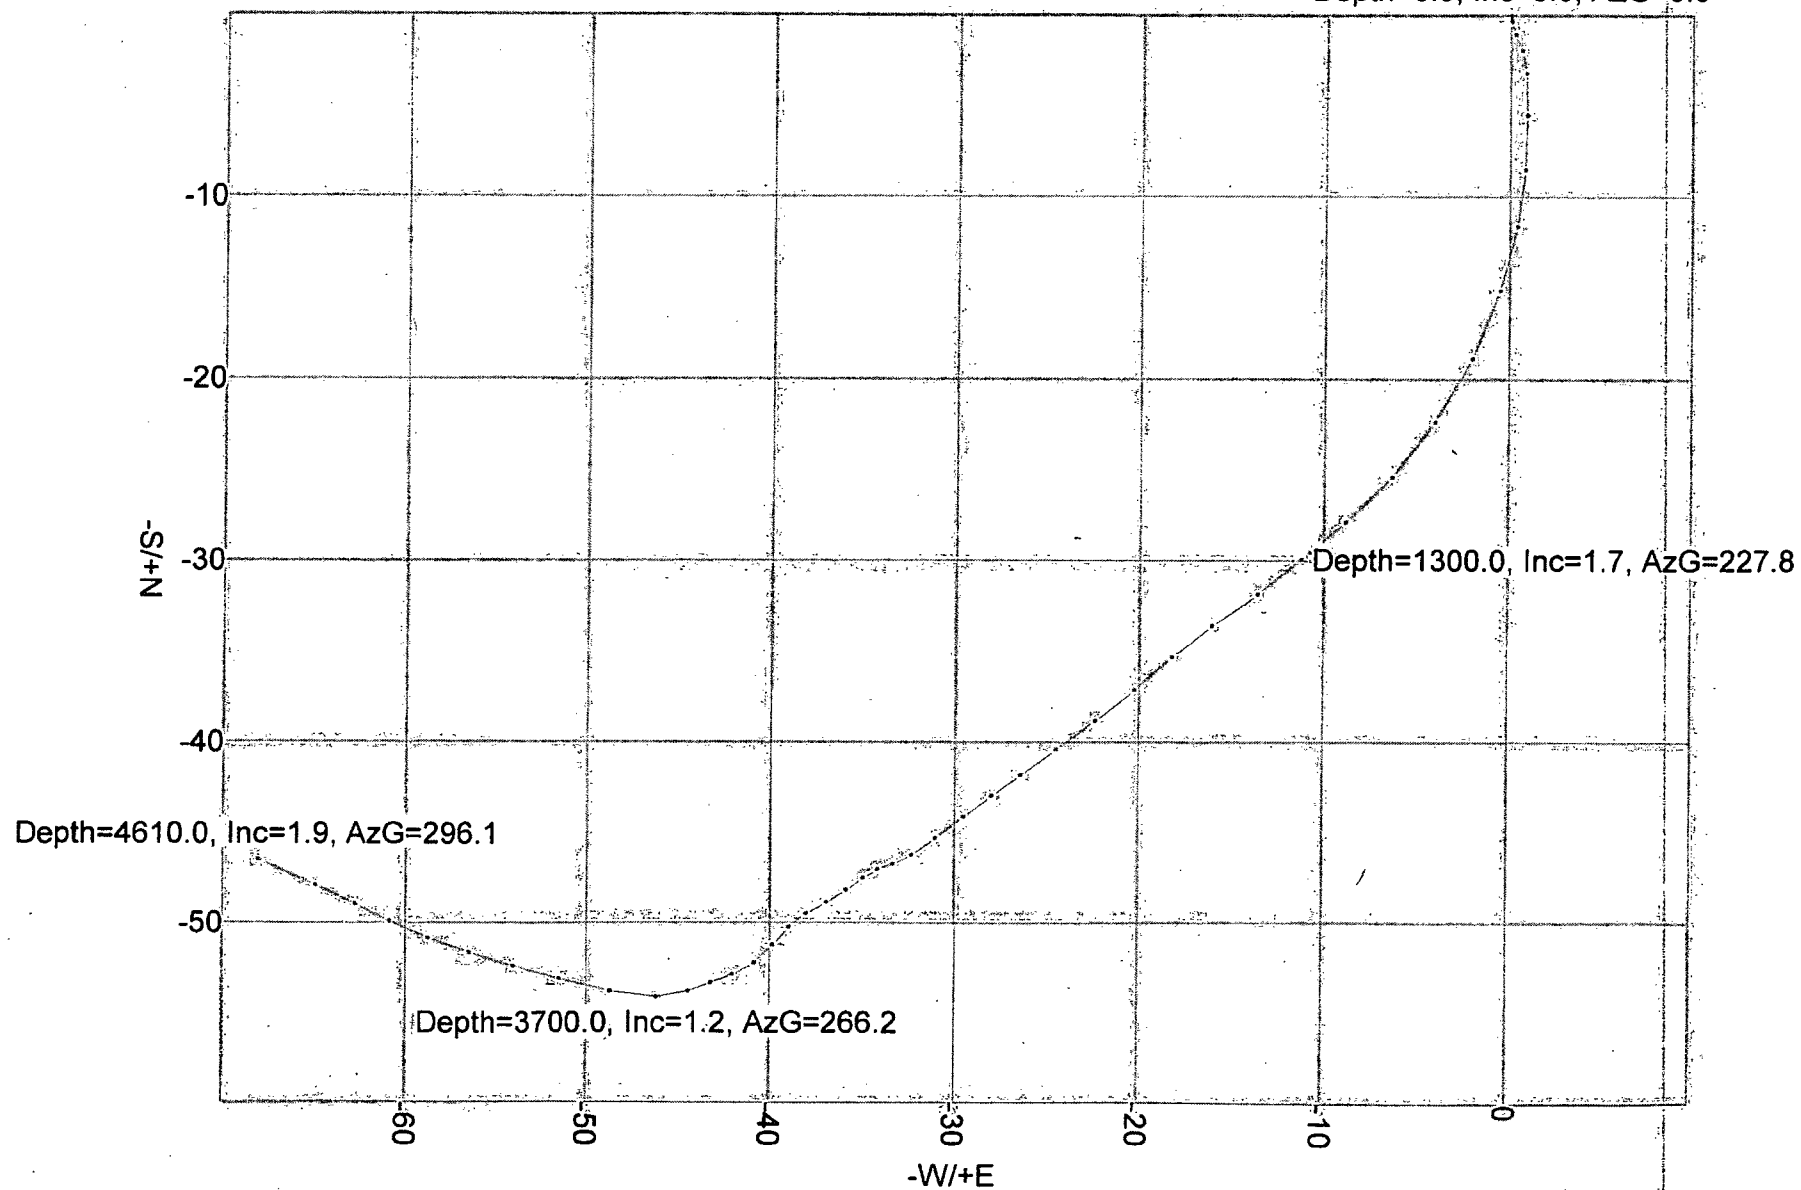

VES Survey Date: 09/14/2013



COG OPER, LLC
RECEIVED
OCT-21-2013
ARTESIA WEST

PO Box 1370
Artesia, NM 88211-1370
(575) 748-1288

October 3, 2013

COG, LLC
One Concho Center
600 W. Illinois Ave.
Midland, TX 79701

RE: Lee 3 Fee #6H
150' FSL & 2310' FWL
Sec. 3, T19S, R26E
Eddy County, New Mexico

Dear Sir,

The attached is the Deviation Survey for the above captioned well.


Very truly yours,

Chris Graham
Drilling Superintendent

State of New Mexico }
County of Eddy }

The foregoing was acknowledged before me this 3rd day of October, 2013.

Notary Public



LEE 3 FEE #6 H

#	Date	Depth	Deviation	Direction	TVD
	9/7/2013	145	0.00	0.00	0.00
	9/7/2013	406	0.70	0.00	0.00
	9/8/2013	672	1.90	0.00	0.00
	9/8/2013	917	2.30	0.00	0.00
	9/8/2013	1169	1.70	0.00	0.00
	9/10/2013	1597	1.70	0.00	0.00
	9/10/2013	1934	1.40	0.00	0.00
	9/11/2013	2247	0.80	0.00	0.00
	9/11/2013	2607	0.20	0.00	0.00
	9/12/2013	3076	1.00	0.00	0.00
	9/12/2013	3326	0.80	0.00	0.00
	9/13/2013	3763	1.10	0.00	0.00
	9/13/2013	4232	1.20	0.00	0.00
	9/18/2013	2752	0.40	265.10	0.00
	9/18/2013	2783	4.70	340.60	0.00
	9/19/2013	2815	0.60	247.50	0.00
	9/19/2013	2846	0.60	298.50	0.00
	9/19/2013	2877	3.90	347.10	0.00
	9/19/2013	2908	9.10	355.70	0.00
	9/19/2013	2939	15.10	359.40	0.00
	9/20/2013	3033	30.40	0.70	0.00
	9/20/2013	3064	35.00	0.70	0.00
	9/20/2013	3095	37.30	0.10	0.00
	9/20/2013	3158	40.60	0.80	0.00
	9/20/2013	3189	43.90	0.60	0.00
	9/20/2013	3375	67.30	0.30	0.00
	9/20/2013	3406	69.90	0.30	0.00
	9/21/2013	3437	70.90	0.20	0.00
	9/21/2013	3468	72.00	359.40	0.00
	9/21/2013	3499	73.70	358.60	0.00
	9/21/2013	3530	76.30	358.00	0.00
	9/21/2013	3561	77.80	57.30	0.00
	9/21/2013	3592	78.30	355.80	0.00
	9/21/2013	3624	80.00	355.30	0.00
	9/21/2013	3655	84.00	355.10	0.00
	9/21/2013	3686	86.60	355.40	0.00
	9/22/2013	3718	88.80	356.60	0.00
	9/22/2013	3749	89.90	357.60	0.00
	9/22/2013	3780	89.80	358.10	0.00
	9/22/2013	3873	90.90	358.90	0.00
	9/22/2013	3967	90.10	359.50	0.00
	9/22/2013	4061	91.30	359.90	0.00
	9/22/2013	4155	91.00	0.30	0.00

#	Date	Depth	Deviation	Direction	TVD
	9/22/2013	4248	90.40	0.90	0.00
	9/22/2013	4342	90.70	359.80	0.00
	9/23/2013	4367	90.60	359.60	0.00
	9/23/2013	4435	90.20	359.10	0.00
	9/23/2013	4529	91.70	359.50	0.00
	9/23/2013	4623	91.50	1.20	0.00
	9/23/2013	4718	91.50	0.80	0.00
	9/23/2013	4810	91.30	0.60	0.00
	9/24/2013	4898	91.40	1.10	0.00
	9/24/2013	4996	91.70	0.70	0.00
	9/24/2013	5095	90.80	0.20	0.00
	9/24/2013	5190	90.80	360.00	0.00
	9/25/2013	5283	92.00	359.50	0.00
	9/25/2013	5377	92.00	358.90	0.00
	9/25/2013	5472	90.70	358.70	0.00
	9/25/2013	5565	91.90	358.90	0.00
	9/25/2013	5659	92.10	359.60	0.00
	9/25/2013	5753	91.00	360.00	0.00
	9/25/2013	5846	91.30	359.70	0.00
	9/26/2013	5940	91.20	0.40	0.00
	9/26/2013	6031	90.70	1.10	0.00
	9/26/2013	6123	91.50	0.90	0.00
	9/26/2013	6214	92.30	0.80	0.00
	9/27/2013	6350	91.10	0.90	3264.00
	9/27/2013	6442	90.80	0.70	0.00
	9/27/2013	6533	90.50	0.70	0.00
	9/28/2013	6814	91.30	0.90	0.00
	9/29/2013	6909	91.30	0.20	0.00
	9/29/2013	7002	91.20	359.80	0.00
	9/29/2013	7096	90.80	359.00	0.00
	9/29/2013	7190	90.20	358.60	0.00
	9/29/2013	7284	90.00	0.00	0.00
	9/29/2013	7377	90.60	359.00	0.00
	9/30/2013	7658	92.30	359.90	0.00
	9/30/2013	7753	90.80	0.20	3237.37
	9/30/2013	7847	91.20	360.00	0.00

EOF
