

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENTNM OIL CONSERVATION
ARTESIA DISTRICTFORM APPROVED
OMB NO. 1004-0137
Expires: January 31, 2018

JAN 31 2018

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an abandoned well. Use form 3160-3 (APD) for such proposals.

RECEIVED

5. Lease Serial No.
NMNM107374

6. If Indian, Allottee or Tribe Name

7. If Unit or CA/Agreement, Name and/or No.

8. Well Name and No. **317459**
DELAWARE RANCH 11 14 B2AP F C 1H9. API Well No.
30-015-44071-00-X110. Field and Pool or Exploratory Area
RED BLUFF11. County or Parish, State
EDDY COUNTY, NM**SUBMIT IN TRIPLICATE - Other instructions on page 2**

1. Type of Well

☒ Oil Well ☐ Gas Well ☐ Other2. Name of Operator
MEWBOURNE OIL COMPANYContact: JACKIE LATHAN
E-Mail: jlathan@mewbourne.com3a. Address
P O BOX 5270
HOBBS, NM 882413b. Phone No. (include area code)
Ph: 575-393-5905

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)

Sec 11 T26S R28E NENE 185FNL 425FEL

12. CHECK THE APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input checked="" type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Hydraulic Fracturing	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment Notice	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug and Abandon	<input type="checkbox"/> Temporarily Abandon	Change to Original A
	<input type="checkbox"/> Convert to Injection	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	PD

13. Describe Proposed or Completed Operation: Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recompleat horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports must be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompleat in a new interval, a Form 3160-4 must be filed once testing has been completed. Final Abandonment Notices must be filed only after all requirements, including reclamation, have been completed and the operator has determined that the site is ready for final inspection.

Mewbourne Oil Company has an approved APD for the above well. Mewbourne requests approval to make the following changes:

- 1) Change well name to Delaware Ranch 11/14 W2AP Fed Com #1H. - *property 324931*
- 2) Change pool to Purple Sage Wolfcamp 98220 (Gas Well).
- 3) Change target zone to Wolfcamp & TVD to 10,713'.
- 4) Change BHL to 330' FSL & 425' FEL, Sec 14, T26S, R28E.
- 5) Change csg depth and cement to suit new plan.
- 6) Change wellhead to multi-bowl type wellhead.

Please see attachments for C-102, wellhead schematic, new drilling plan, casing & cement information.

**SEE ATTACHED FOR
CONDITIONS OF APPROVAL**

14. I hereby certify that the foregoing is true and correct.

Electronic Submission #382735 verified by the BLM Well Information System

For MEWBOURNE OIL COMPANY, sent to the Carlsbad

Committed to AFMSS for processing by PRISCILLA PEREZ on 07/29/2017 (17PP0786SE)

Name (Printed/Typed) ANDY TAYLOR

Title ENGINEER

Signature (Electronic Submission)

Date 07/26/2017

THIS SPACE FOR FEDERAL OR STATE OFFICE USEApproved By ZOTA STEVENSTitle PETROLEUM ENGINEERDate 01/24/2019

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Office Carlsbad

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Instructions on page 2)

**** BLM REVISED ** BLM REVISED ** BLM REVISED ** BLM REVISED ** BLM REVISED *****Rw 2-4-19*

Additional data for EC transaction #382735 that would not fit on the form

32. Additional remarks, continued

Please contact Robert Talley with any questions.

Mewbourne Oil Company, Delaware Ranch 11/14 W2AP Fed Com #1H

Sec 11, T26S, R28E

SL: 185' FNL & 425' FEL, Sec 11

BHL: 330' FSL & 425' FEL, Sec 14

1. Geologic Formations

TVD of target	10713'	Pilot hole depth	NA
MD at TD:	20700'	Deepest expected fresh water:	75'

Basin

Formation	Depth (TVD) from KB	Water/Mineral Bearing/ Target Zone?	Hazards*
Quaternary Fill	Surface		
Rustler	595	Water	
Top Salt	905		
Castile			
Base Salt	2450		
Lamar	2645	Oil/Gas	
Bell Canyon	2675	Oil/Gas	
Cherry Canyon	3535	Oil/Gas	
Manzanita Marker	3660		
Brushy Canyon	4765	Oil/Gas	
Bone Spring	6375	Oil/Gas	
1 st Bone Spring Sand	7320		
2 nd Bone Spring Sand	8035		
3 rd Bone Spring Sand	9161		
Abo			
Wolfcamp	9520	Target Zone	
Devonian			
Fusselman			
Ellenburger			
Granite Wash			

*H2S, water flows, loss of circulation, abnormal pressures, etc.

Mewbourne Oil Company, Delaware Ranch 11/14 W2AP Fed Com #1H

Sec 11, T26S, R28E

SL: 185' FNL & 425' FEL, Sec 11

BHL: 330' FSL & 425' FEL, Sec 14

2. Casing Program

Hole Size	Casing Interval		Csg. Size	Weight (lbs)	Grade	Conn.	SF Collapse	SF Burst	SF Jt Tension	SF Body Tension
	From	To								
17.5"	0'	250'	13.375"	48	H40	STC	6.58	14.79	26.83	45.08
12.25"	0'	2550'	9.625"	36	J55	LTC	1.52	2.65	4.93	6.14
8.75"	0'	10850'	7"	26	HCP110	LTC	1.48	1.89	2.31	2.94
6.125"	10140'	20700'	4.5"	13.5	P110	LTC	1.47	1.71	2.37	2.96
BLM Minimum Safety Factor			1.125	1	1.6 Dry 1.8 Wet	1.6 Dry 1.8 Wet				

All casing strings will be tested in accordance with Onshore Oil and Gas Order #2 III.B.1.h
Must have table for contingency casing

	Y or N
Is casing new? If used, attach certification as required in Onshore Order #1	Y
Is casing API approved? If no, attach casing specification sheet.	Y
Is premium or uncommon casing planned? If yes attach casing specification sheet.	N
Does the above casing design meet or exceed BLM's minimum standards? If not provide justification (loading assumptions, casing design criteria).	Y
Will the pipe be kept at a minimum 1/3 fluid filled to avoid approaching the collapse pressure rating of the casing?	Y
Is well located within Capitan Reef?	N
If yes, does production casing cement tie back a minimum of 50' above the Reef?	
Is well within the designated 4 string boundary.	
Is well located in SOPA but not in R-111-P?	N
If yes, are the first 2 strings cemented to surface and 3 rd string cement tied back 500' into previous casing?	
Is well located in R-111-P and SOPA?	N
If yes, are the first three strings cemented to surface?	
Is 2 nd string set 100' to 600' below the base of salt?	
Is well located in high Cave/Karst?	Y
If yes, are there two strings cemented to surface?	Y
(For 2 string wells) If yes, is there a contingency casing if lost circulation occurs?	
Is well located in critical Cave/Karst?	N
If yes, are there three strings cemented to surface?	

Mewbourne Oil Company, Delaware Ranch 11/14 W2AP Fed Com #1H

Sec 11, T26S, R28E

SL: 185' FNL & 425' FEL, Sec 11

BHL: 330' FSL & 425' FEL, Sec 14

3. Cementing Program

Casing	# Sks	Wt. lb/ gal	Yld ft3/ sack	H₂O gal/ sk	500# Comp. Strength (hours)	Slurry Description
Surf.	265	14.8	1.34	6.3	8	Class C + Retarder
Inter.	360	12.5	2.12	11	10	Lead: Class C + Salt + Gel + Extender + LCM
	200	14.8	1.34	6.3	8	Tail: Class C + Retarder
Prod. Stg 1	420	12.5	2.12	11	9	Lead: Class C + Gel + Retarder + Defoamer + Extender
	400	15.6	1.18	5.2	10	Tail: Class H + Retarder + Fluid Loss + Defoamer
ECP/DV Tool @ 3660'						
Prod. Stg 2	60	12.5	2.12	11	9	Lead: Class C + Gel + Retarder + Defoamer + Extender
	100	14.8	1.34	6.3	8	Tail: Class C + Retarder
Liner	425	11.2	2.97	17	16	Class C + Salt + Gel + Fluid Loss + Retarder + Dispersant + Defoamer + Anti-Settling Agent

A copy of cement test will be available on location at time of cement job providing pump times, compressive strengths, etc.

Casing String	TOC	% Excess
Surface	0'	100%
Intermediate	0'	25%
Production	2350'	25%
Liner	10140'	25%

Mewbourne Oil Company, Delaware Ranch 11/14 W2AP Fed Com #1H
Sec 11, T26S, R28E
SL: 185' FNL & 425' FEL, Sec 11
BHL: 330' FSL & 425' FEL, Sec 14

4. Pressure Control Equipment

	Variance: None
--	----------------

BOP installed and tested before drilling which hole?	Size?	System Rated WP	Type	✓	Tested to:
12-1/4"	13-5/8"	5M	Annular	X	2500#
			Blind Ram	X	5000#
			Pipe Ram	X	
			Double Ram		
			Other*		

*Specify if additional ram is utilized.

BOP/BOPE will be tested by an independent service company to 250 psi low and the high pressure indicated above per Onshore Order 2 requirements. The System may be upgraded to a higher pressure but still tested to the working pressure listed in the table above. If the system is upgraded all the components installed will be functional and tested.

Pipe rams will be operationally checked each 24 hour period. Blind rams will be operationally checked on each trip out of the hole. These checks will be noted on the daily tour sheets. Other accessories to the BOP equipment will include a Kelly cock and floor safety valve (inside BOP) and choke lines and choke manifold. See attached schematics.

X	Formation integrity test will be performed per Onshore Order #2. On Exploratory wells or on that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Will be tested in accordance with Onshore Oil and Gas Order #2 III.B.1.i.
Y	A variance is requested for the use of a flexible choke line from the BOP to Choke Manifold. See attached for specs and hydrostatic test chart.
	N Are anchors required by manufacturer?
Y	A multibowl wellhead is being used. The BOP will be tested per Onshore Order #2 after installation on the surface casing which will cover testing requirements for a maximum of 30 days. If any seal subject to test pressure is broken the system must be tested. <ul style="list-style-type: none"> Provide description here: See attached schematic.

Mewbourne Oil Company, Delaware Ranch 11/14 W2AP Fed Com #1H

Sec 11, T26S, R28E

SL: 185' FNL & 425' FEL, Sec 11

BHL: 330' FSL & 425' FEL, Sec 14

5. Mud Program

Depth		Type	Weight (ppg)	Viscosity	Water Loss
From	To				
0'	250'	Spud Mud	8.6-8.8	28-34	N/C
250'	2550'	BW	10.0	28-34	N/C
2550'	10140'	FW w/ Polymer	8.6-9.7	28-34	N/C
10140'	20700'	OBM	10.0-13.0	30-40	<10cc

Sufficient mud materials to maintain mud properties and meet minimum lost circulation and weight increase requirements will be kept on location at all times. MW up to 13.0 ppg may be required for shale control. The highest mud weight needed to balance formation is expected to be 12.0 ppg.

What will be used to monitor the loss or gain of fluid?	Pason/PVT/Visual Monitoring
---	-----------------------------

6. Logging and Testing Procedures

Logging, Coring and Testing.	
X	Will run GR/CNL from KOP (10140') to surface (horizontal well – vertical portion of hole). Stated logs run will be in the Completion Report and submitted to the BLM.
	No Logs are planned based on well control or offset log information.
	Drill stem test? If yes, explain
	Coring? If yes, explain

Additional logs planned		Interval
X	Gamma Ray	10140' (KOP) to TD
	Density	
	CBL	
	Mud log	
	PEX	

Mewbourne Oil Company, Delaware Ranch 11/14 W2AP Fed Com #1H

Sec 11, T26S, R28E

SL: 185' FNL & 425' FEL, Sec 11

BHL: 330' FSL & 425' FEL, Sec 14

7. Drilling Conditions

Condition	Specify what type and where?
BH Pressure at deepest TVD	6685 psi
Abnormal Temperature	No

Mitigation measure for abnormal conditions. Describe. Lost circulation material/sweeps/mud scavengers in surface hole. Weighted mud for possible over-pressure in Wolfcamp formation.

Hydrogen Sulfide (H₂S) monitors will be installed prior to drilling out the surface shoe. If H₂S is detected in concentrations greater than 100 ppm, the operator will comply with the provisions of Onshore Oil and Gas Order #6. If Hydrogen Sulfide is encountered, measured values and formations will be provided to the BLM.

	H ₂ S is present
X	H ₂ S Plan attached

8. Other facets of operation

Is this a walking operation? If yes, describe.
Will be pre-setting casing? If yes, describe.

Attachments

☐ Directional Plan

☐ Other, describe

Additional data for EC transaction #382735 that would not fit on the form

32. Additional remarks, continued

Please contact Robert Talley with any questions.

District I
1625 N. French Dr., Hobbs, NM 88240
Phone: (575) 393-6161 Fax: (575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone: (575) 748-1283 Fax: (575) 748-9720
District III
1000 Rio Brazos Road, Aztec, NM 87410
Phone: (505) 334-6178 Fax: (505) 334-6170
District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505
Phone: (505) 476-3460 Fax: (505) 476-3462

State of New Mexico
Energy, Minerals & Natural Resources Department
OIL CONSERVATION DIVISION
ARTESIA DISTRICT
1220 South St. Francis Dr.
Santa Fe, NM 87505
Form C-102
Revised August 1, 2011
Submit one copy to appropriate District Office

JAN 31 2019

AMENDED REPORT

RECEIVED

WELL LOCATION AND ACREAGE DEDICATION PLAT



1 API Number 30-015-44071		2 Pool Code 98220		3 Pool Name PURPLE SAGE WOLFCAMP GAS					
4 Property Code 317459		5 Property Name DELAWARE RANCH 11/14 W2AP FED COM						6 Well Number 1H	
7 OGRID NO. 14744		8 Operator Name MEWBOURNE OIL COMPANY						9 Elevation 2968'	
10 Surface Location									
UL or lot no. A	Section 11	Township 26S	Range 28E	Lot Idn	Feet from the 185	North/South line NORTH	Feet From the 425	East/West line EAST	County EDDY
11 Bottom Hole Location If Different From Surface									
UL or lot no. P	Section 14	Township 26S	Range 28E	Lot Idn	Feet from the 330	North/South line SOUTH	Feet from the 425	East/West line EAST	County EDDY
12 Dedicated Acres 640		13 Joint or Infill		14 Consolidation Code		15 Order No.			

No allowable will be assigned to this completion until all interest have been consolidated or a non-standard unit has been approved by the division.

<p>16</p> <p>CORNER DATA NAD 27 GRID - NM EAST</p> <p>A: FOUND BRASS CAP "1995" N 376568.2 - E 582748.6</p> <p>B: FOUND BRASS CAP "1995" N 379270.7 - E 582773.1</p> <p>C: FOUND BRASS CAP "1995" N 381926.5 - E 582797.7</p> <p>D: FOUND BRASS CAP "1995" N 384585.8 - E 582821.3</p> <p>E: CALCULATED CORNER N 387226.1 - E 582853.8</p> <p>F: FOUND BRASS CAP "1995" N 387267.7 - E 585494.6</p> <p>G: FOUND BRASS CAP "1995" N 387222.3 - E 588148.7</p> <p>H: FOUND BRASS CAP "1995" N 384583.0 - E 588145.8</p> <p>I: FOUND BRASS CAP "1995" N 381943.6 - E 588142.9</p> <p>J: FOUND BRASS CAP "1995" N 379308.1 - E 588144.2</p> <p>K: FOUND BRASS CAP "1995" N 376667.0 - E 588147.7</p> <p>L: FOUND BRASS CAP "1995" N 376617.0 - E 585405.3</p> <p>M: FOUND BRASS CAP "1995" N 381931.1 - E 585465.7</p>	<p>DETAIL "A"</p> <p>2961.9' - 600' - 2946.9'</p> <p>2975.0' - 600' - 2954.5'</p> <p>GEODETIC DATA NAD 27 GRID - NM EAST</p> <p>SURFACE LOCATION N 387044.7 - E 587723.7</p> <p>LAT: 32.06378478° N LONG: 104.05015304° W</p> <p>BOTTOM LOCATION N 376991.0 - E 587817.2</p> <p>LAT: 32.03614614° N LONG: 104.04993646° W</p>	<p>SEE DETAIL "A"</p> <p>185' S. L. 425'</p> <p>10.054.07' (HORIZ)</p> <p>10.054.07' (HORIZ)</p> <p>425' B. H. 330'</p>	<p>17 OPERATOR CERTIFICATION</p> <p>I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of such a mineral or working interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division.</p> <p>Signature BRADLEY BISHOP Date 7-26-17</p> <p>Printed Name BBISHOP@MEWBOURNE.COM</p> <p>E-mail Address</p>
	<p>18 SURVEYOR CERTIFICATION</p> <p>I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief.</p> <p>Date of Survey 12-5-14</p> <p>Signature and Seal of Professional Surveyor</p> <p>19680</p> <p>Certificate Number</p>		

RRC - Firm No.: TX 10193838 NM 4655451 - Job No.: LS140534A

RWP 2-04-19.

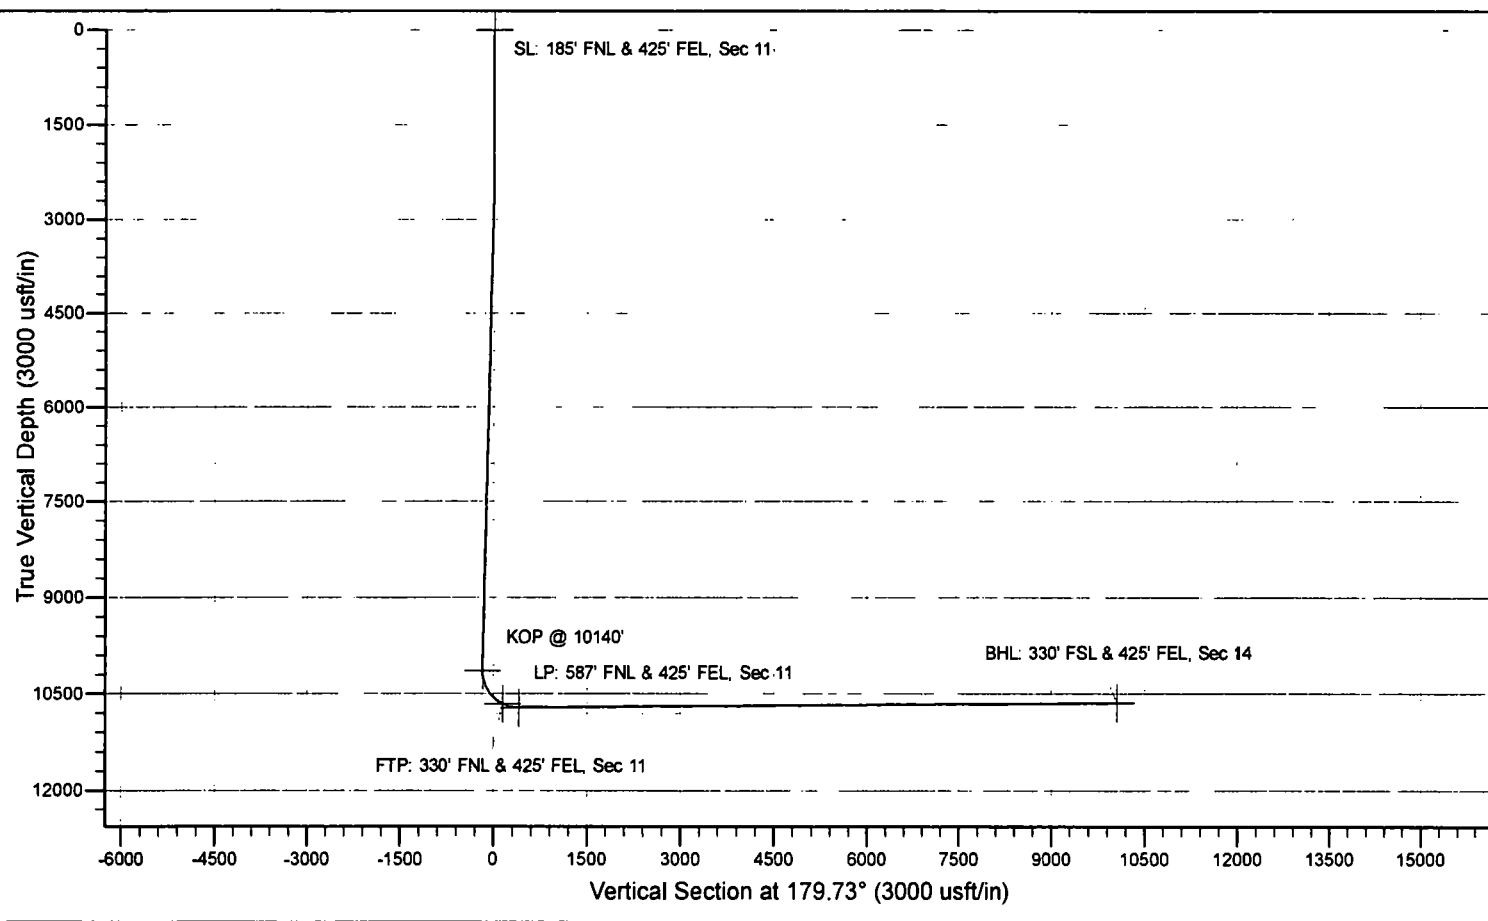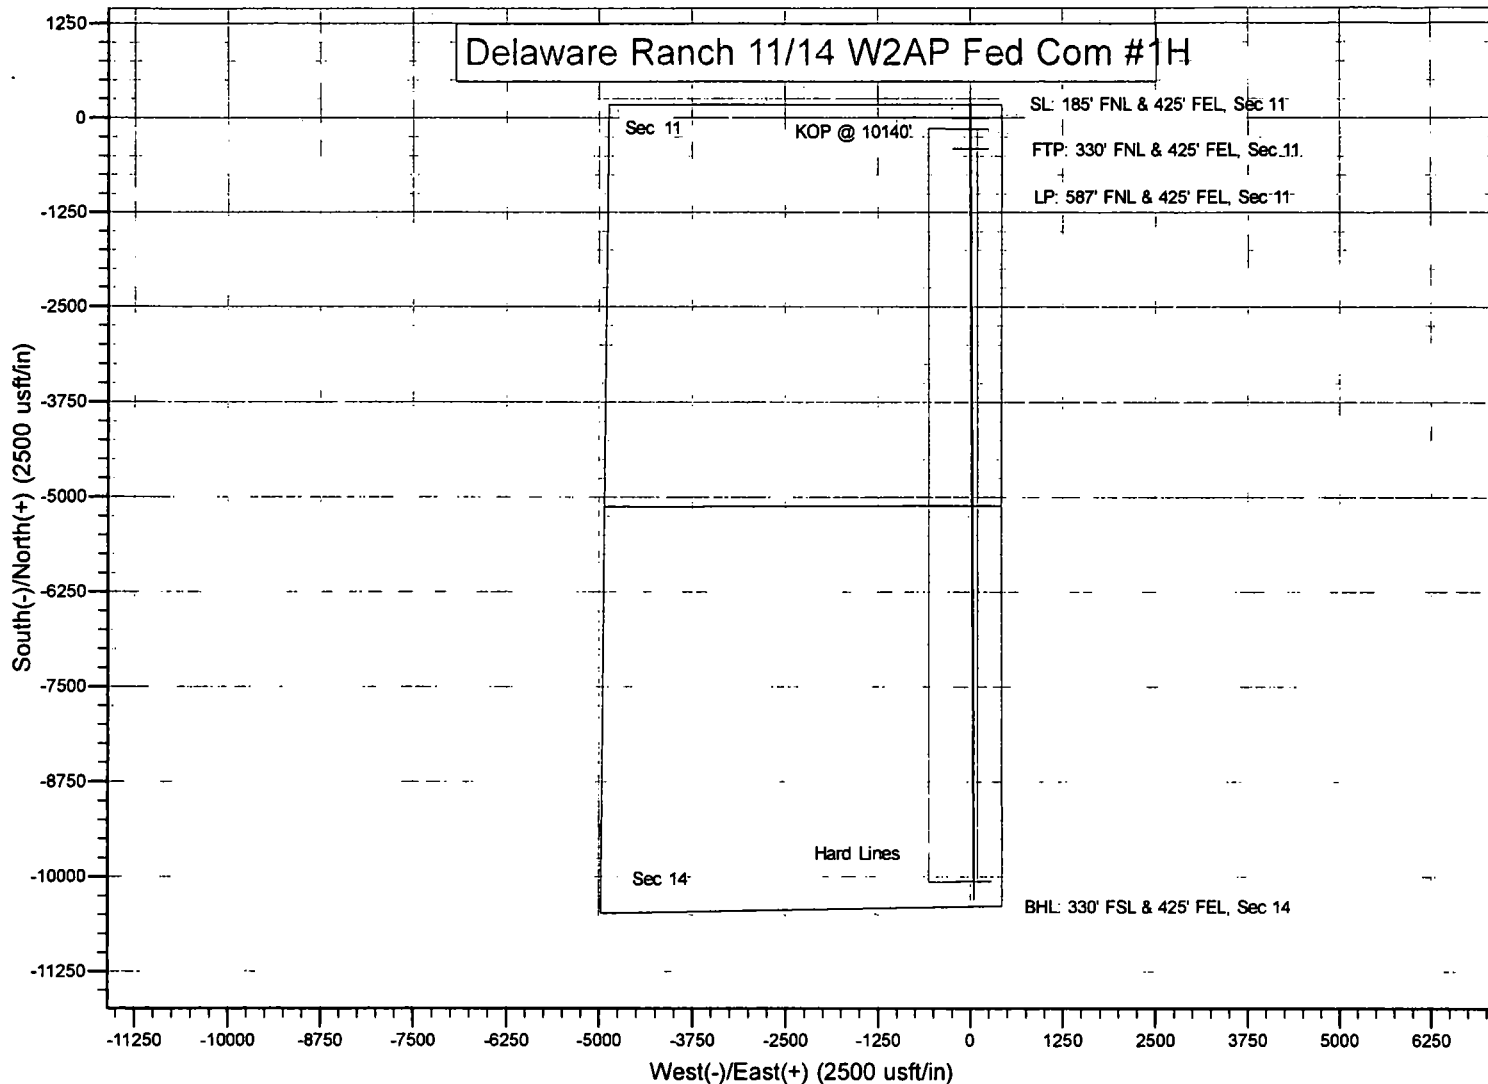

Mewbourne Oil Company

Eddy County, New Mexico

Delaware Ranch 11/14 W2AP Fed Com #1H

Sec 11, T26S, R28E

SL: 185' FNL & 425' FEL, Sec 11

BHL: 330' FSL & 425' FEL, Sec 14

Plan: Design #1

Standard Planning Report

26 July, 2017

Planning Report

Database:	Hobbs	Local Co-ordinate Reference:	Site Delaware Ranch 11/14 W2AP Fed Com #1H
Company:	Mewbourne Oil Company	TVD Reference:	WELL @ 2995.0usft (Original Well Elev)
Project:	Eddy County, New Mexico	MD Reference:	WELL @ 2995.0usft (Original Well Elev)
Site:	Delaware Ranch 11/14 W2AP Fed Com #1H	North Reference:	Grid
Well:	Sec 11, T26S, R28E	Survey Calculation Method:	Minimum Curvature
Wellbore:	BHL: 330' FSL & 425' FEL, Sec 14		
Design:	Design #1		

Project	Eddy County, New Mexico		
Map System:	US State Plane 1927 (Exact solution)	System Datum:	Mean Sea Level
Geo Datum:	NAD 1927 (NADCON CONUS)		
Map Zone:	New Mexico East 3001		

Site	Delaware Ranch 11/14 W2AP Fed Com #1H				
Site Position:		Northing:	387,045.00 usft	Latitude:	32° 3' 49.628 N
From:	Map	Easting:	587,724.00 usft	Longitude:	104° 3' 0.548 W
Position Uncertainty:	0.0 usft	Slot Radius:	13-3/16 "	Grid Convergence:	0.15 °

Well	Sec 11, T26S, R28E					
Well Position	+N/-S	0.0 usft	Northing:	387,045.00 usft	Latitude:	32° 3' 49.628 N
	+E/-W	0.0 usft	Easting:	587,724.00 usft	Longitude:	104° 3' 0.548 W
Position Uncertainty	0.0 usft	Wellhead Elevation:	2,995.0 usft	Ground Level:	2,968.0 usft	

Wellbore	BHL: 330' FSL & 425' FEL, Sec 14				
Magnetics	Model Name	Sample Date	Declination	Dip Angle	Field Strength
			(°)	(°)	(nT)
	IGRF200510	12/31/2009	7.95	60.01	48,645

Design	Design #1			
Audit Notes:				
Version:	Phase:	PROTOTYPE	Tie On Depth:	0.0
Vertical Section:	Depth From (TVD)	+N/-S	+E/-W	Direction
	(usft)	(usft)	(usft)	(°)
	0.0	0.0	0.0	179.73

Plan Sections										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	TFO (°)	Target
0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.00	0.00	
2,600.0	0.00	0.00	2,600.0	0.0	0.0	0.00	0.00	0.00	0.00	
2,689.7	1.35	0.00	2,689.7	1.1	0.0	1.50	1.50	0.00	0.00	
10,052.4	1.35	0.00	10,050.3	173.9	0.0	0.00	0.00	0.00	0.00	
10,142.1	0.00	0.00	10,140.0	175.0	0.0	1.50	-1.50	0.00	180.00	KOP @ 10140'
11,046.4	90.43	179.73	10,713.0	-402.3	2.7	10.00	10.00	0.00	179.73	
20,700.5	90.43	179.73	10,640.0	-10,056.0	48.0	0.00	0.00	0.00	0.00	BHL: 330' FSL & 425'

Planning Report

Database:	Hobbs	Local Co-ordinate Reference:	Site Delaware Ranch 11/14 W2AP Fed Com #1H
Company:	Mewbourne Oil Company	TVD Reference:	WELL @ 2995.0usft (Original Well Elev)
Project:	Eddy County, New Mexico	MD Reference:	WELL @ 2995.0usft (Original Well Elev)
Site:	Delaware Ranch 11/14 W2AP Fed Com #1H	North Reference:	Grid
Well:	Sec 11, T26S, R28E	Survey Calculation Method:	Minimum Curvature
Wellbore:	BHL: 330' FSL & 425' FEL, Sec 14		
Design:	Design #1		

Planned Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
0.0	0.00	0.00	0.0	0.0	0.0	0.0	0.00	0.00	0.00
SL: 185' FNL & 425' FEL, Sec 11									
100.0	0.00	0.00	100.0	0.0	0.0	0.0	0.00	0.00	0.00
200.0	0.00	0.00	200.0	0.0	0.0	0.0	0.00	0.00	0.00
300.0	0.00	0.00	300.0	0.0	0.0	0.0	0.00	0.00	0.00
400.0	0.00	0.00	400.0	0.0	0.0	0.0	0.00	0.00	0.00
500.0	0.00	0.00	500.0	0.0	0.0	0.0	0.00	0.00	0.00
600.0	0.00	0.00	600.0	0.0	0.0	0.0	0.00	0.00	0.00
700.0	0.00	0.00	700.0	0.0	0.0	0.0	0.00	0.00	0.00
800.0	0.00	0.00	800.0	0.0	0.0	0.0	0.00	0.00	0.00
900.0	0.00	0.00	900.0	0.0	0.0	0.0	0.00	0.00	0.00
1,000.0	0.00	0.00	1,000.0	0.0	0.0	0.0	0.00	0.00	0.00
1,100.0	0.00	0.00	1,100.0	0.0	0.0	0.0	0.00	0.00	0.00
1,200.0	0.00	0.00	1,200.0	0.0	0.0	0.0	0.00	0.00	0.00
1,300.0	0.00	0.00	1,300.0	0.0	0.0	0.0	0.00	0.00	0.00
1,400.0	0.00	0.00	1,400.0	0.0	0.0	0.0	0.00	0.00	0.00
1,500.0	0.00	0.00	1,500.0	0.0	0.0	0.0	0.00	0.00	0.00
1,600.0	0.00	0.00	1,600.0	0.0	0.0	0.0	0.00	0.00	0.00
1,700.0	0.00	0.00	1,700.0	0.0	0.0	0.0	0.00	0.00	0.00
1,800.0	0.00	0.00	1,800.0	0.0	0.0	0.0	0.00	0.00	0.00
1,900.0	0.00	0.00	1,900.0	0.0	0.0	0.0	0.00	0.00	0.00
2,000.0	0.00	0.00	2,000.0	0.0	0.0	0.0	0.00	0.00	0.00
2,100.0	0.00	0.00	2,100.0	0.0	0.0	0.0	0.00	0.00	0.00
2,200.0	0.00	0.00	2,200.0	0.0	0.0	0.0	0.00	0.00	0.00
2,300.0	0.00	0.00	2,300.0	0.0	0.0	0.0	0.00	0.00	0.00
2,400.0	0.00	0.00	2,400.0	0.0	0.0	0.0	0.00	0.00	0.00
2,500.0	0.00	0.00	2,500.0	0.0	0.0	0.0	0.00	0.00	0.00
2,600.0	0.00	0.00	2,600.0	0.0	0.0	0.0	0.00	0.00	0.00
2,689.7	1.35	0.00	2,689.7	1.1	0.0	-1.1	1.50	1.50	0.00
2,700.0	1.35	0.00	2,700.0	1.3	0.0	-1.3	0.00	0.00	0.00
2,800.0	1.35	0.00	2,800.0	3.6	0.0	-3.6	0.00	0.00	0.00
2,900.0	1.35	0.00	2,899.9	6.0	0.0	-6.0	0.00	0.00	0.00
3,000.0	1.35	0.00	2,999.9	8.3	0.0	-8.3	0.00	0.00	0.00
3,100.0	1.35	0.00	3,099.9	10.7	0.0	-10.7	0.00	0.00	0.00
3,200.0	1.35	0.00	3,199.9	13.0	0.0	-13.0	0.00	0.00	0.00
3,300.0	1.35	0.00	3,299.8	15.4	0.0	-15.4	0.00	0.00	0.00
3,400.0	1.35	0.00	3,399.8	17.7	0.0	-17.7	0.00	0.00	0.00
3,500.0	1.35	0.00	3,499.8	20.1	0.0	-20.1	0.00	0.00	0.00
3,600.0	1.35	0.00	3,599.7	22.4	0.0	-22.4	0.00	0.00	0.00
3,700.0	1.35	0.00	3,699.7	24.8	0.0	-24.8	0.00	0.00	0.00
3,800.0	1.35	0.00	3,799.7	27.1	0.0	-27.1	0.00	0.00	0.00
3,900.0	1.35	0.00	3,899.7	29.5	0.0	-29.5	0.00	0.00	0.00
4,000.0	1.35	0.00	3,999.6	31.8	0.0	-31.8	0.00	0.00	0.00
4,100.0	1.35	0.00	4,099.6	34.2	0.0	-34.2	0.00	0.00	0.00
4,200.0	1.35	0.00	4,199.6	36.5	0.0	-36.5	0.00	0.00	0.00
4,300.0	1.35	0.00	4,299.5	38.9	0.0	-38.9	0.00	0.00	0.00
4,400.0	1.35	0.00	4,399.5	41.2	0.0	-41.2	0.00	0.00	0.00
4,500.0	1.35	0.00	4,499.5	43.6	0.0	-43.6	0.00	0.00	0.00
4,600.0	1.35	0.00	4,599.5	45.9	0.0	-45.9	0.00	0.00	0.00
4,700.0	1.35	0.00	4,699.4	48.3	0.0	-48.3	0.00	0.00	0.00
4,800.0	1.35	0.00	4,799.4	50.6	0.0	-50.6	0.00	0.00	0.00
4,900.0	1.35	0.00	4,899.4	53.0	0.0	-53.0	0.00	0.00	0.00
5,000.0	1.35	0.00	4,999.4	55.3	0.0	-55.3	0.00	0.00	0.00

Planning Report

Database:	Hobbs	Local Co-ordinate Reference:	Site Delaware Ranch 11/14 W2AP Fed Com #1H
Company:	Mewbourne Oil Company	TVD Reference:	WELL @ 2995.0usft (Original Well Elev)
Project:	Eddy County, New Mexico	MD Reference:	WELL @ 2995.0usft (Original Well Elev)
Site:	Delaware Ranch 11/14 W2AP Fed Com #1H	North Reference:	Grid
Well:	Sec 11, T26S, R28E	Survey Calculation Method:	Minimum Curvature
Wellbore:	BHL: 330' FSL & 425' FEL, Sec 14		
Design:	Design #1		

Planned Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
5,100.0	1.35	0.00	5,099.3	57.7	0.0	-57.7	0.00	0.00	0.00
5,200.0	1.35	0.00	5,199.3	60.0	0.0	-60.0	0.00	0.00	0.00
5,300.0	1.35	0.00	5,299.3	62.3	0.0	-62.3	0.00	0.00	0.00
5,400.0	1.35	0.00	5,399.2	64.7	0.0	-64.7	0.00	0.00	0.00
5,500.0	1.35	0.00	5,499.2	67.0	0.0	-67.0	0.00	0.00	0.00
5,600.0	1.35	0.00	5,599.2	69.4	0.0	-69.4	0.00	0.00	0.00
5,700.0	1.35	0.00	5,699.2	71.7	0.0	-71.7	0.00	0.00	0.00
5,800.0	1.35	0.00	5,799.1	74.1	0.0	-74.1	0.00	0.00	0.00
5,900.0	1.35	0.00	5,899.1	76.4	0.0	-76.4	0.00	0.00	0.00
6,000.0	1.35	0.00	5,999.1	78.8	0.0	-78.8	0.00	0.00	0.00
6,100.0	1.35	0.00	6,099.1	81.1	0.0	-81.1	0.00	0.00	0.00
6,200.0	1.35	0.00	6,199.0	83.5	0.0	-83.5	0.00	0.00	0.00
6,300.0	1.35	0.00	6,299.0	85.8	0.0	-85.8	0.00	0.00	0.00
6,400.0	1.35	0.00	6,399.0	88.2	0.0	-88.2	0.00	0.00	0.00
6,500.0	1.35	0.00	6,498.9	90.5	0.0	-90.5	0.00	0.00	0.00
6,600.0	1.35	0.00	6,598.9	92.9	0.0	-92.9	0.00	0.00	0.00
6,700.0	1.35	0.00	6,698.9	95.2	0.0	-95.2	0.00	0.00	0.00
6,800.0	1.35	0.00	6,798.9	97.6	0.0	-97.6	0.00	0.00	0.00
6,900.0	1.35	0.00	6,898.8	99.9	0.0	-99.9	0.00	0.00	0.00
7,000.0	1.35	0.00	6,998.8	102.3	0.0	-102.3	0.00	0.00	0.00
7,100.0	1.35	0.00	7,098.8	104.6	0.0	-104.6	0.00	0.00	0.00
7,200.0	1.35	0.00	7,198.7	107.0	0.0	-107.0	0.00	0.00	0.00
7,300.0	1.35	0.00	7,298.7	109.3	0.0	-109.3	0.00	0.00	0.00
7,400.0	1.35	0.00	7,398.7	111.7	0.0	-111.7	0.00	0.00	0.00
7,500.0	1.35	0.00	7,498.7	114.0	0.0	-114.0	0.00	0.00	0.00
7,600.0	1.35	0.00	7,598.6	116.4	0.0	-116.4	0.00	0.00	0.00
7,700.0	1.35	0.00	7,698.6	118.7	0.0	-118.7	0.00	0.00	0.00
7,800.0	1.35	0.00	7,798.6	121.1	0.0	-121.1	0.00	0.00	0.00
7,900.0	1.35	0.00	7,898.6	123.4	0.0	-123.4	0.00	0.00	0.00
8,000.0	1.35	0.00	7,998.5	125.8	0.0	-125.8	0.00	0.00	0.00
8,100.0	1.35	0.00	8,098.5	128.1	0.0	-128.1	0.00	0.00	0.00
8,200.0	1.35	0.00	8,198.5	130.4	0.0	-130.4	0.00	0.00	0.00
8,300.0	1.35	0.00	8,298.4	132.8	0.0	-132.8	0.00	0.00	0.00
8,400.0	1.35	0.00	8,398.4	135.1	0.0	-135.1	0.00	0.00	0.00
8,500.0	1.35	0.00	8,498.4	137.5	0.0	-137.5	0.00	0.00	0.00
8,600.0	1.35	0.00	8,598.4	139.8	0.0	-139.8	0.00	0.00	0.00
8,700.0	1.35	0.00	8,698.3	142.2	0.0	-142.2	0.00	0.00	0.00
8,800.0	1.35	0.00	8,798.3	144.5	0.0	-144.5	0.00	0.00	0.00
8,900.0	1.35	0.00	8,898.3	146.9	0.0	-146.9	0.00	0.00	0.00
9,000.0	1.35	0.00	8,998.3	149.2	0.0	-149.2	0.00	0.00	0.00
9,100.0	1.35	0.00	9,098.2	151.6	0.0	-151.6	0.00	0.00	0.00
9,200.0	1.35	0.00	9,198.2	153.9	0.0	-153.9	0.00	0.00	0.00
9,300.0	1.35	0.00	9,298.2	156.3	0.0	-156.3	0.00	0.00	0.00
9,400.0	1.35	0.00	9,398.1	158.6	0.0	-158.6	0.00	0.00	0.00
9,500.0	1.35	0.00	9,498.1	161.0	0.0	-161.0	0.00	0.00	0.00
9,600.0	1.35	0.00	9,598.1	163.3	0.0	-163.3	0.00	0.00	0.00
9,700.0	1.35	0.00	9,698.1	165.7	0.0	-165.7	0.00	0.00	0.00
9,800.0	1.35	0.00	9,798.0	168.0	0.0	-168.0	0.00	0.00	0.00
9,900.0	1.35	0.00	9,898.0	170.4	0.0	-170.4	0.00	0.00	0.00
10,000.0	1.35	0.00	9,998.0	172.7	0.0	-172.7	0.00	0.00	0.00
10,052.4	1.35	0.00	10,050.3	173.9	0.0	-173.9	0.00	0.00	0.00
10,100.0	0.63	0.00	10,098.0	174.8	0.0	-174.8	1.50	-1.50	0.00
10,142.1	0.00	0.00	10,140.0	175.0	0.0	-175.0	1.50	-1.50	0.00

Planning Report

Database:	Hobbs	Local Co-ordinate Reference:	Site Delaware Ranch 11/14 W2AP Fed Com #1H
Company:	Mewbourne Oil Company	TVD Reference:	WELL @ 2995.0usft (Original Well Elev)
Project:	Eddy County, New Mexico	MD Reference:	WELL @ 2995.0usft (Original Well Elev)
Site:	Delaware Ranch 11/14 W2AP Fed Com #1H	North Reference:	Grid
Well:	Sec 11, T26S, R28E	Survey Calculation Method:	Minimum Curvature
Wellbore:	BHL: 330' FSL & 425' FEL, Sec 14		
Design:	Design #1		

Planned Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
KOP @ 10140'									
10,200.0	5.79	179.73	10,197.9	172.1	0.0	-172.1	10.00	10.00	0.00
10,300.0	15.79	179.73	10,296.0	153.4	0.1	-153.4	10.00	10.00	0.00
10,400.0	25.79	179.73	10,389.3	117.9	0.3	-117.9	10.00	10.00	0.00
10,500.0	35.79	179.73	10,475.1	66.8	0.5	-66.8	10.00	10.00	0.00
10,600.0	45.79	179.73	10,550.7	1.6	0.8	-1.6	10.00	10.00	0.00
10,700.0	55.79	179.73	10,613.9	-75.8	1.2	75.8	10.00	10.00	0.00
10,780.1	63.80	179.73	10,654.2	-145.0	1.5	145.0	10.00	10.00	0.00
FTP: 330' FNL & 425' FEL, Sec 11									
10,800.0	65.79	179.73	10,662.6	-163.0	1.6	163.0	10.00	10.00	0.00
10,900.0	75.79	179.73	10,695.5	-257.3	2.0	257.3	10.00	10.00	0.00
11,000.0	85.79	179.73	10,711.5	-355.9	2.5	355.9	10.00	10.00	0.00
11,046.4	90.43	179.73	10,713.0	-402.3	2.7	402.3	10.00	10.00	0.00
LP: 587' FNL & 425' FEL, Sec 11									
11,100.0	90.43	179.73	10,712.6	-455.9	3.0	455.9	0.00	0.00	0.00
11,200.0	90.43	179.73	10,711.8	-555.8	3.4	555.9	0.00	0.00	0.00
11,300.0	90.43	179.73	10,711.1	-655.8	3.9	655.9	0.00	0.00	0.00
11,400.0	90.43	179.73	10,710.3	-755.8	4.4	755.9	0.00	0.00	0.00
11,500.0	90.43	179.73	10,709.6	-855.8	4.8	855.8	0.00	0.00	0.00
11,600.0	90.43	179.73	10,708.8	-955.8	5.3	955.8	0.00	0.00	0.00
11,700.0	90.43	179.73	10,708.1	-1,055.8	5.8	1,055.8	0.00	0.00	0.00
11,800.0	90.43	179.73	10,707.3	-1,155.8	6.2	1,155.8	0.00	0.00	0.00
11,900.0	90.43	179.73	10,706.5	-1,255.8	6.7	1,255.8	0.00	0.00	0.00
12,000.0	90.43	179.73	10,705.8	-1,355.8	7.2	1,355.8	0.00	0.00	0.00
12,100.0	90.43	179.73	10,705.0	-1,455.8	7.7	1,455.8	0.00	0.00	0.00
12,200.0	90.43	179.73	10,704.3	-1,555.8	8.1	1,555.8	0.00	0.00	0.00
12,300.0	90.43	179.73	10,703.5	-1,655.8	8.6	1,655.8	0.00	0.00	0.00
12,400.0	90.43	179.73	10,702.8	-1,755.8	9.1	1,755.8	0.00	0.00	0.00
12,500.0	90.43	179.73	10,702.0	-1,855.8	9.5	1,855.8	0.00	0.00	0.00
12,600.0	90.43	179.73	10,701.3	-1,955.8	10.0	1,955.8	0.00	0.00	0.00
12,700.0	90.43	179.73	10,700.5	-2,055.8	10.5	2,055.8	0.00	0.00	0.00
12,800.0	90.43	179.73	10,699.7	-2,155.8	10.9	2,155.8	0.00	0.00	0.00
12,900.0	90.43	179.73	10,699.0	-2,255.8	11.4	2,255.8	0.00	0.00	0.00
13,000.0	90.43	179.73	10,698.2	-2,355.8	11.9	2,355.8	0.00	0.00	0.00
13,100.0	90.43	179.73	10,697.5	-2,455.8	12.3	2,455.8	0.00	0.00	0.00
13,200.0	90.43	179.73	10,696.7	-2,555.8	12.8	2,555.8	0.00	0.00	0.00
13,300.0	90.43	179.73	10,696.0	-2,655.8	13.3	2,655.8	0.00	0.00	0.00
13,400.0	90.43	179.73	10,695.2	-2,755.8	13.8	2,755.8	0.00	0.00	0.00
13,500.0	90.43	179.73	10,694.4	-2,855.8	14.2	2,855.8	0.00	0.00	0.00
13,600.0	90.43	179.73	10,693.7	-2,955.8	14.7	2,955.8	0.00	0.00	0.00
13,700.0	90.43	179.73	10,692.9	-3,055.7	15.2	3,055.8	0.00	0.00	0.00
13,800.0	90.43	179.73	10,692.2	-3,155.7	15.6	3,155.8	0.00	0.00	0.00
13,900.0	90.43	179.73	10,691.4	-3,255.7	16.1	3,255.8	0.00	0.00	0.00
14,000.0	90.43	179.73	10,690.7	-3,355.7	16.6	3,355.8	0.00	0.00	0.00
14,100.0	90.43	179.73	10,689.9	-3,455.7	17.0	3,455.8	0.00	0.00	0.00
14,200.0	90.43	179.73	10,689.2	-3,555.7	17.5	3,555.8	0.00	0.00	0.00
14,300.0	90.43	179.73	10,688.4	-3,655.7	18.0	3,655.8	0.00	0.00	0.00
14,400.0	90.43	179.73	10,687.6	-3,755.7	18.4	3,755.8	0.00	0.00	0.00
14,500.0	90.43	179.73	10,686.9	-3,855.7	18.9	3,855.8	0.00	0.00	0.00
14,600.0	90.43	179.73	10,686.1	-3,955.7	19.4	3,955.8	0.00	0.00	0.00
14,700.0	90.43	179.73	10,685.4	-4,055.7	19.8	4,055.8	0.00	0.00	0.00
14,800.0	90.43	179.73	10,684.6	-4,155.7	20.3	4,155.8	0.00	0.00	0.00

Planning Report

Database: Hobbs
Company: Mewbourne Oil Company
Project: Eddy County, New Mexico
Site: Delaware Ranch 11/14 W2AP Fed Com #1H
Well: Sec 11, T26S, R28E
Wellbore: BHL: 330' FSL & 425' FEL, Sec 14
Design: Design #1

Local Co-ordinate Reference: Site Delaware Ranch 11/14 W2AP Fed Com #1H
TVD Reference: WELL @ 2995.0usft (Original Well Elev)
MD Reference: WELL @ 2995.0usft (Original Well Elev)
North Reference: Grid
Survey Calculation Method: Minimum Curvature

Planned Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
14,900.0	90.43	179.73	10,683.9	-4,255.7	20.8	4,255.8	0.00	0.00	0.00
15,000.0	90.43	179.73	10,683.1	-4,355.7	21.3	4,355.7	0.00	0.00	0.00
15,100.0	90.43	179.73	10,682.3	-4,455.7	21.7	4,455.7	0.00	0.00	0.00
15,200.0	90.43	179.73	10,681.6	-4,555.7	22.2	4,555.7	0.00	0.00	0.00
15,300.0	90.43	179.73	10,680.8	-4,655.7	22.7	4,655.7	0.00	0.00	0.00
15,400.0	90.43	179.73	10,680.1	-4,755.7	23.1	4,755.7	0.00	0.00	0.00
15,500.0	90.43	179.73	10,679.3	-4,855.7	23.6	4,855.7	0.00	0.00	0.00
15,600.0	90.43	179.73	10,678.6	-4,955.7	24.1	4,955.7	0.00	0.00	0.00
15,700.0	90.43	179.73	10,677.8	-5,055.7	24.5	5,055.7	0.00	0.00	0.00
15,800.0	90.43	179.73	10,677.1	-5,155.7	25.0	5,155.7	0.00	0.00	0.00
15,900.0	90.43	179.73	10,676.3	-5,255.7	25.5	5,255.7	0.00	0.00	0.00
16,000.0	90.43	179.73	10,675.5	-5,355.7	25.9	5,355.7	0.00	0.00	0.00
16,100.0	90.43	179.73	10,674.8	-5,455.7	26.4	5,455.7	0.00	0.00	0.00
16,200.0	90.43	179.73	10,674.0	-5,555.6	26.9	5,555.7	0.00	0.00	0.00
16,300.0	90.43	179.73	10,673.3	-5,655.6	27.4	5,655.7	0.00	0.00	0.00
16,400.0	90.43	179.73	10,672.5	-5,755.6	27.8	5,755.7	0.00	0.00	0.00
16,500.0	90.43	179.73	10,671.8	-5,855.6	28.3	5,855.7	0.00	0.00	0.00
16,600.0	90.43	179.73	10,671.0	-5,955.6	28.8	5,955.7	0.00	0.00	0.00
16,700.0	90.43	179.73	10,670.3	-6,055.6	29.2	6,055.7	0.00	0.00	0.00
16,800.0	90.43	179.73	10,669.5	-6,155.6	29.7	6,155.7	0.00	0.00	0.00
16,900.0	90.43	179.73	10,668.7	-6,255.6	30.2	6,255.7	0.00	0.00	0.00
17,000.0	90.43	179.73	10,668.0	-6,355.6	30.6	6,355.7	0.00	0.00	0.00
17,100.0	90.43	179.73	10,667.2	-6,455.6	31.1	6,455.7	0.00	0.00	0.00
17,200.0	90.43	179.73	10,666.5	-6,555.6	31.6	6,555.7	0.00	0.00	0.00
17,300.0	90.43	179.73	10,665.7	-6,655.6	32.0	6,655.7	0.00	0.00	0.00
17,400.0	90.43	179.73	10,665.0	-6,755.6	32.5	6,755.7	0.00	0.00	0.00
17,500.0	90.43	179.73	10,664.2	-6,855.6	33.0	6,855.7	0.00	0.00	0.00
17,600.0	90.43	179.73	10,663.4	-6,955.6	33.5	6,955.7	0.00	0.00	0.00
17,700.0	90.43	179.73	10,662.7	-7,055.6	33.9	7,055.7	0.00	0.00	0.00
17,800.0	90.43	179.73	10,661.9	-7,155.6	34.4	7,155.7	0.00	0.00	0.00
17,900.0	90.43	179.73	10,661.2	-7,255.6	34.9	7,255.7	0.00	0.00	0.00
18,000.0	90.43	179.73	10,660.4	-7,355.6	35.3	7,355.7	0.00	0.00	0.00
18,100.0	90.43	179.73	10,659.7	-7,455.6	35.8	7,455.7	0.00	0.00	0.00
18,200.0	90.43	179.73	10,658.9	-7,555.6	36.3	7,555.7	0.00	0.00	0.00
18,300.0	90.43	179.73	10,658.2	-7,655.6	36.7	7,655.7	0.00	0.00	0.00
18,400.0	90.43	179.73	10,657.4	-7,755.6	37.2	7,755.7	0.00	0.00	0.00
18,500.0	90.43	179.73	10,656.6	-7,855.6	37.7	7,855.6	0.00	0.00	0.00
18,600.0	90.43	179.73	10,655.9	-7,955.6	38.1	7,955.6	0.00	0.00	0.00
18,700.0	90.43	179.73	10,655.1	-8,055.6	38.6	8,055.6	0.00	0.00	0.00
18,800.0	90.43	179.73	10,654.4	-8,155.5	39.1	8,155.6	0.00	0.00	0.00
18,900.0	90.43	179.73	10,653.6	-8,255.5	39.6	8,255.6	0.00	0.00	0.00
19,000.0	90.43	179.73	10,652.9	-8,355.5	40.0	8,355.6	0.00	0.00	0.00
19,100.0	90.43	179.73	10,652.1	-8,455.5	40.5	8,455.6	0.00	0.00	0.00
19,200.0	90.43	179.73	10,651.3	-8,555.5	41.0	8,555.6	0.00	0.00	0.00
19,300.0	90.43	179.73	10,650.6	-8,655.5	41.4	8,655.6	0.00	0.00	0.00
19,400.0	90.43	179.73	10,649.8	-8,755.5	41.9	8,755.6	0.00	0.00	0.00
19,500.0	90.43	179.73	10,649.1	-8,855.5	42.4	8,855.6	0.00	0.00	0.00
19,600.0	90.43	179.73	10,648.3	-8,955.5	42.8	8,955.6	0.00	0.00	0.00
19,700.0	90.43	179.73	10,647.6	-9,055.5	43.3	9,055.6	0.00	0.00	0.00
19,800.0	90.43	179.73	10,646.8	-9,155.5	43.8	9,155.6	0.00	0.00	0.00
19,900.0	90.43	179.73	10,646.1	-9,255.5	44.2	9,255.6	0.00	0.00	0.00
20,000.0	90.43	179.73	10,645.3	-9,355.5	44.7	9,355.6	0.00	0.00	0.00
20,100.0	90.43	179.73	10,644.5	-9,455.5	45.2	9,455.6	0.00	0.00	0.00

Planning Report

Database:	Hobbs	Local Co-ordinate Reference:	Site Delaware Ranch 11/14 W2AP Fed Com #1H
Company:	Mewbourne Oil Company	TVD Reference:	WELL @ 2995.0usft (Original Well Elev)
Project:	Eddy County, New Mexico	MD Reference:	WELL @ 2995.0usft (Original Well Elev)
Site:	Delaware Ranch 11/14 W2AP Fed Com #1H	North Reference:	Grid
Well:	Sec 11, T26S, R28E	Survey Calculation Method:	Minimum Curvature
Wellbore:	BHL: 330' FSL & 425' FEL, Sec 14		
Design:	Design #1		

Planned Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
20,200.0	90.43	179.73	10,643.8	-9,555.5	45.7	9,555.6	0.00	0.00	0.00
20,300.0	90.43	179.73	10,643.0	-9,655.5	46.1	9,655.6	0.00	0.00	0.00
20,400.0	90.43	179.73	10,642.3	-9,755.5	46.6	9,755.6	0.00	0.00	0.00
20,500.0	90.43	179.73	10,641.5	-9,855.5	47.1	9,855.6	0.00	0.00	0.00
20,600.0	90.43	179.73	10,640.8	-9,955.5	47.5	9,955.6	0.00	0.00	0.00
20,700.0	90.43	179.73	10,640.0	-10,055.5	48.0	10,055.6	0.00	0.00	0.00
20,700.5	90.43	179.73	10,640.0	-10,056.0	48.0	10,056.1	0.00	0.00	0.00

BHL: 330' FSL & 425' FEL, Sec 14

Design Targets

Target Name - hit/miss target - Shape	Dip Angle (°)	Dip Dir. (°)	TVD (usft)	+N/-S (usft)	+E/-W (usft)	Northing (usft)	Easting (usft)	Latitude	Longitude
SL: 185' FNL & 425' FEL - plan hits target center - Point	0.00	0.00	0.0	0.0	0.0	387,045.00	587,724.00	32° 3' 49.628 N	104° 3' 0.548 W
KOP @ 10140' - plan hits target center - Point	0.00	0.00	10,140.0	175.0	0.0	387,220.00	587,724.00	32° 3' 51.360 N	104° 3' 0.542 W
BHL: 330' FSL & 425' FE - plan hits target center - Point	0.00	0.00	10,640.0	-10,056.0	48.0	376,989.00	587,772.00	32° 2' 10.107 N	104° 3' 0.296 W
FTP: 330' FNL & 425' FE - plan hits target center - Point	0.00	0.00	10,654.1	-145.0	1.5	386,900.00	587,725.50	32° 3' 48.193 N	104° 3' 0.535 W
LP: 587' FNL & 425' FEL - plan hits target center - Point	0.00	0.00	10,713.0	-402.3	2.7	386,642.70	587,726.70	32° 3' 45.647 N	104° 3' 0.529 W

5M BOPE & Closed Loop Equipment Schematic



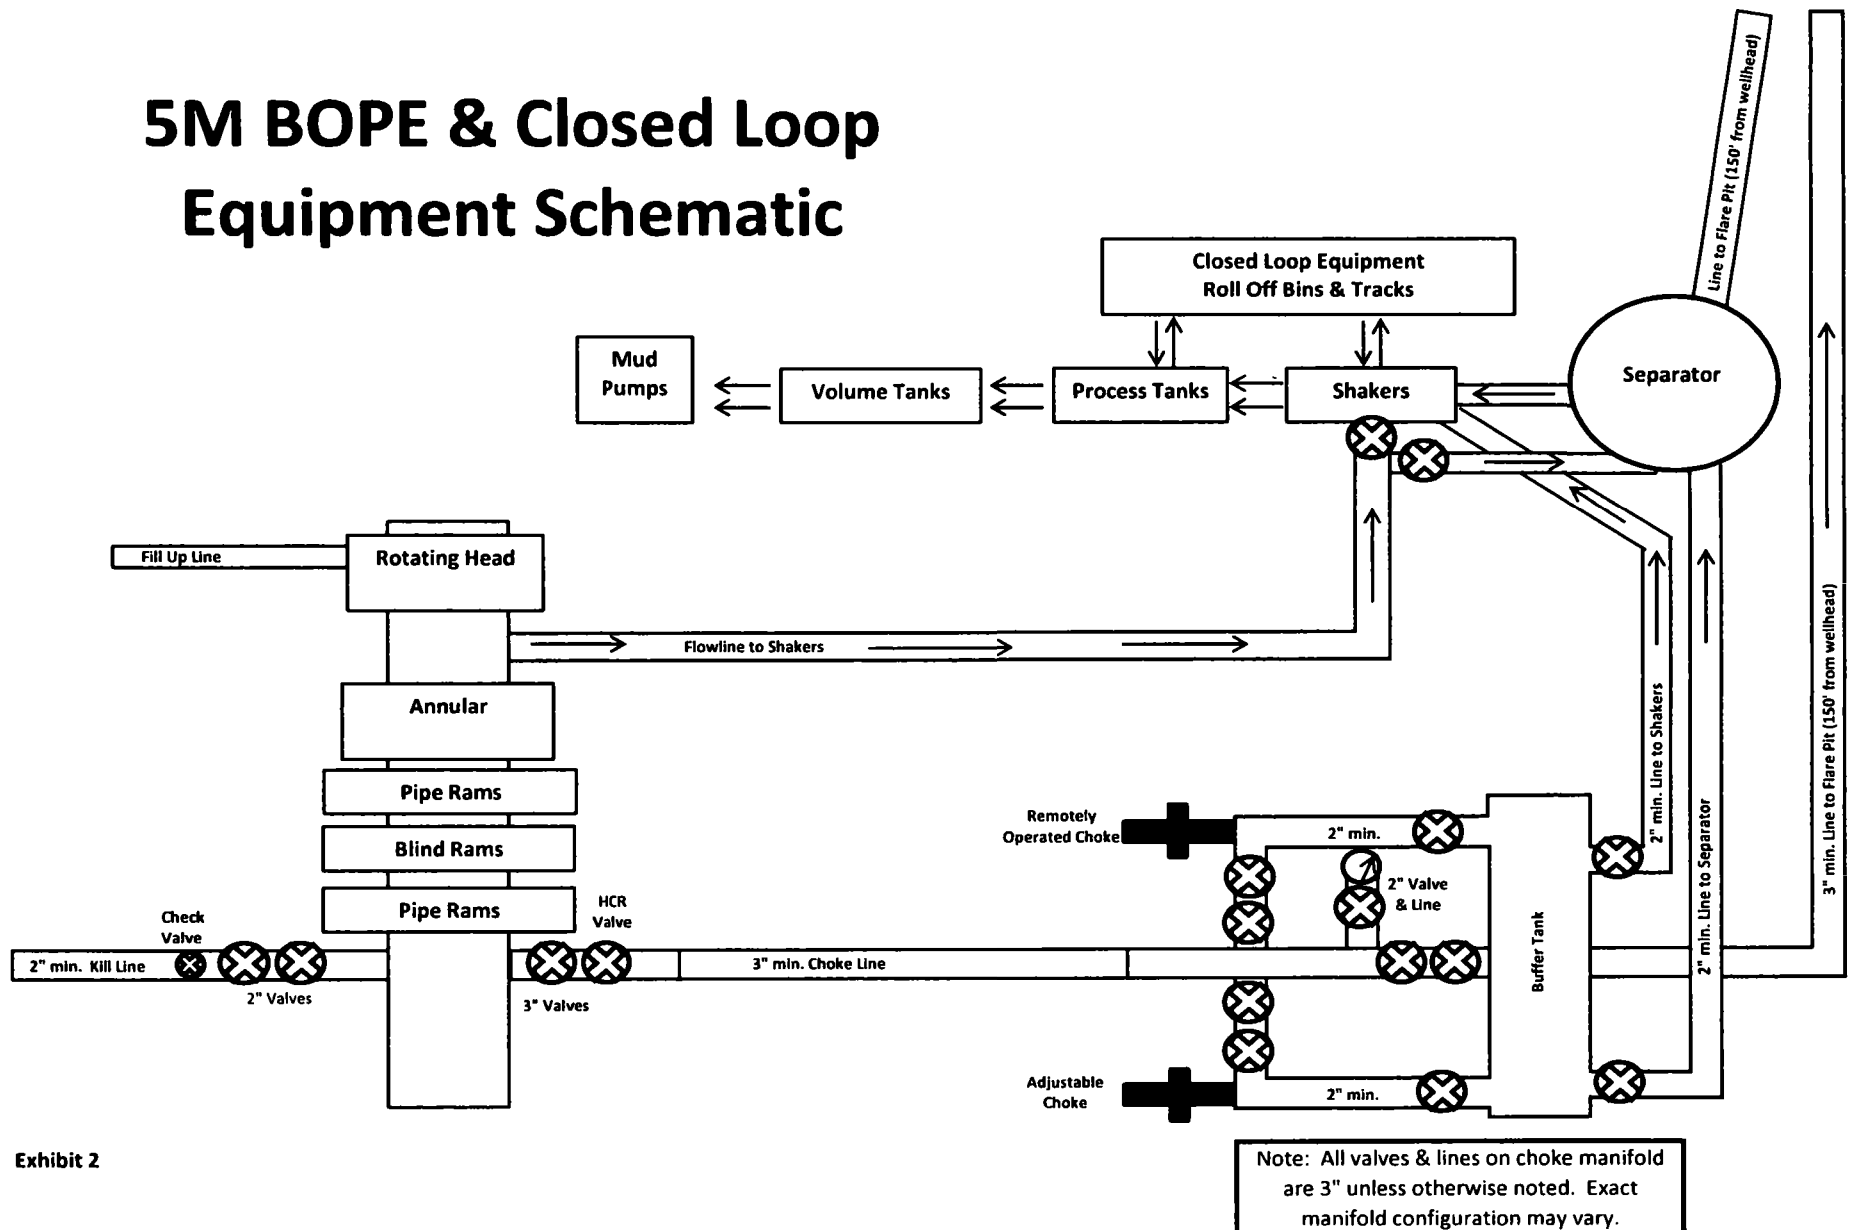


Exhibit 2

Hydril "GK"
13 5/8" 5M

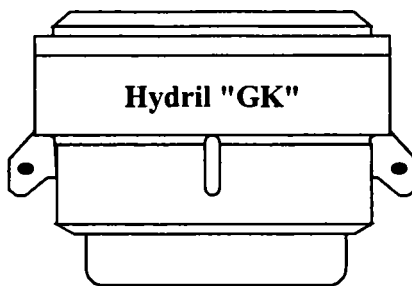


Hydril "GK"


Cameron Type U
13 5/8" 5M



4 1/2" x 5 7/8" VBR



BLIND RAMS

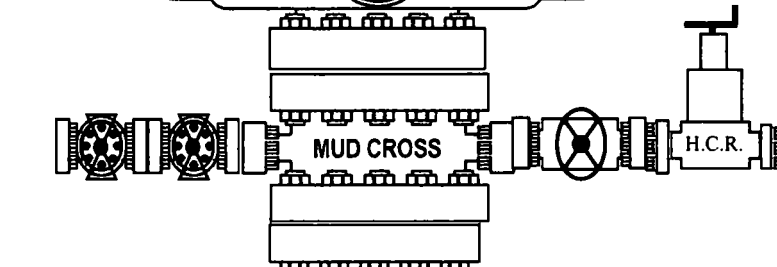

MUD CROSS

H.C.R.




7" RAMS

13 5/8" 5M

13 5/8" 5M


13 5/8" 5M



CAMERON

A Schlumberger Company

13-5/8" MN-DS Wellhead System

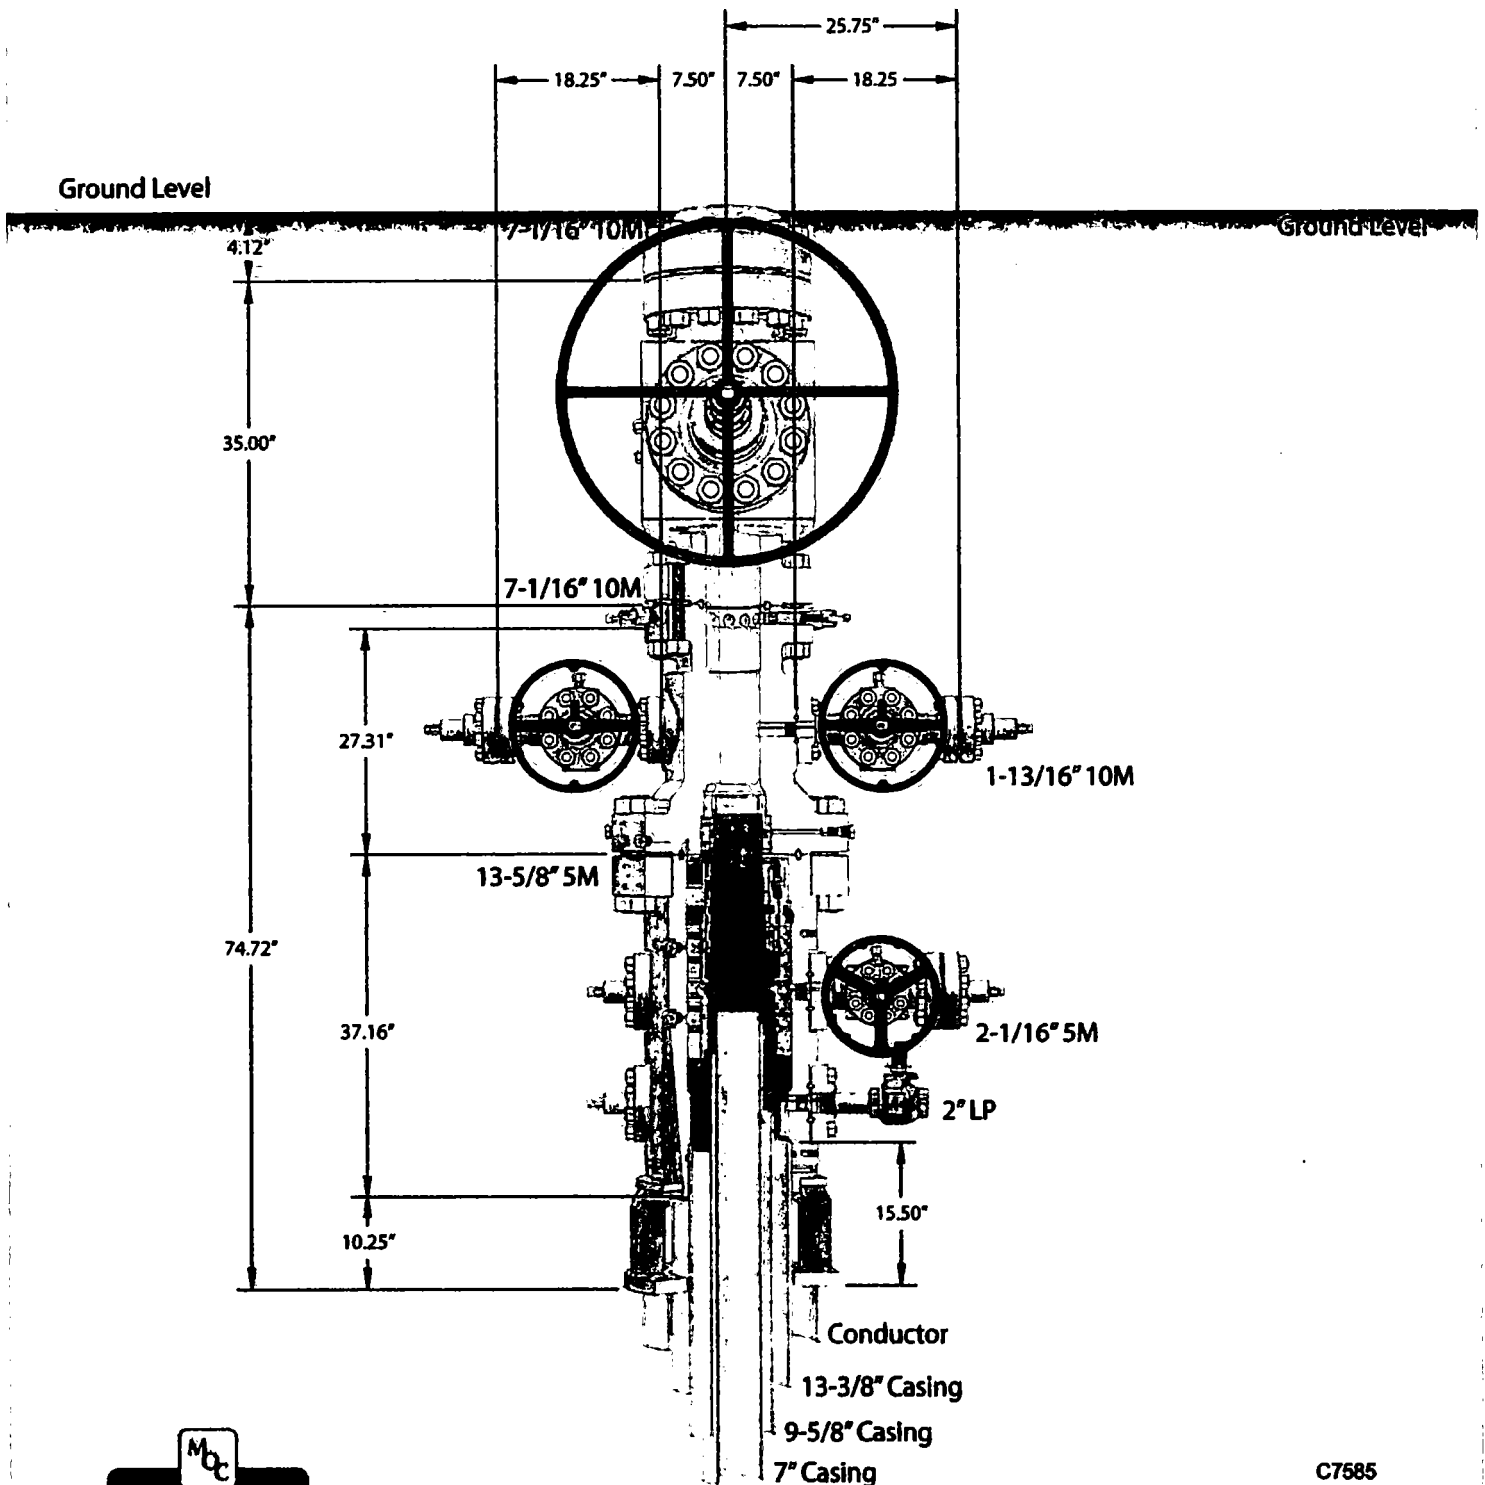

C7585
Rev. 02

NOTE: All dimensions on this drawing are estimated measurements and should be evaluated by engineering.

6 1/2" flange 57" conductor cut-off
79

PECOS DISTRICT

DRILLING CONDITIONS OF APPROVAL

OPERATOR'S NAME:	Mewbourne Oil Company
LEASE NO.:	NMNM107374
WELL NAME & NO.:	DelawareRanch 11/14 W2AP FedCom 1H
SURFACE HOLE FOOTAGE:	185'/N & 425'/E
BOTTOM HOLE FOOTAGE:	330'/S & 425'/E
LOCATION:	Section 11, T.26 S., R.28 E., NMPM
COUNTY:	Eddy County, New Mexico

COA

All previous COAs still apply expect the following:

H2S	<input type="radio"/> Yes	<input checked="" type="radio"/> No	
Potash	<input checked="" type="radio"/> None	<input type="radio"/> Secretary	<input type="radio"/> R-111-P
Cave/Karst Potential	<input type="radio"/> Low	<input checked="" type="radio"/> Medium	<input type="radio"/> High
Variance	<input type="radio"/> None	<input checked="" type="radio"/> Flex Hose	<input type="radio"/> Other
Wellhead	<input type="radio"/> Conventional	<input checked="" type="radio"/> Multibowl	<input type="radio"/> Both
Other	<input type="checkbox"/> 4 String Area	<input type="checkbox"/> Capitan Reef	<input type="checkbox"/> WIPP

A. Hydrogen Sulfide

Hydrogen Sulfide (H2S) monitors shall be installed prior to drilling out the surface shoe. If H2S is detected in concentrations greater than 100 ppm, the Hydrogen Sulfide area shall meet Onshore Order 6 requirements, which includes equipment and personnel/public protection items. If Hydrogen Sulfide is encountered, provide measured values and formations to the BLM.

B. CASING

1. The 13-3/8 inch surface casing shall be set at approximately 250 feet (a minimum of 25 feet into the Rustler Anhydrite and above the salt) and cemented to the surface.
 - a. If cement does not circulate to the surface, the appropriate BLM office shall be notified and a temperature survey utilizing an electronic type temperature survey with surface log readout will be used or a cement bond log shall be run to verify the top of the cement. Temperature survey will be run a minimum of six hours after pumping cement and ideally between 8-10 hours after completing the cement job.
 - b. Wait on cement (WOC) time for a primary cement job will be a minimum of 8 hours or 500 pounds compressive strength, whichever is greater. (This is to include the lead cement)
 - c. Wait on cement (WOC) time for a remedial job will be a minimum of 4 hours

after bringing cement to surface or 500 pounds compressive strength, whichever is greater.

- d. If cement falls back, remedial cementing will be done prior to drilling out that string.

2. The minimum required fill of cement behind the **9-5/8** inch intermediate casing is:
 - Cement to surface. If cement does not circulate see B.1.a, c-d above. **Additional cement maybe required. Excess calculates to 24%.**

Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry due to cave/karst or potash.

- ❖ In Medium Cave/Karst Areas if cement does not circulate to surface on the first two casing strings, the cement on the 3rd casing string must come to surface.

3. The minimum required fill of cement behind the **7** inch production casing is:

Operator has proposed a DV tool, the depth may be adjusted as long as the cement is changed proportionally. The DV tool may be cancelled if cement circulates to surface on the first stage.

- a. First stage to DV tool: Cement to circulate. If cement does not circulate off the DV tool, contact the appropriate BLM office before proceeding with second stage cement job.
 - b. Second stage above DV tool: Cement should tie-back at least 200 feet into previous casing string. Operator shall provide method of verification.
4. The minimum required fill of cement behind the **4-1/2** inch production liner is:
 - Cement should tie-back 100' into the previous casing. Operator shall provide method of verification. **Additional cement maybe required. Excess calculates to -45%.**

C. PRESSURE CONTROL

1. Variance approved to use flex line from BOP to choke manifold. Manufacturer's specification to be readily available. No external damage to flex line. Flex line to be installed as straight as possible (no hard bends).
2. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **5000 (5M)** psi.

GENERAL REQUIREMENTS

The BLM is to be notified in advance for a representative to witness:

- a. Spudding well (minimum of 24 hours)
- b. Setting and/or Cementing of all casing strings (minimum of 4 hours)
- c. BOPE tests (minimum of 4 hours)

☒ Chaves and Roosevelt Counties
Call the Roswell Field Office, 2909 West Second St., Roswell NM 88201.
During office hours call (575) 627-0272.
After office hours call (575)

☒ Eddy County
Call the Carlsbad Field Office, 620 East Greene St., Carlsbad, NM 88220,
(575) 361-2822

☒ Lea County
Call the Hobbs Field Station, 414 West Taylor, Hobbs NM 88240, (575)
393-3612

1. Unless the production casing has been run and cemented or the well has been properly plugged, the drilling rig shall not be removed from over the hole without prior approval.
 - a. In the event the operator has proposed to drill multiple wells utilizing a skid/walking rig. Operator shall secure the wellbore on the current well, after installing and testing the wellhead, by installing a blind flange of like pressure rating to the wellhead and a pressure gauge that can be monitored while drilling is performed on the other well(s).
 - b. When the operator proposes to set surface casing with Spudder Rig
 - Notify the BLM when moving in and removing the Spudder Rig.
 - Notify the BLM when moving in the 2nd Rig. Rig to be moved in within 90 days of notification that Spudder Rig has left the location.
 - BOP/BOPE test to be conducted per Onshore Oil and Gas Order No. 2 as soon as 2nd Rig is rigged up on well.
2. Floor controls are required for 3M or Greater systems. These controls will be on the rig floor, unobstructed, readily accessible to the driller and will be operational at all times during drilling and/or completion activities. Rig floor is defined as the area immediately around the rotary table; the area immediately above the substructure on which the draw works are located, this does not include the dog house or stairway area.

3. The record of the drilling rate along with the GR/N well log (one log per well pad is acceptable) run from TD to surface (horizontal well – vertical portion of hole) shall be submitted to the BLM office as well as all other logs run on the borehole 30 days from completion. If available, a digital copy of the logs is to be submitted in addition to the paper copies. The Rustler top and top and bottom of Salt are to be recorded on the Completion Report.

A.. CASING

1. Changes to the approved APD casing program need prior approval if the items substituted are of lesser grade or different casing size or are Non-API. The Operator can exchange the components of the proposal with that of superior strength (i.e. changing from J-55 to N-80, or from 36# to 40#). Changes to the approved cement program need prior approval if the altered cement plan has less volume or strength or if the changes are substantial (i.e. Multistage tool, ECP, etc.). The initial wellhead installed on the well will remain on the well with spools used as needed.
2. Wait on cement (WOC) for Potash Areas: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi for all cement blends, 2) until cement has been in place at least 24 hours. WOC time will be recorded in the driller's log. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
3. Wait on cement (WOC) for Water Basin: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi at the shoe, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. See individual casing strings for details regarding lead cement slurry requirements. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
4. Provide compressive strengths including hours to reach required 500 pounds compressive strength prior to cementing each casing string. Have well specific cement details onsite prior to pumping the cement for each casing string.
5. No pea gravel permitted for remedial or fall back remedial without prior authorization from the BLM engineer.
6. On that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Formation at the shoe shall be tested to a minimum of the mud weight equivalent anticipated to control the formation pressure to the next casing depth or at total depth of the well. This test shall be performed before drilling more than 20 feet of new hole.

7. If hardband drill pipe is rotated inside casing, returns will be monitored for metal. If metal is found in samples, drill pipe will be pulled and rubber protectors which have a larger diameter than the tool joints of the drill pipe will be installed prior to continuing drilling operations.
8. Whenever a casing string is cemented in the R-111-P potash area, the NMOCD requirements shall be followed.

B. PRESSURE CONTROL

1. All blowout preventer (BOP) and related equipment (BOPE) shall comply with well control requirements as described in Onshore Oil and Gas Order No. 2 and API RP 53 Sec. 17.
2. If a variance is approved for a flexible hose to be installed from the BOP to the choke manifold, the following requirements apply: The flex line must meet the requirements of API 16C. Check condition of flexible line from BOP to choke manifold, replace if exterior is damaged or if line fails test. Line to be as straight as possible with no hard bends and is to be anchored according to Manufacturer's requirements. The flexible hose can be exchanged with a hose of equal size and equal or greater pressure rating. Anchor requirements, specification sheet and hydrostatic pressure test certification matching the hose in service, to be onsite for review. These documents shall be posted in the company man's trailer and on the rig floor.
3. 5M or higher system requires an HCR valve, remote kill line and annular to match. The remote kill line is to be installed prior to testing the system and tested to stack pressure.
4. If the operator has proposed a multi-bowl wellhead assembly in the APD. The following requirements must be met:
 - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
 - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
 - c. Manufacturer representative shall install the test plug for the initial BOP test.
 - d. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
 - e. Whenever any seal subject to test pressure is broken, all the tests in OOGO2.III.A.2.i must be followed.

5. The appropriate BLM office shall be notified a minimum of 4 hours in advance for a representative to witness the tests.
- a. In a water basin, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. The casing cut-off and BOP installation can be initiated four hours after installing the slips, which will be approximately six hours after bumping the plug. For those casing strings not using slips, the minimum wait time before cut-off is eight hours after bumping the plug. BOP/BOPE testing can begin after cut-off or once cement reaches 500 psi compressive strength (including lead when specified), whichever is greater. However, if the float does not hold, cut-off cannot be initiated until cement reaches 500 psi compressive strength (including lead when specified).
 - b. In potash areas, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. For all casing strings, casing cut-off and BOP installation can be initiated at twelve hours after bumping the plug. However, **no tests** shall commence until the cement has had a minimum of 24 hours setup time, except the casing pressure test can be initiated immediately after bumping the plug (only applies to single stage cement jobs).
 - c. The tests shall be done by an independent service company utilizing a test plug. The results of the test shall be reported to the appropriate BLM office.
 - d. The test shall be run on a 5000 psi chart for a 2-3M BOP/BOP, on a 10000 psi chart for a 5M BOP/BOPE and on a 15000 psi chart for a 10M BOP/BOPE. If a linear chart is used, it shall be a one hour chart. A circular chart shall have a maximum 2 hour clock. If a twelve hour or twenty-four hour chart is used, tester shall make a notation that it is run with a two hour clock.
 - e. All tests are required to be recorded on a calibrated test chart. A copy of the BOP/BOPE test chart and a copy of independent service company test will be submitted to the appropriate BLM office.
 - f. The BOP/BOPE test shall include a low pressure test from 250 to 300 psi. The test will be held for a minimum of 10 minutes. This test shall be performed prior to the test at full stack pressure.
 - g. BOP/BOPE must be tested by an independent service company within 500 feet of the top of the Wolfcamp formation if the time between the setting of the intermediate casing and reaching this depth exceeds 20 days. This test does not exclude the test prior to drilling out the casing shoe as per Onshore Order No. 2.

C. DRILLING MUD

Mud system monitoring equipment, with derrick floor indicators and visual and audio alarms, shall be operating before drilling into the Wolfcamp formation, and shall be used until production casing is run and cemented.

D. WASTE MATERIAL AND FLUIDS

All waste (i.e. drilling fluids, trash, salts, chemicals, sewage, gray water, etc.) created as a result of drilling operations and completion operations shall be safely contained and disposed of properly at a waste disposal facility. No waste material or fluid shall be disposed of on the well location or surrounding area.

Porto-johns and trash containers will be on-location during fracturing operations or any other crew-intensive operations.

Waste Minimization Plan (WMP)

In the interest of resource development, submission of additional well gas capture development plan information is deferred but may be required by the BLM Authorized Officer at a later date.

ZS 012419
