

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

Operator

FORM APPROVED
OMB NO. 1004-0137
Expires: January 31, 2018**SUNDRY NOTICES AND REPORTS ON WELLS**
*Do not use this form for proposals to drill or to re-enter an abandoned well. Use form 3160-3 (APD) for such proposals.*5. Lease Serial No.
NMLC063875A

6. If Indian, Allottee or Tribe Name

SUBMIT IN TRIPLICATE - Other instructions on page 27. If Unit or CA/Agreement, Name and/or No.
891000303X1. Type of Well
☐ Oil Well ☒ Gas Well ☐ Other8. Well Name and No.
POKER LAKE-UNIT 27 BD 102H2. Name of Operator
XTO PERMIAN OPERATING LLC
Contact: KELLY KARDOS
E-Mail: kelly_kardos@xtoenergy.com9. API Well No.
30-015-46245-00-X13a. Address
6401 HOLIDAY HILL ROAD BLDG 5
MIDLAND, TX 797073b. Phone No. (include area code)
Ph: 432-620-437410. Field and Pool or Exploratory Area
PURPLE SAGE-WOLFCAMP (GAS)4. Location of Well (Footage, Sec., T., R., M., or Survey Description)
Sec 27 T25S R30E SWNW 2510FNL: 663FWL
32.101524 N Lat, 103.875427 W Lon.11. County or Parish, State
EDDY COUNTY, NM**12. CHECK THE APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA**

TYPE OF SUBMISSION	TYPE OF ACTION			
☒ Notice of Intent	☐ Acidize	☐ Deepen	☐ Production (Start/Resume)	☐ Water Shut-Off
☐ Subsequent Report	☐ Alter Casing	☐ Hydraulic Fracturing	☐ Reclamation	☐ Well Integrity
☐ Final Abandonment Notice	☐ Casing Repair	☐ New Construction	☐ Recomplete	☒ Other
	☐ Change Plans	☐ Plug and Abandon	☐ Temporarily Abandon	Change to Original APD
	☐ Convert to Injection	☐ Plug Back	☐ Water Disposal	

13. Describe Proposed or Completed Operation: Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recompleat horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports must be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompleat in a new interval, a Form 3160-4 must be filed once testing has been completed. Final Abandonment Notices must be filed only after all requirements, including reclamation, have been completed and the operator has determined that the site is ready for final inspection.

XTO Permian Operating, LLC requests permission to make the following changes to the original APD:

Change the casing/cement design per the attached drilling program.

XTO requests to not utilize centralizers in the curve and lateral.

XTO requests a variance to be able to batch drill this well if necessary. In doing so, XTO will set each casing string and ensure that the well is cemented properly and the well is static with floats holding, no pressure on the csg annulus, and the installation of a 10K TA cap as per recommendations. XTO will contact the BLM to skid the rig to drill the remaining wells on the pad. Once surface and intermediate strings are all completed, XTO will begin drilling the production hole on each of the wells.

ATTACHED FOR
RECEIVED
JAN 27 2020

14. I hereby certify that the foregoing is true and correct.

Electronic Submission #497786 verified by the BLM Well Information System
For XTO PERMIAN OPERATING LLC, sent to the Carlsbad
Committed to AFMSS for processing by JENNIFER SANCHEZ on 01/07/2020 (20JAS0073SE)

Name (Printed/Typed) KELLY KARDOS

Title REGULATORY COORDINATOR

Signature (Electronic Submission)

Date 01/06/2020

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved By

Title BUREAU OF LAND MANAGEMENT

Date

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Office S.WELL FIELD OFFICE

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 212 make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Instructions on page 2)

**** BLM REVISED ** BLM REVISED ** BLM REVISED ** BLM REVISED ** BLM REVISED ****

accepted 2/4/20 KS

Additional data for EC transaction #497786 that would not fit on the form

32. Additional remarks, continued

Poker Lake Unit 27 BD 161H 30-015-46249
Poker Lake Unit 27 BD 121H 30-015-46264
Poker Lake Unit 27 BD 102H 30-015-46245
Poker Lake Unit 27 BD 152H 30-015-46257
Poker Lake Unit 27 BD 122H 30-015-46265

Revisions to Operator-Submitted EC Data for Sundry Notice #497786

	Operator Submitted	BLM Revised (AFMSS)
Sundry Type:	APDCH NOI	APDCH NOI
Lease:	NMLC063875A	NMLC063875A
Agreement:	NMNM71016X ⁴	891000303X (NMNM71016X)
Operator:	XTO PERMIAN OPERATING, LLC 6401 HOLIDAY HILL RD.BLDG 5 MIDLAND, TX 79707 Ph: 432-620-4374	XTO PERMIAN OPERATING LLC 6401 HOLIDAY HILL ROAD BLDG 5 MIDLAND, TX 79707 Ph: 432.683 2277
Admin Contact:	KELLY KARDOS REGULATORY COORDINATOR E-Mail: kelly_kardos@xtoenergy.com Ph: 432-620-4374	KELLY KARDOS REGULATORY COORDINATOR E-Mail: kelly_kardos@xtoenergy.com Ph: 432-620-4374
Tech Contact:	KELLY KARDOS REGULATORY COORDINATOR E-Mail: kelly_kardos@xtoenergy.com Ph: 432-620-4374	KELLY KARDOS REGULATORY COORDINATOR E-Mail: kelly_kardos@xtoenergy.com Ph: 432-620-4374
Location:		
State:	NM	NM
County:	EDDY	EDDY
Field/Pool:	PURPLE SAGE WOLFCAMP	PURPLE SAGE-WOLFCAMP (GAS)
Well/Facility:	POKER LAKE UNIT 27 BD 102H Sec 27 T25S R30E Mer NMP SWNW 2510FNL 633FWL	POKER LAKE UNIT 27 BD 102H Sec 27 T25S R30E SWNW 2510FNL 663FWL 32.101524 N Lat, 103.875427 W Lon

DRILLING PLAN: BLM COMPLIANCE
(Supplement to BLM 3160-3)

XTO Energy Inc.
Poker Lake Unit 27 Brushy Draw 102H
Projected TD: 26827' MD / 11099' TVD
SHL: 2510' FNL & 663' FWL, Section 27, T25S, R30E
BHL: 2440' FNL & 750' FWL, Section 10, T26S, R30E
Eddy County, NM

1. Geologic Name of Surface Formation

A. Quaternary

2. Estimated Tops of Geological Markers & Depths of Anticipated Fresh Water, Oil or Gas

Formation	Well Depth (TVD)	Water/Oil/Gas
Rustler	1061'	Water
Top of Salt	1351'	Water
Base of Salt	3641'	Water
Delaware	3856'	Water
Bone Spring	7661'	Water
1st Bone Spring Ss	8596'	Water/Oil/Gas
2nd Bone Spring Ss	9399'	Water/Oil/Gas
3rd Bone Spring Ss	10556'	Water/Oil/Gas
Wolfcamp Shale	10956'	Water/Oil/Gas
Wolfcamp Y	11075'	Water/Oil/Gas
Target/Land Curve	11099'	Water/Oil/Gas

*** Hydrocarbons @ Brushy Canyon

*** Groundwater depth 40' (per NM State Engineers Office).

No other formations are expected to yield oil, gas or fresh water in measurable volumes. The surface fresh water sands will be protected by setting 13 3/8" inch casing @ 1250' (101' above the salt) and circulating cement back to surface. The 9-5/8" intermediate casing will be set at 10450' and bring TOC back 200' inside the previous shoe. An 8-3/4 inch curve and lateral hole will be drilled to MD/TD and 5-1/2 inch casing will be set at TD and cemented back 500' into the 9-5/8" casing shoe.

3. Casing Design

Hole Size	Depth	OD Csg	Weight	Collar	Grade	New/Used	SF Burst	SF Collapse	SF Tension
17-1/2"	0' - 1250'	13 3/8"	68	STC	J-55	New	1.20	3.45	7.94
12-1/4"	0' - 10450'	9-5/8"	40	BTC	HCL-80	New	1.59	1.33	2.27
8-3/4" - 8-1/2"	0' - 26827'	5-1/2"	20	BTC	P-110	New	1.20	1.83	1.98

XTO requests to not utilize centralizers in the curve and lateral

9-5/8" Collapse analyzed using 50% evacuation based on regional experience.

5-1/2" Tension calculated using vertical hanging weight plus the lateral weight multiplied by a friction factor of 0.35

Test on Casing will be limited to 70% burst of the casing or 1500 psi, whichever is less

Wellhead:

Permanent Wellhead - GE RSH Multibowl System

A. Starting Head: 13-5/8" 10M top flange x 13-3/8" SOW bottom

B. Tubing Head: 13-5/8" 10M bottom flange x 7-1/16" 15M top flange

Wellhead will be installed by manufacturer's representatives.

Manufacturer will monitor welding process to ensure appropriate temperature of seal.

Operator will test the 9-5/8" casing per BLM Onshore Order 2

Wellhead Manufacturer representative will not be present for BOP test plug installation

4. Cement Program

Surface Casing: 13 3/8", 68 New J-55, STC casing to be set at +/- 1250'

Lead: 700 sxs EconoCem-HLTRRC (mixed at 12.9 ppg, 1.87 ft³/sx, 10.13 gal/sx water)
Tail: 300 sxs Halcem-C + 2% CaCl (mixed at 14.8 ppg, 1.35 ft³/sx, 6.39 gal/sx water)
Compressives: 12-hr = 900 psi 24 hr = 1500 psi
TOC @ Surface

Intermediate Casing: 9-5/8", 40 New HCL-80, BTC casing to be set at +/- 10450'

ECP/DV Tool to be set at 6000'

1st Stage

Lead: 1150 sxs EconoCem-HLTRRC (mixed at 12.9 ppg, 1.87 ft³/sx, 10.13 gal/sx water)
Tail: 460 sxs Halcem-C + 2% CaCl (mixed at 14.8 ppg, 1.35 ft³/sx, 6.39 gal/sx water)
Compressives: 12-hr = 900 psi 24 hr = 1500 psi

2nd Stage

Lead: 1330 sxs EconoCem-HLTRRC (mixed at 12.9 ppg, 1.88 ft³/sx, 10.13 gal/sx water)
Tail: 470 sxs Halcem-C + 2% CaCl (mixed at 14.8 ppg, 1.33 ft³/sx, 6.39 gal/sx water)
Compressives: 12-hr = 900 psi 24 hr = 1500 psi
TOC @ 1000'

Production Casing: 5-1/2", 20 New P-110, BTC casing to be set at +/- 26827'

Tail: 3140 sxs VersaCem (mixed at 13.2 ppg, 1.61 ft³/sx, 8.38 gal/sx water)
Compressives: 12-hr = 1375 psi 24 hr = 2285 psi

5. Pressure Control Equipment

Once the permanent WH is installed on the 13-3/8 casing, the blow out preventer equipment (BOP) will consist of a 13-5/8" minimum 5M Hydril and a 13-5/8" minimum 5M 3-Ram BOP. MASP should not exceed 3618 psi. In any instance where 10M BOP is required by BLM, XTO requests a variance to utilize 5M annular with 10M ram preventers (a common BOP configuration, which allows use of 10M rams in unlikely event that pressures exceed 5M). Also a variance is requested to test the 5M annular to 70% of working pressure at 3500 psi.

All BOP testing will be done by an independent service company. Annular pressure tests will be limited to 70% of the working pressure. When nipping up on the 13 3/8", 5M bradenhead and flange, the BOP test will be limited to 5000 psi. All BOP tests will include a low pressure test as per BLM regulations. The 5M BOP diagrams are attached. Blind rams will be functioned tested each trip, pipe rams will be functioned tested each day.

A variance is requested to allow use of a flex hose as the choke line from the BOP to the Choke Manifold. If this hose is used, a copy of the manufacturer's certification and pressure test chart will be kept on the rig. Attached is an example of a certification and pressure test chart. The manufacturer does not require anchors.

XTO requests a variance to be able to batch drill this well if necessary. In doing so, XTO will set each casing string and ensure that the well is cemented properly and the well is static. With floats holding, no pressure on the csg annulus, and the installation of a 10K TA cap as per GE recommendations, XTO will contact the BLM to skid the rig to drill the remaining wells on the pad. Once surface and intermediate strings are all completed, XTO will begin drilling the production hole on each of the wells.

6. Proposed Mud Circulation System

INTERVAL	Hole Size	Mud Type	MW (ppg)	Viscosity (sec/qt)	Fluid Loss (cc)
0' - 1250'	17-1/2"	FW / Native	8.4-8.8	35-40	NC
1250' - 10450'	12-1/4"	Brine / Cut Brine / WBM	8.8-9.8	30-32	NC
10450' to 26827'	8-3/4"	Cut Brine / WBM / OBM	10.0-10.5	32-36	NC

The necessary mud products for weight addition and fluid loss control will be on location at all times. Spud with fresh water/native mud and set 13 3/8" surface casing, isolating the fresh water aquifer. Drill out from under 13-3/8" surface casing with a brine/oil direct emulsion water-based mud. Use fibrous materials as needed to control seepage and lost circulation. Pump viscous sweeps as needed for hole cleaning. Pump speed will be recorded on a daily drilling report after mudding up. A Pason or Totco will be used to detect changes in loss or gain of mud volume. A mud test will be performed every 24 hours to determine: density, viscosity, strength, filtration and pH as necessary. Use available solids controls equipment to help keep mud weight down after mud up. Rig up solids control equipment to operate as a closed loop system.

7. Auxiliary Well Control and Monitoring Equipment

- A. A Kelly cock will be in the drill string at all times.
- B. A full opening drill pipe stabbing valve having appropriate connections will be on the rig floor at all times.
- C. H₂S monitors will be on location when drilling below the 13 3/8" casing.

8. Logging, Coring and Testing Program

Mud Logger: Mud Logging Unit (2 man) below intermediate casing.

Open hole logging will not be done on this well.

9. Abnormal Pressures and Temperatures / Potential Hazards


None Anticipated. BHT of 150 to 170 F is anticipated. No H₂S is expected but monitors will be in place to detect any H₂S occurrences. Should these circumstances be encountered the operator and drilling contractor are prepared to take all necessary steps to ensure safety of all personnel and environment. Lost circulation could occur but is not expected to be a serious problem in this area and hole seepage will be compensated for by additions of small amounts of LCM in the drilling fluid. The maximum anticipated bottom hole pressure for this well is 6060 psi.

10. Anticipated Starting Date and Duration of Operations

Road and location construction will begin after Santa Fe and BLM have approved the APD. Anticipated spud date will be as soon after Santa Fe and BLM approval and as soon as a rig will be available. Move in operations and drilling is expected to take 45 days. If production casing is run, an additional 30 days will be needed to complete well and construct surface facilities, and/or lay flow lines in order to place well on production.



GE Oil & Gas

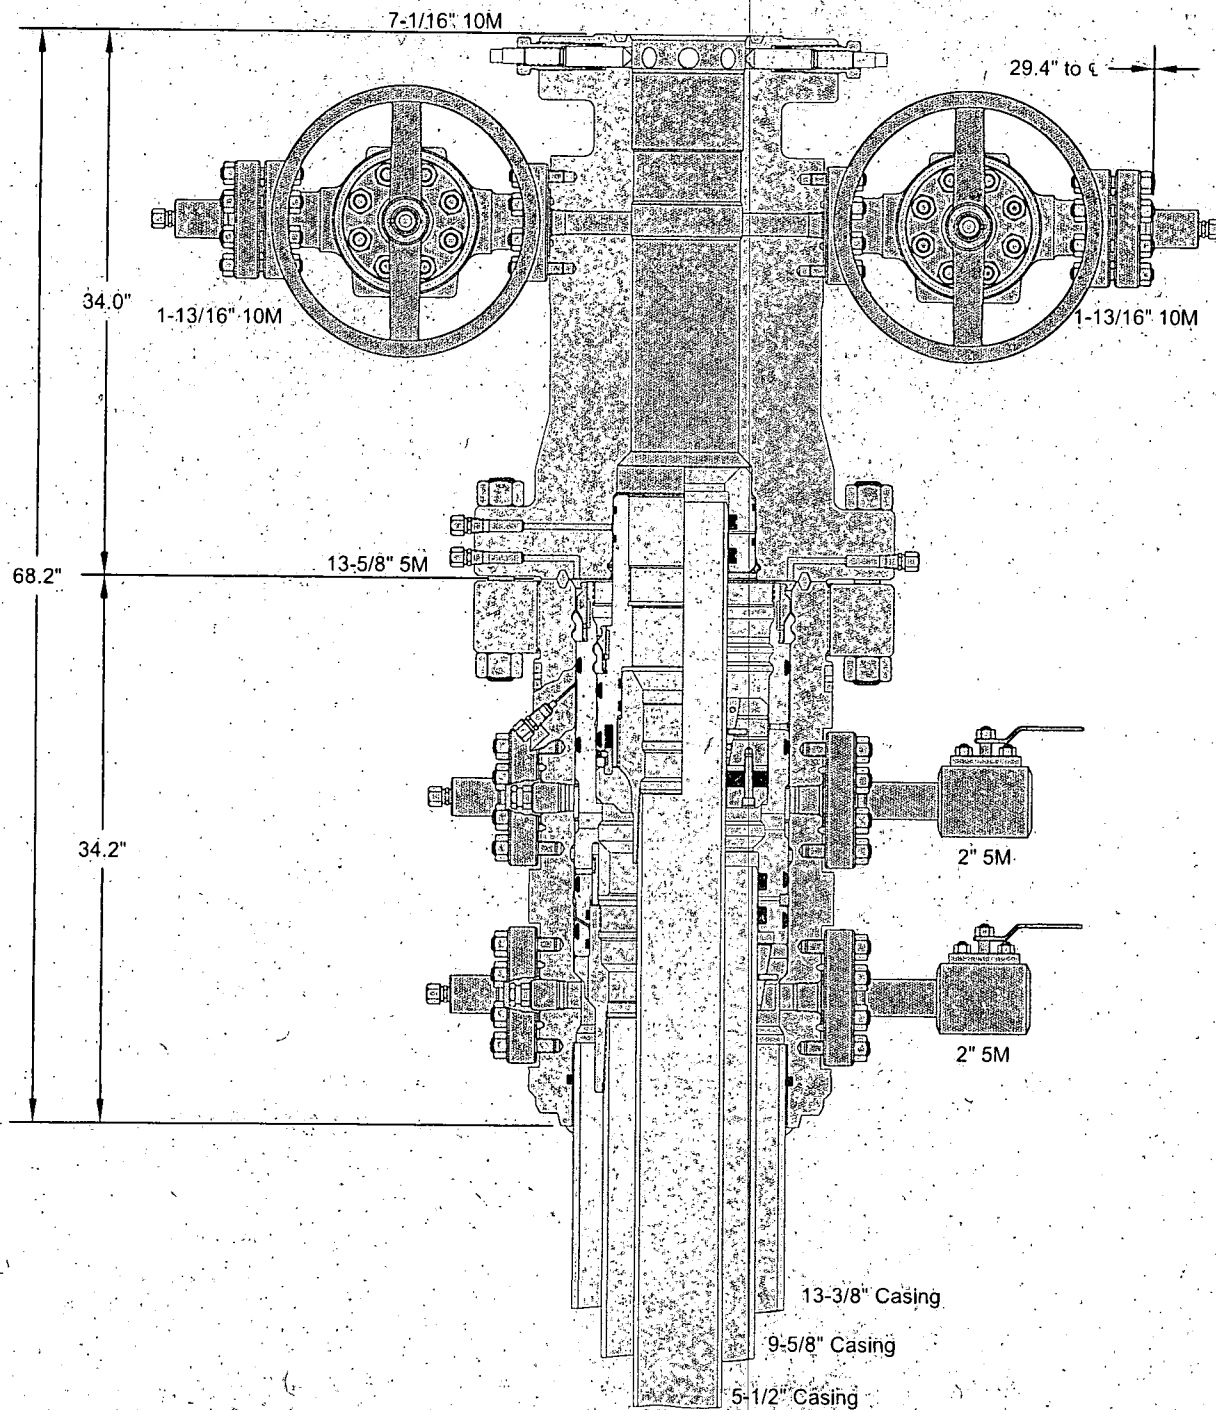


ALL DIMENSIONS ARE APPROXIMATE.


This drawing is the property of GE Oil & Gas Pressure Control LP and is considered confidential. Unless otherwise approved in writing, neither it nor its contents may be used, copied, transmitted or reproduced except for the sole purpose of GE Oil & Gas Pressure Control LP.

XTO ENERGY, INC.

13-3/8" x 9-5/8" x 5-1/2" 10M RSH-2 Wellhead
Assembly, With T-EBS-F Tubing Head


DRAWN	VJK	16FEB17
APPRV	KN	16FEB17
FOR REFERENCE ONLY		
DRAWING NO.		10012842

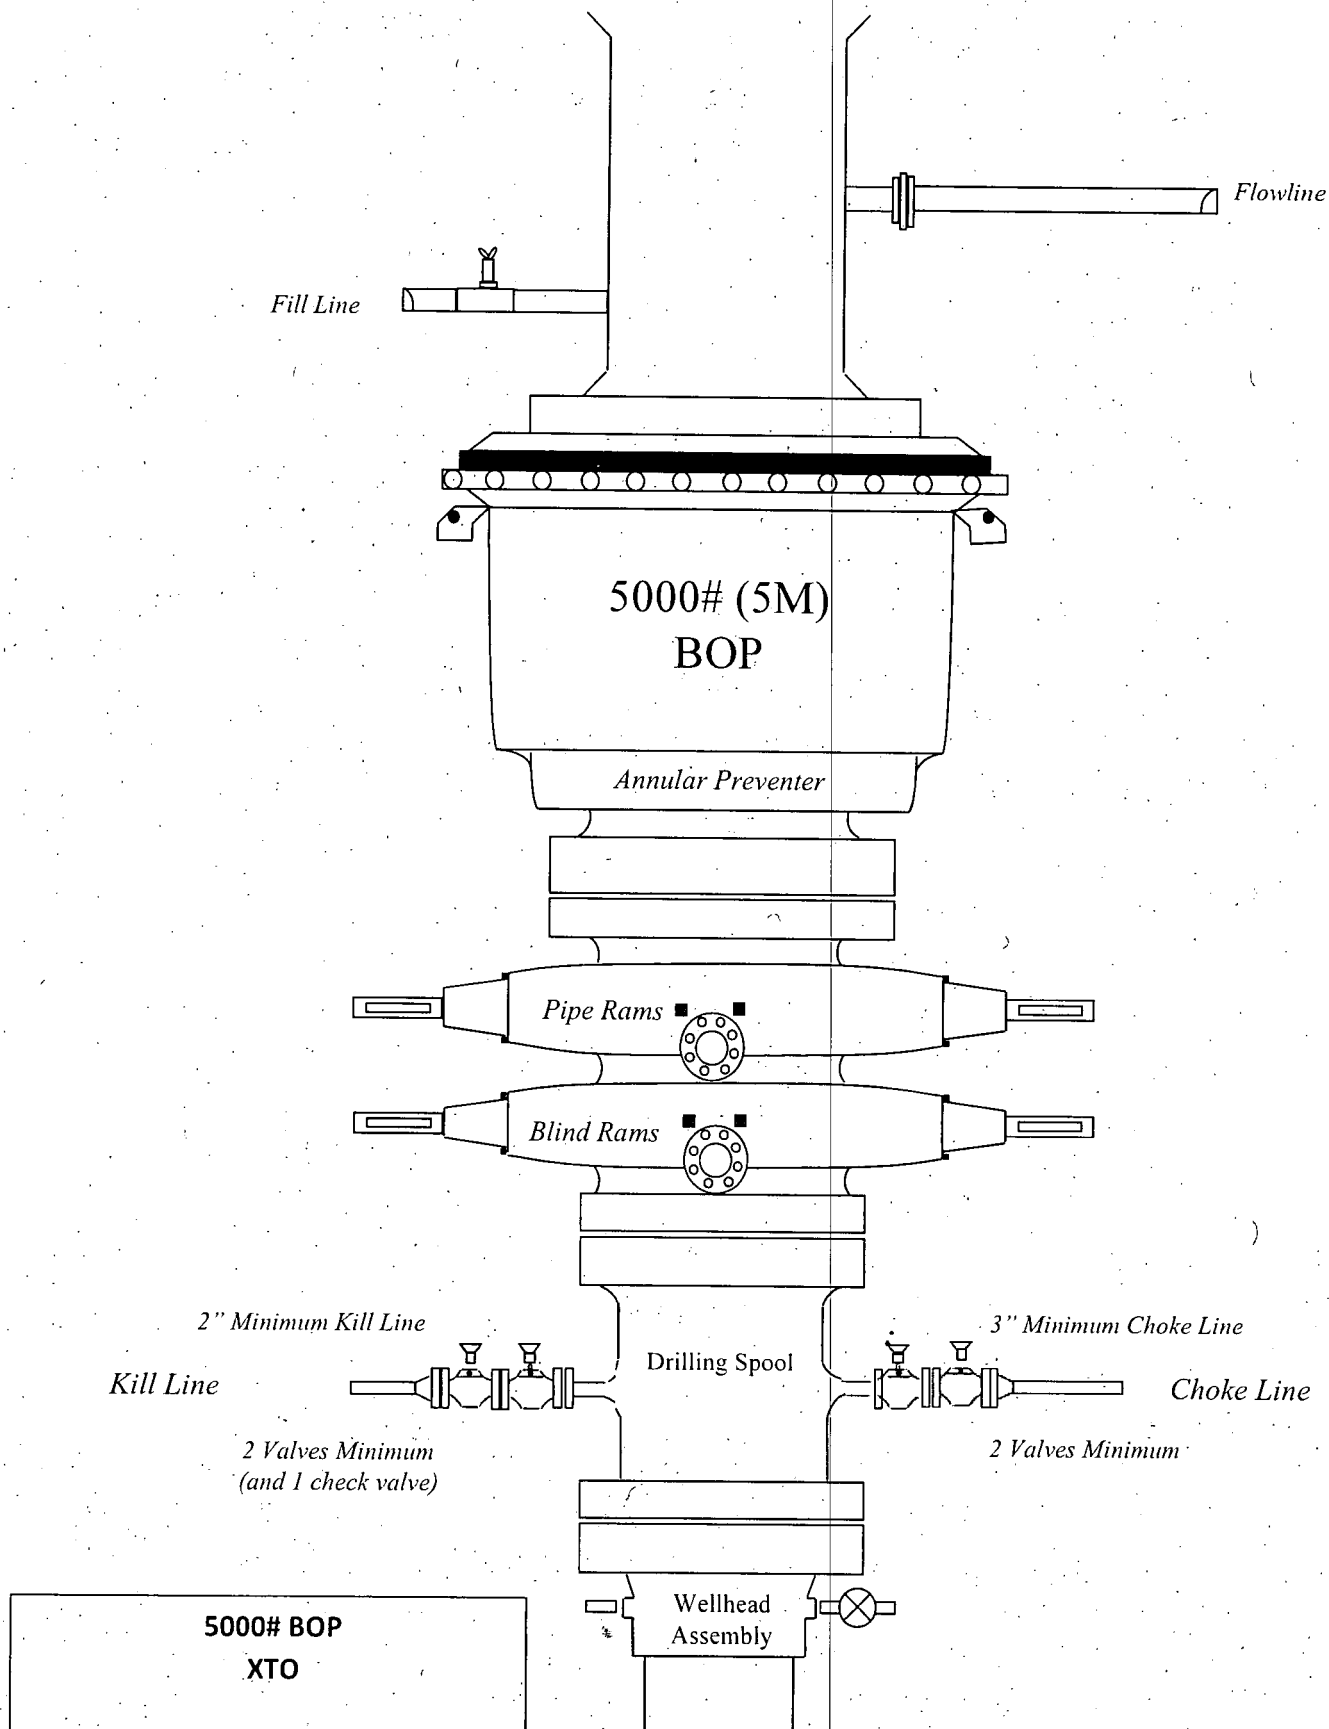

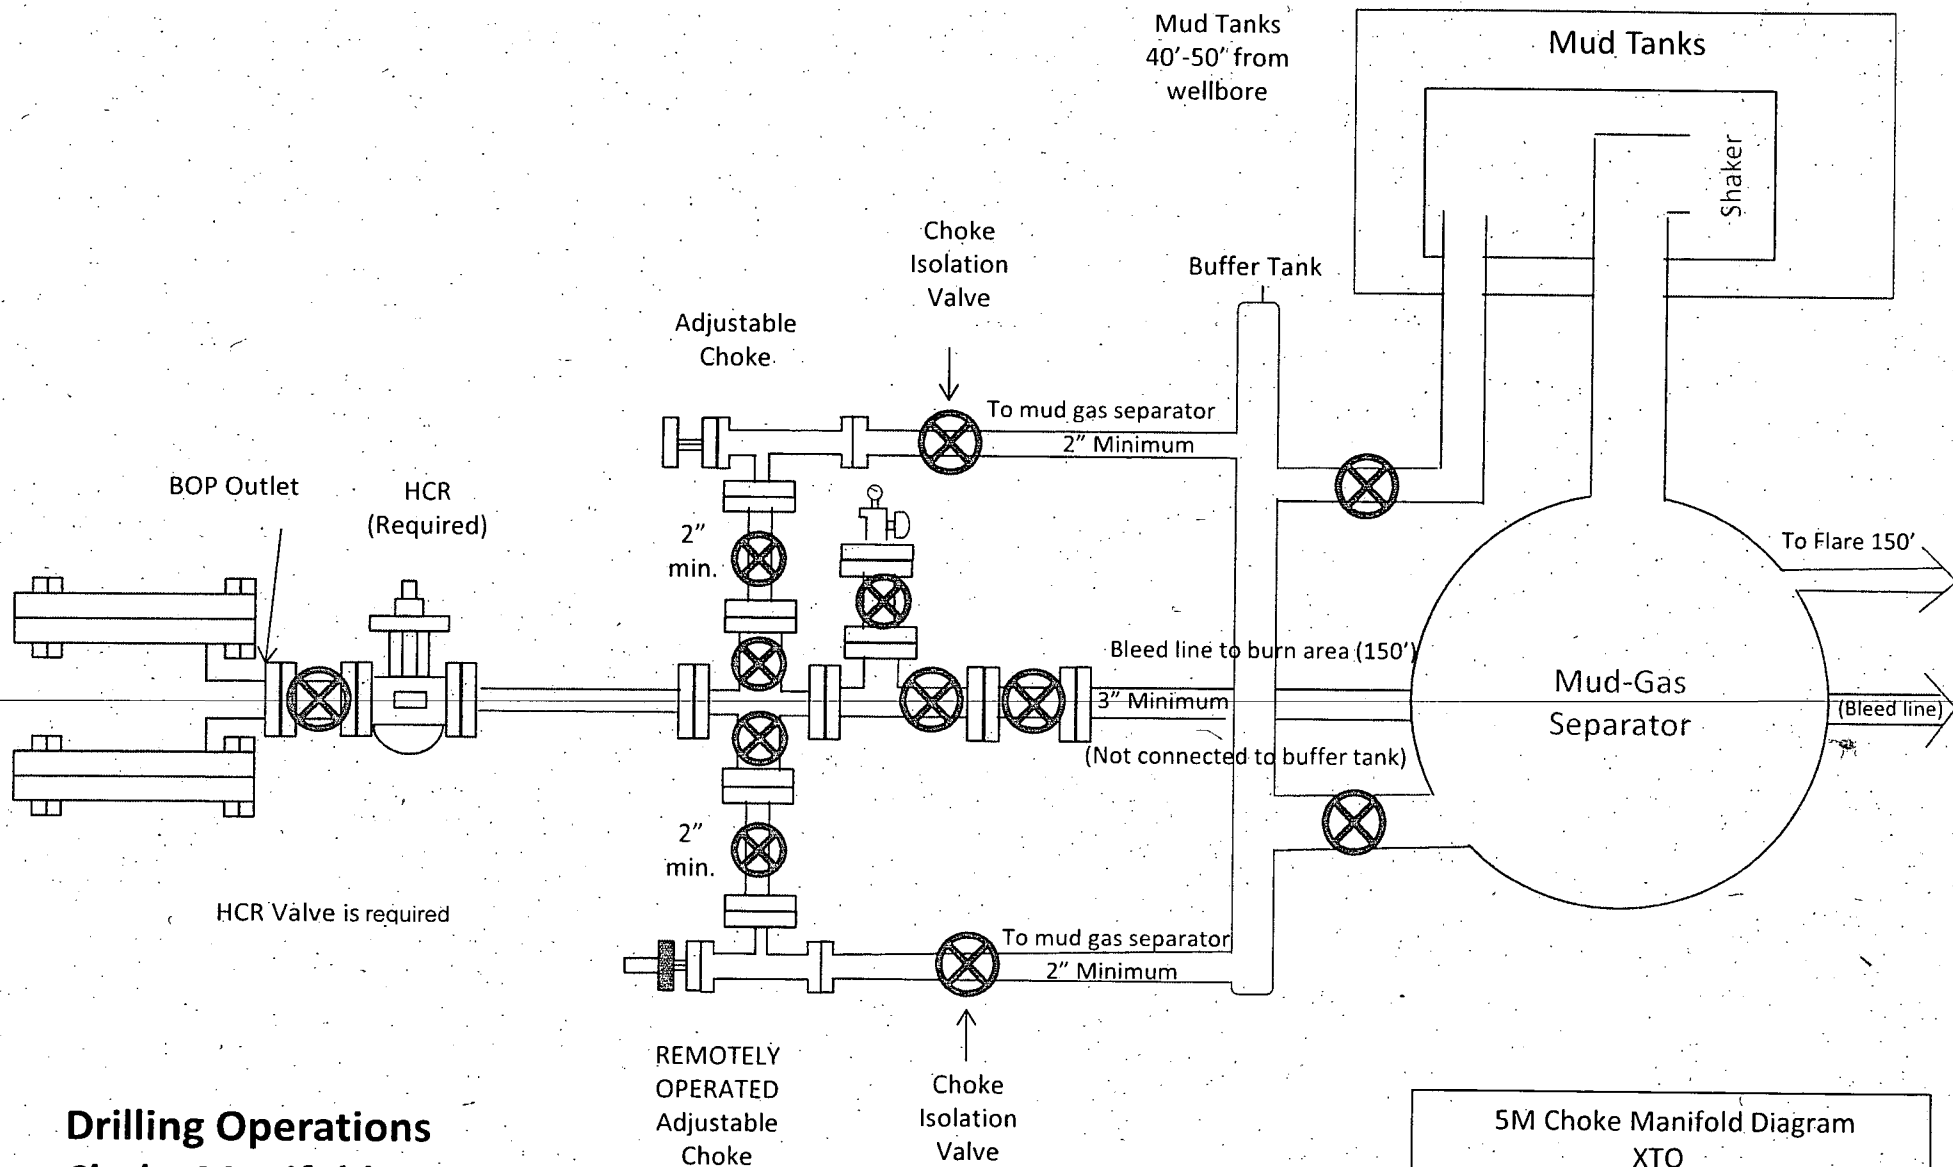

Drilling Operations **Choke Manifold** **5M Service**

5M Choke Manifold Diagram
XTO



GATES E & S NORTH AMERICA, INC
DU-TEX
134 44TH STREET
CORPUS CHRISTI, TEXAS 78405


PHONE: 361-887-9807
FAX: 361-887-0812
EMAIL: crpe@s@gates.com
WEB: www.gates.com

GRADE D PRESSURE TEST CERTIFICATE

Customer:	AUSTIN DISTRIBUTING	Test Date:	6/8/2014
Customer Ref.:	PENDING	Hose Serial No.:	D-060814-1
Invoice No.:	201709	Created By:	NORI-IA
Product Description:	FD1042-0R41/16 SKFLGE/E LE		
End Fitting 1:	4 1/16 in. 5K FLG	End Fitting 2:	4 1/16 in. 5K FLG
Gates Part No.:	4774-6001	Assembly Code:	L33090011513D-060814-1
Working Pressure:	5,000 PSI	Test Pressure:	7,500 PSI

Gates E & S North America, Inc. certifies that the following hose assembly has been tested to the Gates Oilfield Roughneck Agreement/Specification requirements and passed the 15 minute hydrostatic test per API Spec 7K/Q1, Fifth Edition, June 2010, Test pressure 9.6.7 and per Table 9 to 7,500 psi in accordance with this product number. Hose burst pressure 9.6.7.2 exceeds the minimum of 2.5 times the working pressure per Table 9.

Quality:	QUALITY	Technical Supervisor:	PRODUCTION
Date:	6/8/2014	Date:	6/8/2014
Signature:		Signature:	

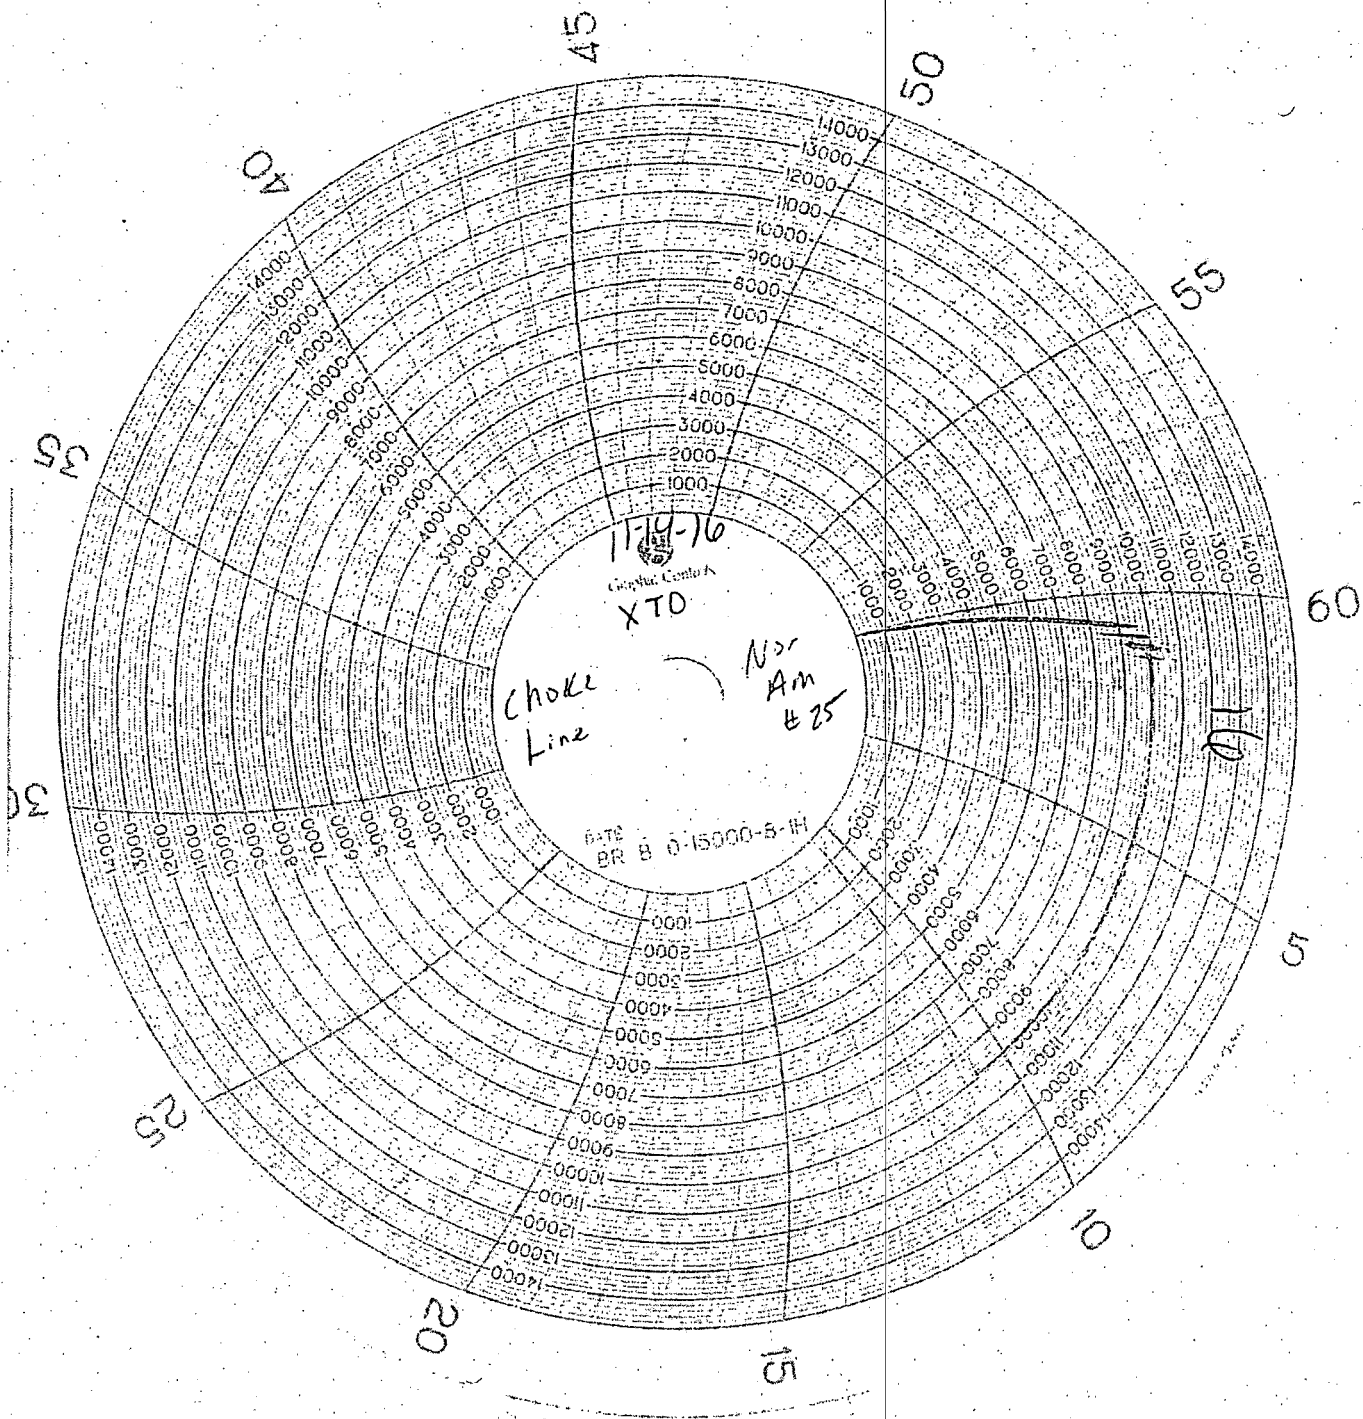

MOON


NOSE I.D. 2.012 LENGTH 42" END 1 4 1/16" 5K PSI END 2 4 1/16" 5K PSI

GRADE 2.010 WORKING PRESSURE 5,000 P.S.I.

TEST PRESSURE 7,500 P.S.I. ASSEMBLY DATE 6-8-14

TEST DATE 6-8-14 SERIAL # 633095011513D-060814-R

NAME D-125 CR # 25613

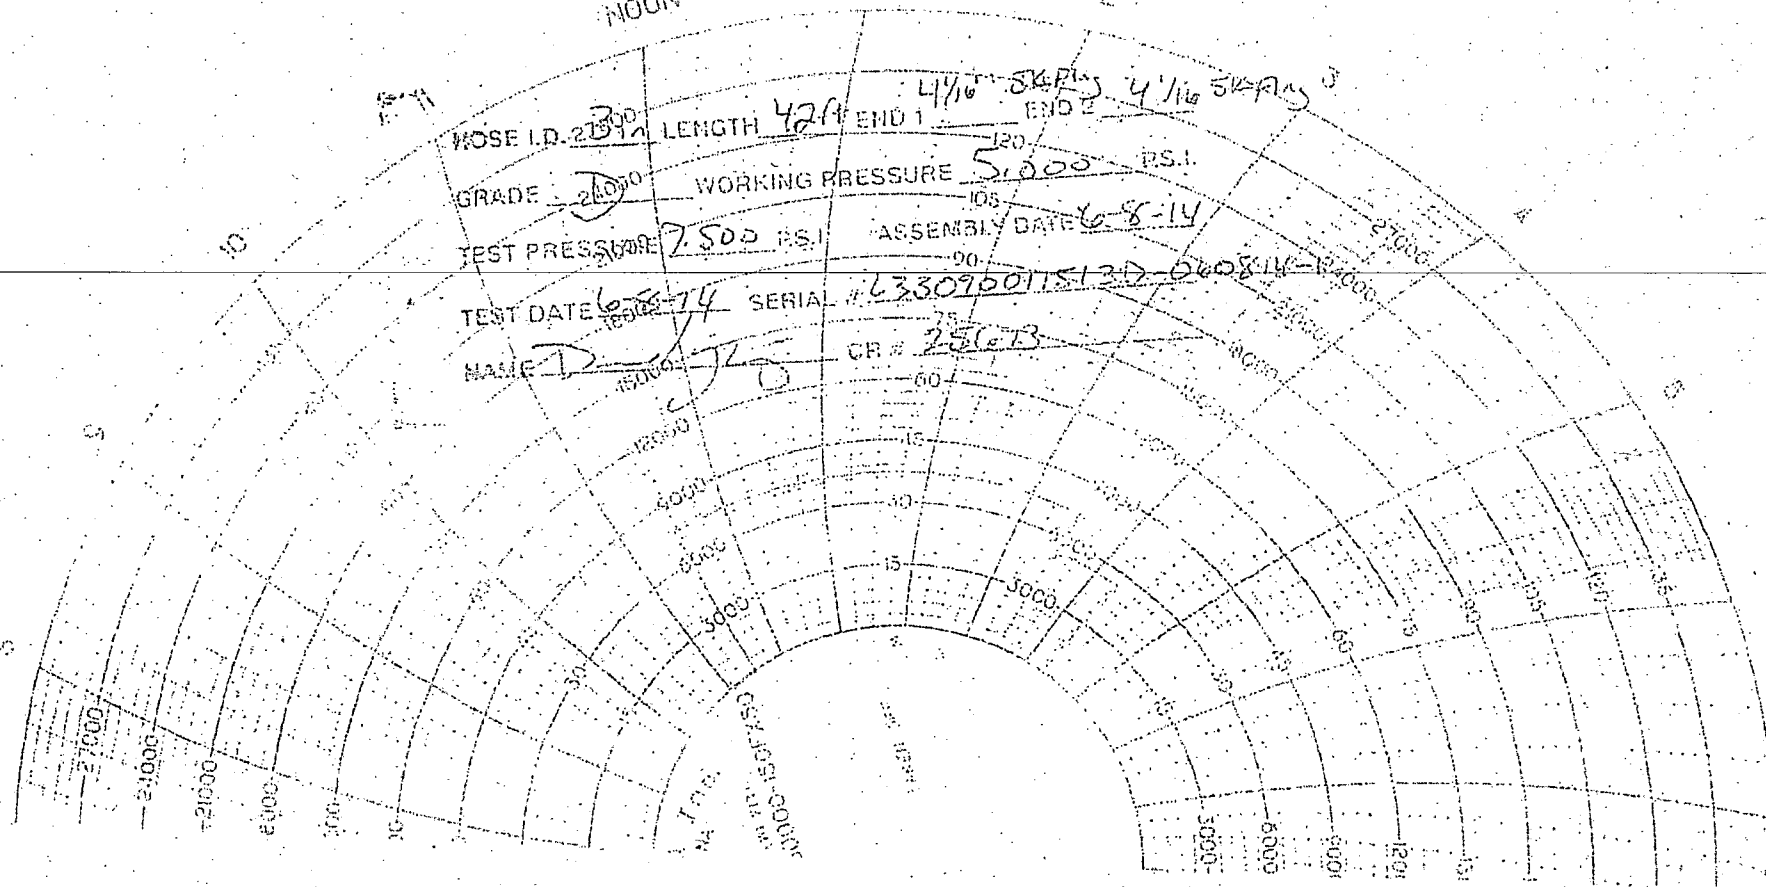

Plan Editor - 102H/102H Lateral/Plan #1

	MD (usft)	CL (usft)	Inc (°)	Azi (°)	TVD (usft)	NS (usft)	EW (usft)	V.Sec (usft)	Dogleg (°/100ft)	T.Face (°)	Build (°/100ft)	Turn (°/100ft)	Section Type	Target
1	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	Tie Line	
2	3500.00	3500.00	0.00	0.00	3500.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	S-Shape	
3	3700.15	200.15	3.00	49.00	3700.05	3.44	3.96	-3.43	1.50	49.00	1.50	0.00	(ditto)	
4	5622.65	1922.50	3.00	49.00	5619.92	69.50	79.95	-69.35	0.00	0.00	0.00	0.00	(ditto)	
5	5922.87	300.22	0.00	0.00	5920.00	74.66	85.88	-74.49	1.00	180.00	-1.00	0.00	(ditto)	
6	10528.9	4606.04	0.00	0.00	10526.04	74.66	85.88	-74.49	0.00	0.00	0.00	0.00	Straight TVD	
7	11428.9	900.00	90.00	179.89	11099.00	-498.30	86.98	498.46	10.00	179.89	10.00	0.00	Inc Azi DLS	
8	26826.7	15397.83	90.00	179.89	11099.00	-15896.10	116.54	15896.30	0.00	0.00	0.00	0.00	Straight VSEC	PLU27BD 102H PBH
9													Insert Line	

Planning Report

Database:	STRYKER_EDM	Local Co-ordinate Reference:	Well 102H - Slot PLU27BD 102H SHL
Company:	XTO Energy	TVD Reference:	3268+23 @ 3291.00usft (M7504)
Project:	Eddy County, NM (NAD27) NMEZ Grid	MD Reference:	3268+23 @ 3291.00usft (M7504)
Site:	PLU 27 BD	North Reference:	Grid
Well:	102H	Survey Calculation Method:	Minimum Curvature
Wellbore:	102H Lateral		
Design:	Plan #1		

Project:	Eddy County, NM (NAD27) NMEZ Grid		
Map System:	US State Plane 1927 (Exact solution)	System Datum:	Mean Sea Level
Geo Datum:	NAD 1927 (NADCON CONUS)		
Map Zone:	New Mexico East 3001		

Site:	PLU 27 BD		
Site Position:		Northing:	400,913.60 usft
From:	Map	Easting:	641,911.20 usft
Position Uncertainty:	0.00 usft	Slot Radius:	13.20 in
		Latitude:	32° 6' 5.03442199 N
		Longitude:	103° 52' 30.16021613 W
		Grid Convergence:	0.24 °

Well	102H - Slot PLU27BD 102H SHL					
Well Position	+N/-S	0.40 usft	Northing:	400,914.00 usft	Latitude:	32° 6' 5.03711837 N
	+E/-W	30.00 usft	Easting:	641,941.20 usft	Longitude:	103° 52' 29.81143011 W
Position Uncertainty	0.00 usft		Wellhead Elevation:		Ground Level:	3,268.00 usft

Wellbore	102H Lateral				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	IGRF2015	12/10/19	6.82	59.87	47,579.99598305

Design	Plan #1				
Audit Notes:					
Version:	Phase:	PROTOTYPE	Tie On Depth:	0.00	
Vertical Section:	Depth From (TVD)	+N/-S	+E/-W	Direction	
	(usft)	(usft)	(usft)	(°)	
	0.00	0.00	0.00	179.89	

Plan Survey Tool Program	Date	12/10/19		
Depth From	Depth To	Survey (Wellbore)	Tool Name	Remarks
(usft)	(usft)			
1	0.00	26,826.74 Plan #1 (102H Lateral)	MWD+IFR1+MS	
			OWSG MWD + IFR1 + Multi-SI	

Plan Sections										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N-S (usft)	+E-W (usft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)	TFO (°)	Target
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
3,500.00	0.00	0.00	3,500.00	0.00	0.00	0.00	0.00	0.00	0.00	
3,700.15	3.00	49.00	3,700.05	3.44	3.96	1.50	1.50	0.00	49.00	
5,622.65	3.00	49.00	5,619.92	69.50	79.95	0.00	0.00	0.00	0.00	
5,922.87	0.00	0.00	5,920.00	74.66	85.88	1.00	-1.00	0.00	180.00	
10,528.91	0.00	0.00	10,526.04	74.66	85.88	0.00	0.00	0.00	0.00	
11,428.91	90.00	179.89	11,099.00	-498.30	86.98	10.00	10.00	0.00	179.89	
26,826.74	90.00	179.89	11,099.00	-15,896.10	116.54	0.00	0.00	0.00	0.00	PLU27BD 102H PBHI

Planning Report

Database:	STRYKER_EDM	Local Co-ordinate Reference:	Well 102H - Slot PLU27BD 102H SHL
Company:	XTO Energy	TVD Reference:	3268+23 @ 3291.00usft (M7504)
Project:	Eddy County, NM (NAD27) NMEZ Grid	MD Reference:	3268+23 @ 3291.00usft (M7504)
Site:	PLU 27 BD	North Reference:	Grid
Well:	102H	Survey Calculation Method:	Minimum Curvature
Wellbore:	102H Lateral		
Design:	Plan #1		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)	
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
100.00	0.00	0.00	100.00	0.00	0.00	0.00	0.00	0.00	0.00	
200.00	0.00	0.00	200.00	0.00	0.00	0.00	0.00	0.00	0.00	
300.00	0.00	0.00	300.00	0.00	0.00	0.00	0.00	0.00	0.00	
400.00	0.00	0.00	400.00	0.00	0.00	0.00	0.00	0.00	0.00	
500.00	0.00	0.00	500.00	0.00	0.00	0.00	0.00	0.00	0.00	
600.00	0.00	0.00	600.00	0.00	0.00	0.00	0.00	0.00	0.00	
700.00	0.00	0.00	700.00	0.00	0.00	0.00	0.00	0.00	0.00	
800.00	0.00	0.00	800.00	0.00	0.00	0.00	0.00	0.00	0.00	
900.00	0.00	0.00	900.00	0.00	0.00	0.00	0.00	0.00	0.00	
1,000.00	0.00	0.00	1,000.00	0.00	0.00	0.00	0.00	0.00	0.00	
1,100.00	0.00	0.00	1,100.00	0.00	0.00	0.00	0.00	0.00	0.00	
1,200.00	0.00	0.00	1,200.00	0.00	0.00	0.00	0.00	0.00	0.00	
1,300.00	0.00	0.00	1,300.00	0.00	0.00	0.00	0.00	0.00	0.00	
1,400.00	0.00	0.00	1,400.00	0.00	0.00	0.00	0.00	0.00	0.00	
1,500.00	0.00	0.00	1,500.00	0.00	0.00	0.00	0.00	0.00	0.00	
1,600.00	0.00	0.00	1,600.00	0.00	0.00	0.00	0.00	0.00	0.00	
1,700.00	0.00	0.00	1,700.00	0.00	0.00	0.00	0.00	0.00	0.00	
1,800.00	0.00	0.00	1,800.00	0.00	0.00	0.00	0.00	0.00	0.00	
1,900.00	0.00	0.00	1,900.00	0.00	0.00	0.00	0.00	0.00	0.00	
2,000.00	0.00	0.00	2,000.00	0.00	0.00	0.00	0.00	0.00	0.00	
2,100.00	0.00	0.00	2,100.00	0.00	0.00	0.00	0.00	0.00	0.00	
2,200.00	0.00	0.00	2,200.00	0.00	0.00	0.00	0.00	0.00	0.00	
2,300.00	0.00	0.00	2,300.00	0.00	0.00	0.00	0.00	0.00	0.00	
2,400.00	0.00	0.00	2,400.00	0.00	0.00	0.00	0.00	0.00	0.00	
2,500.00	0.00	0.00	2,500.00	0.00	0.00	0.00	0.00	0.00	0.00	
2,600.00	0.00	0.00	2,600.00	0.00	0.00	0.00	0.00	0.00	0.00	
2,700.00	0.00	0.00	2,700.00	0.00	0.00	0.00	0.00	0.00	0.00	
2,800.00	0.00	0.00	2,800.00	0.00	0.00	0.00	0.00	0.00	0.00	
2,900.00	0.00	0.00	2,900.00	0.00	0.00	0.00	0.00	0.00	0.00	
3,000.00	0.00	0.00	3,000.00	0.00	0.00	0.00	0.00	0.00	0.00	
3,100.00	0.00	0.00	3,100.00	0.00	0.00	0.00	0.00	0.00	0.00	
3,200.00	0.00	0.00	3,200.00	0.00	0.00	0.00	0.00	0.00	0.00	
3,300.00	0.00	0.00	3,300.00	0.00	0.00	0.00	0.00	0.00	0.00	
3,400.00	0.00	0.00	3,400.00	0.00	0.00	0.00	0.00	0.00	0.00	
3,500.00	0.00	0.00	3,500.00	0.00	0.00	0.00	0.00	0.00	0.00	
3,600.00	1.50	49.00	3,599.99	0.86	0.99	-0.86	1.50	1.50	0.00	
3,700.15	3.00	49.00	3,700.05	3.44	3.96	-3.43	1.50	1.50	0.00	
3,800.00	3.00	49.00	3,799.77	6.87	7.90	-6.86	0.00	0.00	0.00	
3,900.00	3.00	49.00	3,899.63	10.31	11.86	-10.28	0.00	0.00	0.00	
4,000.00	3.00	49.00	3,999.50	13.74	15.81	-13.71	0.00	0.00	0.00	
4,100.00	3.00	49.00	4,099.36	17.18	19.76	-17.14	0.00	0.00	0.00	
4,200.00	3.00	49.00	4,199.22	20.62	23.71	-20.57	0.00	0.00	0.00	
4,300.00	3.00	49.00	4,299.09	24.05	27.67	-24.00	0.00	0.00	0.00	
4,400.00	3.00	49.00	4,398.95	27.49	31.62	-27.43	0.00	0.00	0.00	
4,500.00	3.00	49.00	4,498.81	30.92	35.57	-30.86	0.00	0.00	0.00	
4,600.00	3.00	49.00	4,598.67	34.36	39.52	-34.28	0.00	0.00	0.00	
4,700.00	3.00	49.00	4,698.54	37.80	43.48	-37.71	0.00	0.00	0.00	
4,800.00	3.00	49.00	4,798.40	41.23	47.43	-41.14	0.00	0.00	0.00	
4,900.00	3.00	49.00	4,898.26	44.67	51.38	-44.57	0.00	0.00	0.00	
5,000.00	3.00	49.00	4,998.12	48.11	55.33	-48.00	0.00	0.00	0.00	
5,100.00	3.00	49.00	5,097.99	51.54	59.29	-51.43	0.00	0.00	0.00	
5,200.00	3.00	49.00	5,197.85	54.98	63.24	-54.86	0.00	0.00	0.00	
5,300.00	3.00	49.00	5,297.71	58.41	67.19	-58.28	0.00	0.00	0.00	

Planning Report

Database:	STRYKER_EDM	Local Co-ordinate Reference:	Well 102H - Slot PLU27BD 102H SHL
Company:	XTO Energy	TVD Reference:	3268+23 @ 3291.00usft (M7504)
Project:	Eddy County, NM (NAD27) NMEZ Grid	MD Reference:	3268+23 @ 3291.00usft (M7504)
Site:	PLU 27 BD	North Reference:	Grid
Well:	102H	Survey Calculation Method:	Minimum Curvature
Wellbore:	102H Lateral		
Design:	Plan #1		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N-S (usft)	+E-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
5,400.00	3.00	49.00	5,397.58	61.85	71.14	-61.71	0.00	0.00	0.00
5,500.00	3.00	49.00	5,497.44	65.29	75.10	-65.14	0.00	0.00	0.00
5,600.00	3.00	49.00	5,597.30	68.72	79.05	-68.57	0.00	0.00	0.00
5,622.65	3.00	49.00	5,619.92	69.50	79.95	-69.35	0.00	0.00	0.00
5,700.00	2.23	49.00	5,697.19	71.82	82.61	-71.66	1.00	-1.00	0.00
5,800.00	1.23	49.00	5,797.14	73.80	84.89	-73.63	1.00	-1.00	0.00
5,900.00	0.23	49.00	5,897.13	74.63	85.85	-74.47	1.00	-1.00	0.00
5,922.87	0.00	0.00	5,920.00	74.66	85.88	-74.49	1.00	-1.00	0.00
6,000.00	0.00	0.00	5,997.13	74.66	85.88	-74.49	0.00	0.00	0.00
6,100.00	0.00	0.00	6,097.13	74.66	85.88	-74.49	0.00	0.00	0.00
6,200.00	0.00	0.00	6,197.13	74.66	85.88	-74.49	0.00	0.00	0.00
6,300.00	0.00	0.00	6,297.13	74.66	85.88	-74.49	0.00	0.00	0.00
6,400.00	0.00	0.00	6,397.13	74.66	85.88	-74.49	0.00	0.00	0.00
6,500.00	0.00	0.00	6,497.13	74.66	85.88	-74.49	0.00	0.00	0.00
6,600.00	0.00	0.00	6,597.13	74.66	85.88	-74.49	0.00	0.00	0.00
6,700.00	0.00	0.00	6,697.13	74.66	85.88	-74.49	0.00	0.00	0.00
6,800.00	0.00	0.00	6,797.13	74.66	85.88	-74.49	0.00	0.00	0.00
6,900.00	0.00	0.00	6,897.13	74.66	85.88	-74.49	0.00	0.00	0.00
7,000.00	0.00	0.00	6,997.13	74.66	85.88	-74.49	0.00	0.00	0.00
7,100.00	0.00	0.00	7,097.13	74.66	85.88	-74.49	0.00	0.00	0.00
7,200.00	0.00	0.00	7,197.13	74.66	85.88	-74.49	0.00	0.00	0.00
7,300.00	0.00	0.00	7,297.13	74.66	85.88	-74.49	0.00	0.00	0.00
7,400.00	0.00	0.00	7,397.13	74.66	85.88	-74.49	0.00	0.00	0.00
7,500.00	0.00	0.00	7,497.13	74.66	85.88	-74.49	0.00	0.00	0.00
7,600.00	0.00	0.00	7,597.13	74.66	85.88	-74.49	0.00	0.00	0.00
7,700.00	0.00	0.00	7,697.13	74.66	85.88	-74.49	0.00	0.00	0.00
7,800.00	0.00	0.00	7,797.13	74.66	85.88	-74.49	0.00	0.00	0.00
7,900.00	0.00	0.00	7,897.13	74.66	85.88	-74.49	0.00	0.00	0.00
8,000.00	0.00	0.00	7,997.13	74.66	85.88	-74.49	0.00	0.00	0.00
8,100.00	0.00	0.00	8,097.13	74.66	85.88	-74.49	0.00	0.00	0.00
8,200.00	0.00	0.00	8,197.13	74.66	85.88	-74.49	0.00	0.00	0.00
8,300.00	0.00	0.00	8,297.13	74.66	85.88	-74.49	0.00	0.00	0.00
8,400.00	0.00	0.00	8,397.13	74.66	85.88	-74.49	0.00	0.00	0.00
8,500.00	0.00	0.00	8,497.13	74.66	85.88	-74.49	0.00	0.00	0.00
8,600.00	0.00	0.00	8,597.13	74.66	85.88	-74.49	0.00	0.00	0.00
8,700.00	0.00	0.00	8,697.13	74.66	85.88	-74.49	0.00	0.00	0.00
8,800.00	0.00	0.00	8,797.13	74.66	85.88	-74.49	0.00	0.00	0.00
8,900.00	0.00	0.00	8,897.13	74.66	85.88	-74.49	0.00	0.00	0.00
9,000.00	0.00	0.00	8,997.13	74.66	85.88	-74.49	0.00	0.00	0.00
9,100.00	0.00	0.00	9,097.13	74.66	85.88	-74.49	0.00	0.00	0.00
9,200.00	0.00	0.00	9,197.13	74.66	85.88	-74.49	0.00	0.00	0.00
9,300.00	0.00	0.00	9,297.13	74.66	85.88	-74.49	0.00	0.00	0.00
9,400.00	0.00	0.00	9,397.13	74.66	85.88	-74.49	0.00	0.00	0.00
9,500.00	0.00	0.00	9,497.13	74.66	85.88	-74.49	0.00	0.00	0.00
9,600.00	0.00	0.00	9,597.13	74.66	85.88	-74.49	0.00	0.00	0.00
9,700.00	0.00	0.00	9,697.13	74.66	85.88	-74.49	0.00	0.00	0.00
9,800.00	0.00	0.00	9,797.13	74.66	85.88	-74.49	0.00	0.00	0.00
9,900.00	0.00	0.00	9,897.13	74.66	85.88	-74.49	0.00	0.00	0.00
10,000.00	0.00	0.00	9,997.13	74.66	85.88	-74.49	0.00	0.00	0.00
10,100.00	0.00	0.00	10,097.13	74.66	85.88	-74.49	0.00	0.00	0.00
10,200.00	0.00	0.00	10,197.13	74.66	85.88	-74.49	0.00	0.00	0.00
10,300.00	0.00	0.00	10,297.13	74.66	85.88	-74.49	0.00	0.00	0.00
10,400.00	0.00	0.00	10,397.13	74.66	85.88	-74.49	0.00	0.00	0.00
10,500.00	0.00	0.00	10,497.13	74.66	85.88	-74.49	0.00	0.00	0.00

Planning Report

Database:	STRYKER_EDM	Local Co-ordinate Reference:	Well 102H - Slot PLU27BD 102H SHL
Company:	XTO Energy	TVD Reference:	3268+23 @ 3291.00usft (M7504)
Project:	Eddy County, NM (NAD27) NMEZ Grid	MD Reference:	3268+23 @ 3291.00usft (M7504)
Site:	PLU 27 BD	North Reference:	Grid
Well:	102H	Survey Calculation Method:	Minimum Curvature
Wellbore:	102H Lateral		
Design:	Plan #1		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N-S (usft)	+E-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)	
10,528.91	0.00	0.00	10,526.04	74.66	85.88	-74.49	0.00	0.00	0.00	
10,550.00	2.11	179.89	10,547.13	74.27	85.88	-74.11	10.00	10.00	0.00	
10,600.00	7.11	179.89	10,596.95	70.26	85.89	-70.09	10.00	10.00	0.00	
10,650.00	12.11	179.89	10,646.23	61.91	85.90	-61.75	10.00	10.00	0.00	
10,700.00	17.11	179.89	10,694.60	49.30	85.93	-49.14	10.00	10.00	0.00	
10,750.00	22.11	179.89	10,741.69	32.53	85.96	-32.36	10.00	10.00	0.00	
10,800.00	27.11	179.89	10,787.13	11.71	86.00	-11.55	10.00	10.00	0.00	
10,850.00	32.11	179.89	10,830.59	-12.98	86.05	13.15	10.00	10.00	0.00	
10,900.00	37.11	179.89	10,871.73	-41.37	86.10	41.54	10.00	10.00	0.00	
10,950.00	42.11	179.89	10,910.23	-73.24	86.16	73.40	10.00	10.00	0.00	
11,000.00	47.11	179.89	10,945.82	-108.34	86.23	108.51	10.00	10.00	0.00	
11,050.00	52.11	179.89	10,978.21	-146.41	86.30	146.58	10.00	10.00	0.00	
11,100.00	57.11	179.89	11,007.16	-187.16	86.38	187.32	10.00	10.00	0.00	
11,150.00	62.11	179.89	11,032.44	-230.28	86.47	230.44	10.00	10.00	0.00	
11,200.00	67.11	179.89	11,053.88	-275.43	86.55	275.60	10.00	10.00	0.00	
11,250.00	72.11	179.89	11,071.29	-322.28	86.64	322.45	10.00	10.00	0.00	
11,300.00	77.11	179.89	11,084.56	-370.47	86.73	370.64	10.00	10.00	0.00	
11,350.00	82.11	179.89	11,093.57	-419.64	86.83	419.81	10.00	10.00	0.00	
11,400.00	87.11	179.89	11,098.27	-469.40	86.92	469.57	10.00	10.00	0.00	
11,428.91	90.00	179.89	11,099.00	-498.30	86.98	498.46	10.00	10.00	0.00	
11,500.00	90.00	179.89	11,099.00	-569.39	87.12	569.56	0.00	0.00	0.00	
11,600.00	90.00	179.89	11,099.00	-669.39	87.31	669.56	0.00	0.00	0.00	
11,700.00	90.00	179.89	11,099.00	-769.39	87.50	769.56	0.00	0.00	0.00	
11,800.00	90.00	179.89	11,099.00	-869.39	87.69	869.56	0.00	0.00	0.00	
11,900.00	90.00	179.89	11,099.00	-969.39	87.88	969.56	0.00	0.00	0.00	
12,000.00	90.00	179.89	11,099.00	-1,069.39	88.08	1,069.56	0.00	0.00	0.00	
12,100.00	90.00	179.89	11,099.00	-1,169.39	88.27	1,169.56	0.00	0.00	0.00	
12,200.00	90.00	179.89	11,099.00	-1,269.39	88.46	1,269.56	0.00	0.00	0.00	
12,300.00	90.00	179.89	11,099.00	-1,369.39	88.65	1,369.56	0.00	0.00	0.00	
12,400.00	90.00	179.89	11,099.00	-1,469.39	88.84	1,469.56	0.00	0.00	0.00	
12,500.00	90.00	179.89	11,099.00	-1,569.39	89.04	1,569.56	0.00	0.00	0.00	
12,600.00	90.00	179.89	11,099.00	-1,669.39	89.23	1,669.56	0.00	0.00	0.00	
12,700.00	90.00	179.89	11,099.00	-1,769.39	89.42	1,769.56	0.00	0.00	0.00	
12,800.00	90.00	179.89	11,099.00	-1,869.39	89.61	1,869.56	0.00	0.00	0.00	
12,900.00	90.00	179.89	11,099.00	-1,969.39	89.80	1,969.56	0.00	0.00	0.00	
13,000.00	90.00	179.89	11,099.00	-2,069.39	90.00	2,069.56	0.00	0.00	0.00	
13,100.00	90.00	179.89	11,099.00	-2,169.39	90.19	2,169.56	0.00	0.00	0.00	
13,200.00	90.00	179.89	11,099.00	-2,269.39	90.38	2,269.56	0.00	0.00	0.00	
13,300.00	90.00	179.89	11,099.00	-2,369.39	90.57	2,369.56	0.00	0.00	0.00	
13,400.00	90.00	179.89	11,099.00	-2,469.39	90.76	2,469.56	0.00	0.00	0.00	
13,500.00	90.00	179.89	11,099.00	-2,569.39	90.96	2,569.56	0.00	0.00	0.00	
13,600.00	90.00	179.89	11,099.00	-2,669.39	91.15	2,669.56	0.00	0.00	0.00	
13,700.00	90.00	179.89	11,099.00	-2,769.39	91.34	2,769.56	0.00	0.00	0.00	
13,800.00	90.00	179.89	11,099.00	-2,869.39	91.53	2,869.56	0.00	0.00	0.00	
13,900.00	90.00	179.89	11,099.00	-2,969.39	91.72	2,969.56	0.00	0.00	0.00	
14,000.00	90.00	179.89	11,099.00	-3,069.39	91.92	3,069.56	0.00	0.00	0.00	
14,100.00	90.00	179.89	11,099.00	-3,169.39	92.11	3,169.56	0.00	0.00	0.00	
14,200.00	90.00	179.89	11,099.00	-3,269.38	92.30	3,269.56	0.00	0.00	0.00	
14,300.00	90.00	179.89	11,099.00	-3,369.38	92.49	3,369.56	0.00	0.00	0.00	
14,400.00	90.00	179.89	11,099.00	-3,469.38	92.68	3,469.56	0.00	0.00	0.00	
14,500.00	90.00	179.89	11,099.00	-3,569.38	92.88	3,569.56	0.00	0.00	0.00	
14,600.00	90.00	179.89	11,099.00	-3,669.38	93.07	3,669.56	0.00	0.00	0.00	
14,700.00	90.00	179.89	11,099.00	-3,769.38	93.26	3,769.56	0.00	0.00	0.00	
14,800.00	90.00	179.89	11,099.00	-3,869.38	93.45	3,869.56	0.00	0.00	0.00	

Planning Report

Database:	STRYKER_EDM	Local Co-ordinate Reference:	Well 102H - Slot PLU27BD 102H SHL
Company:	XTO Energy	TVD Reference:	3268+23 @ 3291.00usft (M7504)
Project:	Eddy County, NM (NAD27) NMEZ Grid	MD Reference:	3268+23 @ 3291.00usft (M7504)
Site:	PLU 27 BD	North Reference:	Grid
Well:	102H	Survey Calculation Method:	Minimum Curvature
Wellbore:	102H Lateral		
Design:	Plan #1		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N-S (usft)	+E-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)	
14,900.00	90.00	179.89	11,099.00	-3,969.38	93.64	3,969.56	0.00	0.00	0.00	
15,000.00	90.00	179.89	11,099.00	-4,069.38	93.84	4,069.56	0.00	0.00	0.00	
15,100.00	90.00	179.89	11,099.00	-4,169.38	94.03	4,169.56	0.00	0.00	0.00	
15,200.00	90.00	179.89	11,099.00	-4,269.38	94.22	4,269.56	0.00	0.00	0.00	
15,300.00	90.00	179.89	11,099.00	-4,369.38	94.41	4,369.56	0.00	0.00	0.00	
15,400.00	90.00	179.89	11,099.00	-4,469.38	94.60	4,469.56	0.00	0.00	0.00	
15,500.00	90.00	179.89	11,099.00	-4,569.38	94.80	4,569.56	0.00	0.00	0.00	
15,600.00	90.00	179.89	11,099.00	-4,669.38	94.99	4,669.56	0.00	0.00	0.00	
15,700.00	90.00	179.89	11,099.00	-4,769.38	95.18	4,769.56	0.00	0.00	0.00	
15,800.00	90.00	179.89	11,099.00	-4,869.38	95.37	4,869.56	0.00	0.00	0.00	
15,900.00	90.00	179.89	11,099.00	-4,969.38	95.56	4,969.56	0.00	0.00	0.00	
16,000.00	90.00	179.89	11,099.00	-5,069.38	95.76	5,069.56	0.00	0.00	0.00	
16,100.00	90.00	179.89	11,099.00	-5,169.38	95.95	5,169.56	0.00	0.00	0.00	
16,200.00	90.00	179.89	11,099.00	-5,269.38	96.14	5,269.56	0.00	0.00	0.00	
16,300.00	90.00	179.89	11,099.00	-5,369.38	96.33	5,369.56	0.00	0.00	0.00	
16,400.00	90.00	179.89	11,099.00	-5,469.38	96.52	5,469.56	0.00	0.00	0.00	
16,500.00	90.00	179.89	11,099.00	-5,569.38	96.72	5,569.56	0.00	0.00	0.00	
16,600.00	90.00	179.89	11,099.00	-5,669.38	96.91	5,669.56	0.00	0.00	0.00	
16,700.00	90.00	179.89	11,099.00	-5,769.38	97.10	5,769.56	0.00	0.00	0.00	
16,800.00	90.00	179.89	11,099.00	-5,869.38	97.29	5,869.56	0.00	0.00	0.00	
16,900.00	90.00	179.89	11,099.00	-5,969.38	97.48	5,969.56	0.00	0.00	0.00	
17,000.00	90.00	179.89	11,099.00	-6,069.38	97.68	6,069.56	0.00	0.00	0.00	
17,100.00	90.00	179.89	11,099.00	-6,169.38	97.87	6,169.56	0.00	0.00	0.00	
17,200.00	90.00	179.89	11,099.00	-6,269.38	98.06	6,269.56	0.00	0.00	0.00	
17,300.00	90.00	179.89	11,099.00	-6,369.38	98.25	6,369.56	0.00	0.00	0.00	
17,400.00	90.00	179.89	11,099.00	-6,469.38	98.44	6,469.56	0.00	0.00	0.00	
17,500.00	90.00	179.89	11,099.00	-6,569.38	98.64	6,569.56	0.00	0.00	0.00	
17,600.00	90.00	179.89	11,099.00	-6,669.38	98.83	6,669.56	0.00	0.00	0.00	
17,700.00	90.00	179.89	11,099.00	-6,769.38	99.02	6,769.56	0.00	0.00	0.00	
17,800.00	90.00	179.89	11,099.00	-6,869.38	99.21	6,869.56	0.00	0.00	0.00	
17,900.00	90.00	179.89	11,099.00	-6,969.38	99.40	6,969.56	0.00	0.00	0.00	
18,000.00	90.00	179.89	11,099.00	-7,069.38	99.60	7,069.56	0.00	0.00	0.00	
18,100.00	90.00	179.89	11,099.00	-7,169.38	99.79	7,169.56	0.00	0.00	0.00	
18,200.00	90.00	179.89	11,099.00	-7,269.38	99.98	7,269.56	0.00	0.00	0.00	
18,300.00	90.00	179.89	11,099.00	-7,369.38	100.17	7,369.56	0.00	0.00	0.00	
18,400.00	90.00	179.89	11,099.00	-7,469.38	100.36	7,469.56	0.00	0.00	0.00	
18,500.00	90.00	179.89	11,099.00	-7,569.38	100.56	7,569.56	0.00	0.00	0.00	
18,600.00	90.00	179.89	11,099.00	-7,669.38	100.75	7,669.56	0.00	0.00	0.00	
18,700.00	90.00	179.89	11,099.00	-7,769.38	100.94	7,769.56	0.00	0.00	0.00	
18,800.00	90.00	179.89	11,099.00	-7,869.38	101.13	7,869.56	0.00	0.00	0.00	
18,900.00	90.00	179.89	11,099.00	-7,969.38	101.32	7,969.56	0.00	0.00	0.00	
19,000.00	90.00	179.89	11,099.00	-8,069.38	101.52	8,069.56	0.00	0.00	0.00	
19,100.00	90.00	179.89	11,099.00	-8,169.38	101.71	8,169.56	0.00	0.00	0.00	
19,200.00	90.00	179.89	11,099.00	-8,269.38	101.90	8,269.56	0.00	0.00	0.00	
19,300.00	90.00	179.89	11,099.00	-8,369.38	102.09	8,369.56	0.00	0.00	0.00	
19,400.00	90.00	179.89	11,099.00	-8,469.38	102.28	8,469.56	0.00	0.00	0.00	
19,500.00	90.00	179.89	11,099.00	-8,569.38	102.48	8,569.56	0.00	0.00	0.00	
19,600.00	90.00	179.89	11,099.00	-8,669.38	102.67	8,669.56	0.00	0.00	0.00	
19,700.00	90.00	179.89	11,099.00	-8,769.37	102.86	8,769.56	0.00	0.00	0.00	
19,800.00	90.00	179.89	11,099.00	-8,869.37	103.05	8,869.56	0.00	0.00	0.00	
19,900.00	90.00	179.89	11,099.00	-8,969.37	103.24	8,969.56	0.00	0.00	0.00	
20,000.00	90.00	179.89	11,099.00	-9,069.37	103.44	9,069.56	0.00	0.00	0.00	
20,100.00	90.00	179.89	11,099.00	-9,169.37	103.63	9,169.56	0.00	0.00	0.00	
20,200.00	90.00	179.89	11,099.00	-9,269.37	103.82	9,269.56	0.00	0.00	0.00	

Planning Report

Database:	STRYKER_EDM	Local Co-ordinate Reference:	Well 102H - Slot PLU27BD 102H SHL
Company:	XTO Energy	TVD Reference:	3268+23 @ 3291.00usft (M7504)
Project:	Eddy County, NM (NAD27) NMEZ Grid	MD Reference:	3268+23 @ 3291.00usft (M7504)
Site:	PLU 27 BD	North Reference:	Grid
Well:	102H	Survey Calculation Method:	Minimum Curvature
Wellbore:	102H Lateral		
Design:	Plan #1		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N-S (usft)	+E-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)	
20,300.00	90.00	179.89	11,099.00	-9,369.37	104.01	9,369.56	0.00	0.00	0.00	
20,400.00	90.00	179.89	11,099.00	-9,469.37	104.20	9,469.56	0.00	0.00	0.00	
20,500.00	90.00	179.89	11,099.00	-9,569.37	104.40	9,569.56	0.00	0.00	0.00	
20,600.00	90.00	179.89	11,099.00	-9,669.37	104.59	9,669.56	0.00	0.00	0.00	
20,700.00	90.00	179.89	11,099.00	-9,769.37	104.78	9,769.56	0.00	0.00	0.00	
20,800.00	90.00	179.89	11,099.00	-9,869.37	104.97	9,869.56	0.00	0.00	0.00	
20,900.00	90.00	179.89	11,099.00	-9,969.37	105.16	9,969.56	0.00	0.00	0.00	
21,000.00	90.00	179.89	11,099.00	-10,069.37	105.36	10,069.56	0.00	0.00	0.00	
21,100.00	90.00	179.89	11,099.00	-10,169.37	105.55	10,169.56	0.00	0.00	0.00	
21,200.00	90.00	179.89	11,099.00	-10,269.37	105.74	10,269.56	0.00	0.00	0.00	
21,300.00	90.00	179.89	11,099.00	-10,369.37	105.93	10,369.56	0.00	0.00	0.00	
21,400.00	90.00	179.89	11,099.00	-10,469.37	106.12	10,469.56	0.00	0.00	0.00	
21,500.00	90.00	179.89	11,099.00	-10,569.37	106.32	10,569.56	0.00	0.00	0.00	
21,600.00	90.00	179.89	11,099.00	-10,669.37	106.51	10,669.56	0.00	0.00	0.00	
21,700.00	90.00	179.89	11,099.00	-10,769.37	106.70	10,769.56	0.00	0.00	0.00	
21,800.00	90.00	179.89	11,099.00	-10,869.37	106.89	10,869.56	0.00	0.00	0.00	
21,900.00	90.00	179.89	11,099.00	-10,969.37	107.08	10,969.56	0.00	0.00	0.00	
22,000.00	90.00	179.89	11,099.00	-11,069.37	107.28	11,069.56	0.00	0.00	0.00	
22,100.00	90.00	179.89	11,099.00	-11,169.37	107.47	11,169.56	0.00	0.00	0.00	
22,200.00	90.00	179.89	11,099.00	-11,269.37	107.66	11,269.56	0.00	0.00	0.00	
22,300.00	90.00	179.89	11,099.00	-11,369.37	107.85	11,369.56	0.00	0.00	0.00	
22,400.00	90.00	179.89	11,099.00	-11,469.37	108.04	11,469.56	0.00	0.00	0.00	
22,500.00	90.00	179.89	11,099.00	-11,569.37	108.23	11,569.56	0.00	0.00	0.00	
22,600.00	90.00	179.89	11,099.00	-11,669.37	108.43	11,669.56	0.00	0.00	0.00	
22,700.00	90.00	179.89	11,099.00	-11,769.37	108.62	11,769.56	0.00	0.00	0.00	
22,800.00	90.00	179.89	11,099.00	-11,869.37	108.81	11,869.56	0.00	0.00	0.00	
22,900.00	90.00	179.89	11,099.00	-11,969.37	109.00	11,969.56	0.00	0.00	0.00	
23,000.00	90.00	179.89	11,099.00	-12,069.37	109.19	12,069.56	0.00	0.00	0.00	
23,100.00	90.00	179.89	11,099.00	-12,169.37	109.39	12,169.56	0.00	0.00	0.00	
23,200.00	90.00	179.89	11,099.00	-12,269.37	109.58	12,269.56	0.00	0.00	0.00	
23,300.00	90.00	179.89	11,099.00	-12,369.37	109.77	12,369.56	0.00	0.00	0.00	
23,400.00	90.00	179.89	11,099.00	-12,469.37	109.96	12,469.56	0.00	0.00	0.00	
23,500.00	90.00	179.89	11,099.00	-12,569.37	110.15	12,569.56	0.00	0.00	0.00	
23,600.00	90.00	179.89	11,099.00	-12,669.37	110.35	12,669.56	0.00	0.00	0.00	
23,700.00	90.00	179.89	11,099.00	-12,769.37	110.54	12,769.56	0.00	0.00	0.00	
23,800.00	90.00	179.89	11,099.00	-12,869.37	110.73	12,869.56	0.00	0.00	0.00	
23,900.00	90.00	179.89	11,099.00	-12,969.37	110.92	12,969.56	0.00	0.00	0.00	
24,000.00	90.00	179.89	11,099.00	-13,069.37	111.11	13,069.56	0.00	0.00	0.00	
24,100.00	90.00	179.89	11,099.00	-13,169.37	111.31	13,169.56	0.00	0.00	0.00	
24,200.00	90.00	179.89	11,099.00	-13,269.37	111.50	13,269.56	0.00	0.00	0.00	
24,300.00	90.00	179.89	11,099.00	-13,369.37	111.69	13,369.56	0.00	0.00	0.00	
24,400.00	90.00	179.89	11,099.00	-13,469.37	111.88	13,469.56	0.00	0.00	0.00	
24,500.00	90.00	179.89	11,099.00	-13,569.37	112.07	13,569.56	0.00	0.00	0.00	
24,600.00	90.00	179.89	11,099.00	-13,669.37	112.27	13,669.56	0.00	0.00	0.00	
24,700.00	90.00	179.89	11,099.00	-13,769.37	112.46	13,769.56	0.00	0.00	0.00	
24,800.00	90.00	179.89	11,099.00	-13,869.37	112.65	13,869.56	0.00	0.00	0.00	
24,900.00	90.00	179.89	11,099.00	-13,969.37	112.84	13,969.56	0.00	0.00	0.00	
25,000.00	90.00	179.89	11,099.00	-14,069.37	113.03	14,069.56	0.00	0.00	0.00	
25,100.00	90.00	179.89	11,099.00	-14,169.36	113.23	14,169.56	0.00	0.00	0.00	
25,200.00	90.00	179.89	11,099.00	-14,269.36	113.42	14,269.56	0.00	0.00	0.00	
25,300.00	90.00	179.89	11,099.00	-14,369.36	113.61	14,369.56	0.00	0.00	0.00	
25,400.00	90.00	179.89	11,099.00	-14,469.36	113.80	14,469.56	0.00	0.00	0.00	
25,500.00	90.00	179.89	11,099.00	-14,569.36	113.99	14,569.56	0.00	0.00	0.00	
25,600.00	90.00	179.89	11,099.00	-14,669.36	114.19	14,669.56	0.00	0.00	0.00	

Planning Report

Database:	STRYKER_EDM	Local Co-ordinate Reference:	Well 102H - Slot PLU27BD 102H SHL
Company:	XTO Energy	TVD Reference:	3268+23 @ 3291.00usft (M7504)
Project:	Eddy County, NM (NAD27) NMEZ Grid	MD Reference:	3268+23 @ 3291.00usft (M7504)
Site:	PLU 27 BD	North Reference	Grid
Well:	102H	Survey Calculation Method:	Minimum Curvature
Wellbore:	102H Lateral		
Design:	Plan #1		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)	
25,700.00	90.00	179.89	11,099.00	-14,769.36	114.38	14,769.56	0.00	0.00	0.00	
25,800.00	90.00	179.89	11,099.00	-14,869.36	114.57	14,869.56	0.00	0.00	0.00	
25,900.00	90.00	179.89	11,099.00	-14,969.36	114.76	14,969.56	0.00	0.00	0.00	
26,000.00	90.00	179.89	11,099.00	-15,069.36	114.95	15,069.56	0.00	0.00	0.00	
26,100.00	90.00	179.89	11,099.00	-15,169.36	115.15	15,169.56	0.00	0.00	0.00	
26,200.00	90.00	179.89	11,099.00	-15,269.36	115.34	15,269.56	0.00	0.00	0.00	
26,300.00	90.00	179.89	11,099.00	-15,369.36	115.53	15,369.56	0.00	0.00	0.00	
26,400.00	90.00	179.89	11,099.00	-15,469.36	115.72	15,469.56	0.00	0.00	0.00	
26,500.00	90.00	179.89	11,099.00	-15,569.36	115.91	15,569.56	0.00	0.00	0.00	
26,600.00	90.00	179.89	11,099.00	-15,669.36	116.11	15,669.56	0.00	0.00	0.00	
26,700.00	90.00	179.89	11,099.00	-15,769.36	116.30	15,769.56	0.00	0.00	0.00	
26,800.00	90.00	179.89	11,099.00	-15,869.36	116.49	15,869.56	0.00	0.00	0.00	
26,826.74	90.00	179.89	11,099.00	-15,896.10	116.54	15,896.30	0.00	0.00	0.00	

Design Targets										
Target Name	Dip Angle (°)	Dip Dir. (°)	TVD (usft)	+N/-S (usft)	+E/-W (usft)	Northing (usft)	Easting (usft)	Latitude	Longitude	
PLU27BD KOPA	0.00	0.00	0.00	74.66	85.88	400988.66	642,027.08	32° 6' 5.77234786 N	3° 52' 28.80938734 W	
- plan misses target center by 113.79usft at 0.00usft MD (0.00 TVD, 0.00 N, 0.00 E)										
- Point										
PLU27BD 102H SHL	0.00	0.00	0.00	0.00	0.00	400914.00	641,941.20	32° 6' 5.03711837 N	3° 52' 29.81143011 W	
- plan hits target center										
- Point										
PLU27BD 102H FTP_35	0.00	0.00	11,099.00	-502.30	87.00	400411.70	642,028.20	32° 6' 0.06256509 N	3° 52' 28.82484981 W	
- plan misses target center by 0.01usft at 11432.91usft MD (11099.00 TVD, -502.30 N, 86.99 E)										
- Point										
PLU27BD 102H PBHL_1	0.00	0.00	11,099.00	-15,896.10	117.00	385,017.90	642,058.20	32° 3' 27.71971593 N	3° 52' 29.23674138 W	
- plan misses target center by 0.46usft at 26826.74usft MD (11099.00 TVD, -15896.10 N, 116.54 E)										
- Point										
PLU27BD 102H LTP_34	0.00	0.00	11,099.00	-15,766.20	116.20	385,147.80	642,057.40	32° 3' 29.00528261 N	3° 52' 29.23962537 W	
- plan misses target center by 0.09usft at 26696.84usft MD (11099.00 TVD, -15766.20 N, 116.29 E)										
- Point										

PECOS DISTRICT DRILLING CONDITIONS OF APPROVAL

OPERATOR'S NAME:	XTO Permian Operating, LLC
LEASE NO.:	NMLC-0063875A
WELL NAME & NO.:	Poker Lake Unit 27 BD 102H
SURFACE HOLE FOOTAGE:	2510' FNL & 0663' FWL
BOTTOM HOLE FOOTAGE:	2440' FNL & 0750' FWL Sec. 10, T. 26 S., R 30 E.
LOCATION:	Section 27, T. 25 S., R 30 E., NMPM
COUNTY:	Eddy County, New Mexico

Commercial Well Determination

A commercial well determination shall be submitted after production has been established for at least six months.

Unit Wells

The well sign for a unit well shall include the unit number in addition to the surface and bottom hole lease numbers. This also applies to participating area numbers. If a participating area has not been established, the operator can use the general unit designation, but will replace the unit number with the participating area number when the sign is replaced.

A. DRILLING OPERATIONS REQUIREMENTS

The BLM is to be notified in advance for a representative to witness:

- a. Spudding well (minimum of 24 hours)
- b. Setting and/or Cementing of all casing strings (minimum of 4 hours)
- c. BOPE tests (minimum of 4 hours)

☒ **Eddy County**

Call the Carlsbad Field Office, 620 East Greene St., Carlsbad, NM 88220,
(575) 361-2822

1. **Hydrogen Sulfide (H₂S) monitors shall be installed prior to drilling out the surface shoe. If H₂S is detected in concentrations greater than 100 ppm, the Hydrogen Sulfide area shall meet Onshore Order 6 requirements, which includes equipment and personnel/public protection items. If Hydrogen Sulfide is encountered, provide measured values and formations to the BLM.**
2. Unless the production casing has been run and cemented or the well has been properly plugged, the drilling rig shall not be removed from over the hole without prior approval. **If the drilling rig is removed without approval – an Incident of Non-Compliance will be written and will be a “Major” violation.**

3. **The operator has proposed to drill multiple wells utilizing a skid/walking rig. Operator shall secure the wellbore on the current well, after installing and testing the wellhead, by installing a blind flange of like pressure rating to the wellhead and a pressure gauge that can be monitored while drilling is performed on the other wells.**
4. **Floor controls are required for 3M or Greater systems. These controls will be on the rig floor, unobstructed, readily accessible to the driller and will be operational at all times during drilling and/or completion activities. Rig floor is defined as the area immediately around the rotary table; the area immediately above the substructure on which the draw works is located, this does not include the dog house or stairway area.**
5. **The record of the drilling rate along with the GR/N well log run from TD to surface (horizontal well – vertical portion of hole) shall be submitted to the BLM office as well as all other logs run on the borehole 30 days from completion. If available, a digital copy of the logs is to be submitted in addition to the paper copies. The Rustler top and top and bottom of Salt are to be recorded on the Completion Report.**

B. CASING

Changes to the approved APD casing program need prior approval if the items substituted are of lesser grade or different casing size or are Non-API. The Operator can exchange the components of the proposal with that of superior strength (i.e. changing from J-55 to N-80, or from 36# to 40#). Changes to the approved cement program need prior approval if the altered cement plan has less volume or strength or if the changes are substantial (i.e. Multistage tool, ECP, etc.). The initial wellhead installed on the well will remain on the well with spools used as needed.

Centralizers required on surface casing per Onshore Order 2.III.B.1.f.

Wait on cement (WOC) for Water Basin:

After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi at the shoe, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. See individual casing strings for details regarding lead cement slurry requirements.

Provide compressive strengths including hours to reach required 500 pounds compressive strength prior to cementing each casing string. Have well specific cement details onsite prior to pumping the cement for each casing string.

No pea gravel permitted for remedial or fall back remedial without prior authorization from the BLM engineer.

Possibility of water flows in the Salado and Castile.

Possibility of lost circulation in the Red beds, Rustler, and Delaware.

Abnormal pressures may be encountered in the 3rd Bone Spring and all subsequent formations.

1. The 13-3/8 inch surface casing shall be set at approximately 1250 feet (in a competent bed below the Magenta Dolomite, which is a Member of the Rustler, and if salt is encountered, set casing at least 25 feet above the salt) and cemented to the surface.
 - a. If cement does not circulate to the surface, the appropriate BLM office shall be notified and a temperature survey utilizing an electronic type temperature survey with surface log readout will be used or a cement bond log shall be run to verify the top of the cement. Temperature survey will be run a minimum of six hours after pumping cement and ideally between 8-10 hours after completing the cement job.
 - b. Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry.
 - c. Wait on cement (WOC) time for a remedial job will be a minimum of 4 hours after bringing cement to surface or 500 pounds compressive strength, whichever is greater.
 - d. If cement falls back, remedial cementing will be done prior to drilling out that string.

Formation below the 13-3/8" shoe to be tested according to Onshore Order

2.III.B.1.i. Test to be done as a mud equivalency test using the mud weight necessary for the pore pressure of the formation below the shoe and the mud weight for the bottom of the hole. Report results to BLM office.

Intermediate casing shall be kept fluid filled while running into hole to meet BLM minimum collapse requirements.

2. The minimum required fill of cement behind the 9-5/8 inch intermediate casing is:

Operator has proposed DV tool at depth of 6000', but will adjust cement proportionately if moved. DV tool shall be set a minimum of 50' below previous shoe and a minimum of 200' above current shoe. Operator shall submit sundry if DV tool depth cannot be set in this range. If an ECP is used, it is to be set a minimum of 50' below the shoe to provide cement across the shoe. If it cannot be set below the shoe, a CBL shall be run to verify cement coverage.

a. First stage to DV tool:

- ☒ Cement to circulate. If cement does not circulate, contact the appropriate BLM office before proceeding with second stage cement job. Operator should have plans as to how they will achieve circulation on the next stage.

b. Second stage above DV tool:

- ☒ Cement to surface. If cement does not circulate, contact the appropriate BLM office.

Formation below the 9-5/8" shoe to be tested according to Onshore Order 2.III.B.1.i. Test to be done as a mud equivalency test using the mud weight necessary for the pore pressure of the formation below the shoe and the mud weight for the bottom of the hole. Report results to BLM office.

Centralizers required through the curve and a minimum of one every other joint.

3. The minimum required fill of cement behind the 5-1/2 inch production casing is:

- ☒ Cement should tie-back at least 200 feet into previous casing string. Operator shall provide method of verification. **Excess calculates to 21% - Additional cement may be required.**

4. If hardband drill pipe is rotated inside casing, returns will be monitored for metal. If metal is found in samples, drill pipe will be pulled and rubber protectors which have a larger diameter than the tool joints of the drill pipe will be installed prior to continuing drilling operations.

C. PRESSURE CONTROL

1. All blowout preventer (BOP) and related equipment (BOPE) shall comply with well control requirements as described in Onshore Oil and Gas Order No. 2 and API 53.
2. Variance approved to use flex line from BOP to choke manifold. Check condition of flexible line from BOP to choke manifold, replace if exterior is damaged or if line fails test. Line to be as straight as possible with no hard bends and is to be anchored according to Manufacturer's requirements. The flexible hose can be exchanged with a hose of equal size and equal or greater pressure rating. **Anchor requirements, specification sheet and hydrostatic pressure test certification matching the hose in service, to be onsite for review. These documents shall be posted in the company man's trailer and on the rig floor.** If the BLM inspector questions the straightness of the hose, a BLM engineer will be contacted and will review in the field or via picture supplied by inspector to determine if changes are required (operator shall expect delays if this occurs).

3. Operator has proposed a multi-bowl wellhead assembly. This assembly will only be tested when installed on the surface casing. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be 5000 (5M) psi.
- a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
 - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
 - c. Manufacturer representative shall install the test plug for the initial BOP test.
 - d. Operator shall perform the intermediate casing integrity test to 70% of the casing burst. This will test the multi-bowl seals.
 - e. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.

5M system requires an HCR valve, remote kill line and annular to match. The remote kill line is to be installed prior to testing the system and tested to stack pressure.

4. The appropriate BLM office shall be notified a minimum of 4 hours in advance for a representative to witness the tests.
- a. In a water basin, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. The casing cut-off and BOP installation can be initiated four hours after installing the slips, which will be approximately six hours after bumping the plug. For those casing strings not using slips, the minimum wait time before cut-off is eight hours after bumping the plug. BOP/BOPE testing can begin after cut-off or once cement reaches 500 psi compressive strength (including lead when specified), whichever is greater. However, if the float does not hold, cut-off cannot be initiated until cement reaches 500 psi compressive strength (including lead when specified).
 - b. The tests shall be done by an independent service company utilizing a test plug **not a cup or J-packer**.
 - c. The test shall be run on a 5000 psi chart for a 2-3M BOP/BOP, on a 10000 psi chart for a 5M BOP/BOPE and on a 15000 psi chart for a 10M BOP/BOPE. If a linear chart is used, it shall be a one hour chart. A circular chart shall have a maximum 2 hour clock. If a twelve hour or twenty-four hour chart is used, tester shall make a notation that it is run with a two hour clock.
 - d. The results of the test shall be reported to the appropriate BLM office.

- e. All tests are required to be recorded on a calibrated test chart. **A copy of the BOP/BOPE test chart and a copy of independent service company test will be submitted to the appropriate BLM office.**
- f. The BOP/BOPE test shall include a low pressure test from 250 to 300 psi. The test will be held for a minimum of 10 minutes if test is done with a test plug and 30 minutes without a test plug. This test shall be performed prior to the test at full stack pressure.
- g. BOP/BOPE must be tested by an independent service company within 500 feet of the top of the **Wolfcamp** formation if the time between the setting of the intermediate casing and reaching this depth exceeds 20 days. This test does not exclude the test prior to drilling out the casing shoe as per Onshore Order No. 2.

D. DRILLING MUD

Mud system monitoring equipment, with derrick floor indicators and visual and audio alarms, shall be operating before drilling into the **Wolfcamp** formation, and shall be used until production casing is run and cemented.

E. DRILL STEM TEST

If drill stem tests are performed, Onshore Order 2.III.D shall be followed.

F. WASTE MATERIAL AND FLUIDS

All waste (i.e. drilling fluids, trash, salts, chemicals, sewage, gray water, etc.) created as a result of drilling operations and completion operations shall be safely contained and disposed of properly at a waste disposal facility. No waste material or fluid shall be disposed of on the well location or surrounding area.

Porto-johns and trash containers will be on-location during fracturing operations or any other crew-intensive operations.

JAM 011420
