

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

RECEIVED

NOV 25 2019

FORM APPROVED
OMB NO. 1004-0137
Expires: January 31, 2018**SUNDRY NOTICES AND REPORTS ON WELLS**
Do not use this form for proposals to drill or re-enter an abandoned well. Use form 3160-3 (APD) for such proposals.5. Lease Serial No.
NMMN030453

6. If Indian, Allottee or Tribe Name

SUBMIT IN TRIPLICATE - Other instructions on page 27. If Unit or CA/Agreement, Name and/or No.
891000303X1. Type of Well
☒ Oil Well ☐ Gas Well ☐ Other8. Well Name and No.
POKER LAKE UNIT 13 DTD 905H2. Name of Operator
XTO PERMIAN OPERATING LLC
Contact: KELLY KARDOS
E-Mail: kelly_kardos@xtoenergy.com9. API Well No.
30-015-46106-00-X13a. Address
6401 HOLIDAY HILL ROAD BLDG 5
MIDLAND, TX 797073b. Phone No. (include area code)
Ph: 432-620-437410. Field and Pool or Exploratory Area
PURPLE SAGE-WOLFCAMP (GAS)

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)

Sec 24 T24S R30E NWNE 477FNL 2205FEL
32.209316 N Lat, 103.832809 W Lon11. County or Parish, State
EDDY COUNTY, NM**12. CHECK THE APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA**

TYPE OF SUBMISSION	TYPE OF ACTION			
☒ Notice of Intent	☐ Acidize	☐ Deepen	☐ Production (Start/Resume)	☐ Water Shut-Off
☐ Subsequent Report	☐ Alter Casing	☐ Hydraulic Fracturing	☐ Reclamation	☐ Well Integrity
☐ Final Abandonment Notice	☐ Casing Repair	☐ New Construction	☐ Recomplete	☒ Other
	☐ Change Plans	☐ Plug and Abandon	☐ Temporarily Abandon	Change to Original APD
	☐ Convert to Injection	☐ Plug Back	☐ Water Disposal	

13. Describe Proposed or Completed Operation: Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recompleat horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports must be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompleat in a new interval, a Form 3160-4 must be filed once testing has been completed. Final Abandonment Notices must be filed only after all requirements, including reclamation, have been completed and the operator has determined that the site is ready for final inspection.

XTO Permian Operating, LLC requests permission to make the following changes to the original APD:

Change target formation from WC Bone Spring (Oil) to Purple Sage, Wolfcamp (Gas).

Change the BHL from 2440' FNL & 2310' FEL in Sec. 36-T24S-R30E to 200' FSL & 2169' FEL in Sec. 25-T24S-R30E.

Change the casing/cement design per the attached drilling program.

XTO requests to utilize centralizers from KOP to TOC only a minimum of one every other joint.

In addition, XTO requests a variance to be able to batch drill these wells if necessary. In doing

14. I hereby certify that the foregoing is true and correct.

**Electronic Submission #492933 verified by the BLM Well Information System
For XTO PERMIAN OPERATING LLC, sent to the Carlsbad
Committed to AFMSS for processing by PRISCILLA PEREZ on 11/19/2019 (20PP0459SE)**

Name (Printed/Typed) KELLY KARDOS

Title REGULATORY COORDINATOR

Signature (Electronic Submission)

Date 11/19/2019

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved By (BLM Approver Not Specified)

Title

Date 11/21/2019

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Office Carlsbad

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Instructions on page 2)

**** BLM REVISED ** BLM REVISED ** BLM REVISED ** BLM REVISED ** BLM REVISED ****

1/27/20 KS

Additional data for EC transaction #492933 that would not fit on the form

32. Additional remarks, continued

so, XTO will set intermediate casing and ensure that the well is cemented properly and the well is dead. With floats holding, no pressure on the intermediate csg annulus, and the installation of a TA cap as per GE recommendations, XTO will contact the BLM to skid the rig to drill the surface and intermediate for the remaining wells on the pad. Once surface and intermediate are all completed, XTO will begin drilling the production hole on each of the wells.

Poker Lake Unit 13 DTD 125H ? 30-015-45821

Poker Lake Unit 13 DTD 705H - 30-015-45827

Poker Lake Unit 13 DTD 905H - 30-015-46106

Revisions to Operator-Submitted EC Data for Sundry Notice #492933

	Operator Submitted	BLM Revised (AFMSS)
Sundry Type:	APDCH NOI	APDCH NOI
Lease:	NMNM030453	NMNM030453
Agreement:	NMNM71016X	891000303X (NMNM71016X)
Operator:	XTO PERMIAN OPERATING, LLC 6401 HOLIDAY HILL RD BLDG 5 MIDLAND, TX 79707 Ph: 432-620-4374	XTO PERMIAN OPERATING LLC 6401 HOLIDAY HILL ROAD BLDG 5 MIDLAND, TX 79707 Ph: 432.683 2277
Admin Contact:	KELLY KARDOS REGULATORY COORDINATOR E-Mail: kelly_kardos@xtoenergy.com Ph: 432-620-4374	KELLY KARDOS REGULATORY COORDINATOR E-Mail: kelly_kardos@xtoenergy.com Ph: 432-620-4374
Tech Contact:	KELLY KARDOS REGULATORY COORDINATOR E-Mail: kelly_kardos@xtoenergy.com Ph: 432-620-4374	KELLY KARDOS REGULATORY COORDINATOR E-Mail: kelly_kardos@xtoenergy.com Ph: 432-620-4374
Location: State: County:	NM EDDY	NM EDDY
Field/Pool:	WC BONE SPRING	PURPLE SAGE-WOLFCAMP (GAS)
Well/Facility:	POKER LAKE UNIT 13 DTD 905H Sec 24 T24S R30E Mer NMP NWNE 477FNL 2205FEL	POKER LAKE UNIT 13 DTD 905H Sec 24 T24S R30E NWNE 477FNL 2205FEL 32.209316 N Lat, 103.832809 W Lon

RECEIVED

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

NOV 25 2019

FORM APPROVED
OMB NO. 1004-0137
Expires: January 31, 2018**SUNDRY NOTICES AND REPORTS ON WELLS**
Do not use this form for proposals to drill or to re-enter an abandoned well. Use form 3160-3 (APD) for such proposals.5. Lease Serial No.
NMNM030453
6. If Indian, Allottee or Tribe Name**SUBMIT IN TRIPLICATE - Other instructions on page 2**7. If Unit or CA/Agreement, Name and/or No.
891000303X

1. Type of Well

☒ Oil Well ☐ Gas Well ☐ Other8. Well Name and No.
POKER LAKE UNIT 13 DTD 905H

2. Name of Operator

XTO PERMIAN OPERATING LLC

Contact: KELLY KARDOS
E-Mail: kelly_kardos@xtoenergy.com9. API Well No.
30-015-46106-00-X1

3a. Address

6401 HOLIDAY HILL ROAD BLDG 5
MIDLAND, TX 79707

3b. Phone No. (include area code)

Ph: 432-620-4374

10. Field and Pool or Exploratory Area
WILDCAT - BONE SPRING

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)

Sec 24 T24S R30E NWNE 477FNL 2205FEL
32.209316 N Lat, 103.832809 W Lon11. County or Parish, State
EDDY COUNTY, NM

12. CHECK THE APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
☒ Notice of Intent	☐ Acidize	☐ Deepen	☐ Production (Start/Resume)	☐ Water Shut-Off
☐ Subsequent Report	☐ Alter Casing	☐ Hydraulic Fracturing	☐ Reclamation	☐ Well Integrity
☐ Final Abandonment Notice	☐ Casing Repair	☐ New Construction	☐ Recomplete	☒ Other
	☐ Change Plans	☐ Plug and Abandon	☐ Temporarily Abandon	Change to Original A
	☐ Convert to Injection	☐ Plug Back	☐ Water Disposal	PD

13. Describe Proposed or Completed Operation: Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomple horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports must be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompletion in a new interval, a Form 3160-4 must be filed once testing has been completed. Final Abandonment Notices must be filed only after all requirements, including reclamation, have been completed and the operator has determined that the site is ready for final inspection.

XTO Permian Operating, LLC requests permission to make the following changes to the original APD:

Change target formation from WC Bone Spring (Oil) to Purple Sage; Wolfcamp (Gas).

Change the BHL from 2440' FNL & 2310' FEL in Sec. 36-T24S-R30E to 200' FSL & 2169' FEL in Sec. 25-T24S-R30E.

Change the casing/cement design per the attached drilling program.

XTO requests to utilize centralizers from KOP to TOC only a minimum of one every other joint.

In addition, XTO requests a variance to be able to batch drill these wells if necessary. In doing

SEE ATTACHED FOR
CONDITIONS OF APPROVAL

14. I hereby certify that the foregoing is true and correct.	
Electronic Submission #492933 verified by the BLM Well Information System For XTO PERMIAN OPERATING LLC, sent to the Carlsbad Committed to AFMSS for processing by PRISCILLA PEREZ on 11/19/2019 (20PP0459SE)	
Name (Printed/Typed) KELLY KARDOS	Title REGULATORY COORDINATOR
Signature (Electronic Submission)	Date 11/19/2019 APPROVED
THIS SPACE FOR FEDERAL OR STATE OFFICE USE	
NOV 21 2019	
Approved By	Title
BUREAU OF LAND MANAGEMENT ROSWELL FIELD OFFICE	
Office	
Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.	
Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.	

(Instructions on page 2)

** BLM REVISED ** BLM REVISED ** BLM REVISED ** BLM REVISED ** BLM REVISED **

Additional data for EC transaction #492933 that would not fit on the form

32. Additional remarks, continued

so, XTO will set intermediate casing and ensure that the well is cemented properly and the well is dead. With floats holding, no pressure on the intermediate csg annulus, and the installation of a TA cap as per GE recommendations, XTO will contact the BLM to skid the rig to drill the surface and intermediate for the remaining wells on the pad. Once surface and intermediate are all completed, XTO will begin drilling the production hole on each of the wells.

Poker Lake Unit 13 DTD 125H ? 30-015-45821
Poker Lake Unit 13 DTD 705H - 30-015-45827
Poker Lake Unit 13 DTD 905H - 30-015-46106

Revisions to Operator-Submitted EC Data for Sundry Notice #492933

	Operator Submitted	BLM Revised (AFMSS)
Sundry Type:	APDCH NOI	APDCH NOI
Lease:	NMNM030453	NMNM030453
Agreement:	NMNM71016X	891000303X (NMNM71016X)
Operator:	XTO PERMIAN OPERATING, LLC 6401 HOLIDAY HILL RD BLDG 5 MIDLAND, TX 79707 Ph: 432-620-4374	XTO PERMIAN OPERATING LLC 6401 HOLIDAY HILL ROAD BLDG 5 MIDLAND, TX 79707 Ph: 432.683 2277
Admin Contact:	KELLY KARDOS REGULATORY COORDINATOR E-Mail: kelly_kardos@xtoenergy.com Ph: 432-620-4374	KELLY KARDOS REGULATORY COORDINATOR E-Mail: kelly_kardos@xtoenergy.com Ph: 432-620-4374
Tech Contact:	KELLY KARDOS REGULATORY COORDINATOR E-Mail: kelly_kardos@xtoenergy.com Ph: 432-620-4374	KELLY KARDOS REGULATORY COORDINATOR E-Mail: kelly_kardos@xtoenergy.com Ph: 432-620-4374
Location:		
State:	NM	NM
County:	EDDY	EDDY
Field/Pool:	WC BONE SPRING	WILDCAT - BONE SPRING
Well/Facility:	POKER LAKE UNIT 13 DTD 905H Sec 24 T24S R30E Mer NMP NWNE 477FNL 2205FEL	POKER LAKE UNIT 13 DTD 905H Sec 24 T24S R30E NWNE 477FNL 2205FEL 32.209316 N Lat, 103.832809 W Lon

RECEIVED

District I
1625 N. French Dr., Hobbs, NM 88240
Phone: (575) 393-6161 Fax: (575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone: (575) 748-1283 Fax: (575) 748-9720
District III
1000 Rio Brazos Road, Aztec, NM 87410
Phone: (505) 334-6178 Fax: (505) 334-6170
District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505
Phone: (505) 476-3460 Fax: (505) 476-3462

State of New Mexico
Energy, Minerals & Natural Resources Department

OIL CONSERVATION DIVISION
DISTRICT ARTESIA O.C.D.

1220 South St. Francis Dr.

Santa Fe, NM 87505

Form C-102

Revised August 1, 2011

Submit one copy to appropriate

District Office

☒ AMENDED REPORT

WELL LOCATION AND ACREAGE DEDICATION PLAT

¹ API Number 30-015-46106	² Pool Code 98220	³ Pool Name PURPLE SAGE; WOLFCAMP
⁴ Property Code	⁵ Property Name POKER LAKE UNIT 13 DTD	⁶ Well Number 905H
⁷ OGRID No. 373075	⁸ Operator Name XTO PERMIAN OPERATING, LLC	⁹ Elevation 3,471'

¹⁰ Surface Location


UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
B	24	24 S	30 E		477	NORTH	2,205	EAST	EDDY

¹¹ Bottom Hole Location If Different From Surface

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
O	25	24 S	30 E		200	SOUTH	2,169	EAST	EDDY

¹² Dedicated Acres 640	¹³ Joint or Infill	¹⁴ Consolidation Code	¹⁵ Order No.
--------------------------------------	-------------------------------	----------------------------------	-------------------------

No allowable will be assigned to this completion until all interests have been consolidated or a non-standard unit has been approved by the division.

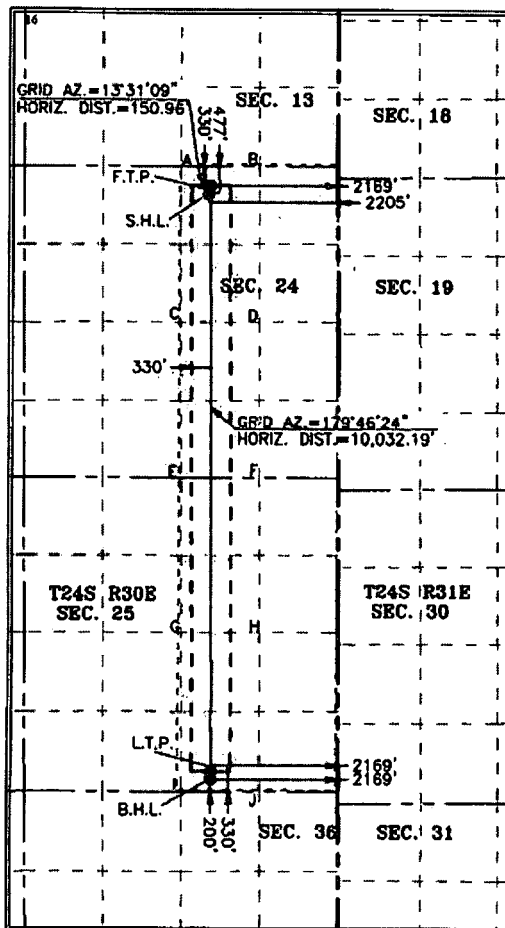

GEODETIC COORDINATES
NAD 83 NME
SURFACE LOCATION
Y = 440,243.5
X = 696,141.8
LAT. = 32.209318°N
LONG. = 103.832808°W
FIRST TAKE POINT
NAD 83 NME
Y = 440,390.3
X = 696,177.1
LAT. = 32.209719°N
LONG. = 103.832691°W

CORNER COORDINATES TABLE

NAD 83 NME
A - Y = 440,718.6 N, X = 695,668.2 E
B - Y = 440,723.1 N, X = 697,006.5 E
C - Y = 438,079.8 N, X = 695,677.6 E
D - Y = 438,084.4 N, X = 697,016.3 E
E - Y = 435,438.2 N, X = 695,687.0 E
F - Y = 435,442.2 N, X = 697,026.2 E
G - Y = 432,798.6 N, X = 695,700.7 E
H - Y = 432,801.0 N, X = 697,038.3 E
I - Y = 430,157.5 N, X = 695,714.4 E
J - Y = 430,159.4 N, X = 697,050.5 E

CORNER COORDINATES TABLE

NAD 27 NME
A - Y = 440,859.8 N, X = 654,484.2 E
B - Y = 440,864.3 N, X = 655,822.5 E
C - Y = 438,021.1 N, X = 654,493.6 E
D - Y = 438,025.7 N, X = 655,832.2 E
E - Y = 435,378.5 N, X = 654,502.9 E
F - Y = 435,383.5 N, X = 655,842.0 E
G - Y = 432,740.0 N, X = 654,516.5 E
H - Y = 432,742.4 N, X = 655,854.0 E
I - Y = 430,088.9 N, X = 654,530.1 E
J - Y = 430,100.8 N, X = 655,866.2 E

LAST TAKE POINT

NAD 83 NME
Y = 430,488.2
X = 696,216.3
LAT. = 32.182489°N
LONG. = 103.832714°W

LAST TAKE POINT

NAD 27 NME
Y = 430,429.6
X = 655,032.0
LAT. = 32.182375°N
LONG. = 103.832230°W

BOTTOM HOLE LOCATION

NAD 83 NME
Y = 430,358.2
X = 696,216.8
LAT. = 32.182142°N
LONG. = 103.832714°W

BOTTOM HOLE LOCATION

NAD 27 NME
Y = 430,298.6
X = 655,032.9
LAT. = 32.182018°N
LONG. = 103.832230°W

¹⁷ OPERATOR CERTIFICATION

I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and that this or gazette either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of such a mineral or working interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division.

Kelly Kardos

11/15/19

Signature

Date

Kelly Kardos

Printed Name

kelly_kardos@xtoenergy.com

E-mail Address

¹⁸ SURVEYOR CERTIFICATION

I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief.

04-29-2019

Date of Survey

Signature and Seal of
Professional Surveyor:

MARK DILLON HARP 23786
Certificate Number



RR

2018010156

Intent ☒ As Drilled ☐

API # 30-015-46106			
Operator Name: XTO Permian Operating, LLC		Property Name: Poker Lake Unit 13 DTD	Well Number 905H

Kick Off Point (KOP)

UL B	Section 24	Township 24S	Range 30E	Lot	Feet 477	From N/S North	Feet 2205	From E/W East	County Eddy
Latitude 32.209316					Longitude -103.832808			NAD NAD83	

First Take Point (FTP)

UL B	Section 24	Township 24S	Range 30E	Lot	Feet 330	From N/S North	Feet 2169	From E/W East	County Eddy
Latitude 32.209719					Longitude -103.832691			NAD NAD83	

Last Take Point (LTP)

UL O	Section 25	Township 24S	Range 30E	Lot	Feet 330	From N/S South	Feet 2169	From E/W East	County Eddy
Latitude 32.182499					Longitude -103.832714			NAD NAD83	

Is this well the defining well for the Horizontal Spacing Unit? ☒

Is this well an infill well? ☐

If infill is yes please provide API if available, Operator Name and well number for Defining well for Horizontal Spacing Unit.

API # 30-015-46251			
Operator Name: XTO Permian Operating, LLC		Property Name: Poker Lake Unit 13 DTD	Well Number 206H

KZ 06/29/2018

DRILLING PLAN: BLM COMPLIANCE
(Supplement to BLM 3160-3)

XTO Energy Inc.
PLU 13 Dog Town Draw 905H
Projected TD: 21510' MD / 11423' TVD
SHL: 477' FNL & 2205' FEL , Section 24, T24S, R30E
BHL: 200' FSL & 2169' FEL , Section 25, T24S, R30E
Eddy County, NM

1. Geologic Name of Surface Formation

A. Permian

2. Estimated Tops of Geological Markers & Depths of Anticipated Fresh Water, Oil or Gas:

Formation	Well Depth (TVD)	Water/Oil/Gas
Rustler	508'	Water
Top of Salt	918'	Water
Base of Salt	3973'	Water
Delaware	4193'	Water
Bone Spring	8168'	Water/Oil/Gas
1st Bone Spring Ss	9118'	Water/Oil/Gas
2nd Bone Spring Ss	9798'	Water/Oil/Gas
3rd Bone Spring Ss	10928'	Water/Oil/Gas
Wolfcamp	11343'	Water/Oil/Gas
Wolfcamp X	11418'	Water/Oil/Gas
Target/Land Curve	11423'	Water/Oil/Gas

*** Hydrocarbons @ Brushy Canyon

*** Groundwater depth 40' (per NM State Engineers Office).

No other formations are expected to yield oil, gas or fresh water in measurable volumes. The surface fresh water sands will be protected by setting 13-3/8 inch casing @ 760' (158' above the salt) and circulating cement back to surface. The salt will be isolated by setting 9-5/8 inch casing at 4110' and circulating cement to surface. An 8-3/4 inch vertical and curve hole will be drilled and 7 inch casing run and cemented 200' into the 9-5/8 inch casing. A 6 inch curve and lateral hole will be drilled to MD/TD and 4-1/2 inch liner will be set at TD and cemented back 250' into the 7 inch casing shoe.

3. Casing Design

Hole Size	Depth	OD Csg	Weight	Collar	Grade	New/Used	SF Burst	SF Collapse	SF Tension
17-1/2"	0' - 760'	13-3/8"	54.5	BTC	J-55	New	2.14	3.25	20.59
12-1/4"	0' - 4110'	9-5/8"	40	BTC	J-55	New	1.39	1.99	3.83
8-3/4"	0' - 11772'	7"	32	BTC	P-110	New	1.19	2.01	2.38
6"	11772' - 21510'	4-1/2"	13.5	BTC	P-110	New	1.18	2.52	2.06

- XTO requests to utilize centralizers only in the curve after the KOP and only a minimum of one every other joint.
- 9-5/8" & 4-1/2" Collapse analyzed using 50% evacuation based on regional experience.
- 4-1/2" tension calculated using vertical hanging weight plus the lateral weight multiplied by a friction factor of 0.35

WELLHEAD:

A. Starting Head (RSH System): 13-3/8" SOW bottom x 13-5/8" 5M top flange

B. Tubing Head: 13-5/8" 5M bottom flange x 7-1/16" 10M top flange

- Wellhead will be installed by manufacturer's representatives.
- Manufacturer will monitor welding process to ensure appropriate temperature of seal.
- Operator will test the 9-5/8" casing to per Onshore Order 2.
- Wellhead manufacturer representative will not be present for BOP test plug installation

4. Cement Program

Surface Casing: 13-3/8", 54.5 New J-55, BTC casing to be set at +/- 760'

Lead: 340 sxs EconoCem-HLTRRC (mixed at 12.9 ppg, 1.87 ft³/sx, 10.13 gal/sx water)

Tail: 300 sxs Halcem-C + 2% CaCl (mixed at 14.8 ppg, 1.35 ft³/sx, 6.39 gal/sx water)

Compressives: 12-hr = 900 psi 24 hr = 1500 psi

Top of cement: Surface

Intermediate Casing: 9-5/8", 40 New J-55, BTC casing to be set at +/- 4110'

Lead: 1090 sxs Halcem-C + 2% CaCl (mixed at 12.9 ppg, 1.88 ft³/sx, 9.61 gal/sx water)

Tail: 380 sxs Halcem-C + 2% CaCl (mixed at 14.8 ppg, 1.33 ft³/sx, 6.39 gal/sx water)

Compressives: 12-hr = 900 psi 24 hr = 1500 psi

Top of cement: Surface

2nd Intermediate Casing: 7", 32 New P-110, BTC casing to be set at +/- 11772'

Lead: 650 sxs Halcem-C + 2% CaCl (mixed at 12.9 ppg, 1.88 ft³/sx, 9.61 gal/sx water)

Tail: 130 sxs Halcem-C + 2% CaCl (mixed at 14.8 ppg, 1.33 ft³/sx, 6.39 gal/sx water)

Compressives: 12-hr = 900 psi 24 hr = 1500 psi

Top of cement: 200' inside previous casing

Production Casing: 4-1/2", 13.5 New P-110, BTC casing to be set at +/- 21510'

Tail: 820 sxs VersaCem (mixed at 13.2 ppg, 10872 ft³/sx, 8.38 gal/sx water)

Compressives: 12-hr = 1375 psi 24 hr = 2285 psi

Top of cement: ~~Top of liner~~ 11,472' (100' tie back minimum)

5. Pressure Control Equipment

The blow out preventer equipment (BOP) for this well consists of a 13-5/8" minimum 5M Hydral and a 13-5/8" minimum 5M Double Ram BOP. MASP should not exceed 4199 psi.

All BOP testing will be done by an independent service company. Annular pressure tests will be limited to 50% of the working pressure. When nipping up on the 13-5/8" 5M bradenhead and flange, the BOP test will be limited to 5000 psi. When the 9-5/8" and 7" casing is set, the packoff seals will be tested to a minimum of 5000 psi. All BOP tests will include a low pressure test as per BLM regulations. The 5M BOP diagrams are attached. Blind rams will be functioned tested each trip, pipe rams will be functioned tested each day.

A variance is requested to allow use of a flex hose as the choke line from the BOP to the Choke Manifold. If this hose is used, a copy of the manufacturer's certification and pressure test chart will be kept on the rig. Attached is an example of a certification and pressure test chart. The manufacturer does not require anchors.

6. Proposed Mud Circulation System

INTERVAL	Hole Size	Mud Type	MW (ppg)	Viscosity (sec/qt)	Fluid Loss (cc)
0' to 760'	17-1/2"	FW/Native	8.4-8.8	35-40	NC
760' to 4110'	12-1/4"	Brine/Gel Sweeps	9.8-10.2	30-32	NC
4110' to 11772'	8-3/4"	FW/ Cut Brine	8.6-9.3	29-32	NC - 20
11772' to 21510'	6"	OBM	11-11.6	32-50	NC-20

The necessary mud products for weight addition and fluid loss control will be on location at all times.

Spud with fresh water/native mud. Drill out from under 13-3/8" surface casing with brine solution. A 9.8ppg-10.2ppg brine mud will be used while drilling through the salt formation. Use fibrous materials as needed to control seepage and lost circulation. Pump viscous sweeps as needed for hole cleaning. Pump speed will be recorded on a daily drilling report after mudding up. A Pason or Totco will be used to detect changes in loss or gain of mud volume. A mud test will be performed every 24 hours to determine: density, viscosity, strength, filtration and pH as necessary. Use available solids controls equipment to help keep mud weight down after mud up. Rig up solids control equipment to operate as a closed loop system.

7. Auxiliary Well Control and Monitoring Equipment

- A. A Kelly cock will be in the drill string at all times.
- B. A full opening drill pipe stabbing valve having appropriate connections will be on the rig floor at all times.
- C. H2S monitors will be on location when drilling below the 13-3/8" casing.

8. Logging, Coring and Testing Program

Mud Logger: Mud Logging Unit (2 man) below intermediate casing.


Open hole logging will not be done on this well.


9. Abnormal Pressures and Temperatures / Potential Hazards

None Anticipated. BHT of 150 to 170 F is anticipated. No H2S is expected but monitors will be in place to detect any H2S occurrences. Should these circumstances be encountered the operator and drilling contractor are prepared to take all necessary steps to ensure safety of all personnel and environment. Lost circulation could occur but is not expected to be a serious problem in this area and hole seepage will be compensated for by additions of small amounts of LCM in the drilling fluid. The maximum anticipated bottom hole pressure for this well is 6712 psi.

10. Anticipated Starting Date and Duration of Operations


Road and location construction will begin after Santa Fe and BLM have approved the APD. Anticipated spud date will be as soon after Santa Fe and BLM approval and as soon as a rig will be available. Move in operations and drilling is expected to take 40 days. If production casing is run, an additional 30 days will be needed to complete well and construct surface facilities and/or lay flow lines in order to place well on production.

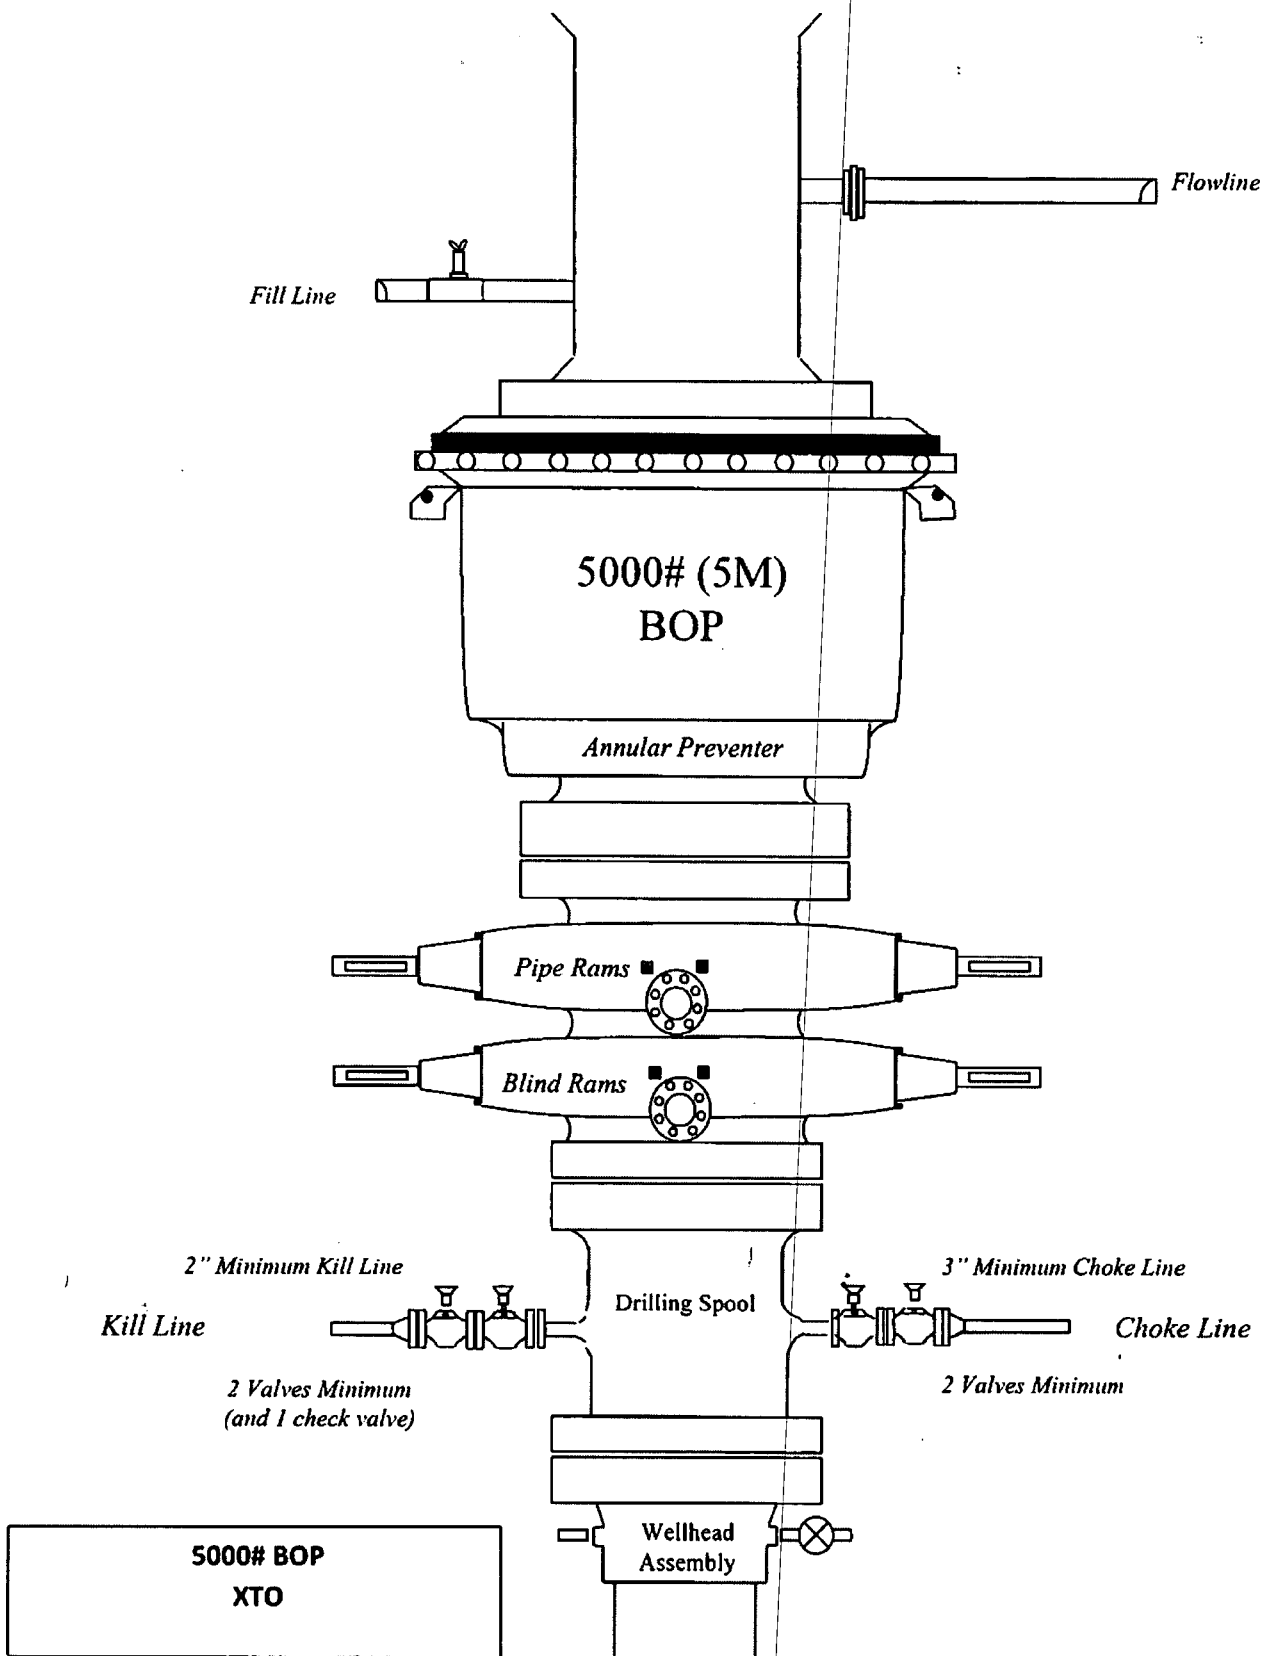

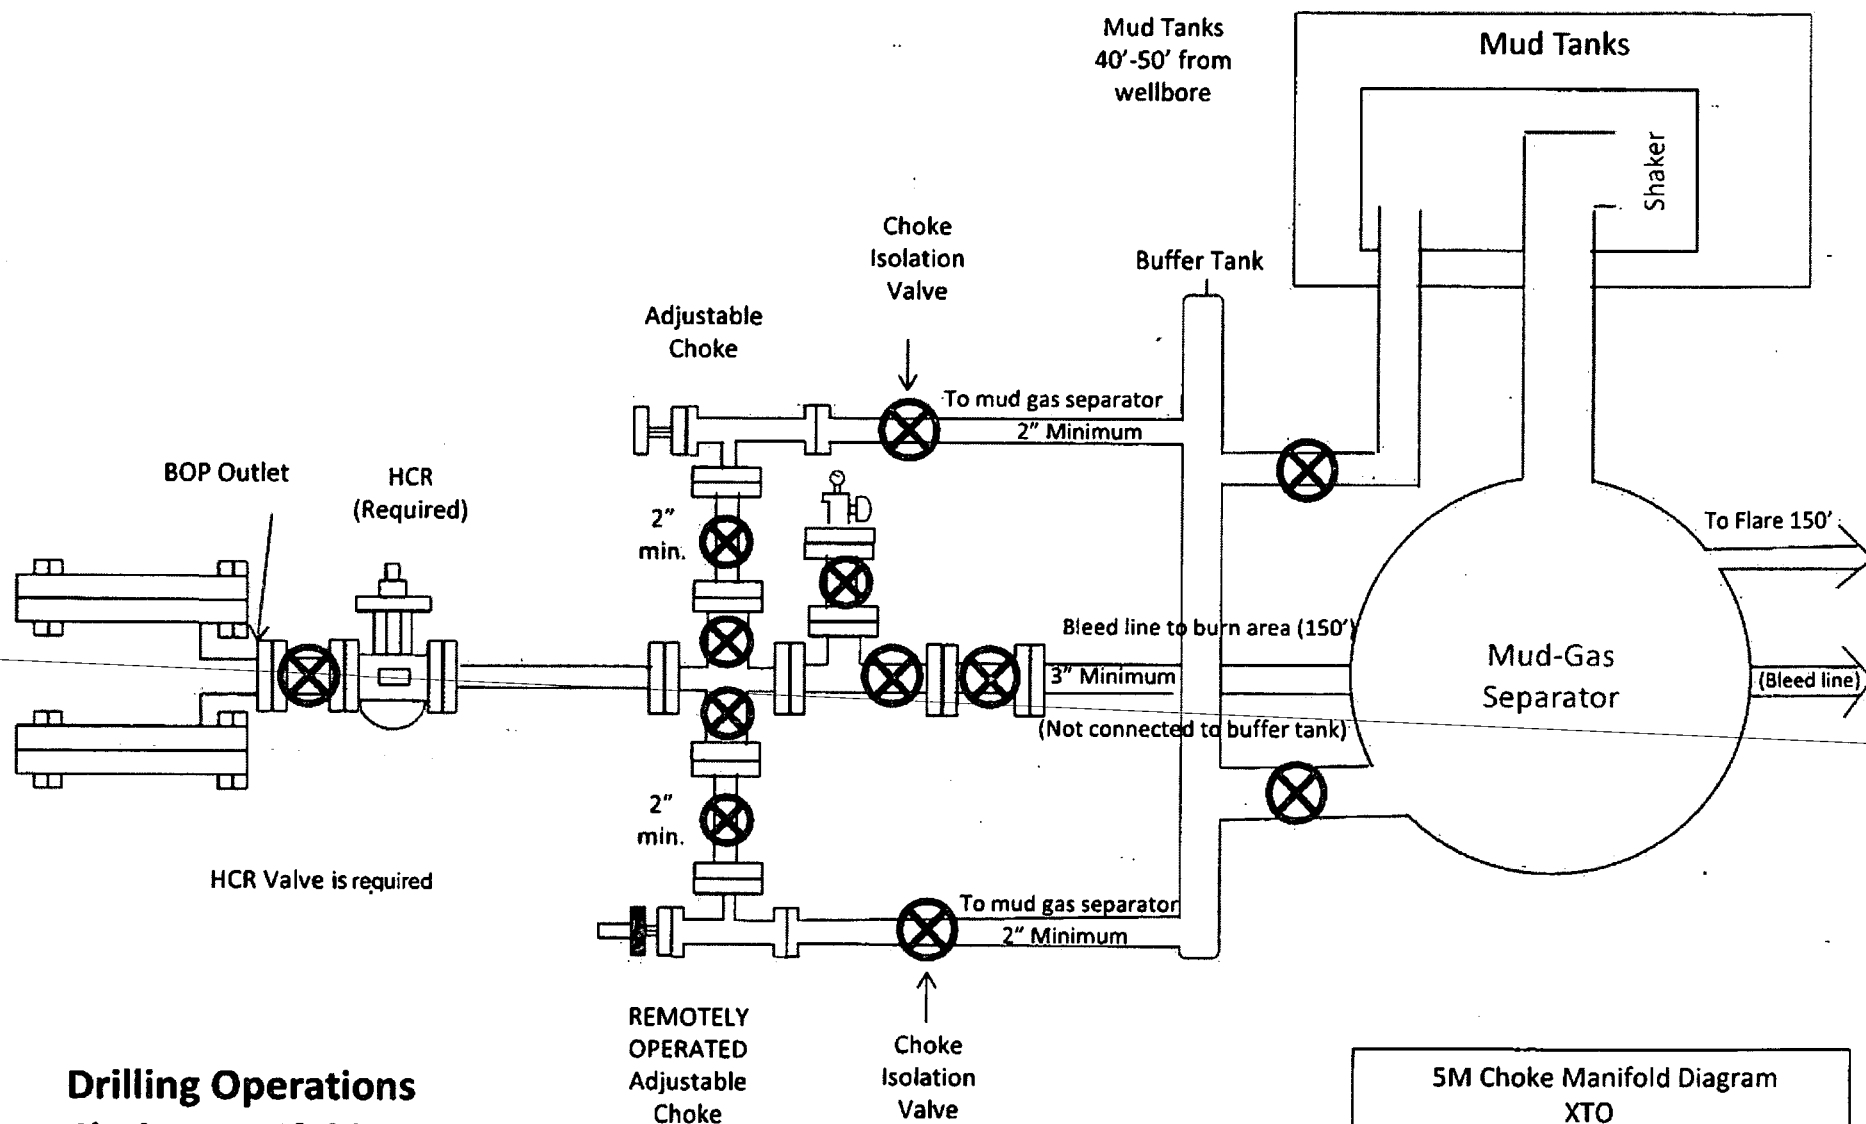

Drilling Operations
Choke Manifold
5M Service

5M Choke Manifold Diagram
XTO



GATES E & S NORTH AMERICA, INC
DU-TEX
134 44TH STREET
CORPUS CHRISTI, TEXAS 78405


PHONE: 361-887-9807
FAX: 361-887-0812
EMAIL: crpe&s@gates.com
WEB: www.gates.com


GRADE D PRESSURE TEST CERTIFICATE

Customer :	AUSTIN DISTRIBUTING	Test Date:	6/8/2014
Customer Ref. :	PENDING	Hose Serial No.:	D-060814-1
Invoice No. :	201709	Created By:	NORMA
Product Description:	FD3.012.0R41/16.SKFLGE/E LE		
End Fitting 1 :	1 1/16 in.SK FLG	End Fitting 2 :	1 1/16 in.SK FLG
Gates Part No. :	4774-6001	Assembly Code :	L33090011513D-060814-1
Working Pressure :	5,000 PSI	Test Pressure :	7,500 PSI

Gates E & S North America, Inc. certifies that the following hose assembly has been tested to the Gates Oilfield Roughneck Agreement/Specification requirements and passed the 15 minute hydrostatic test per API Spec 7K/Q1, Fifth Edition, June 2010, Test pressure 9.6.7 and per Table 9 to 7,500 psi in accordance with this product number. Hose burst pressure 9.6.7.2 exceeds the minimum of 2.5 times the working pressure per Table 9.

Quality:	QUALITY	Technical Supervisor:	PRODUCTION
Date :	6/8/2014	Date :	6/8/2014
Signature :		Signature :	

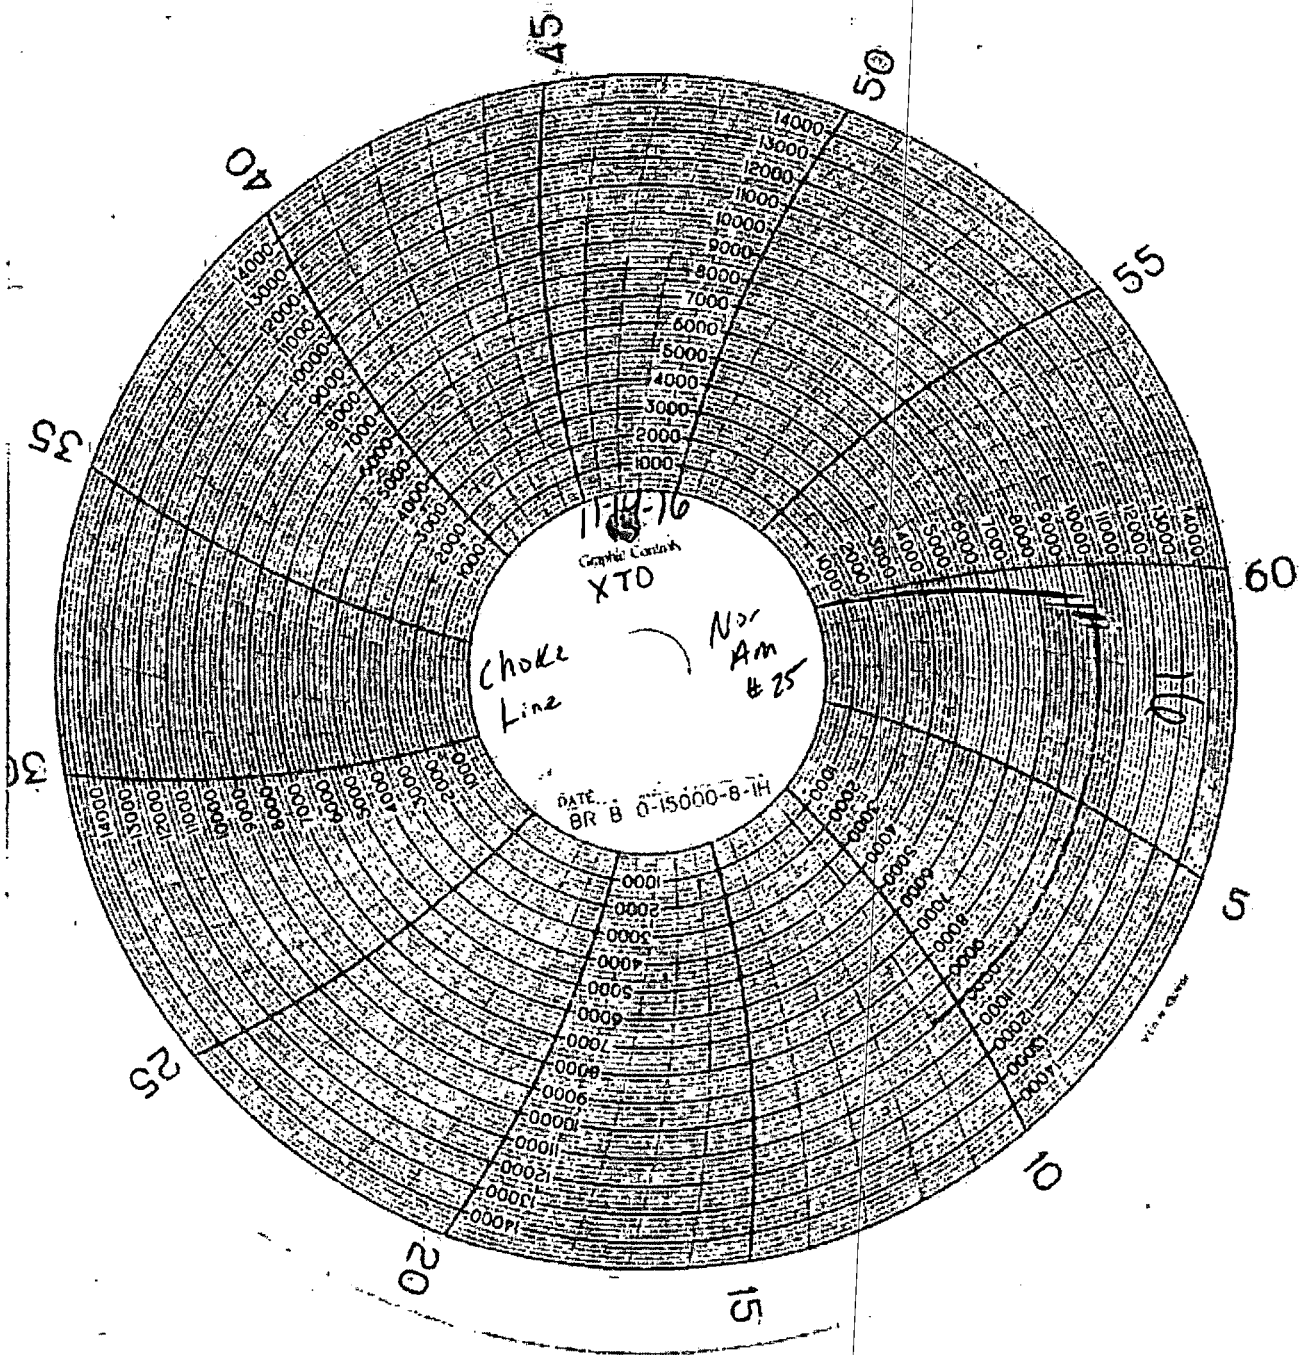

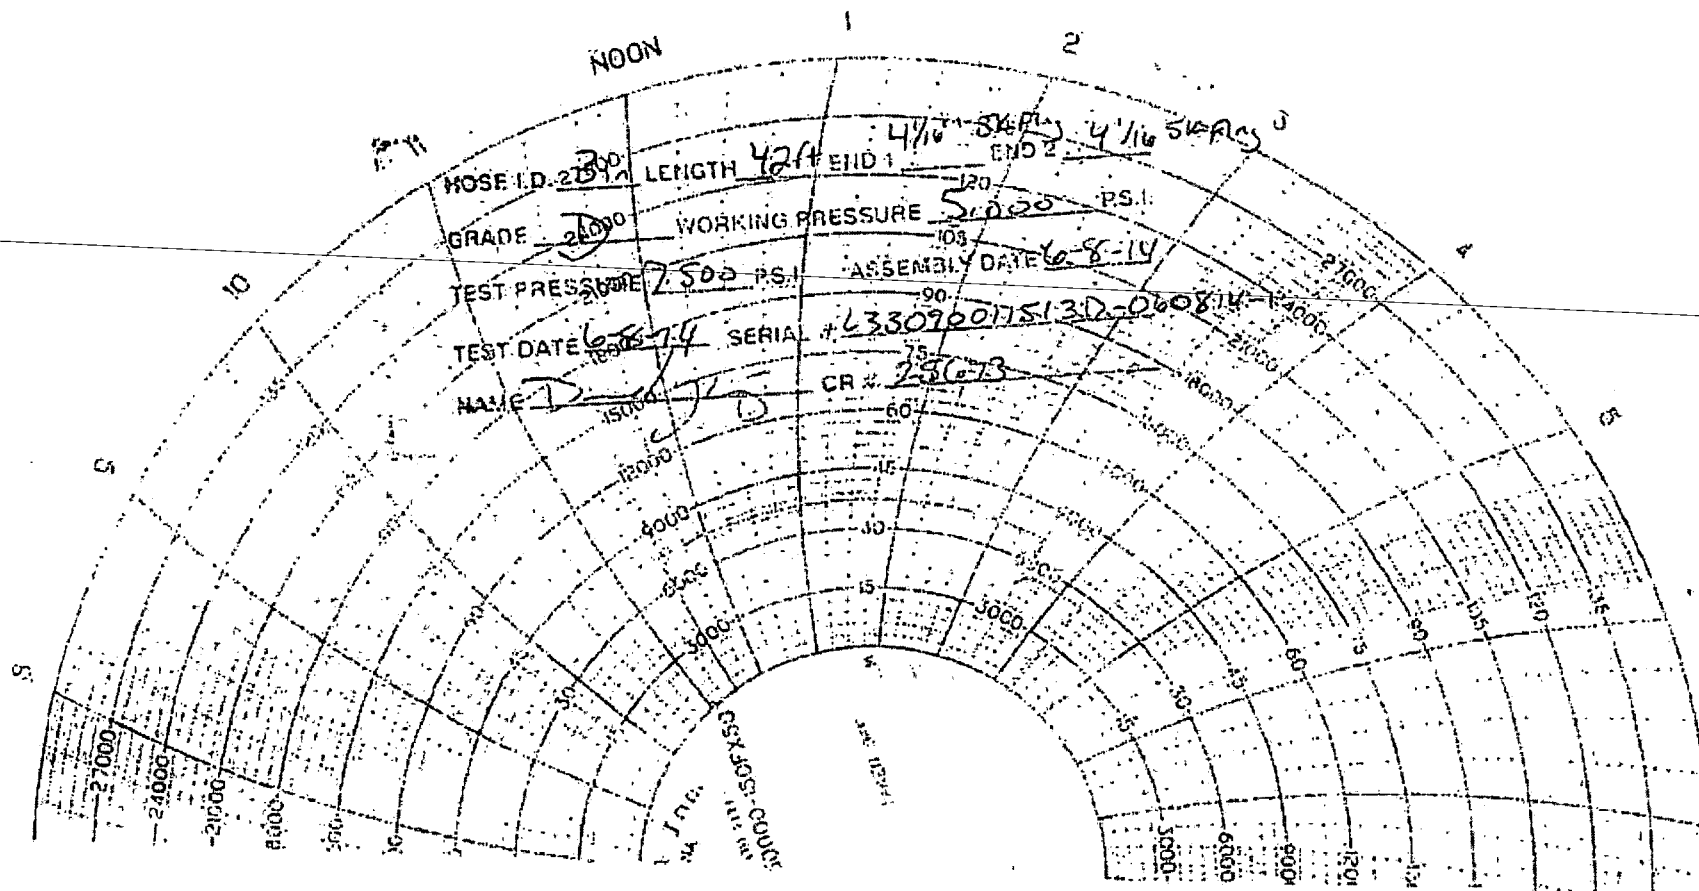

XTO Energy

Project: Eddy County, NM (NAD27) NMEZ Grid
 Site: PLU 13 Dog Town Draw
 Well: 13-905H
 Wellbore: 905H Lateral
 Design: Plan #2

3471+27 @ 3498.00usf (GL+KB)
 NAD 1927 (NADCON CONUS)

FORMATION TOP DETAILS

TVDPath	MOPath	Formation
508.00	508.00	Rustler
598.00	598.00	Magenta Dolomite
918.00	918.00	Top Salt
3973.00	3980.01	Base Salt
4193.00	4201.22	Delaware
8168.00	8189.83	Bone Spring
9118.00	9139.83	1st Bone Spring Ss
9798.00	9819.83	2nd Bone Spring Ss
10193.00	10214.83	3rd Bone Spring Lm
10928.00	10950.07	3rd Bone Spring Ss
11343.00	11465.46	Wolfcamp
11418.00	11696.12	Wolfcamp X
11423.00	11771.87	LP



Azimuths to Grid North
 True North: -0.27°
 Magnetic North: 6.55°

Magnetic Field
 Strength: 47654.1nT
 Dip Angle: 69.98°
 Date: 11/14/2019
 Model: IGRF2015




TARGET DETAILS

Name	TVD	+N/-S	+E/-W	Northing	Easting	Shape
PLU 13 DTD 905H SHL	0.00	0.00	0.00	440184.70	654957.80	Point
PLU 13 DTD 905H FTP_330FNL_508FWL	1423.00	146.80	35.30	440331.50	654993.10	Point
PLU 13 DTD 905H LTP_330FSL_504FWL	1423.00	-9755.10	74.20	430429.80	655032.00	Point
PLU 13 DTD 905H PBHL_200FSL_503FWL	1423.00	-9885.10	74.70	430299.60	655032.50	Point

SECTION DETAILS

MD	Inc	Azi	TVD	+N/-S	+E/-W	Dleg	TFace	VSect
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
2500.00	0.00	0.00	2500.00	0.00	0.00	0.00	0.00	0.00
2800.00	6.00	4.80	2799.45	15.84	1.31	2.00	4.80	-15.63
8585.00	6.00	4.80	8563.72	409.89	34.42	0.00	0.00	-409.76
8885.00	0.00	0.00	8863.17	425.53	35.73	2.00	180.00	-425.39
10871.87	0.00	0.00	10850.04	425.53	35.73	0.00	0.00	-425.39
11771.87	90.00	179.78	11423.00	-147.42	37.90	10.00	179.78	147.57
21509.62	90.00	179.78	11423.00	-9885.10	74.70	0.00	0.00	9885.31

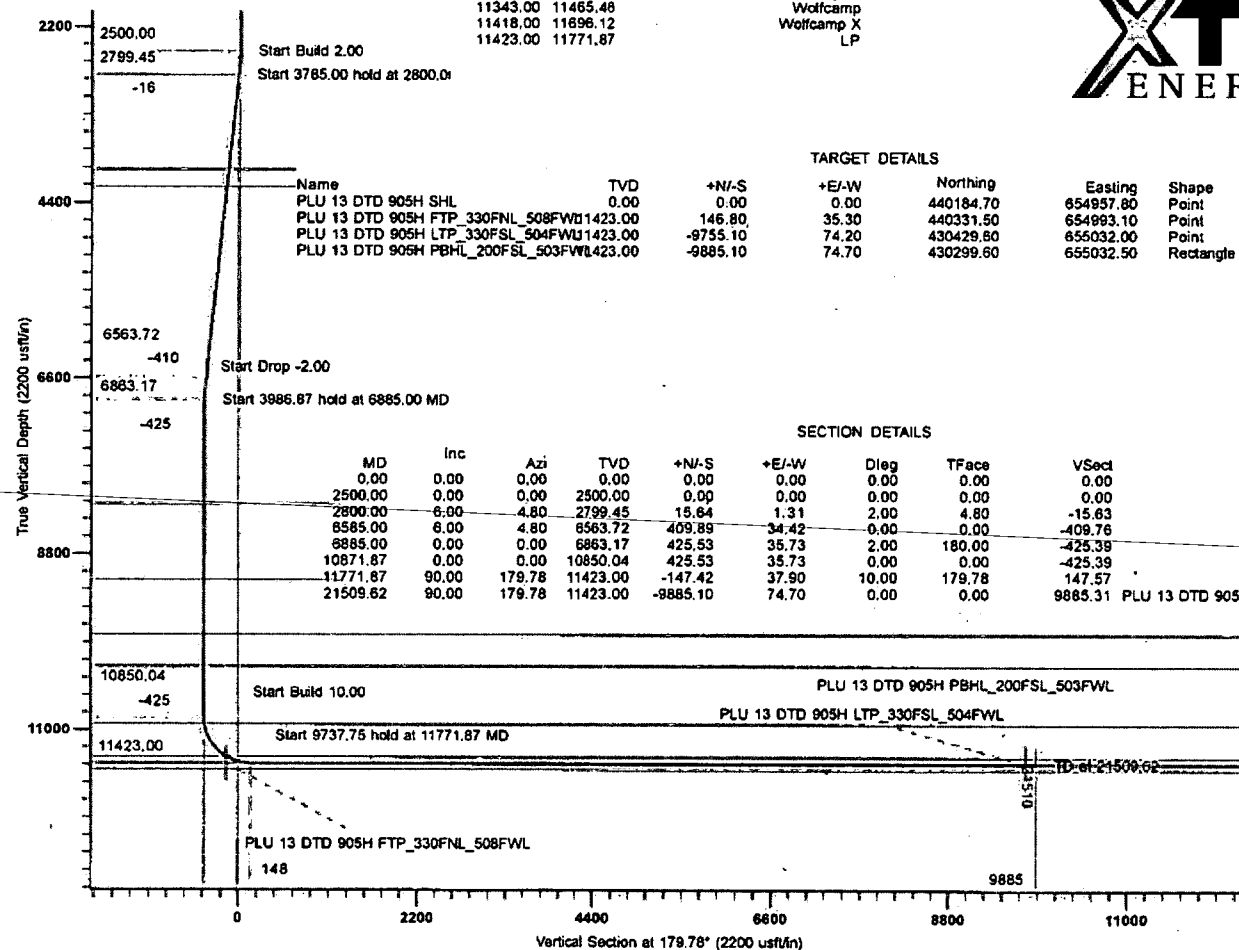

To convert a Magnetic Direction to a Grid Direction, Add 6.55°
 To convert a Magnetic Direction to a True Direction, Add 6.81° East
 Magnetic North is 6.55° East of Grid North (Magnetic Convergence)
 Magnetic North is 6.81° East of True North (Magnetic Declination)

Plan: Plan #2 (13-905H/905H Lateral)
 Created By: Mekka Williams
 eSomina Well Design
 mekka@esominawelldesign.com
 14:27, November 18 2019

PREDATOR DIRECTIONAL
 11323 MONARCHS WAY
 Montgomery TX, 77316



Planning Report

Database:	PREDATOR EDM	Local Co-ordinate Reference:	Well 13-905H
Company:	XTO Energy	TVD Reference:	3471+27 @ 3498.00usft (GL+KB)
Project:	Eddy County, NM (NAD27) NMEZ Grid	MD Reference:	3471+27 @ 3498.00usft (GL+KB)
Site:	PLU 13 Dog Town Draw	North Reference:	Grid
Well:	13-905H	Survey Calculation Method:	Minimum Curvature
Wellbore:	905H Lateral		
Design:	Plan #2		

Project	Eddy County, NM (NAD27) NMEZ Grid		
Map System:	US State Plane 1927 (Exact solution)	System Datum:	Mean Sea Level
Geo Datum:	NAD 1927 (NADCON CONUS)		
Map Zone:	New Mexico East 3001		

Site	PLU 13 Dog Town Draw				
Site Position:		Northing:	440,075.00 usft	Latitude:	32.20890166
From:	Map	Easting:	654,089.10 usft	Longitude:	-103.83513310
Position Uncertainty:	0.00 usft	Slot Radius:	13.20 in	Grid Convergence:	0.27

Well	13-905H					
Well Position	+N/-S	109.70 usft	Northing:	440,184.70 usft	Latitude:	32.2091921
	+E/-W	868.70 usft	Easting:	654,957.80 usft	Longitude:	-103.8323228
Position Uncertainty		0.00 usft	Wellhead Elevation:		Ground Level:	3,471.00 usft

Wellbore	905H Lateral				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	IGRF2015	11/14/19	6.81	59.98	47,654,13708047

Design	Plan #2			
Audit Notes:				
Version:	Phase:	PLAN	Tie On Depth:	0.00
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)	Direction (°)
	27.00	0.00	0.00	179.78

Plan Survey Tool Program		Date 11/18/19		
Depth From (usft)	Depth To (usft)	Survey (Wellbore)	Tool Name	Remarks
1	0.00	21,509.62	Plan #2 (905H Lateral)	A008Mb_MWD+IFR1+MS OWSG MWD + IFR1 + Multi-SI

Plan Sections										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)	TFO (°)	Target
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
2,500.00	0.00	0.00	2,500.00	0.00	0.00	0.00	0.00	0.00	0.00	
2,800.00	6.00	4.80	2,799.45	15.64	1.31	2.00	2.00	0.00	4.80	
6,585.00	6.00	4.80	6,563.72	409.89	34.42	0.00	0.00	0.00	0.00	
6,885.00	0.00	0.00	6,863.17	425.53	35.73	2.00	-2.00	0.00	180.00	
10,871.87	0.00	0.00	10,850.04	425.53	35.73	0.00	0.00	0.00	0.00	
11,771.87	90.00	179.78	11,423.00	-147.42	37.90	10.00	10.00	0.00	179.78	
21,509.62	90.00	179.78	11,423.00	-9,885.10	74.70	0.00	0.00	0.00	0.00	PLU 13 DTD 905H PE

Planning Report

Database:	PREDATOR_EDM	Local Co-ordinate Reference:	Well 13-905H
Company:	XTO Energy	TVD Reference:	3471+27 @ 3498.00usft (GL+KB)
Project:	Eddy County, NM (NAD27) NMEZ Grid	MD Reference:	3471+27 @ 3498.00usft (GL+KB)
Site:	PLU 13 Dog Town Draw	North Reference:	Grid
Well:	13-905H	Survey Calculation Method:	Minimum Curvature
Wellbore:	905H Lateral		
Design:	Plan #2		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)	
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
100.00	0.00	0.00	100.00	0.00	0.00	0.00	0.00	0.00	0.00	
200.00	0.00	0.00	200.00	0.00	0.00	0.00	0.00	0.00	0.00	
300.00	0.00	0.00	300.00	0.00	0.00	0.00	0.00	0.00	0.00	
400.00	0.00	0.00	400.00	0.00	0.00	0.00	0.00	0.00	0.00	
500.00	0.00	0.00	500.00	0.00	0.00	0.00	0.00	0.00	0.00	
508.00	0.00	0.00	508.00	0.00	0.00	0.00	0.00	0.00	0.00	
Rustler										
598.00	0.00	0.00	598.00	0.00	0.00	0.00	0.00	0.00	0.00	
Magenta Dolomite										
600.00	0.00	0.00	600.00	0.00	0.00	0.00	0.00	0.00	0.00	
700.00	0.00	0.00	700.00	0.00	0.00	0.00	0.00	0.00	0.00	
800.00	0.00	0.00	800.00	0.00	0.00	0.00	0.00	0.00	0.00	
900.00	0.00	0.00	900.00	0.00	0.00	0.00	0.00	0.00	0.00	
918.00	0.00	0.00	918.00	0.00	0.00	0.00	0.00	0.00	0.00	
Top Salt										
1,000.00	0.00	0.00	1,000.00	0.00	0.00	0.00	0.00	0.00	0.00	
1,100.00	0.00	0.00	1,100.00	0.00	0.00	0.00	0.00	0.00	0.00	
1,200.00	0.00	0.00	1,200.00	0.00	0.00	0.00	0.00	0.00	0.00	
1,300.00	0.00	0.00	1,300.00	0.00	0.00	0.00	0.00	0.00	0.00	
1,400.00	0.00	0.00	1,400.00	0.00	0.00	0.00	0.00	0.00	0.00	
1,500.00	0.00	0.00	1,500.00	0.00	0.00	0.00	0.00	0.00	0.00	
1,600.00	0.00	0.00	1,600.00	0.00	0.00	0.00	0.00	0.00	0.00	
1,700.00	0.00	0.00	1,700.00	0.00	0.00	0.00	0.00	0.00	0.00	
1,800.00	0.00	0.00	1,800.00	0.00	0.00	0.00	0.00	0.00	0.00	
1,900.00	0.00	0.00	1,900.00	0.00	0.00	0.00	0.00	0.00	0.00	
2,000.00	0.00	0.00	2,000.00	0.00	0.00	0.00	0.00	0.00	0.00	
2,100.00	0.00	0.00	2,100.00	0.00	0.00	0.00	0.00	0.00	0.00	
2,200.00	0.00	0.00	2,200.00	0.00	0.00	0.00	0.00	0.00	0.00	
2,300.00	0.00	0.00	2,300.00	0.00	0.00	0.00	0.00	0.00	0.00	
2,400.00	0.00	0.00	2,400.00	0.00	0.00	0.00	0.00	0.00	0.00	
2,500.00	0.00	0.00	2,500.00	0.00	0.00	0.00	0.00	0.00	0.00	
2,600.00	2.00	4.80	2,599.98	1.74	0.15	-1.74	2.00	2.00	0.00	
2,700.00	4.00	4.80	2,699.84	6.95	0.58	-6.95	2.00	2.00	0.00	
2,800.00	6.00	4.80	2,799.45	15.64	1.31	-15.63	2.00	2.00	0.00	
2,900.00	6.00	4.80	2,898.90	26.05	2.19	-26.05	0.00	0.00	0.00	
3,000.00	6.00	4.80	2,898.36	38.47	3.06	-38.46	0.00	0.00	0.00	
3,100.00	6.00	4.80	3,097.81	46.89	3.94	-46.87	0.00	0.00	0.00	
3,200.00	6.00	4.80	3,197.26	57.30	4.81	-57.28	0.00	0.00	0.00	
3,300.00	6.00	4.80	3,296.71	67.72	5.69	-67.70	0.00	0.00	0.00	
3,400.00	6.00	4.80	3,396.17	78.14	6.56	-78.11	0.00	0.00	0.00	
3,500.00	6.00	4.80	3,495.62	88.55	7.44	-88.52	0.00	0.00	0.00	
3,600.00	8.00	4.80	3,595.07	98.97	8.31	-98.94	0.00	0.00	0.00	
3,700.00	8.00	4.80	3,694.52	109.38	9.19	-109.35	0.00	0.00	0.00	
3,800.00	8.00	4.80	3,793.97	119.80	10.06	-119.76	0.00	0.00	0.00	
3,900.00	6.00	4.80	3,893.43	130.22	10.93	-130.17	0.00	0.00	0.00	
3,980.01	6.00	4.80	3,973.00	138.55	11.63	-138.51	0.00	0.00	0.00	
Base Salt										
4,000.00	8.00	4.80	3,992.88	140.63	11.81	-140.59	0.00	0.00	0.00	
4,100.00	8.00	4.80	4,092.33	151.05	12.88	-151.00	0.00	0.00	0.00	
4,200.00	8.00	4.80	4,191.78	161.47	13.56	-161.41	0.00	0.00	0.00	
4,201.22	8.00	4.80	4,193.00	161.59	13.57	-161.54	0.00	0.00	0.00	
Delaware										

Planning Report

Database:	PREDATOR EDM	Local Co-ordinate Reference:	Well-13-905H
Company:	XTO Energy	TVD Reference:	3471+27 @ 3498.00usft (GL+KB)
Project:	Eddy County NM (NAD27) NMEZ Grid	MD Reference:	3471+27 @ 3498.00usft (GL+KB)
Site:	PLU-13 Dog Town Draw	North Reference:	Grid
Well:	13-905H	Survey Calculation Method:	Minimum Curvature
Wellbore:	905H Lateral		
Design:	Plan #2		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)	
4,300.00	6.00	4.80	4,291.23	171.88	14.43	-171.82	0.00	0.00	0.00	
4,400.00	6.00	4.80	4,390.69	182.30	15.31	-182.24	0.00	0.00	0.00	
4,500.00	6.00	4.80	4,490.14	192.71	16.18	-192.65	0.00	0.00	0.00	
4,600.00	6.00	4.80	4,589.59	203.13	17.06	-203.06	0.00	0.00	0.00	
4,700.00	6.00	4.80	4,689.04	213.55	17.93	-213.48	0.00	0.00	0.00	
4,800.00	6.00	4.80	4,788.50	223.96	18.81	-223.89	0.00	0.00	0.00	
4,900.00	6.00	4.80	4,887.95	234.38	19.68	-234.30	0.00	0.00	0.00	
5,000.00	6.00	4.80	4,987.40	244.79	20.56	-244.71	0.00	0.00	0.00	
5,100.00	6.00	4.80	5,086.85	255.21	21.43	-255.13	0.00	0.00	0.00	
5,200.00	6.00	4.80	5,186.30	265.63	22.31	-265.54	0.00	0.00	0.00	
5,300.00	6.00	4.80	5,285.76	276.04	23.18	-275.95	0.00	0.00	0.00	
5,400.00	6.00	4.80	5,385.21	286.46	24.05	-286.36	0.00	0.00	0.00	
5,500.00	6.00	4.80	5,484.66	296.88	24.93	-296.78	0.00	0.00	0.00	
5,600.00	6.00	4.80	5,584.11	307.29	25.80	-307.19	0.00	0.00	0.00	
5,700.00	6.00	4.80	5,683.57	317.71	26.68	-317.60	0.00	0.00	0.00	
5,800.00	6.00	4.80	5,783.02	328.12	27.55	-328.02	0.00	0.00	0.00	
5,900.00	6.00	4.80	5,882.47	338.54	28.43	-338.43	0.00	0.00	0.00	
6,000.00	6.00	4.80	5,981.92	348.96	29.30	-348.84	0.00	0.00	0.00	
6,100.00	6.00	4.80	6,081.37	359.37	30.18	-359.25	0.00	0.00	0.00	
6,200.00	6.00	4.80	6,180.83	369.79	31.05	-369.67	0.00	0.00	0.00	
6,300.00	6.00	4.80	6,280.28	380.21	31.93	-380.08	0.00	0.00	0.00	
6,400.00	6.00	4.80	6,379.73	390.62	32.80	-390.49	0.00	0.00	0.00	
6,500.00	6.00	4.80	6,479.18	401.04	33.68	-400.91	0.00	0.00	0.00	
6,585.00	6.00	4.80	6,563.72	409.89	34.42	-409.76	0.00	0.00	0.00	
6,600.00	5.70	4.80	6,578.64	411.41	34.55	-411.28	2.00	-2.00	0.00	
6,700.00	3.70	4.80	6,678.30	419.58	35.23	-419.44	2.00	-2.00	0.00	
6,800.00	1.70	4.80	6,778.18	424.27	35.63	-424.13	2.00	-2.00	0.00	
6,885.00	0.00	0.00	6,863.17	425.53	35.73	-425.39	2.00	-2.00	0.00	
6,900.00	0.00	0.00	6,878.17	425.53	35.73	-425.39	0.00	0.00	0.00	
7,000.00	0.00	0.00	6,978.17	425.53	35.73	-425.39	0.00	0.00	0.00	
7,100.00	0.00	0.00	7,078.17	425.53	35.73	-425.39	0.00	0.00	0.00	
7,200.00	0.00	0.00	7,178.17	425.53	35.73	-425.39	0.00	0.00	0.00	
7,300.00	0.00	0.00	7,278.17	425.53	35.73	-425.39	0.00	0.00	0.00	
7,400.00	0.00	0.00	7,378.17	425.53	35.73	-425.39	0.00	0.00	0.00	
7,500.00	0.00	0.00	7,478.17	425.53	35.73	-425.39	0.00	0.00	0.00	
7,600.00	0.00	0.00	7,578.17	425.53	35.73	-425.39	0.00	0.00	0.00	
7,700.00	0.00	0.00	7,678.17	425.53	35.73	-425.39	0.00	0.00	0.00	
7,800.00	0.00	0.00	7,778.17	425.53	35.73	-425.39	0.00	0.00	0.00	
7,900.00	0.00	0.00	7,878.17	425.53	35.73	-425.39	0.00	0.00	0.00	
8,000.00	0.00	0.00	7,978.17	425.53	35.73	-425.39	0.00	0.00	0.00	
8,100.00	0.00	0.00	8,078.17	425.53	35.73	-425.39	0.00	0.00	0.00	
8,189.83	0.00	0.00	8,168.00	425.53	35.73	-425.39	0.00	0.00	0.00	
Bone Spring										
8,200.00	0.00	0.00	8,178.17	425.53	35.73	-425.39	0.00	0.00	0.00	
8,300.00	0.00	0.00	8,278.17	425.53	35.73	-425.39	0.00	0.00	0.00	
8,400.00	0.00	0.00	8,378.17	425.53	35.73	-425.39	0.00	0.00	0.00	
8,500.00	0.00	0.00	8,478.17	425.53	35.73	-425.39	0.00	0.00	0.00	
8,600.00	0.00	0.00	8,578.17	425.53	35.73	-425.39	0.00	0.00	0.00	
8,700.00	0.00	0.00	8,678.17	425.53	35.73	-425.39	0.00	0.00	0.00	
8,800.00	0.00	0.00	8,778.17	425.53	35.73	-425.39	0.00	0.00	0.00	
8,900.00	0.00	0.00	8,878.17	425.53	35.73	-425.39	0.00	0.00	0.00	
9,000.00	0.00	0.00	8,978.17	425.53	35.73	-425.39	0.00	0.00	0.00	
9,100.00	0.00	0.00	9,078.17	425.53	35.73	-425.39	0.00	0.00	0.00	

Planning Report

Database:	PREDATOR EDM	Local Co-ordinate Reference:	Well 13-905H
Company:	XTO Energy	TVD Reference:	3471+27 @ 3498.00usft (GL+KB)
Project:	Eddy County, NM (NAD27) NMEZ Grid	MD Reference:	3471+27 @ 3498.00usft (GL+KB)
Site:	PLU 13 Dog Town Draw	North Reference:	Grid
Well:	13-905H	Survey Calculation Method:	Minimum Curvature
Wellbore:	905H Lateral		
Design:	Plan #2		

Planned Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
9,139.83	0.00	0.00	9,118.00	425.53	35.73	-425.39	0.00	0.00	0.00
1st Bone Spring Sa									
9,200.00	0.00	0.00	9,178.17	425.53	35.73	-425.39	0.00	0.00	0.00
9,300.00	0.00	0.00	9,278.17	425.53	35.73	-425.39	0.00	0.00	0.00
9,400.00	0.00	0.00	9,378.17	425.53	35.73	-425.39	0.00	0.00	0.00
9,500.00	0.00	0.00	9,478.17	425.53	35.73	-425.39	0.00	0.00	0.00
9,600.00	0.00	0.00	9,578.17	425.53	35.73	-425.39	0.00	0.00	0.00
9,700.00	0.00	0.00	9,678.17	425.53	35.73	-425.39	0.00	0.00	0.00
9,800.00	0.00	0.00	9,778.17	425.53	35.73	-425.39	0.00	0.00	0.00
9,819.83	0.00	0.00	9,798.00	425.53	35.73	-425.39	0.00	0.00	0.00
2nd Bone Spring Sa									
9,900.00	0.00	0.00	9,878.17	425.53	35.73	-425.39	0.00	0.00	0.00
10,000.00	0.00	0.00	9,978.17	425.53	35.73	-425.39	0.00	0.00	0.00
10,100.00	0.00	0.00	10,078.17	425.53	35.73	-425.39	0.00	0.00	0.00
10,200.00	0.00	0.00	10,178.17	425.53	35.73	-425.39	0.00	0.00	0.00
10,214.83	0.00	0.00	10,193.00	425.53	35.73	-425.39	0.00	0.00	0.00
3rd Bone Spring Lm									
10,300.00	0.00	0.00	10,278.17	425.53	35.73	-425.39	0.00	0.00	0.00
10,400.00	0.00	0.00	10,378.17	425.53	35.73	-425.39	0.00	0.00	0.00
10,500.00	0.00	0.00	10,478.17	425.53	35.73	-425.39	0.00	0.00	0.00
10,600.00	0.00	0.00	10,578.17	425.53	35.73	-425.39	0.00	0.00	0.00
10,700.00	0.00	0.00	10,678.17	425.53	35.73	-425.39	0.00	0.00	0.00
10,800.00	0.00	0.00	10,778.17	425.53	35.73	-425.39	0.00	0.00	0.00
10,871.87	0.00	0.00	10,850.04	425.53	35.73	-425.39	0.00	0.00	0.00
10,900.00	2.81	179.78	10,878.16	424.84	35.74	-424.70	10.00	10.00	0.00
10,950.00	7.81	179.78	10,927.93	420.21	35.75	-420.07	10.00	10.00	0.00
10,950.07	7.81	179.78	10,928.00	420.20	35.75	-420.06	0.00	0.00	0.00
3rd Bone Spring Ss									
11,000.00	12.81	179.78	10,977.10	411.26	35.79	-411.12	10.01	10.01	0.00
11,050.00	17.81	179.78	11,025.31	398.06	35.84	-397.92	10.00	10.00	0.00
11,100.00	22.81	179.78	11,072.19	380.71	35.90	-380.57	10.00	10.00	0.00
11,150.00	27.81	179.78	11,117.37	359.34	35.98	-359.20	10.00	10.00	0.00
11,200.00	32.81	179.78	11,160.53	334.11	36.08	-333.97	10.00	10.00	0.00
11,250.00	37.81	179.78	11,201.31	305.22	36.19	-305.08	10.00	10.00	0.00
11,300.00	42.81	179.78	11,239.43	272.88	36.31	-272.74	10.00	10.00	0.00
11,350.00	47.81	179.78	11,274.58	237.35	36.44	-237.21	10.00	10.00	0.00
11,400.00	52.81	179.78	11,306.50	198.88	36.59	-198.74	10.00	10.00	0.00
11,450.00	57.81	179.78	11,334.94	157.78	36.74	-157.64	10.00	10.00	0.00
11,465.46	59.38	179.78	11,343.00	144.59	36.79	-144.45	10.00	10.00	0.00
Wolfcamp									
11,500.00	62.81	179.78	11,359.70	114.36	36.91	-114.22	10.00	10.00	0.00
11,550.00	67.81	179.78	11,380.58	68.94	37.08	-68.80	10.00	10.00	0.00
11,600.00	72.81	179.78	11,397.41	21.88	37.26	-21.74	10.00	10.00	0.00
11,650.00	77.81	179.78	11,410.09	-26.47	37.44	26.61	10.00	10.00	0.00
11,698.12	82.43	179.78	11,418.00	-71.90	37.61	72.04	10.00	10.00	0.00
Wolfcamp Xi									
11,700.00	82.81	179.78	11,418.50	-75.74	37.63	75.88	10.00	10.00	0.00
11,750.00	87.81	179.78	11,422.58	-125.56	37.82	125.70	10.00	10.00	0.00
11,771.87	90.00	179.78	11,423.00	-147.42	37.90	147.57	10.00	10.00	0.00
LP									
11,800.00	90.00	179.78	11,423.00	-175.55	38.00	175.70	0.00	0.00	0.00
11,900.00	90.00	179.78	11,423.00	-275.55	38.38	275.70	0.00	0.00	0.00
12,000.00	90.00	179.78	11,423.00	-375.55	38.76	375.70	0.00	0.00	0.00

Planning Report

Database:	PREDATOR.EDM	Local Co-ordinate Reference:	Well 13-905H
Company:	XTO Energy	TVD Reference:	3471+27 @ 3498.00usft (GL+KB)
Project:	Eddy County, NM (NAD27) NMEZ Grid	MD Reference:	3471+27 @ 3498.00usft (GL+KB)
Site:	PLU 13 Dog Town Draw	North Reference:	Grid
Well:	13-905H	Survey Calculation Method:	Minimum Curvature
Wellbore:	905H Lateral		
Design:	Plan #2		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
12,100.00	90.00	179.78	11,423.00	-475.55	39.14	475.70	0.00	0.00	0.00
12,200.00	90.00	179.78	11,423.00	-575.55	39.52	575.70	0.00	0.00	0.00
12,300.00	90.00	179.78	11,423.00	-675.55	39.89	675.70	0.00	0.00	0.00
12,400.00	90.00	179.78	11,423.00	-775.55	40.27	775.70	0.00	0.00	0.00
12,500.00	90.00	179.78	11,423.00	-875.55	40.65	875.70	0.00	0.00	0.00
12,600.00	90.00	179.78	11,423.00	-975.55	41.03	975.70	0.00	0.00	0.00
12,700.00	90.00	179.78	11,423.00	-1,075.54	41.41	1,075.70	0.00	0.00	0.00
12,800.00	90.00	179.78	11,423.00	-1,175.54	41.78	1,175.70	0.00	0.00	0.00
12,900.00	90.00	179.78	11,423.00	-1,275.54	42.16	1,275.70	0.00	0.00	0.00
13,000.00	90.00	179.78	11,423.00	-1,375.54	42.54	1,375.70	0.00	0.00	0.00
13,100.00	90.00	179.78	11,423.00	-1,475.54	42.92	1,475.70	0.00	0.00	0.00
13,200.00	90.00	179.78	11,423.00	-1,575.54	43.30	1,575.70	0.00	0.00	0.00
13,300.00	90.00	179.78	11,423.00	-1,675.54	43.67	1,675.70	0.00	0.00	0.00
13,400.00	90.00	179.78	11,423.00	-1,775.54	44.05	1,775.70	0.00	0.00	0.00
13,500.00	90.00	179.78	11,423.00	-1,875.54	44.43	1,875.70	0.00	0.00	0.00
13,600.00	90.00	179.78	11,423.00	-1,975.54	44.81	1,975.70	0.00	0.00	0.00
13,700.00	90.00	179.78	11,423.00	-2,075.54	45.19	2,075.70	0.00	0.00	0.00
13,800.00	90.00	179.78	11,423.00	-2,175.54	45.56	2,175.70	0.00	0.00	0.00
13,900.00	90.00	179.78	11,423.00	-2,275.54	45.94	2,275.70	0.00	0.00	0.00
14,000.00	90.00	179.78	11,423.00	-2,375.54	46.32	2,375.70	0.00	0.00	0.00
14,100.00	90.00	179.78	11,423.00	-2,475.53	46.70	2,475.70	0.00	0.00	0.00
14,200.00	90.00	179.78	11,423.00	-2,575.53	47.07	2,575.70	0.00	0.00	0.00
14,300.00	90.00	179.78	11,423.00	-2,675.53	47.45	2,675.70	0.00	0.00	0.00
14,400.00	90.00	179.78	11,423.00	-2,775.53	47.83	2,775.70	0.00	0.00	0.00
14,500.00	90.00	179.78	11,423.00	-2,875.53	48.21	2,875.70	0.00	0.00	0.00
14,600.00	90.00	179.78	11,423.00	-2,975.53	48.59	2,975.70	0.00	0.00	0.00
14,700.00	90.00	179.78	11,423.00	-3,075.53	48.96	3,075.70	0.00	0.00	0.00
14,800.00	90.00	179.78	11,423.00	-3,175.53	49.34	3,175.70	0.00	0.00	0.00
14,900.00	90.00	179.78	11,423.00	-3,275.53	49.72	3,275.70	0.00	0.00	0.00
15,000.00	90.00	179.78	11,423.00	-3,375.53	50.10	3,375.70	0.00	0.00	0.00
15,100.00	90.00	179.78	11,423.00	-3,475.53	50.48	3,475.70	0.00	0.00	0.00
15,200.00	90.00	179.78	11,423.00	-3,575.53	50.85	3,575.70	0.00	0.00	0.00
15,300.00	90.00	179.78	11,423.00	-3,675.53	51.23	3,675.70	0.00	0.00	0.00
15,400.00	90.00	179.78	11,423.00	-3,775.53	51.61	3,775.70	0.00	0.00	0.00
15,500.00	90.00	179.78	11,423.00	-3,875.52	51.99	3,875.70	0.00	0.00	0.00
15,600.00	90.00	179.78	11,423.00	-3,975.52	52.37	3,975.70	0.00	0.00	0.00
15,700.00	90.00	179.78	11,423.00	-4,075.52	52.74	4,075.70	0.00	0.00	0.00
15,800.00	90.00	179.78	11,423.00	-4,175.52	53.12	4,175.70	0.00	0.00	0.00
15,900.00	90.00	179.78	11,423.00	-4,275.52	53.50	4,275.70	0.00	0.00	0.00
16,000.00	90.00	179.78	11,423.00	-4,375.52	53.88	4,375.70	0.00	0.00	0.00
16,100.00	90.00	179.78	11,423.00	-4,475.52	54.26	4,475.70	0.00	0.00	0.00
16,200.00	90.00	179.78	11,423.00	-4,575.52	54.63	4,575.70	0.00	0.00	0.00
16,300.00	90.00	179.78	11,423.00	-4,675.52	55.01	4,675.70	0.00	0.00	0.00
16,400.00	90.00	179.78	11,423.00	-4,775.52	55.39	4,775.70	0.00	0.00	0.00
16,500.00	90.00	179.78	11,423.00	-4,875.52	55.77	4,875.70	0.00	0.00	0.00
16,600.00	90.00	179.78	11,423.00	-4,975.52	56.15	4,975.70	0.00	0.00	0.00
16,700.00	90.00	179.78	11,423.00	-5,075.52	56.52	5,075.70	0.00	0.00	0.00
16,800.00	90.00	179.78	11,423.00	-5,175.52	56.90	5,175.70	0.00	0.00	0.00
16,900.00	90.00	179.78	11,423.00	-5,275.51	57.28	5,275.70	0.00	0.00	0.00
17,000.00	90.00	179.78	11,423.00	-5,375.51	57.66	5,375.70	0.00	0.00	0.00
17,100.00	90.00	179.78	11,423.00	-5,475.51	58.03	5,475.70	0.00	0.00	0.00
17,200.00	90.00	179.78	11,423.00	-5,575.51	58.41	5,575.70	0.00	0.00	0.00
17,300.00	90.00	179.78	11,423.00	-5,675.51	58.79	5,675.70	0.00	0.00	0.00
17,400.00	90.00	179.78	11,423.00	-5,775.51	59.17	5,775.70	0.00	0.00	0.00

Planning Report

Database:	PREDATOR EDM	Local Co-ordinate Reference:	Well 13-905H
Company:	XTO Energy	TVD Reference:	3471+27 @ 3498.00usft (GL+KB)
Project:	Eddy County NM (NAD27) NMEZ Grid	MD Reference:	3471+27 @ 3498.00usft (GL+KB)
Site:	PLU 13 Dog Town Draw	North Reference:	Grid
Well:	13-905H	Survey Calculation Method:	Minimum Curvature
Wellbore:	905H Lateral		
Design:	Plan #2		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)	
17,500.00	90.00	179.78	11,423.00	-5,875.51	59.55	5,875.70	0.00	0.00	0.00	
17,600.00	90.00	179.78	11,423.00	-5,975.51	59.92	5,975.70	0.00	0.00	0.00	
17,700.00	90.00	179.78	11,423.00	-6,075.51	60.30	6,075.70	0.00	0.00	0.00	
17,800.00	90.00	179.78	11,423.00	-6,175.51	60.68	6,175.70	0.00	0.00	0.00	
17,900.00	90.00	179.78	11,423.00	-6,275.51	61.06	6,275.70	0.00	0.00	0.00	
18,000.00	90.00	179.78	11,423.00	-6,375.51	61.44	6,375.70	0.00	0.00	0.00	
18,100.00	90.00	179.78	11,423.00	-6,475.51	61.81	6,475.70	0.00	0.00	0.00	
18,200.00	90.00	179.78	11,423.00	-6,575.51	62.19	6,575.70	0.00	0.00	0.00	
18,300.00	90.00	179.78	11,423.00	-6,675.50	62.57	6,675.70	0.00	0.00	0.00	
18,400.00	90.00	179.78	11,423.00	-6,775.50	62.95	6,775.70	0.00	0.00	0.00	
18,500.00	90.00	179.78	11,423.00	-6,875.50	63.33	6,875.70	0.00	0.00	0.00	
18,600.00	90.00	179.78	11,423.00	-6,975.50	63.70	6,975.70	0.00	0.00	0.00	
18,700.00	90.00	179.78	11,423.00	-7,075.50	64.08	7,075.70	0.00	0.00	0.00	
18,800.00	90.00	179.78	11,423.00	-7,175.50	64.46	7,175.70	0.00	0.00	0.00	
18,900.00	90.00	179.78	11,423.00	-7,275.50	64.84	7,275.70	0.00	0.00	0.00	
19,000.00	90.00	179.78	11,423.00	-7,375.50	65.22	7,375.70	0.00	0.00	0.00	
19,100.00	90.00	179.78	11,423.00	-7,475.50	65.59	7,475.70	0.00	0.00	0.00	
19,200.00	90.00	179.78	11,423.00	-7,575.50	65.97	7,575.70	0.00	0.00	0.00	
19,300.00	90.00	179.78	11,423.00	-7,675.50	66.35	7,675.70	0.00	0.00	0.00	
19,400.00	90.00	179.78	11,423.00	-7,775.50	66.73	7,775.70	0.00	0.00	0.00	
19,500.00	90.00	179.78	11,423.00	-7,875.50	67.11	7,875.70	0.00	0.00	0.00	
19,600.00	90.00	179.78	11,423.00	-7,975.50	67.48	7,975.70	0.00	0.00	0.00	
19,700.00	90.00	179.78	11,423.00	-8,075.49	67.86	8,075.70	0.00	0.00	0.00	
19,800.00	90.00	179.78	11,423.00	-8,175.49	68.24	8,175.70	0.00	0.00	0.00	
19,900.00	90.00	179.78	11,423.00	-8,275.49	68.62	8,275.70	0.00	0.00	0.00	
20,000.00	90.00	179.78	11,423.00	-8,375.49	68.99	8,375.70	0.00	0.00	0.00	
20,100.00	90.00	179.78	11,423.00	-8,475.49	69.37	8,475.70	0.00	0.00	0.00	
20,200.00	90.00	179.78	11,423.00	-8,575.49	69.75	8,575.70	0.00	0.00	0.00	
20,300.00	90.00	179.78	11,423.00	-8,675.49	70.13	8,675.70	0.00	0.00	0.00	
20,400.00	90.00	179.78	11,423.00	-8,775.49	70.51	8,775.70	0.00	0.00	0.00	
20,500.00	90.00	179.78	11,423.00	-8,875.49	70.88	8,875.70	0.00	0.00	0.00	
20,600.00	90.00	179.78	11,423.00	-8,975.49	71.26	8,975.70	0.00	0.00	0.00	
20,700.00	90.00	179.78	11,423.00	-9,075.49	71.64	9,075.70	0.00	0.00	0.00	
20,800.00	90.00	179.78	11,423.00	-9,175.49	72.02	9,175.70	0.00	0.00	0.00	
20,900.00	90.00	179.78	11,423.00	-9,275.49	72.40	9,275.70	0.00	0.00	0.00	
21,000.00	90.00	179.78	11,423.00	-9,375.49	72.77	9,375.70	0.00	0.00	0.00	
21,100.00	90.00	179.78	11,423.00	-9,475.48	73.15	9,475.70	0.00	0.00	0.00	
21,200.00	90.00	179.78	11,423.00	-9,575.48	73.53	9,575.70	0.00	0.00	0.00	
21,300.00	90.00	179.78	11,423.00	-9,675.48	73.91	9,675.70	0.00	0.00	0.00	
21,400.00	90.00	179.78	11,423.00	-9,775.48	74.29	9,775.70	0.00	0.00	0.00	
21,509.62	90.00	179.78	11,423.00	-9,885.10	74.70	9,885.31	0.00	0.00	0.00	

Planning Report

Database:	PREDATOR EDM	Local Co-ordinate Reference:	Well 13-905H
Company:	XTO Energy	TVD Reference:	3471+27 @ 3498.00usft (GL+KB)
Project:	Eddy County NM (NAD27) NMEZ Grid	MD Reference:	3471+27 @ 3498.00usft (GL+KB)
Site:	PLU 13 Dog Town Draw	North Reference:	Grid
Well:	13-905H	Survey Calculation Method:	Minimum Curvature
Wellbore:	905H Lateral		
Design:	Plan #2		

Design Targets									
Target Name	Dip Angle	Dip Dir.	TVD	+N/-S	+E/-W	Northing	Easting	Latitude	Longitude
- hit/miss target	(°)	(°)	(usft)	(usft)	(usft)	(usft)	(usft)		
- Shape									
PLU 13 DTD 905H SHL	0.00	0.00	0.00	0.00	0.00	440,184.70	654,957.80	32,20919211	-103.83232286
- plan hits target center									
- Point									
PLU 13 DTD 905H LTP	0.00	0.00	11,423.00	-9,755.10	74.20	430,429.60	655,032.00	32.18237535	-103.83222994
- plan misses target center by 0.01usft at 21379.62usft MD (11423.00 TVD, -9755.10 N, 74.21 E)									
- Point									
PLU 13 DTD 905H FTP	0.00	0.00	11,423.00	146.80	35.30	440,331.50	654,993.10	32.20959520	-103.83220652
- plan misses target center by 71.15usft at 11500.00usft MD (11359.70 TVD, 114.39 N, 36.91 E)									
- Point									
PLU 13 DTD 905H PBH	0.00	0.00	11,423.00	-9,885.10	74.70	430,299.60	655,032.50	32.18201798	-103.83223028
- plan hits target center									
- Rectangle (sides W100.00 H10,031.00 D0.00)									

Formations					
Measured Depth	Vertical Depth	Name	Lithology	Dip	Dip Direction
(usft)	(usft)			(°)	(°)
508.00	508.00	Rustler			
598.00	598.00	Magenta Dolomite			
918.00	918.00	Top Salt			
3,980.01	3,973.00	Base Salt			
4,201.22	4,193.00	Delaware			
8,189.83	8,168.00	Bone Spring			
9,139.83	9,118.00	1st Bone Spring Ss			
9,819.83	9,798.00	2nd Bone Spring Ss			
10,214.83	10,193.00	3rd Bone Spring Lm			
10,950.07	10,928.00	3rd Bone Spring Ss			
11,465.46	11,343.00	Wolfcamp			
11,696.12	11,418.00	Wolfcamp X			
11,771.87	11,423.00	LP			

PECOS DISTRICT DRILLING CONDITIONS OF APPROVAL

OPERATOR'S NAME:	XTO Permian Operating, LLC
LEASE NO.:	NMNM-0030453
WELL NAME & NO.:	Poker Lake Unit 13 DTD 905H
SURFACE HOLE FOOTAGE:	0477' FNL & 2205' FEL
BOTTOM HOLE FOOTAGE:	0200' FSL & 2169' FEL Sec. 25, T. 24 S., R 30 E.
LOCATION:	Section 24, T. 24 S., R 30 E., NMPM
COUNTY:	Eddy County, New Mexico

Commercial Well Determination

A commercial well determination shall be submitted after production has been established for at least six months.

Unit Wells

The well sign for a unit well shall include the unit number in addition to the surface and bottom hole lease numbers. This also applies to participating area numbers. If a participating area has not been established, the operator can use the general unit designation, but will replace the unit number with the participating area number when the sign is replaced.

A. DRILLING OPERATIONS REQUIREMENTS

The BLM is to be notified in advance for a representative to witness:

- a. Spudding well (minimum of 24 hours)
- b. Setting and/or Cementing of all casing strings (minimum of 4 hours)
- c. BOPE tests (minimum of 4 hours)

☒ **Eddy County**

Call the Carlsbad Field Office, 620 East Greene St., Carlsbad, NM 88220,
(575) 361-2822

1. **Hydrogen Sulfide (H₂S) monitors shall be installed prior to drilling out the surface shoe. If H₂S is detected in concentrations greater than 100 ppm, the Hydrogen Sulfide area shall meet Onshore Order 6 requirements, which includes equipment and personnel/public protection items. If Hydrogen Sulfide is encountered, provide measured values and formations to the BLM.**
2. **Unless the production casing has been run and cemented or the well has been properly plugged, the drilling rig shall not be removed from over the hole without prior approval. If the drilling rig is removed without approval – an Incident of Non-Compliance will be written and will be a “Major” violation.**

3. **The operator has proposed to drill multiple wells utilizing a skid/walking rig. Operator shall secure the wellbore on the current well, after installing and testing the wellhead, by installing a blind flange of like pressure rating to the wellhead and a pressure gauge that can be monitored while drilling is performed on the other wells.**
4. **Floor controls are required for 3M or Greater systems. These controls will be on the rig floor, unobstructed, readily accessible to the driller and will be operational at all times during drilling and/or completion activities. Rig floor is defined as the area immediately around the rotary table; the area immediately above the substructure on which the draw works is located, this does not include the dog house or stairway area.**
5. **The record of the drilling rate along with the GR/N well log run from TD to surface (horizontal well – vertical portion of hole) shall be submitted to the BLM office as well as all other logs run on the borehole 30 days from completion. If available, a digital copy of the logs is to be submitted in addition to the paper copies. The Rustler top and top and bottom of Salt are to be recorded on the Completion Report.**

B. CASING

Changes to the approved APD casing program need prior approval if the items substituted are of lesser grade or different casing size or are Non-API. The Operator can exchange the components of the proposal with that of superior strength (i.e. changing from J-55 to N-80, or from 36# to 40#). Changes to the approved cement program need prior approval if the altered cement plan has less volume or strength or if the changes are substantial (i.e. Multistage tool, ECP, etc.). The initial wellhead installed on the well will remain on the well with spools used as needed.

Centralizers required on surface casing per Onshore Order 2.III.B.1.f.

Wait on cement (WOC) for Water Basin:

After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi at the shoe, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. See individual casing strings for details regarding lead cement slurry requirements.

Provide compressive strengths including hours to reach required 500 pounds compressive strength prior to cementing each casing string. Have well specific cement details onsite prior to pumping the cement for each casing string.

No pea gravel permitted for remedial or fall back remedial without prior authorization from the BLM engineer.

Possibility of water flows in the Salado and Castile.

Possibility of lost circulation in the Red Beds, Rustler, and Delaware.

Abnormal pressure may be encountered in the 3rd Bone Spring and all subsequent formations.

1. The 13-3/8 inch surface casing shall be set at approximately 760 feet (in a competent bed below the Magenta Dolomite, which is a Member of the Rustler, and if salt is encountered, set casing at least 25 feet above the salt) and cemented to the surface.
 - a. If cement does not circulate to the surface, the appropriate BLM office shall be notified and a temperature survey utilizing an electronic type temperature survey with surface log readout will be used or a cement bond log shall be run to verify the top of the cement. Temperature survey will be run a minimum of six hours after pumping cement and ideally between 8-10 hours after completing the cement job.
 - b. Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry.
 - c. Wait on cement (WOC) time for a remedial job will be a minimum of 4 hours after bringing cement to surface or 500 pounds compressive strength, whichever is greater.
 - d. If cement falls back, remedial cementing will be done prior to drilling out that string.

Formation below the 13-3/8" shoe to be tested according to Onshore Order

2.III.B.1.i. Test to be done as a mud equivalency test using the mud weight necessary for the pore pressure of the formation below the shoe and the mud weight for the bottom of the hole. Report results to BLM office.

2. The minimum required fill of cement behind the 9-5/8 inch intermediate casing is:

☒ Cement to surface. If cement does not circulate see B.1.a, c-d above.

Formation below the 9-5/8" shoe to be tested according to Onshore Order 2.III.B.1.i.

Test to be done as a mud equivalency test using the mud weight necessary for the pore pressure of the formation below the shoe (not the mud weight required to prevent dissolving the salt formation) and the mud weight for the bottom of the hole. Report results to BLM office.

Centralizers required on horizontal leg, must be type for horizontal service and a minimum of one every other joint.

3. The minimum required fill of cement behind the 7 inch production casing is:

☒ Cement should tie-back at least 200 feet into previous casing string. Operator shall provide method of verification. **Excess calculates to 17% - Additional cement may be required.**

Formation below the 7" shoe to be tested according to Onshore Order 2.III.B.1.i. Test to be done as a mud equivalency test using the mud weight necessary for the pore pressure of the formation below the shoe and the mud weight for the bottom of the hole. Report results to BLM office.

4. The minimum required fill of cement behind the 4-1/2 inch production Liner is:

☒ Cement as proposed. Operator shall provide method of verification. **Excess calculates to 15% - Additional cement may be required.**

NOTE: Liner to tie back a minimum of 100' into previous casing.

5. If hardband drill pipe is rotated inside casing, returns will be monitored for metal. If metal is found in samples, drill pipe will be pulled and rubber protectors which have a larger diameter than the tool joints of the drill pipe will be installed prior to continuing drilling operations.

C. PRESSURE CONTROL

1. All blowout preventer (BOP) and related equipment (BOPE) shall comply with well control requirements as described in Onshore Oil and Gas Order No. 2 and API 53.
2. Variance approved to use flex line from BOP to choke manifold. Check condition of flexible line from BOP to choke manifold, replace if exterior is damaged or if line fails test. Line to be as straight as possible with no hard bends and is to be anchored according to Manufacturer's requirements. The flexible hose can be exchanged with a hose of equal size and equal or greater pressure rating. **Anchor requirements, specification sheet and hydrostatic pressure test certification matching the hose in service, to be onsite for review. These documents shall be posted in the company man's trailer and on the rig floor.** If the BLM inspector questions the straightness of the hose, a BLM engineer will be contacted and will review in the field or via picture supplied by inspector to determine if changes are required (operator shall expect delays if this occurs).
3. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **5000 (5M) psi. 5M system requires an HCR valve, remote kill line and annular to match. The remote kill line is to be installed prior to testing the system and tested to stack pressure.**

4. The appropriate BLM office shall be notified a minimum of 4 hours in advance for a representative to witness the tests.
- a. In a water basin, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. The casing cut-off and BOP installation can be initiated four hours after installing the slips, which will be approximately six hours after bumping the plug. For those casing strings not using slips, the minimum wait time before cut-off is eight hours after bumping the plug. BOP/BOPE testing can begin after cut-off or once cement reaches 500 psi compressive strength (including lead when specified), whichever is greater. However, if the float does not hold, cut-off cannot be initiated until cement reaches 500 psi compressive strength (including lead when specified).
 - b. The tests shall be done by an independent service company utilizing a test plug **not a cup or J-packer**.
 - c. The test shall be run on a 5000 psi chart for a 2-3M BOP/BOP, on a 10000 psi chart for a 5M BOP/BOPE and on a 15000 psi chart for a 10M BOP/BOPE. If a linear chart is used, it shall be a one hour chart. A circular chart shall have a maximum 2 hour clock. If a twelve hour or twenty-four hour chart is used, tester shall make a notation that it is run with a two hour clock.
 - d. The results of the test shall be reported to the appropriate BLM office.
 - e. All tests are required to be recorded on a calibrated test chart. **A copy of the BOP/BOPE test chart and a copy of independent service company test will be submitted to the appropriate BLM office.**
 - f. The BOP/BOPE test shall include a low pressure test from 250 to 300 psi. The test will be held for a minimum of 10 minutes if test is done with a test plug and 30 minutes without a test plug. This test shall be performed prior to the test at full stack pressure.
 - g. BOP/BOPE must be tested by an independent service company within 500 feet of the top of the **Wolfcamp** formation if the time between the setting of the intermediate casing and reaching this depth exceeds 20 days. This test does not exclude the test prior to drilling out the casing shoe as per Onshore Order No. 2.

D. DRILLING MUD

Mud system monitoring equipment, with derrick floor indicators and visual and audio alarms, shall be operating before drilling into the **Wolfcamp** formation, and shall be used until production casing is run and cemented.

E. DRILL STEM TEST

If drill stem tests are performed, Onshore Order 2.III.D shall be followed.

F. WASTE MATERIAL AND FLUIDS

All waste (i.e. drilling fluids, trash, salts, chemicals, sewage, gray water, etc.) created as a result of drilling operations and completion operations shall be safely contained and disposed of properly at a waste disposal facility. No waste material or fluid shall be disposed of on the well location or surrounding area.

Porto-johns and trash containers will be on-location during fracturing operations or any other crew-intensive operations.

JAM 112119
