

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT**SUNDRY NOTICES AND REPORTS ON WELLS**
Do not use this form for proposals to drill or to re-enter an abandoned well. Use form 3160-3 (APD) for such proposals.

RECEIVED

JAN 20 2020

EMNRD-OC0 ARTESIA

FORM APPROVED
OMB NO. 1004-0137
Expires: January 31, 20185. Lease Serial No.
NMLC063136A

6. If Indian, Allottee or Tribe Name

7. If Unit or CA/Agreement, Name and/or No.
891000303X8. Well Name and No.
POKER LAKE UNIT 28 BS 106H9. API Well No.
30-015-45507-00-X110. Field and Pool or Exploratory Area
PURPLE SAGE-WOLFCAMP (GAS)11. County or Parish, State
EDDY COUNTY, NM**SUBMIT IN TRIPLICATE - Other instructions on page 2**

1. Type of Well

☐ Oil Well ☒ Gas Well ☐ Other

2. Name of Operator

XTO PERMIAN OPERATING LLC

Contact: KELLY KARDOS

E-Mail: kelly_kardos@xtoenergy.com

3a. Address

6401 HOLIDAY HILL ROAD BLDG 5
MIDLAND, TX 79707

3b. Phone No. (include area code)

Ph: 432-620-4374

4. Location of Well* (Footage, Sec., T., R., M., or Survey Description)

Sec 28 T25S R31E SWNE 2310FNL 1920FEL
32.102207 N Lat, 103.780739 W Lon**12. CHECK THE APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA**

TYPE OF SUBMISSION

TYPE OF ACTION

☒ Notice of Intent☐ Subsequent Report☐ Final Abandonment Notice☐ Acidize☐ Alter Casing☐ Casing Repair☐ Change Plans☐ Convert to Injection☐ Deepen☐ Hydraulic Fracturing☐ New Construction☐ Plug and Abandon☐ Plug Back☐ Production (Start/Resume)☐ Reclamation☐ Recomplete☐ Temporarily Abandon☐ Water Disposal☐ Water Shut-Off☐ Well Integrity☒ Other
Change to Original A
PD

13. Describe Proposed or Completed Operation: Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recompleat horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports must be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompleat in a new interval, a Form 3160-4 must be filed once testing has been completed. Final Abandonment Notices must be filed only after all requirements, including reclamation, have been completed and the operator has determined that the site is ready for final inspection.

XTO Permian Operating, LLC requests permission to make the following changes to the original APD:

Change the casing/cement design per the attached drilling program.

XTO requests to not utilize centralizers in the curve and lateral.

SEE ATTACHED FOR
CONDITIONS OF APPROVAL

14. I hereby certify that the foregoing is true and correct.

Electronic Submission #496556 verified by the BLM Well Information System
For XTO PERMIAN OPERATING LLC, sent to the Carlsbad
Committed to AFMSS for processing by PRISCILLA PEREZ on 12/19/2019 (20PP0725SE)

Name (Printed/Typed) KELLY KARDOS

Title REGULATORY COORDINATOR

Signature (Electronic Submission)

Date 12/19/2019

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved By

Title

BUREAU OF LAND MANAGEMENT
ROSWELL FIELD OFFICE

Date

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Office

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Instructions on page 2)

** BLM REVISED ** BLM REVISED ** BLM REVISED ** BLM REVISED ** BLM REVISED **

1/28/20 47

DRILLING PLAN: BLM COMPLIANCE
(Supplement to BLM 3160-3)

XTO Energy Inc.
Poker Lake Unit 28 Big Sinks 106H
Projected TD: 24988' MD / 11819' TVD
SHL: 2310' FNL & 1920' FEL, Section 28, T25S, R31E
BHL: 200' FSL & 1590' FEL, Section 4, T26S, R31E
Eddy County, NM

1. Geologic Name of Surface Formation

A. Quaternary

2. Estimated Tops of Geological Markers & Depths of Anticipated Fresh Water, Oil or Gas:

Formation	Well Depth (TVD)	Water/Oil/Gas
Rustler	909'	Water
Top of Salt	1272'	Water
Base of Salt	4008'	Water
Delaware	4222'	Water
Bone Spring	8164'	Water/Oil/Gas
1st Bone Spring Ss	9161'	Water/Oil/Gas
2nd Bone Spring Ss	10022'	Water/Oil/Gas
3rd Bone Spring Ss	11116'	Water/Oil/Gas
Wolfcamp Shale	11527'	Water/Oil/Gas
Target/Land Curve	11819'	Water/Oil/Gas

*** Hydrocarbons @ Brushy Canyon

*** Groundwater depth 40' (per NM State Engineers Office).

No other formations are expected to yield oil, gas or fresh water in measurable volumes. The surface fresh water sands will be protected by setting 13-3/8 inch casing @ 1240' (32' above the salt) and circulating cement back to surface. A 12-1/4 inch vertical hole will be drilled to 10918' and 9-5/8 inch casing ran and cemented 200' into the 13-3/8 inch casing. An 8-3/4 inch curve and lateral hole will be drilled to MD/TD and 5-1/2 casing will be set at TD and cemented back 300' into the 9-5/8 inch casing shoe.

3. Casing Design

Hole Size	Depth	OD Csg	Weight	Collar	Grade	New/Used	SF Burst	SF Collapse	SF Tension
17-1/2"	0' - 1240'	13-3/8"	68	BTC	J-55	New	1.33	3.48	12.68
12-1/4"	0' - 10918'	9-5/8"	40	BTC	HCL-80	New	1.27	1.47	2.10
8-3/4-8-1/2"	0' - 24988'	5-1/2"	20	BTC	P-110	New	1.18	1.60	1.92

XTO requests to not utilize centralizers in the curve and lateral.

9-5/8" Collapse analyzed using 50% evacuation based on regional experience.

5-1/2" tension calculated using vertical hanging weight plus the lateral weight multiplied by a friction factor of 0.35

Test on Casing will be limited to 70% burst of the casing or 1500 psi, whichever is less

WELLHEAD:

Permanent Wellhead - GE-RSH Multibowl System

A. Starting Head (RSH System): 13-3/8" SOW bottom x 13-5/8" 5M top flange

B. Tubing Head: 13-5/8" 5M bottom flange x 7-1/16" 10M top flange

- Wellhead will be installed by manufacturer's representatives.
- Manufacturer will monitor welding process to ensure appropriate temperature of seal.
- Operator will test the 9-5/8" casing per Onshore Order 2.
- Wellhead manufacturer representative may not be present for BOP test plug installation

4. Cement Program

Surface Casing: 13-3/8", 68 New J-55, BTC casing to be set at +/- 1240'

Lead: 690 sxs EconoCem-HLTRRC (mixed at 12.8 ppg, 1.87 ft³/sx, 10.13 gal/sx water)

Tail: 300 sxs Halcem-C + 2% CaCl (mixed at 14.8 ppg, 1.35 ft³/sx, 6.39 gal/sx water)

Compressives: 12-hr = 900 psi 24-hr = 1500 psi

Top of Cement: Surface

Intermediate Casing (Stage 2): 9-5/8", 40 New HCL-80, BTC casing to be set at +/- 10918'

ECP/DV Tool to be set at 4922'

1st Stage

Lead: 710 sxs Halcem-C + 2% CaCl (mixed at 11.0 ppg, 3.45 ft³/sx, 21.14 gal/sx water)

Tail: 460 sxs Halcem-C + 2% CaCl (mixed at 14.8 ppg, 1.32 ft³/sx, 6.39 gal/sx water)

Compressives: 12-hr = 500 psi 24 hr = 1151 psi

2nd Stage

Lead: 900 sxs Halcem-C + 2% CaCl (mixed at 11.0 ppg, 3.45 ft³/sx, 21.14 gal/sx water)

Tail: 470 sxs Halcem-C + 2% CaCl (mixed at 14.8 ppg, 1.32 ft³/sx, 6.39 gal/sx water)

Compressives:

Top of Cement: Surface

Production Casing: 5-1/2", 20 New P-110, BTC casing to be set at +/- 24988'

Lead: 0 sxs Halcem-C + 2% CaCl (mixed at 11.5 ppg, 1.88 ft³/sx, 9.61 gal/sx water)

Tail: 3270 sxs VersaCem (mixed at 13.2 ppg, 1.33 ft³/sx, 8.38 gal/sx water)

Compressives: 12-hr = 1375 psi 24 hr = 2285 psi

Top of Cement: 300' inside previous casing shoe

5. Pressure Control Equipment

The blow out preventer equipment (BOP) for this well consists of a 13-5/8" minimum 5M Hydril, and a 13-5/8" minimum 5M Double Ram BOP. MASP should not exceed 4345 psi.

All BOP testing will be done by an independent service company. Annular pressure tests will be limited to 50% of the working pressure. When nipping up on the 13-5/8" 5M bradenhead and flange, the BOP test will be limited to 5000 psi. When the 13-3/8" and 9-5/8" casing is set, the packoff seals will be tested to a minimum of 5000 psi. All BOP tests will include a low pressure test as per BLM regulations. The 5M BOP diagrams are attached. Blind rams will be functioned tested each trip, pipe rams will be functioned tested each day.

A variance is requested to allow use of a flex hose as the choke line from the BOP to the Choke Manifold. If this hose is used, a copy of the manufacturer's certification and pressure test chart will be kept on the rig. Attached is an example of a certification and pressure test chart. The manufacturer does not require anchors.

6. Proposed Mud Circulation System

INTERVAL	Hole Size	Mud Type	MW (ppg)	Viscosity (sec/qt)	Fluid Loss (cc)
0' to 1240'	17-1/2"	FW/Native	8.4-8.8	35-40	NC
1240' to 10918'	12-1/4"	FW / Cut Brine / Direct Emulsion	8.3-9.3	29-32	NC - 20
10918' to 24988'	8-3/4-8-1/2"	FW / Cut Brine / Polymer / OBM	11-11.6	32-50	NC - 20

The necessary mud products for weight addition and fluid loss control will be on location at all times.

Spud with fresh water/native mud. Drill out from under 13-3/8" surface casing with brine/oil direct emulsion water-based mud. Use fibrous materials as needed to control seepage and lost circulation. Pump viscous sweeps as needed for hole cleaning. Pump speed will be recorded on a daily drilling report after mudding up. A Pason or Totco will be used to detect changes in loss or gain of mud volume. A mud test will be performed every 24 hours to determine: density, viscosity, strength, filtration and pH as necessary. Use available solids controls equipment to help keep mud weight down after mud up. Rig up solids control equipment to operate as a closed loop system.

7. Auxiliary Well Control and Monitoring Equipment

- A. A Kelly cock will be in the drill string at all times.
- B. A full opening drill pipe stabbing valve having appropriate connections will be on the rig floor at all times.
- C. H2S monitors will be on location when drilling below the 13-3/8" casing.

8. Logging, Coring and Testing Program

Mud Logger: Mud Logging Unit (2 man) below intermediate casing.

Open hole logging will include Quad Combo

9. Abnormal Pressures and Temperatures / Potential Hazards


None Anticipated. BHT of 155 to 175 F is anticipated. No H2S is expected but monitors will be in place to detect any H2S occurrences. Should these circumstances be encountered the operator and drilling contractor are prepared to take all necessary steps to ensure safety of all personnel and environment. Lost circulation could occur but is not expected to be a serious problem in this area and hole seepage will be compensated for by additions of small amounts of LCM in the drilling fluid. The maximum anticipated bottom hole pressure for this well is 6945 psi.

10. Anticipated Starting Date and Duration of Operations

Road and location construction will begin after Santa Fe and BLM have approved the APD. Anticipated spud date will be as soon after Santa Fe and BLM approval and as soon as a rig will be available. Move in operations and drilling is expected to take 40 days. If production casing is run, an additional 30 days will be needed to complete well and construct surface facilities and/or lay flow lines in order to place well on production.



GE Oil & Gas

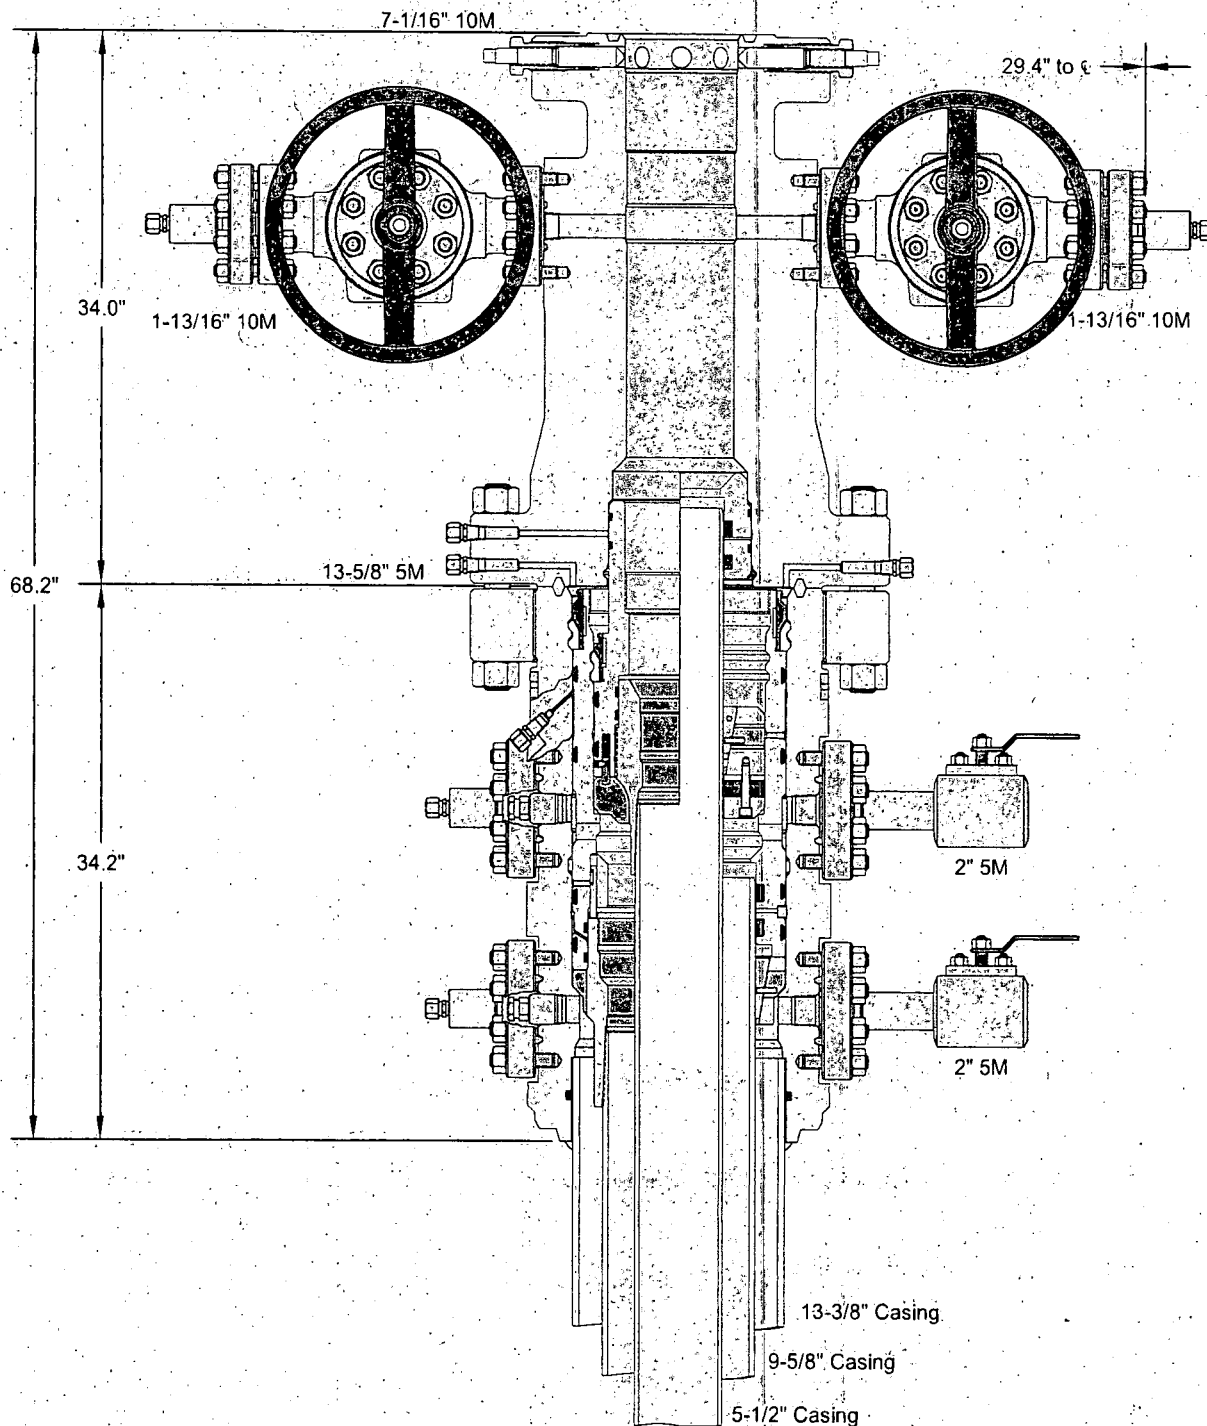

ALL DIMENSIONS ARE APPROXIMATE.

This drawing is the property of GE Oil & Gas Pressure Control LP and is considered confidential. Unless otherwise approved in writing, neither it nor its contents may be used, copied, transmitted or reproduced except for the sole purpose of GE Oil & Gas Pressure Control LP.


XTO ENERGY, INC.


13-3/8" x 9-5/8" x 5-1/2" 10M RSH-2 Wellhead
Assembly, With T-EBS-F Tubing Head

DRAWN VJK 16FEB17

APPRV KN 16FEB17


FOR REFERENCE ONLY
DRAWING NO. 10012842

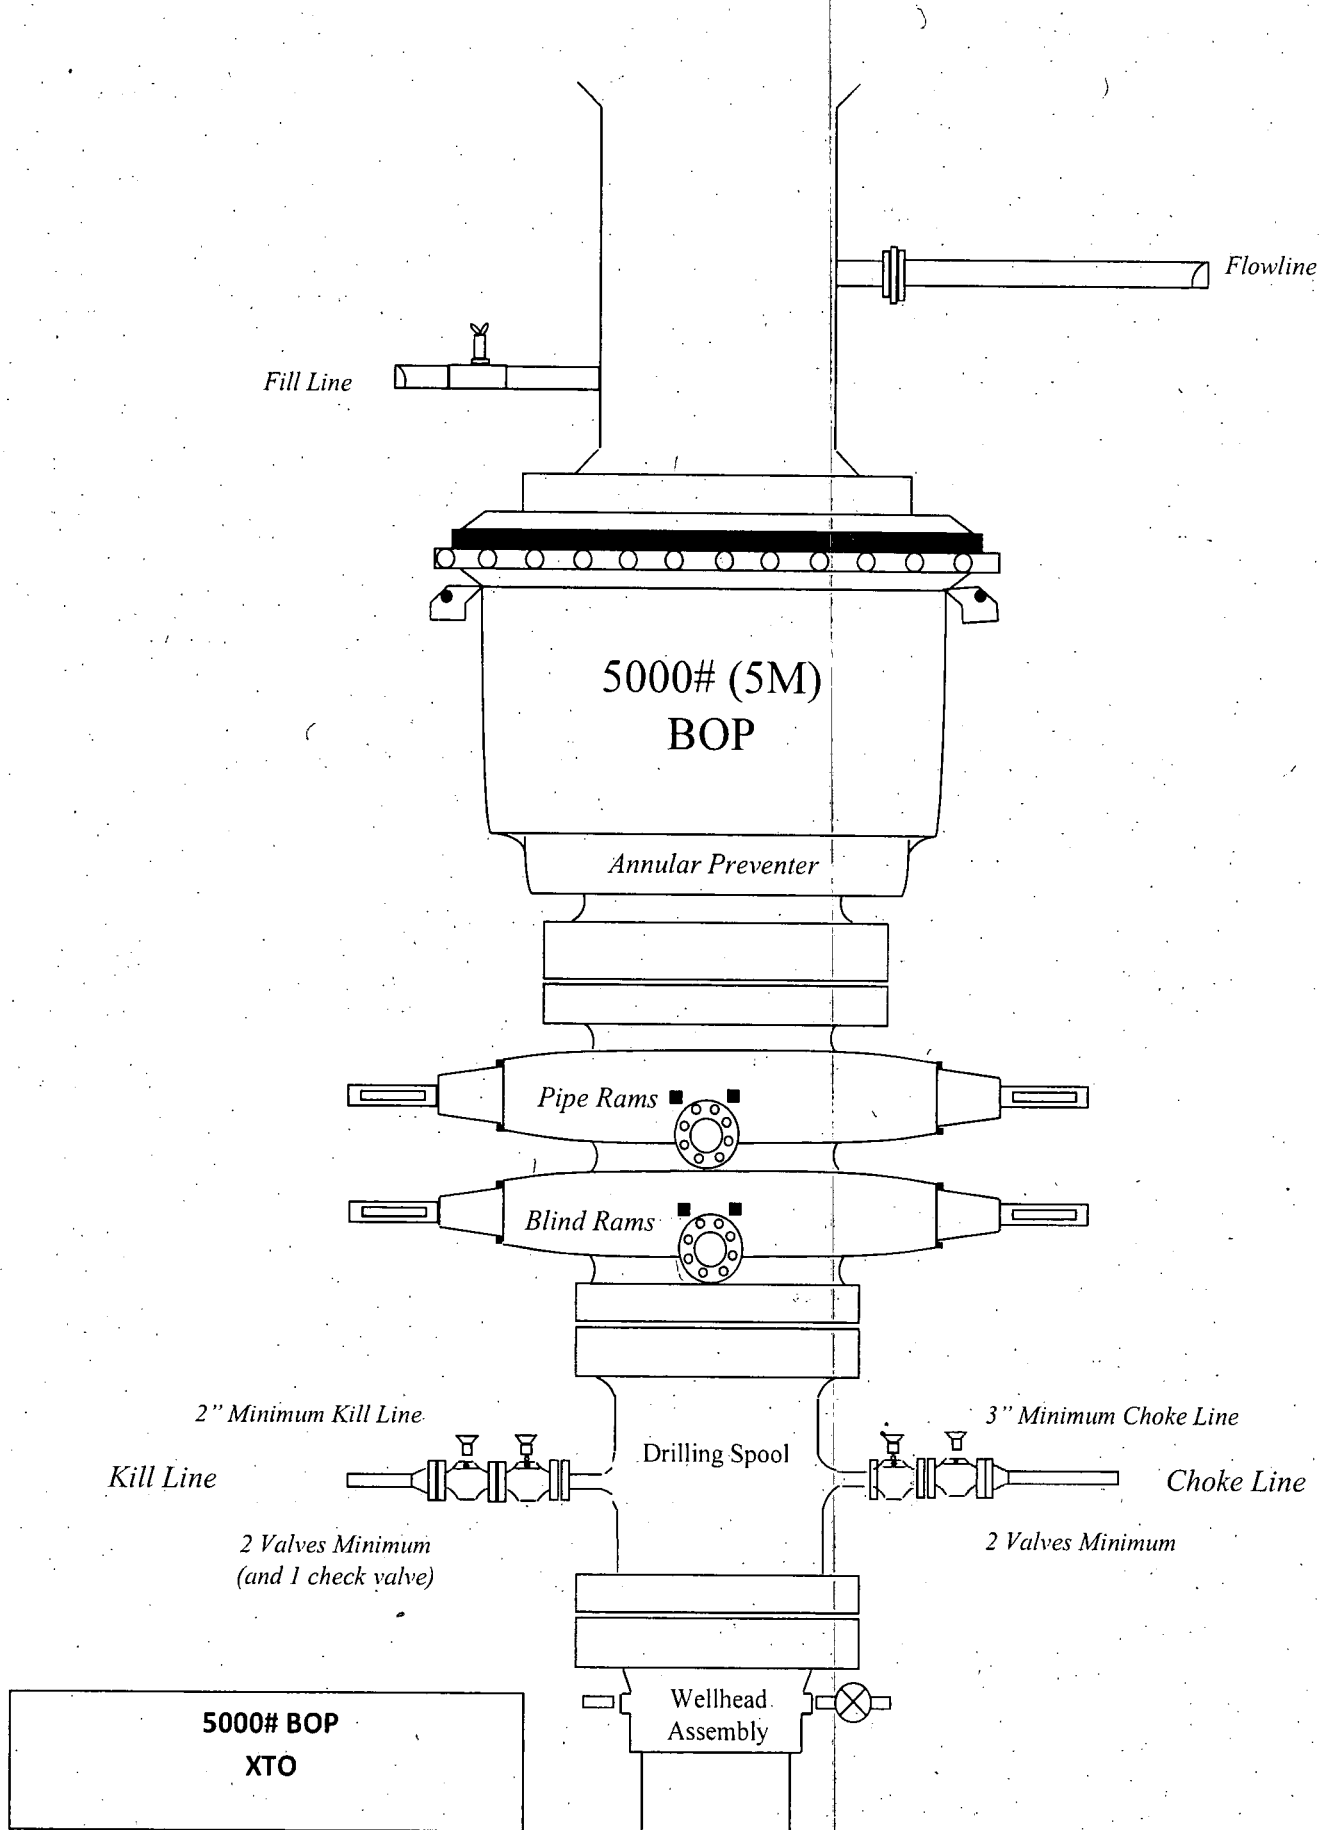

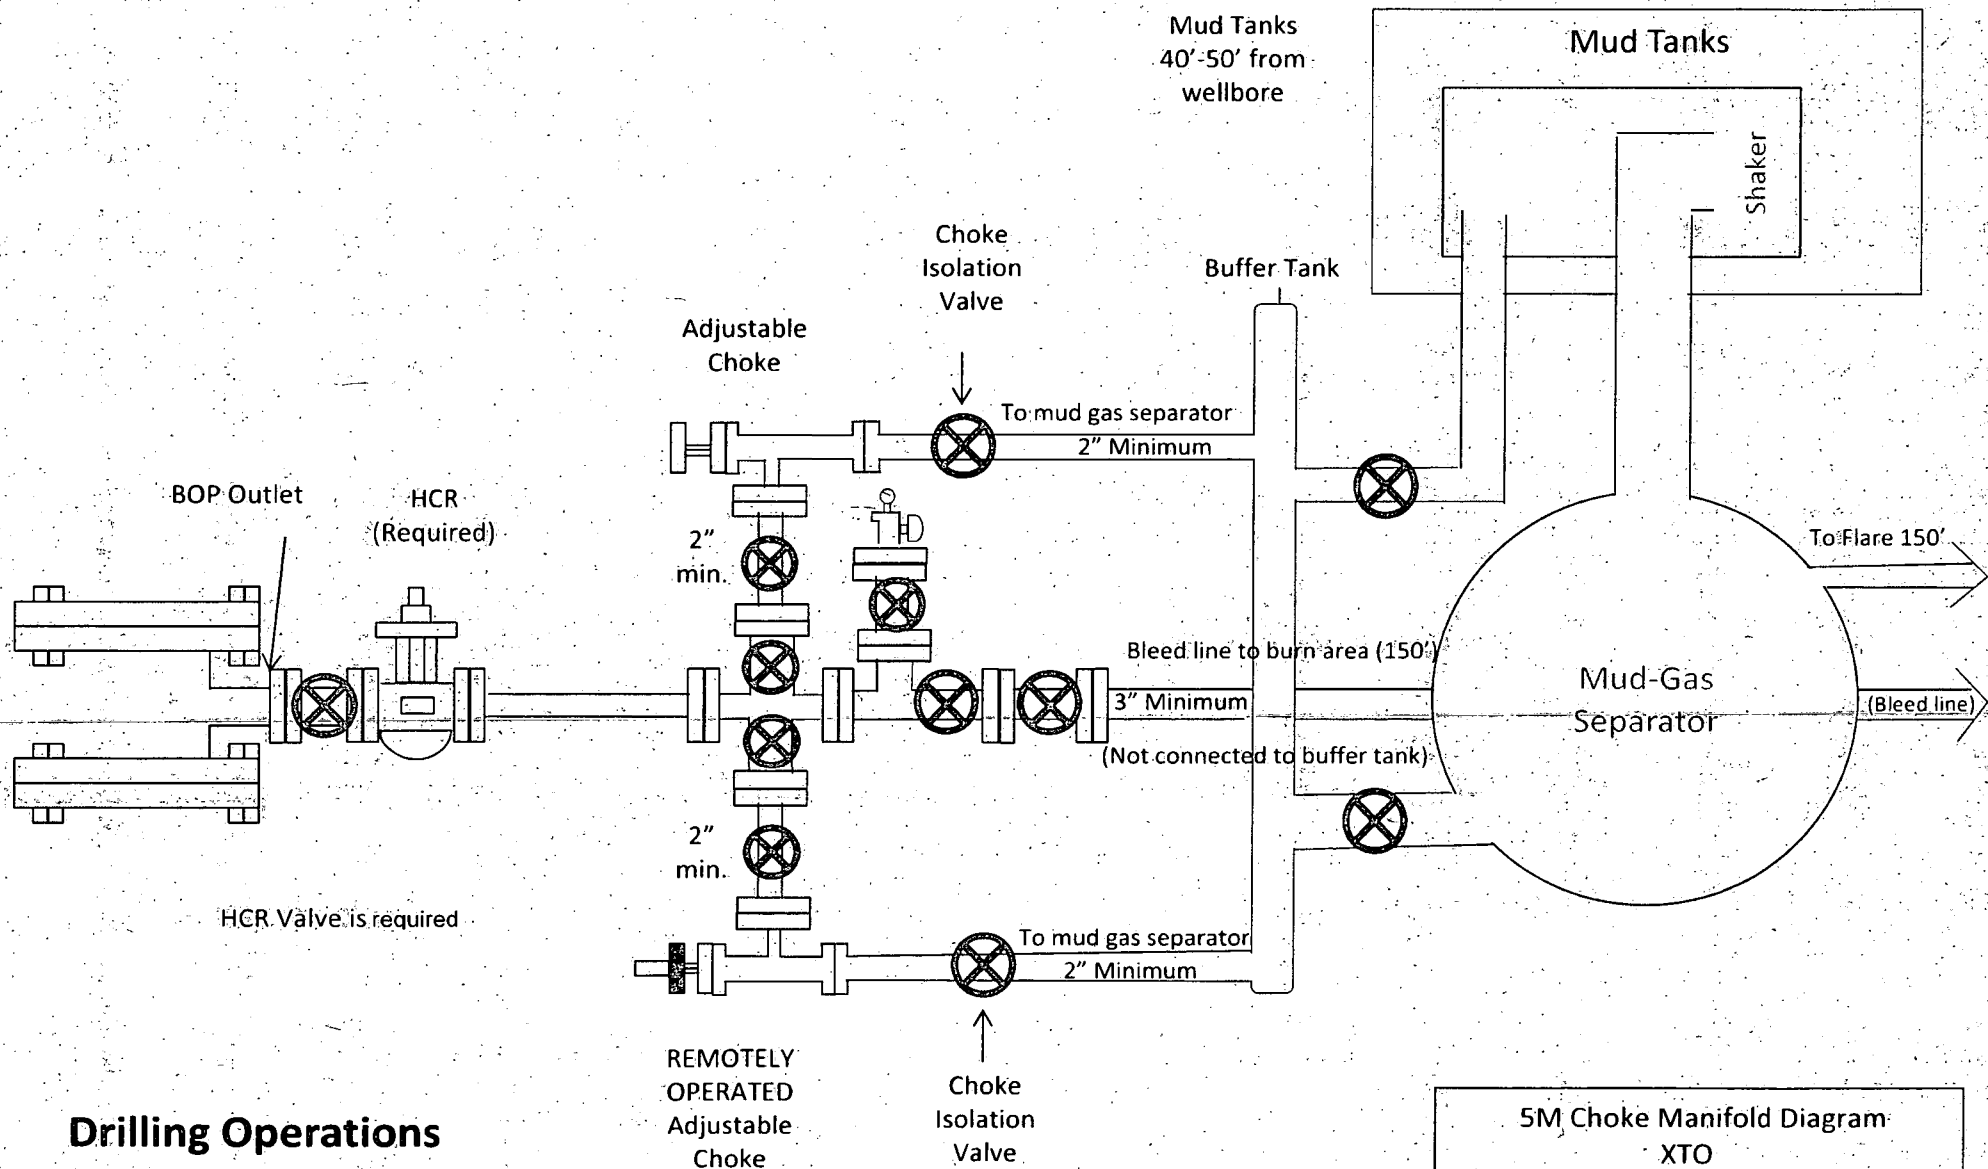

Drilling Operations Choke Manifold 5M Service

5M Choke Manifold Diagram
XTO



GATES E & S NORTH AMERICA, INC
DU-TEX
134 44TH STREET
CORPUS CHRISTI, TEXAS 78405


PHONE: 361-887-9807
FAX: 361-887-0812
EMAIL: crpe@s@gates.com
WEB: www.gates.com

GRADE D PRESSURE TEST CERTIFICATE

Customer :	AUSTIN DISTRIBUTING	Test Date:	6/8/2014
Customer Ref. :	PENDING	Hose Serial No.:	D-060814-1
Invoice No. :	201709	Created By:	NORMA
Product Description:	FD3.042.0R41/16.5KFLGE/E LE		
End Fitting 1 :	4 1/16 in.5K.FLG	End Fitting 2 :	4 1/16 in.5K.FLG
Gates Part No. :	4774-6001	Assembly Code:	L33090011513D-060814-1
Working Pressure :	5,000 PSI	Test Pressure :	7,500 PSI


Gates E & S North America, Inc. certifies that the following hose assembly has been tested to the Gates Oilfield Roughneck Agreement/Specification requirements and passed the 15 minute hydrostatic test per API Spec 7K/Q1, Fifth Edition, June 2010, Test pressure 9.6.7 and per Table 9 to 7,500 psi in accordance with this product number. Hose burst pressure 9.6.7.2 exceeds the minimum of 2.5 times the working pressure per Table 9.

Quality:	QUALITY	Technical Supervisor:	PRODUCTION
Date:	6/8/2014	Date:	6/8/2014
Signature:		Signature:	

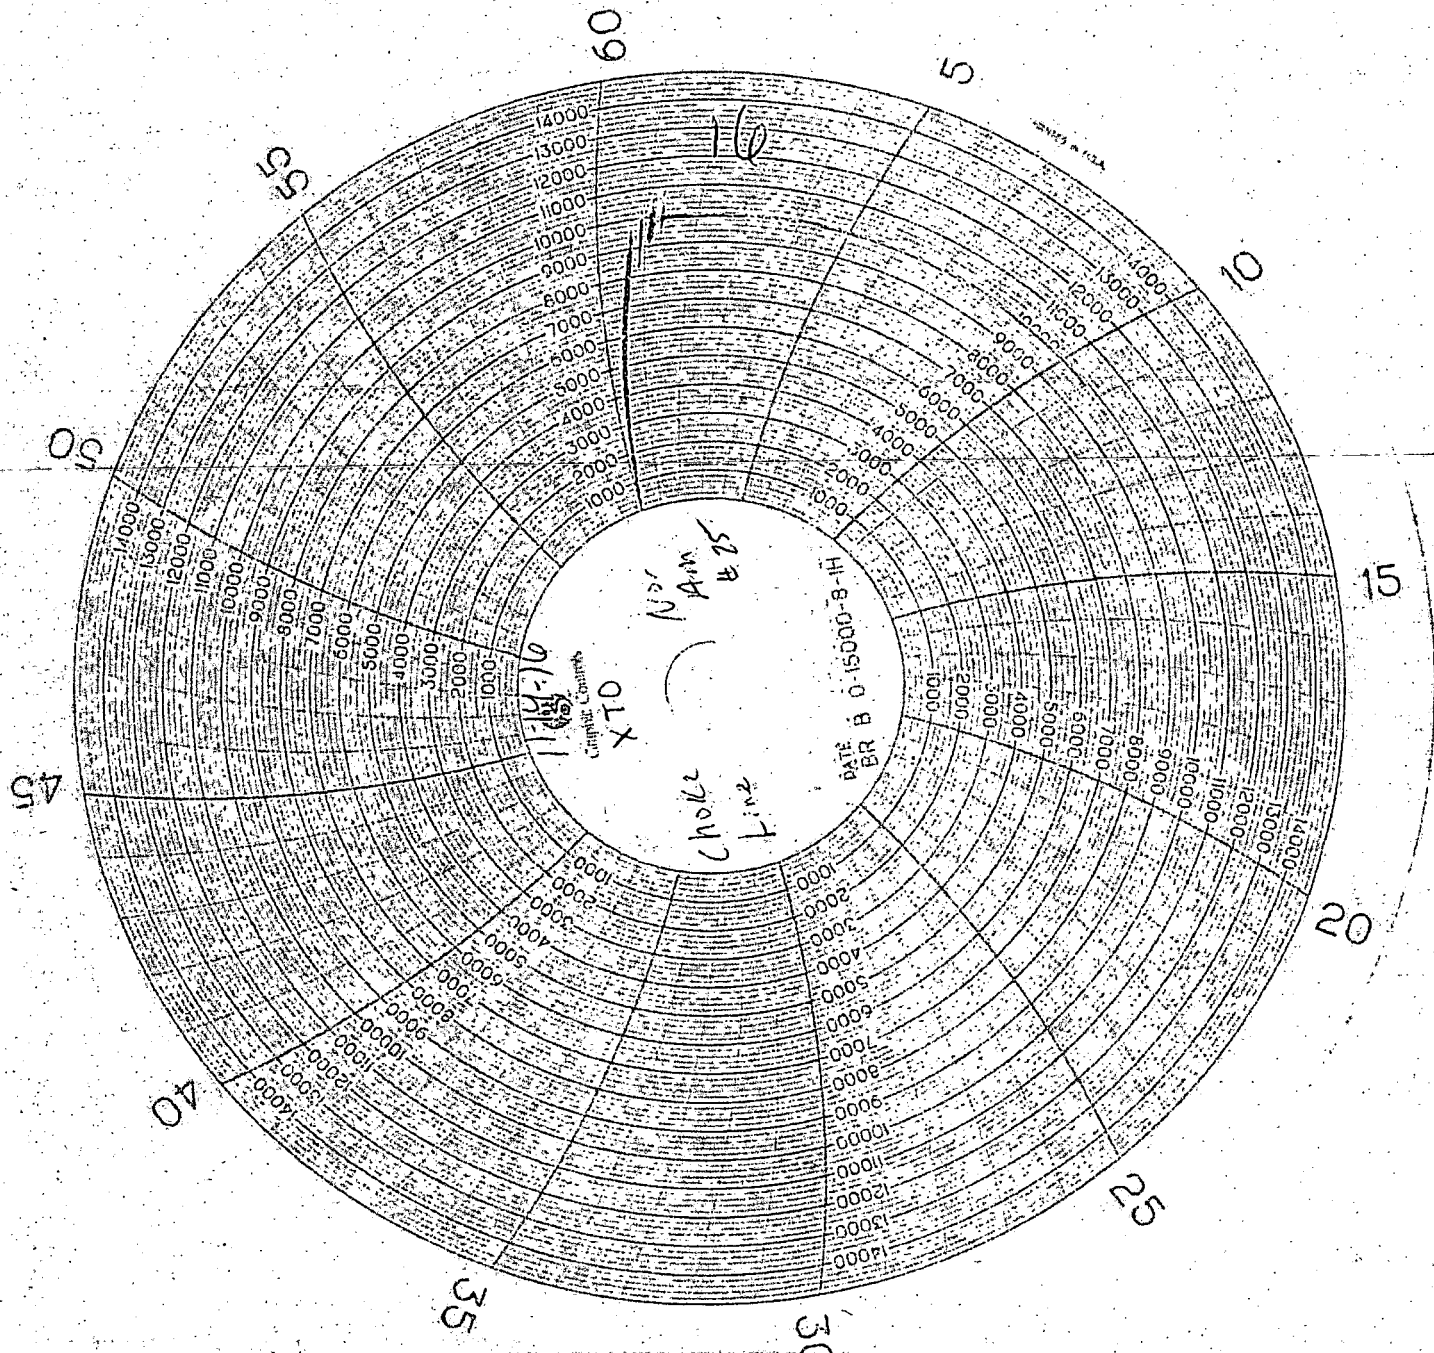

NOON

HOSE I.D. 3 1/2" LENGTH 42ft END 1 4 1/16" SKF END 2 4 1/16" SKF
GRADE D WORKING PRESSURE 5,000 P.S.I.
TEST PRESSURE 7,500 P.S.I. ASSEMBLY DATE 6-8-14
TEST DATE 6-8-14 SERIAL # 633096011513D-060814-1400
NAME D-1725 CRN 25123

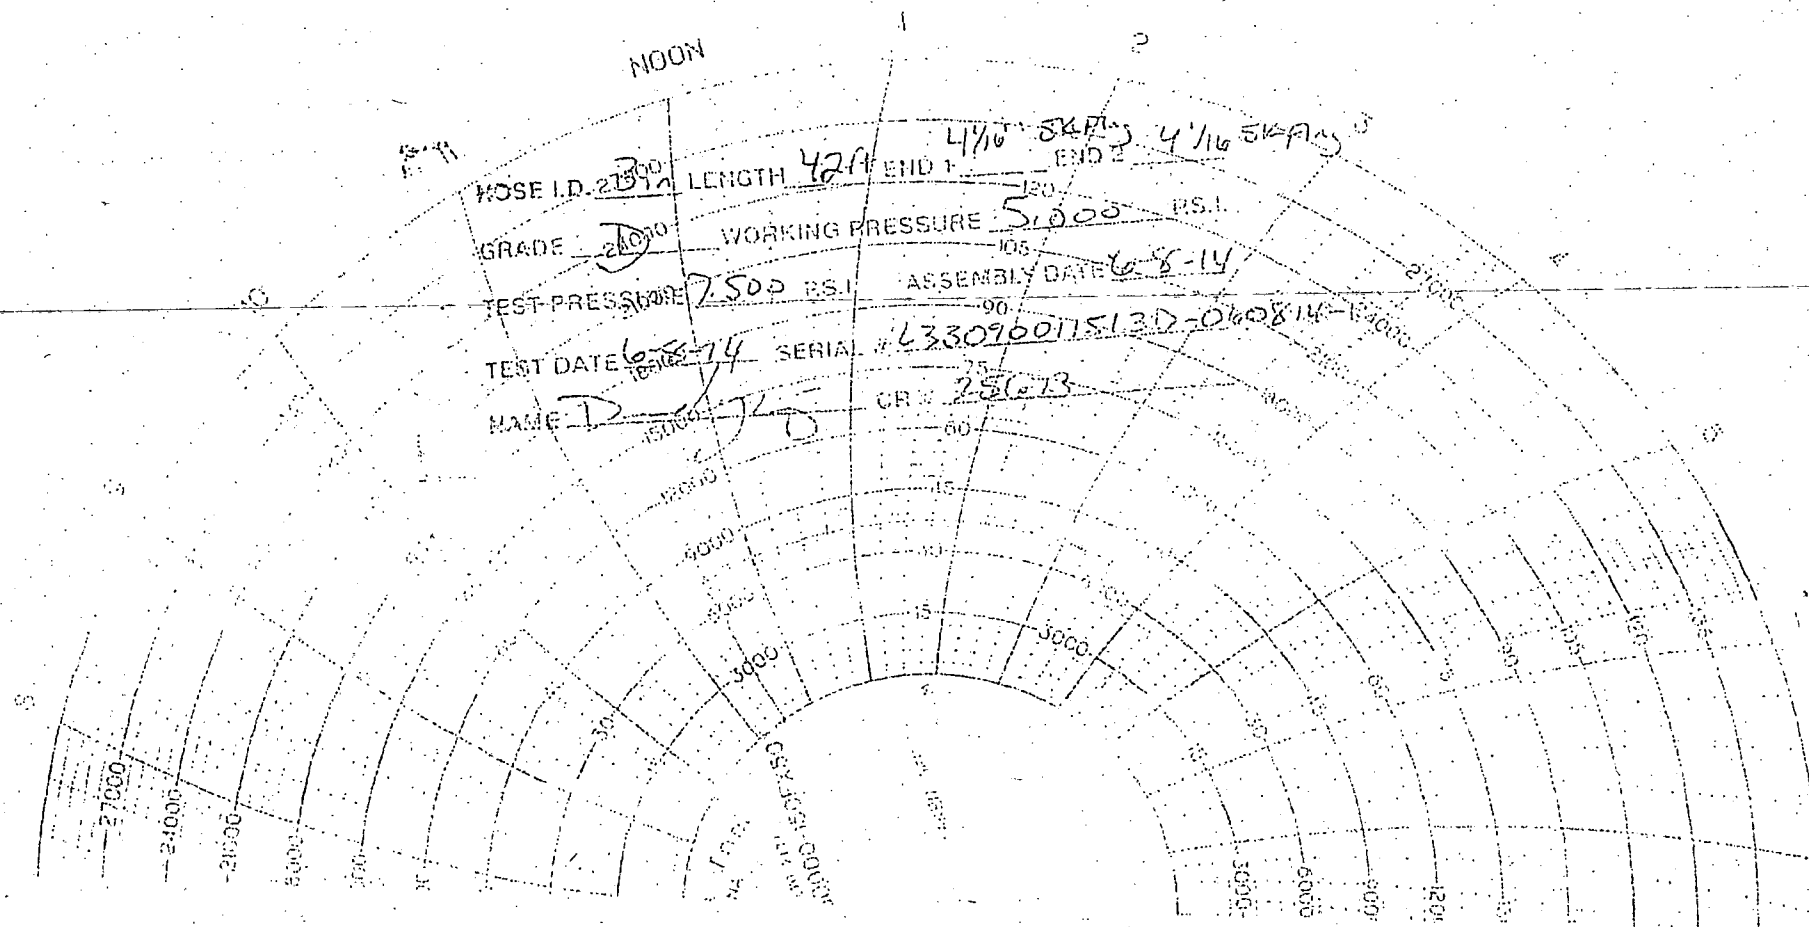

XTO Energy PLU 28 BS 106H Rev0 JP 15May19 Proposal Geodetic Report

(Non-Def Plan)

Report Date: December 18, 2019 - 01:37 PM
 Client: XTO Energy
 Field: NM Eddy County (NAD 27)
 Structure / Slot: XTO Energy PLU 28 BS 106H / New Slot
 Well: PLU 28 BS 106H
 Borehole: PLU 28 BS 106H
 UWI / API#: Unknown / Unknown
 Survey Name: XTO Energy PLU 28 BS 106H Rev0 JP 15May19
 Survey Date: May 15, 2019
 Tort / AHD / DDI / ERD Ratio: 101.805' / 13789.375 ft / 6.472' / 1.167
 Coordinate Reference System: NAD27 New Mexico State Plane, Eastern Zone, US Feet
 Location Lat / Long: N 32° 6' 7.50092", W 103° 46' 48.93060"
 Location Grid N/E Y/X: N 401300.500 ftUS, E 671261.200 ftUS
 CRS Grid Convergence Angle: 0.2939°
 Grid Scale Factor: 0.99994268
 Version / Patch: 2.10.787.0

Survey / DLS Computation: Minimum Curvature / Lubinski
 Vertical Section Azimuth: 179.830° (Grid North)
 Vertical Section Origin: 0.000 ft, 0.000 ft
 TVD Reference Datum: RKB
 TVD Reference Elevation: 3369.000 ft above MSL
 Seabed / Ground Elevation: 3339.000 ft above MSL
 Magnetic Declination: 6.686°
 Total Gravity Field Strength: 998.4233mgn (9.80665 Based)
 Gravity Model: GARM
 Total Magnetic Field Strength: 47805.749 nT
 Magnetic Dip Angle: 59.728°
 Declination Date: May 15, 2019
 Magnetic Declination Model: HDGM 2019
 North Reference: Grid North
 Grid Convergence Used: 0.2939°
 Total Corr Mag North->Grid: 6.3916°
 North: 6.3916°
 Local Coord Referenced To: Well Head

Comments	MD (ft)	Incl (°)	Azim Grid (°)	TVD (ft)	VSEC (ft)	NS (ft)	EW (ft)	DLS (°/100ft)	Northing (ftUS)	Easting (ftUS)	Latitude (N/S ° ' ")	Longitude (E/W ° ' ")
SHL	0.00	0.00	0.00	0.00	0.00	0.00	0.00	N/A	401300.50	671261.20	N 32 6 7.50	W 103 46 48.93
Nudge 1.5° DLS	3700.00	0.00	83.00	3700.00	0.00	0.00	0.00	0.00	401300.50	671261.20	N 32 6 7.50	W 103 46 48.93
Hold	4080.00	5.70	83.00	4079.37	-2.25	2.30	18.75	1.50	401302.80	671279.94	N 32 6 7.52	W 103 46 48.71
Drop 1.5° DLS	7015.14	5.70	83.00	7000.00	-36.91	37.83	308.09	0.00	401338.33	671569.27	N 32 6 7.86	W 103 46 45.35
Hold to KOP	7395.14	0.00	83.00	7379.37	-39.16	40.13	326.84	1.50	401340.63	671588.02	N 32 6 7.88	W 103 46 45.13
KOP, Build 8°	11118.59	0.00	83.00	11102.82	-39.16	40.13	326.84	0.00	401340.63	671588.02	N 32 6 7.88	W 103 46 45.13
DLS	12248.65	90.40	179.83	11819.00	682.10	-681.12	328.96	8.00	400619.42	671590.14	N 32 6 0.74	W 103 46 45.15
Landing Point	24987.79	90.40	179.83	11729.00	13420.92	-13419.90	366.42	0.00	387881.40	671627.60	N 32 3 54.68	W 103 46 45.47
XTO Energy												
PLU 28 BS												
106H - PBHL												

Survey Type: Non-Def Plan

Survey Error Model: ISCWSA Rev 0 *** 3-D 95.000% Confidence 2.7855 sigma
 Survey Program:

Description	Part	MD From (ft)	MD To (ft)	EOU Freq (ft)	Hole Size Casing Diameter (in)	Expected Max Inclination (deg)	Survey Tool Type	Borehole / Survey
	1	0.000	30.000	1/100.000	30.000	30.000	NAL_MWD_IFR1+MS-Depth Only	PLU 28 BS 106H / XTO Energy PLU 28 BS 106H Rev0 JP 15May19
	1	30.000	24987.791	1/100.000	30.000	30.000	NAL_MWD_IFR1+MS	PLU 28 BS 106H / XTO Energy PLU 28 BS 106H Rev0 JP

XTO Energy PLU 28 BS 106H Rev0 JP 15May19 Proposal Geodetic Report



(Non-Def Plan)

Report Date: December 18, 2019 - 01:38 PM
 Client: XTO Energy
 Field: NM Eddy County (NAD 27)
 Structure / Slot: XTO Energy PLU 28 BS 106H / New Slot
 Well: PLU 28 BS 106H
 Borehole: PLU 28 BS 106H
 UWI / API#: Unknown / Unknown
 Survey Name: XTO Energy PLU 28 BS 106H Rev0 JP 15May19
 Survey Date: May 15, 2019
 Tort / AHD / DDI / ERD Ratio: 101.805 * / 13789.375 ft / 6.472 / 1.167
 Coordinate Reference System: NAD27 New Mexico State Plane, Eastern Zone, US Feet
 Location Lat / Long: N 32° 6' 7.50082", W 103° 46' 48.93060"
 Location Grid N/E Y/X: N 401300.500 ftUS, E 671261.200 ftUS
 CRS Grid Convergence Angle: 0.2939 *
 Grid Scale Factor: 0.99994268
 Version / Patch: 2.10.787.0

Survey / DLS Computation: Minimum Curvature / Lubinski
 Vertical Section Azimuth: 179.830 * (Grid North)
 Vertical Section Origin: 0.000 ft, 0.000 ft
 TVD Reference Datum: RKB
 TVD Reference Elevation: 3369.000 ft above MSL
 Seabed / Ground Elevation: 3339.000 ft above MSL
 Magnetic Declination: 6.686 *
 Total Gravity Field Strength: 998.4233mgn (9.80665 Based)
 Gravity Model: GARM
 Total Magnetic Field Strength: 47805.749 nT
 Magnetic Dip Angle: 59.728 *
 Declination Date: May 15, 2019
 Magnetic Declination Model: HDGM 2019
 North Reference: Grid North
 Grid Convergence Used: 0.2939 *
 Total Corr Mag North->Grid: 6.3916 *
 North: 6.3916 *
 Local Coord Referenced To: Well Head

Comments	MD (ft)	Incl (°)	Azim Grid (°)	TVD (ft)	VSEC (ft)	NS (ft)	EW (ft)	DLS (*/100ft)	Northing (ftUS)	Easting (ftUS)	Latitude (N/S ° ' ")	Longitude (E/W ° ' ")
SHL	0.00	0.00	83.00	0.00	0.00	0.00	0.00	N/A	401300.50	671261.20	N 32° 6' 7.50 W	103 46 48.93
	100.00	0.00	83.00	100.00	0.00	0.00	0.00	0.00	401300.50	671261.20	N 32° 6' 7.50 W	103 46 48.93
	200.00	0.00	83.00	200.00	0.00	0.00	0.00	0.00	401300.50	671261.20	N 32° 6' 7.50 W	103 46 48.93
	300.00	0.00	83.00	300.00	0.00	0.00	0.00	0.00	401300.50	671261.20	N 32° 6' 7.50 W	103 46 48.93
	400.00	0.00	83.00	400.00	0.00	0.00	0.00	0.00	401300.50	671261.20	N 32° 6' 7.50 W	103 46 48.93
	500.00	0.00	83.00	500.00	0.00	0.00	0.00	0.00	401300.50	671261.20	N 32° 6' 7.50 W	103 46 48.93
	600.00	0.00	83.00	600.00	0.00	0.00	0.00	0.00	401300.50	671261.20	N 32° 6' 7.50 W	103 46 48.93
	700.00	0.00	83.00	700.00	0.00	0.00	0.00	0.00	401300.50	671261.20	N 32° 6' 7.50 W	103 46 48.93
	800.00	0.00	83.00	800.00	0.00	0.00	0.00	0.00	401300.50	671261.20	N 32° 6' 7.50 W	103 46 48.93
	900.00	0.00	83.00	900.00	0.00	0.00	0.00	0.00	401300.50	671261.20	N 32° 6' 7.50 W	103 46 48.93
	1000.00	0.00	83.00	1000.00	0.00	0.00	0.00	0.00	401300.50	671261.20	N 32° 6' 7.50 W	103 46 48.93
	1100.00	0.00	83.00	1100.00	0.00	0.00	0.00	0.00	401300.50	671261.20	N 32° 6' 7.50 W	103 46 48.93
	1200.00	0.00	83.00	1200.00	0.00	0.00	0.00	0.00	401300.50	671261.20	N 32° 6' 7.50 W	103 46 48.93
	1300.00	0.00	83.00	1300.00	0.00	0.00	0.00	0.00	401300.50	671261.20	N 32° 6' 7.50 W	103 46 48.93
	1400.00	0.00	83.00	1400.00	0.00	0.00	0.00	0.00	401300.50	671261.20	N 32° 6' 7.50 W	103 46 48.93
	1500.00	0.00	83.00	1500.00	0.00	0.00	0.00	0.00	401300.50	671261.20	N 32° 6' 7.50 W	103 46 48.93
	1600.00	0.00	83.00	1600.00	0.00	0.00	0.00	0.00	401300.50	671261.20	N 32° 6' 7.50 W	103 46 48.93
	1700.00	0.00	83.00	1700.00	0.00	0.00	0.00	0.00	401300.50	671261.20	N 32° 6' 7.50 W	103 46 48.93
	1800.00	0.00	83.00	1800.00	0.00	0.00	0.00	0.00	401300.50	671261.20	N 32° 6' 7.50 W	103 46 48.93
	1900.00	0.00	83.00	1900.00	0.00	0.00	0.00	0.00	401300.50	671261.20	N 32° 6' 7.50 W	103 46 48.93
	2000.00	0.00	83.00	2000.00	0.00	0.00	0.00	0.00	401300.50	671261.20	N 32° 6' 7.50 W	103 46 48.93
	2100.00	0.00	83.00	2100.00	0.00	0.00	0.00	0.00	401300.50	671261.20	N 32° 6' 7.50 W	103 46 48.93
	2200.00	0.00	83.00	2200.00	0.00	0.00	0.00	0.00	401300.50	671261.20	N 32° 6' 7.50 W	103 46 48.93
	2300.00	0.00	83.00	2300.00	0.00	0.00	0.00	0.00	401300.50	671261.20	N 32° 6' 7.50 W	103 46 48.93
	2400.00	0.00	83.00	2400.00	0.00	0.00	0.00	0.00	401300.50	671261.20	N 32° 6' 7.50 W	103 46 48.93
	2500.00	0.00	83.00	2500.00	0.00	0.00	0.00	0.00	401300.50	671261.20	N 32° 6' 7.50 W	103 46 48.93
	2600.00	0.00	83.00	2600.00	0.00	0.00	0.00	0.00	401300.50	671261.20	N 32° 6' 7.50 W	103 46 48.93
	2700.00	0.00	83.00	2700.00	0.00	0.00	0.00	0.00	401300.50	671261.20	N 32° 6' 7.50 W	103 46 48.93
	2800.00	0.00	83.00	2800.00	0.00	0.00	0.00	0.00	401300.50	671261.20	N 32° 6' 7.50 W	103 46 48.93
	2900.00	0.00	83.00	2900.00	0.00	0.00	0.00	0.00	401300.50	671261.20	N 32° 6' 7.50 W	103 46 48.93
	3000.00	0.00	83.00	3000.00	0.00	0.00	0.00	0.00	401300.50	671261.20	N 32° 6' 7.50 W	103 46 48.93
	3100.00	0.00	83.00	3100.00	0.00	0.00	0.00	0.00	401300.50	671261.20	N 32° 6' 7.50 W	103 46 48.93
	3200.00	0.00	83.00	3200.00	0.00	0.00	0.00	0.00	401300.50	671261.20	N 32° 6' 7.50 W	103 46 48.93
	3300.00	0.00	83.00	3300.00	0.00	0.00	0.00	0.00	401300.50	671261.20	N 32° 6' 7.50 W	103 46 48.93
	3400.00	0.00	83.00	3400.00	0.00	0.00	0.00	0.00	401300.50	671261.20	N 32° 6' 7.50 W	103 46 48.93
	3500.00	0.00	83.00	3500.00	0.00	0.00	0.00	0.00	401300.50	671261.20	N 32° 6' 7.50 W	103 46 48.93
	3600.00	0.00	83.00	3600.00	0.00	0.00	0.00	0.00	401300.50	671261.20	N 32° 6' 7.50 W	103 46 48.93
Nudge 1.5° DLS	3700.00	0.00	83.00	3700.00	0.00	0.00	0.00	0.00	401300.50	671261.20	N 32° 6' 7.50 W	103 46 48.93
	3800.00	1.50	83.00	3799.99	-0.16	0.16	1.30	1.50	401300.66	671262.50	N 32° 6' 7.50 W	103 46 48.92
	3900.00	3.00	83.00	3899.91	-0.82	0.64	5.20	1.50	401301.14	671266.40	N 32° 6' 7.51 W	103 46 48.87
	4000.00	4.50	83.00	3999.69	-1.40	1.44	11.69	1.50	401301.93	671272.89	N 32° 6' 7.51 W	103 46 48.79
Hold	4080.00	5.70	83.00	4079.37	-2.25	2.30	18.75	1.50	401302.80	671276.94	N 32° 6' 7.52 W	103 46 48.71
	4100.00	5.70	83.00	4099.27	-2.48	2.54	20.72	0.00	401303.04	671281.92	N 32° 6' 7.53 W	103 46 48.69
	4200.00	5.70	83.00	4198.78	-3.66	3.75	30.58	0.00	401304.25	671291.77	N 32° 6' 7.54 W	103 46 48.57
	4300.00	5.70	83.00	4298.29	-4.84	4.96	40.43	0.00	401305.46	671301.63	N 32° 6' 7.55 W	103 46 48.46
	4400.00	5.70	83.00	4397.79	-6.03	6.17	50.29	0.00	401306.67	671311.49	N 32° 6' 7.56 W	103 46 48.35
	4500.00	5.70	83.00	4497.30	-7.21	7.39	60.15	0.00	401307.88	671321.35	N 32° 6' 7.57 W	103 46 48.23
	4600.00	5.70	83.00	4596.80	-8.39	8.60	70.01	0.00	401309.10	671331.20	N 32° 6' 7.58 W	103 46 48.12
	4700.00	5.70	83.00	4696.31	-9.57	9.81	79.86	0.00	401310.31	671341.06	N 32° 6' 7.59 W	103 46 48.00
	4800.00	5.70	83.00	4795.81	-10.75	11.02	89.72	0.00	401311.52	671350.92	N 32° 6' 7.61 W	103 46 47.89
	4900.00	5.70	83.00	4895.32	-11.93	12.23	99.58	0.00	401312.73	671360.77	N 32° 6' 7.62 W	103 46 47.77
	5000.00	5.70	83.00	4994.82	-13.11	13.44	109.44	0.00	401313.94	671370.63	N 32° 6' 7.63 W	103 46 47.66
	5100.00	5.70	83.00	5094.33	-14.29	14.65	119.30	0.00	401315.15	671380.49	N 32° 6' 7.64 W	103 46 47.54
	5200.00	5.70	83.00	5193.84	-15.47	15.86	129.15	0.00	401316.36	671390.35	N 32° 6' 7.65 W	103 46 47.43
	5300.00	5.70	83.00	5293.34	-16.66	17.07	139.01	0.00	401317.57	671400.20	N 32° 6' 7.66 W	103 46 47.31
	5400.00	5.70	83.00	5392.85	-17.84	18.28	148.87	0.00	401318.78	671410.06	N 32° 6' 7.67 W	103 46 47.20
	5500.00	5.70	83.00	5492.35	-19.02	19.49	158.73	0.00	401319.99	671419.92	N 32° 6' 7.69 W	103 46 47.08
	5600.00	5.70	83.00	5591.86	-20.20	20.70	168.59	0.00	401321.20	671429.78	N 32° 6' 7.70 W	103 46 46.97
	5700.00	5.70	83.00	5691.36	-21.38	21.91	178.44	0.00	401322.41	671439.63	N 32° 6' 7.71 W	103 46 46.85
	5800.00	5.70	83.00	5790.87	-22.56	23.12	188.30	0.00	401323.62	671449.49	N 32° 6' 7.72 W	103 46 46.74
	5900.00	5.70	83.00	5890.37	-23.74	24.33	198.16	0.00	401324.83	671459.35	N 32° 6' 7.73 W	103 46 46.63
	6000.00	5.70	83.00	5989.88	-24.92	25.54	208.02	0.00	401326.04	671469.21	N 32° 6' 7.74 W	103 46 46.51
	6100.00	5.70	83.00	6089.39	-26.11	26.75	217.88	0.00	401327.25	671479.06	N 32° 6' 7.75 W	103 46 46.40
	6200.00	5.70	83.00	6188.89	-27.29	27.96	227.73	0.00	401328.46	671488.92	N 32° 6' 7.77 W	103 46 46.28
	6300.00	5.70	83.00	6288.40	-28.47	29.17	237.59	0.00	401329.67	671498.78	N 32° 6' 7.78 W	103 46 46.17
	6400.00	5.70	83.00	6387.90	-29.65	30.38	247.45	0.00	401330.88	671508.64	N 32° 6' 7.79 W	103 46 46.05
	6500.00	5.70	83.00	6487.41	-30.83	31.59	257.31	0.00	401332.09	671518.49	N 32° 6' 7.80 W	103 46 45.94
	6600.00	5.70	83.00	6586.91	-32.01	32.80	267.17	0.00	401333.30	671528.35	N 32° 6' 7.81 W	103 46 45.82
	6700.00	5.70	83.00	6686.42	-33.19	34.01	277.02	0.00	401334.51	671538.21	N 32° 6' 7.82 W	103 46 45.71
	6800.00	5.70	83.00	6785.92	-34.37	35.22	286.88	0.00	401335.72	671548.06	N 32° 6' 7.83 W	103 46 45.59
	6900.00	5.70	83.00	6885.43	-35.55	36.44	296.74	0.00	401336.93	671557.92	N 32° 6' 7.85 W	103 46 45.48
	7000.00	5.70	83.00	6984.94	-36.74	37.65	306.60	0.00	401338.14	671567.78	N 32° 6' 7.86 W	103 46 45.36
Drop 1.5° DLS	7015.14	5.70	83.00	7000.00	-36.91	37.83	308.09	0.00	401338.35	671569.27	N 32° 6' 7.88 W	103 46 45.35
	7100.00	4.43	83.00	7084.53	-37.81	38.74	315.52	1.50	401339.24	671576.71	N 32° 6' 7.87 W	103

Comments	MD (ft)	Incl (°)	Azim Grid (°)	TVD (ft)	VSEC (ft)	NS (ft)	EW (ft)	DLS (ft/100ft)	Northing (ftUS)	Easting (ftUS)	Latitude (N/S ° ' ")	Longitude (E/W ° ' ")
	7500.00	0.00	83.00	7484.23	-39.16	40.13	326.84	0.00	401340.63	671588.02	N 32 6 7.88 W	103 46 45.13
	7600.00	0.00	83.00	7584.23	-39.16	40.13	326.84	0.00	401340.63	671588.02	N 32 6 7.88 W	103 46 45.13
	7700.00	0.00	83.00	7684.23	-39.16	40.13	326.84	0.00	401340.63	671588.02	N 32 6 7.88 W	103 46 45.13
	7800.00	0.00	83.00	7784.23	-39.16	40.13	326.84	0.00	401340.63	671588.02	N 32 6 7.88 W	103 46 45.13
	7900.00	0.00	83.00	7884.23	-39.16	40.13	326.84	0.00	401340.63	671588.02	N 32 6 7.88 W	103 46 45.13
	8000.00	0.00	83.00	7984.23	-39.16	40.13	326.84	0.00	401340.63	671588.02	N 32 6 7.88 W	103 46 45.13
	8100.00	0.00	83.00	8084.23	-39.16	40.13	326.84	0.00	401340.63	671588.02	N 32 6 7.88 W	103 46 45.13
	8200.00	0.00	83.00	8184.23	-39.16	40.13	326.84	0.00	401340.63	671588.02	N 32 6 7.88 W	103 46 45.13
	8300.00	0.00	83.00	8284.23	-39.16	40.13	326.84	0.00	401340.63	671588.02	N 32 6 7.88 W	103 46 45.13
	8400.00	0.00	83.00	8384.23	-39.16	40.13	326.84	0.00	401340.63	671588.02	N 32 6 7.88 W	103 46 45.13
	8500.00	0.00	83.00	8484.23	-39.16	40.13	326.84	0.00	401340.63	671588.02	N 32 6 7.88 W	103 46 45.13
	8600.00	0.00	83.00	8584.23	-39.16	40.13	326.84	0.00	401340.63	671588.02	N 32 6 7.88 W	103 46 45.13
	8700.00	0.00	83.00	8684.23	-39.16	40.13	326.84	0.00	401340.63	671588.02	N 32 6 7.88 W	103 46 45.13
	8800.00	0.00	83.00	8784.23	-39.16	40.13	326.84	0.00	401340.63	671588.02	N 32 6 7.88 W	103 46 45.13
	8900.00	0.00	83.00	8884.23	-39.16	40.13	326.84	0.00	401340.63	671588.02	N 32 6 7.88 W	103 46 45.13
	9000.00	0.00	83.00	8984.23	-39.16	40.13	326.84	0.00	401340.63	671588.02	N 32 6 7.88 W	103 46 45.13
	9100.00	0.00	83.00	9084.23	-39.16	40.13	326.84	0.00	401340.63	671588.02	N 32 6 7.88 W	103 46 45.13
	9200.00	0.00	83.00	9184.23	-39.16	40.13	326.84	0.00	401340.63	671588.02	N 32 6 7.88 W	103 46 45.13
	9300.00	0.00	83.00	9284.23	-39.16	40.13	326.84	0.00	401340.63	671588.02	N 32 6 7.88 W	103 46 45.13
	9400.00	0.00	83.00	9384.23	-39.16	40.13	326.84	0.00	401340.63	671588.02	N 32 6 7.88 W	103 46 45.13
	9500.00	0.00	83.00	9484.23	-39.16	40.13	326.84	0.00	401340.63	671588.02	N 32 6 7.88 W	103 46 45.13
	9600.00	0.00	83.00	9584.23	-39.16	40.13	326.84	0.00	401340.63	671588.02	N 32 6 7.88 W	103 46 45.13
	9700.00	0.00	83.00	9684.23	-39.16	40.13	326.84	0.00	401340.63	671588.02	N 32 6 7.88 W	103 46 45.13
	9800.00	0.00	83.00	9784.23	-39.16	40.13	326.84	0.00	401340.63	671588.02	N 32 6 7.88 W	103 46 45.13
	9900.00	0.00	83.00	9884.23	-39.16	40.13	326.84	0.00	401340.63	671588.02	N 32 6 7.88 W	103 46 45.13
	10000.00	0.00	83.00	9984.23	-39.16	40.13	326.84	0.00	401340.63	671588.02	N 32 6 7.88 W	103 46 45.13
	10100.00	0.00	83.00	10084.23	-39.16	40.13	326.84	0.00	401340.63	671588.02	N 32 6 7.88 W	103 46 45.13
	10200.00	0.00	83.00	10184.23	-39.16	40.13	326.84	0.00	401340.63	671588.02	N 32 6 7.88 W	103 46 45.13
	10300.00	0.00	83.00	10284.23	-39.16	40.13	326.84	0.00	401340.63	671588.02	N 32 6 7.88 W	103 46 45.13
	10400.00	0.00	83.00	10384.23	-39.16	40.13	326.84	0.00	401340.63	671588.02	N 32 6 7.88 W	103 46 45.13
	10500.00	0.00	83.00	10484.23	-39.16	40.13	326.84	0.00	401340.63	671588.02	N 32 6 7.88 W	103 46 45.13
	10600.00	0.00	83.00	10584.23	-39.16	40.13	326.84	0.00	401340.63	671588.02	N 32 6 7.88 W	103 46 45.13
	10700.00	0.00	83.00	10684.23	-39.16	40.13	326.84	0.00	401340.63	671588.02	N 32 6 7.88 W	103 46 45.13
	10800.00	0.00	83.00	10784.23	-39.16	40.13	326.84	0.00	401340.63	671588.02	N 32 6 7.88 W	103 46 45.13
	10900.00	0.00	83.00	10884.23	-39.16	40.13	326.84	0.00	401340.63	671588.02	N 32 6 7.88 W	103 46 45.13
	11000.00	0.00	83.00	10984.23	-39.16	40.13	326.84	0.00	401340.63	671588.02	N 32 6 7.88 W	103 46 45.13
	11100.00	0.00	83.00	11084.23	-39.16	40.13	326.84	0.00	401340.63	671588.02	N 32 6 7.88 W	103 46 45.13
KOP, Build 8° DLS	11118.59	0.00	83.00	11102.82	-39.16	40.13	326.84	0.00	401340.63	671588.02	N 32 6 7.88 W	103 46 45.13
	11200.00	6.51	179.83	11184.06	-34.54	35.51	326.85	8.00	401336.01	671588.03	N 32 6 7.84 W	103 46 45.13
	11300.00	14.51	179.83	11282.30	-16.31	17.28	326.90	8.00	401317.78	671588.08	N 32 6 7.66 W	103 46 45.13
	11400.00	22.51	179.83	11377.05	15.42	-14.45	327.00	8.00	401286.05	671588.18	N 32 6 7.34 W	103 46 45.13
	11500.00	30.51	179.83	11466.46	60.02	-59.05	327.13	8.00	401241.45	671588.31	N 32 6 6.90 W	103 46 45.13
	11600.00	38.51	179.83	11548.79	116.64	-115.67	327.29	8.00	401184.84	671588.47	N 32 6 6.34 W	103 46 45.13
	11700.00	46.51	179.83	11622.44	184.16	-183.19	327.49	8.00	401117.32	671588.67	N 32 6 5.67 W	103 46 45.13
	11800.00	54.51	179.83	11685.98	261.27	-260.30	327.72	8.00	401040.21	671588.90	N 32 6 4.91 W	103 46 45.14
	11900.00	62.51	179.83	11738.17	346.48	-345.51	327.97	8.00	400855.01	671588.15	N 32 6 4.07 W	103 46 45.14
	12000.00	70.51	179.83	11777.99	438.12	-437.15	328.24	8.00	400683.38	671589.42	N 32 6 3.16 W	103 46 45.14
	12100.00	78.51	179.83	11804.67	534.41	-533.44	328.52	8.00	400767.09	671589.70	N 32 6 2.21 W	103 46 45.14
	12200.00	86.51	179.83	11817.69	633.48	-632.51	328.81	8.00	400689.03	671589.99	N 32 6 1.23 W	103 46 45.15
Landing Point	12248.65	90.40	179.83	11819.00	682.10	-681.12	328.96	8.00	400619.42	671590.14	N 32 6 0.74 W	103 46 45.15
	12300.00	90.40	179.83	11818.64	733.45	-732.48	329.11	0.00	400568.07	671590.29	N 32 6 0.24 W	103 46 45.15
	12400.00	90.40	179.83	11817.93	833.45	-832.47	329.40	0.00	400468.08	671590.58	N 32 6 5.92 W	103 46 45.15
	12500.00	90.40	179.83	11817.22	933.44	-932.47	329.70	0.00	400368.08	671590.88	N 32 6 5.58 W	103 46 45.15
	12600.00	90.40	179.83	11816.52	1033.44	-1032.47	329.99	0.00	400268.09	671591.17	N 32 6 5.27 W	103 46 45.16
	12700.00	90.40	179.83	11815.81	1133.44	-1132.46	330.28	0.00	400168.10	671591.46	N 32 6 5.56 W	103 46 45.16
	12800.00	90.40	179.83	11815.10	1233.44	-1232.46	330.58	0.00	400068.11	671591.76	N 32 6 5.55 W	103 46 45.16
	12900.00	90.40	179.83	11814.40	1333.43	-1332.46	330.87	0.00	399968.12	671592.05	N 32 6 5.54 W	103 46 45.16
	13000.00	90.40	179.83	11813.69	1433.43	-1432.46	331.17	0.00	399868.13	671592.35	N 32 6 5.53 W	103 46 45.17
	13100.00	90.40	179.83	11812.98	1533.43	-1532.45	331.46	0.00	399768.14	671592.64	N 32 6 5.52 W	103 46 45.17
	13200.00	90.40	179.83	11812.28	1633.43	-1632.45	331.75	0.00	399668.15	671592.93	N 32 6 5.51 W	103 46 45.17
	13300.00	90.40	179.83	11811.57	1733.42	-1732.45	332.05	0.00	399568.16	671593.23	N 32 6 5.50 W	103 46 45.17
	13400.00	90.40	179.83	11810.87	1833.42	-1832.44	332.34	0.00	399468.16	671593.52	N 32 6 5.49 W	103 46 45.18
	13500.00	90.40	179.83	11810.16	1933.42	-1932.44	332.64	0.00	399368.17	671593.82	N 32 6 5.48 W	103 46 45.18
	13600.00	90.40	179.83	11809.45	2033.42	-2032.44	332.93	0.00	399268.18	671594.11	N 32 6 5.47 W	103 46 45.18
	13700.00	90.40	179.83	11808.75	2133.41	-2132.44	333.23	0.00	399168.19	671594.41	N 32 6 5.46 W	103 46 45.18
	13800.00	90.40	179.83	11808.04	2233.41	-2232.43	333.52	0.00	399068.20	671594.70	N 32 6 5.45 W	103 46 45.19
	13900.00	90.40	179.83	11807.33	2333.41	-2332.43	333.81	0.00	398968.21	671594.99	N 32 6 5.44 W	103 46 45.19
	14000.00	90.40	179.83	11806.63	2433.41	-2432.43	334.11	0.00	398868.22	671595.29	N 32 6 5.43 W	103 46 45.19
	14100.00	90.40	179.83	11805.92	2533.40	-2532.42	334.40	0.00	398768.23	671595.58	N 32 6 5.42 W	103 46 45.19
	14200.00	90.40	179.83	11805.21	2633.40	-2632.42	334.70	0.00	398668.24	671595.88	N 32 6 5.41 W	103 46 45.20
	14300.00	90.40	179.83	11804.51	2733.40	-2732.42	334.99	0.00	398568.25	671596.17	N 32 6 5.40 W	103 46 45.20
	14400.00	90.40	179.83	11803.80	2833.40	-2832.42	335.28	0.00	398468.26	671596.46	N 32 6 5.39 W	103 46 45.20
	14500.00	90.40	179.83	11803.09	2933.39	-2932.41	335.58	0.00	398368.27	671596.76	N 32 6 5.38 W	103 46 45.20
	14600.00	90.40	179.83	11802.39	3033.39	-3032.41	335.87	0.00	398268.27	671597.05	N 32 6 5.37 W	103 46 45.21
	14700.00	90.40	179.83	11801.68	3133.39	-3132.41	336.17	0.00	398168.28	671597.35	N 32 6 5.36 W	103 46 45.21
	14800.00	90.40	179.83	11800.97	3233.39	-3232.40	336.46	0.00	398068.29	671597.64	N 32 6 5.35 W	103 46 45.21
	14900.00	90.40	179.83	11800.27	3333.39	-3332.40	336.75	0.00	397968.30	671597.93	N 32 6 5.34 W	103 46 45.21
	15000.00	90.40	179.83	11799.56	3433.38	-3432.40	337.05	0.00	397868.31			

Comments	MD (ft)	Incl (°)	Azim Grid (°)	TVD (ft)	VSEC (ft)	NS (ft)	EW (ft)	DLS (°/100ft)	Northing (ftUS)	Easting (ftUS)	Latitude (N/S ° ' '')	Longitude (E/W ° ' '')
	18100.00	90.40	179.83	11777.66	6533.31	-6532.31	3461.7	0.00	394768.58	671607.34	N 32 5 2.84	W 103 46 45.30
	18200.00	90.40	179.83	11778.95	6633.30	-6632.30	3461.46	0.00	394668.59	671607.64	N 32 5 1.85	W 103 46 45.30
	18300.00	90.40	179.83	11778.25	6733.30	-6732.30	3467.5	0.00	394568.60	671607.93	N 32 5 0.86	W 103 46 45.30
	18400.00	90.40	179.83	11775.54	6833.30	-6832.30	3471.05	0.00	394468.61	671608.23	N 32 4 59.87	W 103 46 45.30
	18500.00	90.40	179.83	11774.83	6933.30	-6932.30	3471.34	0.00	394368.62	671608.52	N 32 4 58.88	W 103 46 45.31
	18600.00	90.40	179.83	11774.13	7033.29	-7032.29	3471.64	0.00	394268.62	671608.82	N 32 4 57.89	W 103 46 45.31
	18700.00	90.40	179.83	11773.42	7133.29	-7132.29	3471.93	0.00	394168.63	671609.11	N 32 4 56.91	W 103 46 45.31
	18800.00	90.40	179.83	11772.72	7233.29	-7232.29	3482.22	0.00	394068.64	671609.40	N 32 4 55.92	W 103 46 45.31
	18900.00	90.40	179.83	11772.01	7333.29	-7332.28	3482.52	0.00	393968.65	671609.70	N 32 4 54.93	W 103 46 45.32
	19000.00	90.40	179.83	11771.30	7433.28	-7432.28	3481.81	0.00	393868.66	671610.00	N 32 4 53.94	W 103 46 45.32
	19100.00	90.40	179.83	11770.60	7533.28	-7532.28	3491.11	0.00	393768.67	671610.29	N 32 4 52.95	W 103 46 45.32
	19200.00	90.40	179.83	11769.89	7633.28	-7632.27	3491.40	0.00	393668.68	671610.59	N 32 4 51.96	W 103 46 45.32
	19300.00	90.40	179.83	11769.18	7733.28	-7732.27	3491.69	0.00	393568.69	671610.87	N 32 4 50.97	W 103 46 45.33
	19400.00	90.40	179.83	11768.48	7833.27	-7832.27	3491.99	0.00	393468.70	671611.17	N 32 4 49.98	W 103 46 45.33
	19500.00	90.40	179.83	11767.77	7933.27	-7932.27	3502.28	0.00	393368.71	671611.46	N 32 4 48.99	W 103 46 45.33
	19600.00	90.40	179.83	11767.07	8033.27	-8032.26	3502.58	0.00	393268.72	671611.76	N 32 4 48.00	W 103 46 45.33
	19700.00	90.40	179.83	11766.36	8133.27	-8132.26	3502.87	0.00	393168.72	671612.05	N 32 4 47.01	W 103 46 45.34
	19800.00	90.40	179.83	11765.65	8233.26	-8232.26	3511.16	0.00	393068.73	671612.34	N 32 4 46.02	W 103 46 45.34
	19900.00	90.40	179.83	11764.94	8333.26	-8332.25	3511.46	0.00	392968.74	671612.64	N 32 4 45.03	W 103 46 45.34
	20000.00	90.40	179.83	11764.24	8433.26	-8432.25	3511.75	0.00	392868.75	671612.93	N 32 4 44.04	W 103 46 45.35
	20100.00	90.40	179.83	11763.53	8533.26	-8532.25	3521.05	0.00	392768.76	671613.23	N 32 4 43.05	W 103 46 45.35
	20200.00	90.40	179.83	11762.82	8633.25	-8632.25	3521.34	0.00	392668.77	671613.52	N 32 4 42.06	W 103 46 45.35
	20300.00	90.40	179.83	11762.12	8733.25	-8732.24	3521.64	0.00	392568.78	671613.81	N 32 4 41.07	W 103 46 45.35
	20400.00	90.40	179.83	11761.41	8833.25	-8832.24	3521.93	0.00	392468.78	671614.11	N 32 4 40.08	W 103 46 45.36
	20500.00	90.40	179.83	11760.71	8933.25	-8932.24	3532.22	0.00	392368.79	671614.40	N 32 4 39.09	W 103 46 45.36
	20600.00	90.40	179.83	11760.00	9033.24	-9032.23	3532.52	0.00	392268.80	671614.70	N 32 4 38.10	W 103 46 45.36
	20700.00	90.40	179.83	11759.29	9133.24	-9132.23	3531.81	0.00	392168.81	671615.00	N 32 4 37.11	W 103 46 45.36
	20800.00	90.40	179.83	11758.59	9233.24	-9232.23	3541.11	0.00	392068.82	671615.29	N 32 4 36.13	W 103 46 45.37
	20900.00	90.40	179.83	11757.88	9333.24	-9332.22	3541.40	0.00	391968.83	671615.58	N 32 4 35.14	W 103 46 45.37
	21000.00	90.40	179.83	11757.17	9433.23	-9432.22	3541.69	0.00	391868.84	671615.87	N 32 4 34.15	W 103 46 45.37
	21100.00	90.40	179.83	11756.47	9533.23	-9532.22	3541.99	0.00	391768.85	671616.17	N 32 4 33.16	W 103 46 45.37
	21200.00	90.40	179.83	11755.76	9633.23	-9632.22	3552.28	0.00	391668.86	671616.46	N 32 4 32.17	W 103 46 45.38
	21300.00	90.40	179.83	11755.05	9733.23	-9732.21	3552.58	0.00	391568.86	671616.76	N 32 4 31.18	W 103 46 45.38
	21400.00	90.40	179.83	11754.35	9833.22	-9832.21	3552.87	0.00	391468.87	671617.05	N 32 4 30.19	W 103 46 45.38
	21500.00	90.40	179.83	11753.64	9933.22	-9932.21	3552.16	0.00	391368.88	671617.34	N 32 4 29.20	W 103 46 45.38
	21600.00	90.40	179.83	11752.93	10033.22	-10032.20	3552.46	0.00	391268.89	671617.64	N 32 4 28.21	W 103 46 45.39
	21700.00	90.40	179.83	11752.23	10133.22	-10132.20	3552.75	0.00	391168.90	671617.93	N 32 4 27.22	W 103 46 45.39
	21800.00	90.40	179.83	11751.52	10233.21	-10232.20	3552.05	0.00	391068.91	671618.23	N 32 4 26.23	W 103 46 45.39
	21900.00	90.40	179.83	11750.81	10333.21	-10332.20	3552.34	0.00	390968.92	671618.52	N 32 4 25.24	W 103 46 45.39
	22000.00	90.40	179.83	11750.11	10433.21	-10432.19	3552.63	0.00	390868.93	671618.81	N 32 4 24.25	W 103 46 45.40
	22100.00	90.40	179.83	11749.40	10533.21	-10532.19	3552.93	0.00	390768.94	671619.11	N 32 4 23.26	W 103 46 45.40
	22200.00	90.40	179.83	11748.70	10633.20	-10632.19	3552.22	0.00	390668.94	671619.40	N 32 4 22.27	W 103 46 45.40
	22300.00	90.40	179.83	11747.99	10733.20	-10732.18	3552.52	0.00	390568.95	671619.70	N 32 4 21.28	W 103 46 45.40
	22400.00	90.40	179.83	11747.28	10833.20	-10832.18	3552.81	0.00	390468.96	671620.00	N 32 4 20.29	W 103 46 45.41
	22500.00	90.40	179.83	11746.58	10933.20	-10932.18	3552.11	0.00	390368.97	671620.29	N 32 4 19.30	W 103 46 45.41
	22600.00	90.40	179.83	11745.87	11033.19	-11032.18	3552.40	0.00	390268.98	671620.59	N 32 4 18.31	W 103 46 45.41
	22700.00	90.40	179.83	11745.16	11133.19	-11132.17	3552.69	0.00	390168.99	671620.87	N 32 4 17.32	W 103 46 45.41
	22800.00	90.40	179.83	11744.46	11233.19	-11232.17	3552.99	0.00	390069.00	671621.17	N 32 4 16.33	W 103 46 45.42
	22900.00	90.40	179.83	11743.75	11333.19	-11332.17	3552.28	0.00	389969.01	671621.46	N 32 4 15.34	W 103 46 45.42
	23000.00	90.40	179.83	11743.04	11433.18	-11432.16	3552.58	0.00	389869.02	671621.75	N 32 4 14.35	W 103 46 45.42
	23100.00	90.40	179.83	11742.34	11533.18	-11532.16	3552.87	0.00	389769.02	671622.05	N 32 4 13.37	W 103 46 45.42
	23200.00	90.40	179.83	11741.63	11633.18	-11632.16	3552.16	0.00	389669.03	671622.34	N 32 4 12.38	W 103 46 45.43
	23300.00	90.40	179.83	11740.92	11733.18	-11732.15	3552.46	0.00	389569.04	671622.64	N 32 4 11.39	W 103 46 45.43
	23400.00	90.40	179.83	11740.22	11833.17	-11832.15	3552.75	0.00	389469.05	671622.93	N 32 4 10.40	W 103 46 45.43
	23500.00	90.40	179.83	11739.51	11933.17	-11932.15	3552.05	0.00	389369.06	671623.22	N 32 4 9.41	W 103 46 45.43
	23600.00	90.40	179.83	11738.80	12033.17	-12032.15	3552.34	0.00	389269.07	671623.52	N 32 4 8.42	W 103 46 45.44
	23700.00	90.40	179.83	11738.10	12133.17	-12132.14	3552.63	0.00	389169.08	671623.81	N 32 4 7.43	W 103 46 45.44
	23800.00	90.40	179.83	11737.39	12233.16	-12232.14	3552.93	0.00	389069.09	671624.11	N 32 4 6.44	W 103 46 45.44
	23900.00	90.40	179.83	11736.69	12333.16	-12332.14	3552.22	0.00	388969.10	671624.40	N 32 4 5.45	W 103 46 45.44
	24000.00	90.40	179.83	11735.98	12433.16	-12432.13	3552.52	0.00	388869.11	671624.70	N 32 4 4.46	W 103 46 45.45
	24100.00	90.40	179.83	11735.27	12533.16	-12532.13	3552.81	0.00	388769.12	671625.00	N 32 4 3.47	W 103 46 45.45
	24200.00	90.40	179.83	11734.57	12633.15	-12632.13	3552.10	0.00	388669.13	671625.29	N 32 4 2.48	W 103 46 45.45
	24300.00	90.40	179.83	11733.86	12733.15	-12732.13	3552.40	0.00	388569.14	671625.58	N 32 4 1.49	W 103 46 45.45
	24400.00	90.40	179.83	11733.15	12833.15	-12832.12	3552.69	0.00	388469.15	671625.87	N 32 4 0.50	W 103 46 45.46
	24500.00	90.40	179.83	11732.45	12933.15	-12932.12	3552.99	0.00	388369.16	671626.17	N 32 3 59.51	W 103 46 45.46
	24600.00	90.40	179.83	11731.74	13033.14	-13032.12	3552.28	0.00	388269.17	671626.46	N 32 3 58.52	W 103 46 45.46
	24700.00	90.40	179.83	11731.03	13133.14	-13132.11	3552.58	0.00	388169.18	671626.75	N 32 3 57.53	W 103 46 45.46
	24800.00	90.40	179.83	11730.33	13233.14	-13232.11	3552.87	0.00	388069.19	671627.05	N 32 3 56.54	W 103 46 45.47
	24900.00	90.40	179.83	11729.62	13333.14	-13332.11	3552.16	0.00	387969.20	671627.34	N 32 3 55.55	W 103 46 45.47
XTO Energy PLU 28 BS 106H - PBHL	24987.79	90.40	179.83	11729.00	13420.92	-13419.90	366.42	0.00	387881.40	671627.60	N 32 3 54.58	W 103 46 45.47

Survey Type: Non-Def Plan

Survey Error Model: ICSWSA Rev 0 *** 3-D 95.000% Confidence 2.7955 sigma
Survey Program:

Description	Part	MD From (ft)	MD To (ft)	EOU Freq (ft)	Hole Size Casing Diameter (in)	Expected Max Inclination (deg)	Survey Tool Type	Borehole / Survey
	1	0.000	30.000	1/100.000	30.000	30.000	NAL_MWD_IFR1+MS-Depth Only	PLU 28 BS 106H / XTO Energy PLU 28 BS 106H Rev0 JP 15May19
	1	30.000	24987.791	1/100.000	30.000	30.000	NAL_MWD_IFR1+MS	PLU 28 BS 106H / XTO Energy PLU 28 BS 106H Rev0 JP

PECOS DISTRICT DRILLING CONDITIONS OF APPROVAL

OPERATOR'S NAME:	XTO Permian Operating, LLC.
LEASE NO.:	NMLC-063136A
WELL NAME & NO.:	Poker Lake Unit 28 BS 106H
SURFACE HOLE FOOTAGE:	2310 FNL & 1920' FEL
BOTTOM HOLE FOOTAGE:	0200' FSL & 1590' FEL Sec. 04, T. 26 S., R 31 E.
LOCATION:	Section 28, T. 25 S., R 31 E., NMPM
COUNTY:	Eddy County, New Mexico

Commercial Well Determination

A commercial well determination shall be submitted after production has been established for at least six months.

Unit Wells

The well sign for a unit well shall include the unit number in addition to the surface and bottom hole lease numbers. This also applies to participating area numbers. If a participating area has not been established, the operator can use the general unit designation, but will replace the unit number with the participating area number when the sign is replaced.

A. DRILLING OPERATIONS REQUIREMENTS

The BLM is to be notified in advance for a representative to witness:

- a. Spudding well (minimum of 24 hours)
- b. Setting and/or Cementing of all casing strings (minimum of 4 hours)
- c. BOPE tests (minimum of 4 hours)

☒ **Eddy County**

Call the Carlsbad Field Office, 620 East Greene St., Carlsbad, NM 88220,
(575) 361-2822

1. A Hydrogen Sulfide (H₂S) Drilling Plan shall be activated 500 feet prior to drilling into the Delaware formation. **As a result, the Hydrogen Sulfide area must meet Onshore Order 6 requirements, which includes equipment and personnel/public protection items. If Hydrogen Sulfide is encountered, please provide measured values and formations to the BLM.**
2. Unless the production casing has been run and cemented or the well has been properly plugged, the drilling rig shall not be removed from over the hole without prior approval. **If the drilling rig is removed without approval – an Incident of Non-Compliance will be written and will be a “Major” violation.**

3. Floor controls are required for 3M or Greater systems. These controls will be on the rig floor, unobstructed, readily accessible to the driller and will be operational at all times during drilling and/or completion activities. Rig floor is defined as the area immediately around the rotary table; the area immediately above the substructure on which the draw works is located, this does not include the dog house or stairway area.
4. The record of the drilling rate along with the GR/N well log run from TD to surface (horizontal well – vertical portion of hole) shall be submitted to the BLM office as well as all other logs run on the borehole 30 days from completion. If available, a digital copy of the logs is to be submitted in addition to the paper copies. The Rustler top and top and bottom of Salt are to be recorded on the Completion Report.

B. CASING

Changes to the approved APD casing program need prior approval if the items substituted are of lesser grade or different casing size or are Non-API. The Operator can exchange the components of the proposal with that of superior strength (i.e. changing from J-55 to N-80, or from 36# to 40#). Changes to the approved cement program need prior approval if the altered cement plan has less volume or strength or if the changes are substantial (i.e. Multistage tool, ECP, etc.). The initial wellhead installed on the well will remain on the well with spools used as needed.

Centralizers required on surface casing per Onshore Order 2.III.B.1.f.

Wait on cement (WOC) for Water Basin:

After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi at the shoe, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. See individual casing strings for details regarding lead cement slurry requirements.

Provide compressive strengths including hours to reach required 500 pounds compressive strength prior to cementing each casing string. Have well specific cement details onsite prior to pumping the cement for each casing string.

No pea gravel permitted for remedial or fall back remedial without prior authorization from the BLM engineer.

Medium Cave/Karst

Possibility of water flows in the Salado and Castile.

Possibility of lost circulation in the Red beds, Rustler, and Delaware.

Abnormal pressures may be encountered upon penetrating the 3rd Bone Spring Sandstone and all subsequent formations.

1. The 13-3/8 inch surface casing shall be set at approximately 1240 feet (in a competent bed below the Magenta Dolomite, which is a Member of the Rustler, and if salt is encountered, set casing at least 25 feet above the salt) and cemented to the surface.
 - a. If cement does not circulate to the surface, the appropriate BLM office shall be notified and a temperature survey utilizing an electronic type temperature survey with surface log readout will be used or a cement bond log shall be run to verify the top of the cement. Temperature survey will be run a minimum of six hours after pumping cement and ideally between 8-10 hours after completing the cement job.
 - b. Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry.
 - c. Wait on cement (WOC) time for a remedial job will be a minimum of 4 hours after bringing cement to surface or 500 pounds compressive strength, whichever is greater.
 - d. If cement falls back, remedial cementing will be done prior to drilling out that string.

Formation below the 13-3/8" shoe to be tested according to Onshore Order 2.III.B.1.i. Test to be done as a mud equivalency test using the mud weight necessary for the pore pressure of the formation below the shoe and the mud weight for the bottom of the hole. Report results to BLM office.

Intermediate casing shall be kept fluid filled while running into hole to meet BLM minimum collapse requirements.

2. The minimum required fill of cement behind the 9-5/8 inch intermediate casing is:

Operator has proposed DV tool at depth of 4922', but will adjust cement proportionately if moved. DV tool shall be set a minimum of 50' below previous shoe and a minimum of 200' above current shoe. Operator shall submit sundry if DV tool depth cannot be set in this range. If an ECP is used, it is to be set a minimum of 50' below the shoe to provide cement across the shoe. If it cannot be set below the shoe, a CBL shall be run to verify cement coverage.

- a. First stage to DV tool:

☒ Cement to circulate. If cement does not circulate, contact the appropriate BLM office before proceeding with second stage cement job. Operator should have plans as to how they will achieve circulation on the next stage.

- b. Second stage above DV tool:

☒ Cement to surface. If cement does not circulate, contact the appropriate BLM office.

Formation below the 9-5/8" shoe to be tested according to Onshore Order 2.III.B.1.i. Test to be done as a mud equivalency test using the mud weight necessary for the pore pressure of the formation below the shoe (not the mud weight required to prevent dissolving the salt formation) and the mud weight for the bottom of the hole. Report results to BLM office.

Centralizers required through the curve and a minimum of one every other joint.

3. The minimum required fill of cement behind the 5-1/2 inch production casing is:

☒ Cement should tie-back at least 200 feet into previous casing string. Operator shall provide method of verification. **Excess calculates to 20% - Additional cement may be required.**

4. If hardband drill pipe is rotated inside casing, returns will be monitored for metal. If metal is found in samples, drill pipe will be pulled and rubber protectors which have a larger diameter than the tool joints of the drill pipe will be installed prior to continuing drilling operations.

C. PRESSURE CONTROL

1. All blowout preventer (BOP) and related equipment (BOPE) shall comply with well control requirements as described in Onshore Oil and Gas Order No. 2 and API 53.
2. Variance approved to use flex line from BOP to choke manifold. Check condition of flexible line from BOP to choke manifold, replace if exterior is damaged or if line fails test. Line to be as straight as possible with no hard bends and is to be anchored according to Manufacturer's requirements. The flexible hose can be exchanged with a hose of equal size and equal or greater pressure rating. **Anchor requirements, specification sheet and hydrostatic pressure test certification matching the hose in service, to be onsite for review. These documents shall be posted in the company man's trailer and on the rig floor.** If the BLM inspector questions the straightness of the hose, a BLM engineer will be contacted and will review in the field or via picture supplied by inspector to determine if changes are required (operator shall expect delays if this occurs).

3. **Operator has proposed a multi-bowl wellhead assembly. This assembly will only be tested when installed on the surface casing. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be 5000 (5M) psi.**
- a. **Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.**
 - b. **If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.**
 - c. **Manufacturer representative shall install the test plug for the initial BOP test.**
 - d. **Operator shall perform the intermediate casing integrity test to 70% of the casing burst. This will test the multi-bowl seals.**
 - e. **If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.**

5M system requires an HCR valve, remote kill line and annular to match. The remote kill line is to be installed prior to testing the system and tested to stack pressure.

4. **The appropriate BLM office shall be notified a minimum of 4 hours in advance for a representative to witness the tests.**
- a. **In a water basin, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. The casing cut-off and BOP installation can be initiated four hours after installing the slips, which will be approximately six hours after bumping the plug. For those casing strings not using slips, the minimum wait time before cut-off is eight hours after bumping the plug. BOP/BOPE testing can begin after cut-off or once cement reaches 500 psi compressive strength (including lead when specified), whichever is greater. However, if the float does not hold, cut-off cannot be initiated until cement reaches 500 psi compressive strength (including lead when specified).**
 - b. **The tests shall be done by an independent service company utilizing a test plug not a cup or J-packer.**
 - c. **The test shall be run on a 5000 psi chart for a 2-3M BOP/BOP, on a 10000 psi chart for a 5M BOP/BOPE and on a 15000 psi chart for a 10M BOP/BOPE. If a linear chart is used, it shall be a one hour chart. A circular chart shall have a maximum 2 hour clock. If a twelve hour or twenty-four hour chart is used, tester shall make a notation that it is run with a two hour clock.**

- d. The results of the test shall be reported to the appropriate BLM office.
- e. All tests are required to be recorded on a calibrated test chart. **A copy of the BOP/BOPE test chart and a copy of independent service company test will be submitted to the appropriate BLM office.**
- f. The BOP/BOPE test shall include a low pressure test from 250 to 300 psi. The test will be held for a minimum of 10 minutes if test is done with a test plug and 30 minutes without a test plug. This test shall be performed prior to the test at full stack pressure.
- g. BOP/BOPE must be tested by an independent service company within 500 feet of the top of the **Wolfcamp** formation if the time between the setting of the intermediate casing and reaching this depth exceeds 20 days. This test does not exclude the test prior to drilling out the casing shoe as per Onshore Order No. 2.

D. DRILLING MUD

Mud system monitoring equipment, with derrick floor indicators and visual and audio alarms, shall be operating before drilling into the **Wolfcamp** formation, and shall be used until production casing is run and cemented.

E. DRILL STEM TEST

If drill stem tests are performed, Onshore Order 2.III.D shall be followed.

F. WASTE MATERIAL AND FLUIDS

All waste (i.e. drilling fluids, trash, salts, chemicals, sewage, gray water, etc.) created as a result of drilling operations and completion operations shall be safely contained and disposed of properly at a waste disposal facility. No waste material or fluid shall be disposed of on the well location or surrounding area.

Porto-johns and trash containers will be on-location during fracturing operations or any other crew-intensive operations.

JAM 011320
