

30-015-38144


CEMENT JOB REPORT



CUSTOMER Lynx Petroleum Consultants Inc			DATE 01-JAN-11		F.R. # 700610052		SERV. SUPV. RICHARD B ANEZ					
LEASE & WELL NAME EDDY BD ST. #3			LOCATION SEC32-T20S-R30E				COUNTY-PARISH-BLOCK Eddy New Mexico					
DISTRICT Artesia			DRILLING CONTRACTOR RIG # MCVAY #4				TYPE OF JOB Intermediate					
SIZE & TYPE OF PLUGS			LIST-CSG-HARDWARE			PHYSICAL SLURRY PROPERTIES						
9-5/8" Top Cem Plug, Nitrile cvr, Phc			Float Collar, Al Flap, 9-5/8 - 8rd			SACKS OF CEMENT	SLURRY WGT PPG	SLURRY YLD FT ³	WATER GPS	PUMP TIME HR:MIN	Bbl SLURRY	Bbl MIX WATER
			Guide Shoe, Cement Nose, 9-5/8 i									
MATERIALS FURNISHED BY BJ												
FRESH WATER						0	8.34	1	0	00:00	10	0
35-65-4C+5%MPA-5+.5%SMS+5%SALT+5#LCM-1+1/8#CF						885	12.7	1.99	10.25	03:42	303	208.64
C+.1%R-3						300	14.8	1.33	6.33	02:54	71	45.17
FRESH WATER						0	8.34	1	0	00:00	296.6	0
Available Mix Water 1000 Bbl. Available Displ. Fluid 1000 Bbl.						TOTAL			680.6 253.82			
HOLE			TBG-CSG-D.P.					COLLAR DEPTHS				
SIZE	% EXCESS	DEPTH	SIZE	WGT.	TYPE	DEPTH	GRADE	SHOE	FLOAT	STAGE		
12.25	0	3898	9.625	36	CSG	3904	J-55	3904	3837	0		
LAST CASING			PKR-CMT RET-BR PL-LINER			PERF. DEPTH		TOP CONN		WELL FLUID		
SIZE	WGT	TYPE	DEPTH	BRAND & TYPE		DEPTH	TOP	BTM	SIZE	THREAD	TYPE	WGT.
13.38	48	CSG	1468	NO PACKER		0	0	0	9.625	BUTT		
DISPL. VOLUME		DISPL. FLUID		CAL. PSI	CAL. MAX PSI	OP. MAX	MAX TBG PSI		MAX CSG PSI		MIX WATER	
VOLUME	UOM	TYPE	WGT.	BUMP PLUG	TO REV.	SQ. PSI	RATED	Operator	RATED	Operator		
296.6	BBLs	FRESH WATER	8.34	1006	0	0	0	0	3520	2816	RIG	
EXPLANATION: TROUBLE SETTING TOOL, RUNNING CSG, ETC. PRIOR TO CEMENTING: NONE												
PRESSURE/RATE DETAIL						EXPLANATION						
TIME HR:MIN.	PRESSURE - PSI		RATE BPM	Bbl. FLUID PUMPED	FLUID TYPE	SAFETY MEETING: BJ CREW ☒ CO. REP. ☒						
	PIPE	ANNULUS				TEST LINES 3400 PSI						
						CIRCULATING WELL - RIG ☒ BJ ☐						
08:00	0	0	0	0	0	YARD UP.						
10:00	0	0	0	0	0	LV YARD.						
11:00	0	0	0	0	0	ARRIVE LOC. HAZZARD ASSESSMENT.						
12:00	0	0	0	0	0	PRIME UP LOOP TEST.						
12:30	0	0	0	0	0	WAITING ON GUIDE SHOE.						
14:00	0	0	0	0	0	RUNNING CASING.						
19:50	0	0	0	0	0	PRE JOB SAFETY MEETING.						
20:05	3400	0	.5	.5	H2O	TEST LINES						
20:10	215	0	5	10	H2O	SPACER						
20:15	206	0	5	303	CMT	LEAD SLURRY						
21:20	283	0	5	71	CMT	TAIL SLURRY						
21:40	0	0	0	0	CMT	SHUT DOWN DROP PLUG.						
21:45	1789	0	7	287	H2O	DISPLACEMENT						
22:15	2050	0	3	10	H2O	SLOW RATE.						
22:20	2520	0	3	0	H2O	PLUG DOWN, FLOAT DIDN'T HOLD, DID NOT CIRCULATE CMT.						
23:00	0	0	0	0	0	WAIT 12 HRS. ON TEMPERATURE SURVEY.						
10:15	0	0	0	0	0	TEMP SURVEY. FOUND CMT AT 100'. OK TO RIG DOWN.						
00:00	0	0	0	0	0	THANK YOU RICHARD AND CREW.						
BUMPED PLUG	PSI TO BUMP PLUG	TEST FLOAT EQUIP.	BBL.CMT RETURNS/ REVERSED	TOTAL BBL. PUMPED	PSI LEFT ON CSG	SPOT TOP OUT CEMENT	SERVICE SUPERVISOR SIGNATURE:					
☒ Y ☐ N	2520	☒ Y ☐ N	0	681	0	☒ Y ☐ N						



BJ Services JobMaster Program Version 3.50
Job Number: 700610052
Customer: LYNX PET. CONSULT.
Well Name: EDDY BD ST. #3

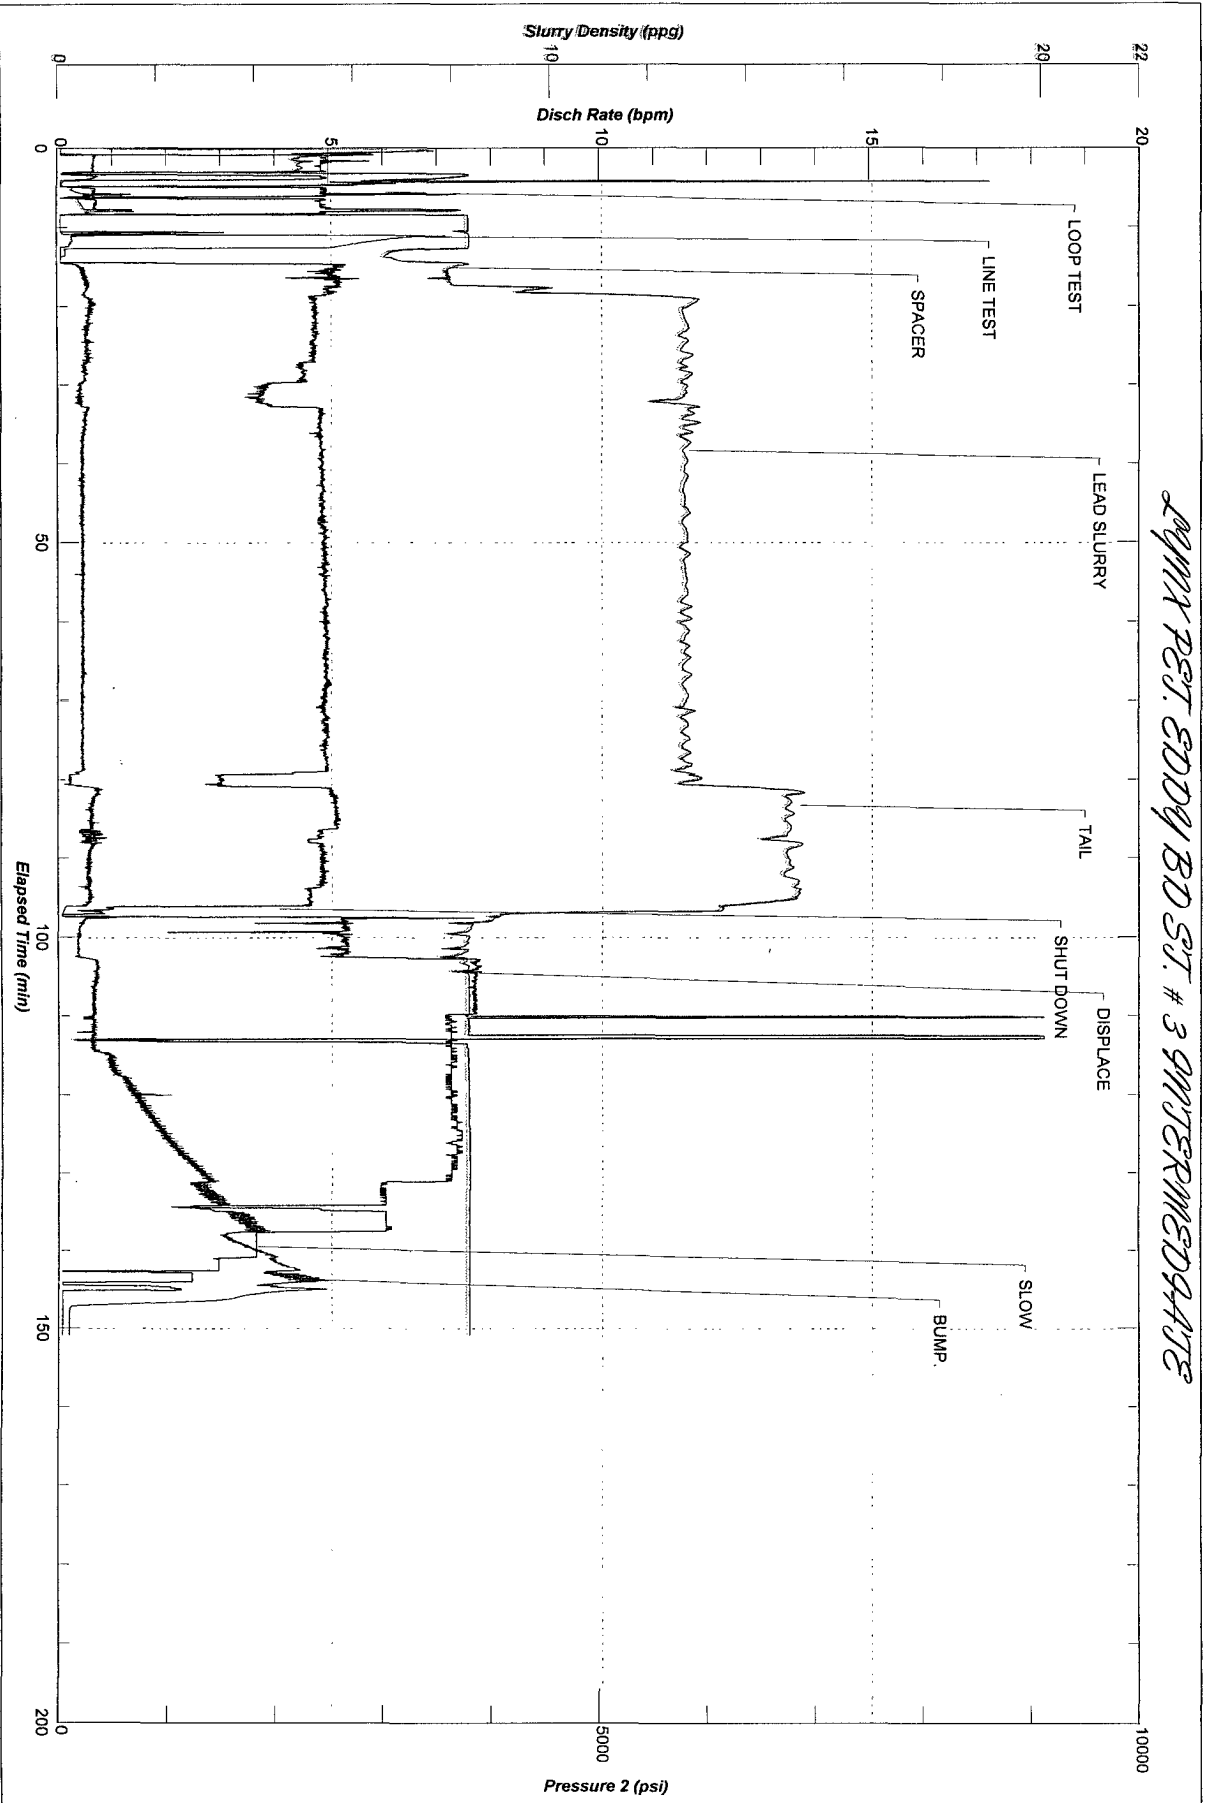

CEMENT JOB REPORT



CUSTOMER Lynx Petroleum Consultants Inc			DATE 27-JAN-11		F.R. # 722210014		SERV. SUPV. RICHARD B ANEZ					
LEASE & WELL NAME BD ST #3			LOCATION				COUNTY-PARISH-BLOCK Eddy New Mexico					
DISTRICT Artesia			DRILLING CONTRACTOR RIG # MCVAY # 4				TYPE OF JOB Long String					
SIZE & TYPE OF PLUGS			LIST-CSG-HARDWARE			PHYSICAL SLURRY PROPERTIES						
			Float Collar, AI Flap, 5-1/2 - 8rd			SACKS OF CEMENT	SLURRY WGT PPG	SLURRY YLD FT³	WATER GPS	PUMP TIME HR:MIN	Bbl SLURRY	Bbl MIX WATER
			Guide Shoe, Cement Nose, 5-1/2 i									
MATERIALS FURNISHED BY BJ												
MUD CLEAN 2						0	8.34	1	0	00:00	10	0
15-61-11CSE-2+.5%FL-52+.5%FL-25+.5%BA-58+.25%R-3+3						1,040	13.2	1.57	7.68	04:24	291	190.30
FRESH WATER						0	8.34	1	0	00:00	110	0
MUD						0	11	1	0	00:00	151	0
35-65-6H+.3%FL-52+.35%SMS+5%SALT+1/8#CF						645	12.5	2.05	11.26	04:16	235	172.56
H+.05%R-3						300	15.6	1.18	5.23	03:16	63	37.33
FRESH WATER						0	8.34	1	0	00:00	163	0
Available Mix Water 1500 Bbl. Available Displ. Fluid 1500 Bbl.									TOTAL		1023	400.19
HOLE			TBG-CSG-D.P.				COLLAR DEPTHS					
SIZE	% EXCESS	DEPTH	SIZE	WGT.	TYPE	DEPTH	GRADE	SHOE	FLOAT	STAGE		
8.75	0	11332	5.5	17	CSG	11335	P-110	11335	11257.27	1		
LAST CASING			PKR-CMT RET-BR PL-LINER			PERF. DEPTH		TOP CONN		WELL FLUID		
SIZE	WGT	TYPE	DEPTH	BRAND & TYPE		DEPTH	TOP	BTM	SIZE	THREAD	TYPE	WGT.
9.625	36	CSG	3898	NO PACKER		0	0	0	5.5	8RND	WATER BASED MU	11
DISPL. VOLUME		DISPL. FLUID		CAL. PSI	CAL. MAX PSI	OP. MAX	MAX TBG PSI		MAX CSG PSI		MIX WATER	
VOLUME	UOM	TYPE	WGT.	BUMP PLUG	TO REV.	SQ. PSI	RATED	Operator	RATED	Operator		
424	BBLS	FRESH WATER	8.34	1450	0	0	0	0	10640	8512	RIG	
		MUD	11									
EXPLANATION: TROUBLE SETTING TOOL, RUNNING CSG, ETC. PRIOR TO CEMENTING: NONE												
PRESSURE/RATE DETAIL							EXPLANATION					
TIME HR:MIN.	PRESSURE - PSI		RATE BPM	Bbl. FLUID PUMPED	FLUID TYPE	SAFETY MEETING: BJ CREW ☒ CO. REP. ☒						
	PIPE	ANNULUS				TEST LINES 5723 PSI						
						CIRCULATING WELL - RIG ☒ BJ ☒						
17:00	0	0	0	0	0	1-26-11 YARD UP.						
18:30	0	0	0	0	0	LV YARD.						
19:30	0	0	0	0	0	ARRIVE LOC. HAZZARD ASSESSMENT.						
19:35	0	0	0	0	0	SPOT EQUIP. MEETING RIG UP.						
22:30	0	0	0	0	0	PRE JOB SAFETY MEETING.						
22:35	0	0	0	0	0	PRIME UP, LOOP TEST.						
23:05	4480	0	.5	.5	H2O	TEST LINES.						
23:07	583	0	5	24	MUD CLN.	MUD CLEAN 2 SPACER.						
23:15	217	0	2.5	291	CMT	PUMPING CEMENT SLURRY						
00:30	0	0	0	0	0	WENT TO BULK TRUCK, SLURRY BECAME UNPUMPABLE.						
01:00	0	0	0	0	0	WENT TO 2ND PUMP.						
01:30	0	0	0	0	0	SWITCHED TO RIG TO PUMP TO PIT.						
04:30	0	0	0	0	0	RECIEVED REPLACEMENT SLURRY.						
07:15	0	0	0	0	0	PRE JOB SAFETY MEETING						
07:25	0	0	0	0	0	PRIME UP, LOOP TEST.						
07:45	5723	0	.5	.5	H2O	LINE TEST.						
07:47	546	0	5	24	MUD CLN.	MUD CLEAN 2 SPACER.						
07:55	996	0	7	291	CMT	1ST STG SLURRY.						
08:50	0	0	0	0	CMT	SHUT DOWN DROP PLUG WASH UP.						
09:00	1450	0	6	251	H2O	110 H2O, 241 MUD.						

CEMENT JOB REPORT



PRESSURE/RATE DETAIL						EXPLANATION	
TIME HR:MIN.	PRESSURE - PSI		RATE BPM	Bbl. FLUID PUMPED	FLUID TYPE	SAFETY MEETING: BJ CREW ☒ CO. REP. ☒	
	PIPE	ANNULUS				TEST LINES	5723 PSI
						CIRCULATING WELL - RIG ☒ BJ ☒	
10:15	1457	0	2	10	MUD	SLOW RATE.	
10:35	1905	0	2	0	MUD	PLUG DOWN.	
10:40	0	0	0	0	0	DROP BOMB.	
11:25	1144	0	2	1	MUD	OPEN TOOL.	
11:37	965	0	6	250	MUD	CIRCULATE OFF TOOL, 179 SKS.	
00:00	0	0	0	0	0	CLEAN UP WAIT ON CMT.	
13:15	0	0	0	0	0	PRE JOB SAFTY MEETING.	
13:53	3034	0	.5	.5	H2O	TEST LINES.	
13:55	129	0	5	5	H2O	FRESH WATER SPACER	
13:57	306	0	5	235	CMT	2ND STG LEAD SLURRY.	
14:45	390	0	5	63	CMT	TAIL SLURRY	
15:00	0	0	0	0	0	SHUT DOWN.	
15:05	1555	0	7	153	H2O	DISPLACEMENT	
15:30	1549	0	3	10	H2O	SLOW RATE.	
15:35	3430	0	3	0	H2O	PLUG DOWN.	
00:00	0	0	0	0	0	THANK YOU RICHARD AND CREW.	

BUMPED PLUG	PSI TO BUMP PLUG	TEST FLOAT EQUIP.	BBL.CMT RETURNS/ REVERSED	TOTAL BBL. PUMPED	PSI LEFT ON CSG	SPOT TOP OUT CEMENT	SERVICE SUPERVISOR SIGNATURE:
☒ Y ☐ N	1905	☒ Y ☐ N	50	846	0	☒ Y ☐ N	
