

NO. OF COPIES RECEIVED		
DISTRIBUTION		
ANTA FE	1	
ILE	1	✓
J.S.G.S.		
AND OFFICE		
OPERATOR	1	

NEW MEXICO OIL CONSERVATION COMMISSION

30-005-60925

Form C-103
Supersedes Old
C-102 and C-103
Effective 1-1-65

SUNDRY NOTICES AND REPORTS ON WELLS
(DO NOT USE THIS FORM FOR PROPOSALS TO DRILL OR TO RE-OPEN OR PLUG BACK TO A DIFFERENT USE. APPLICATION FOR PERMIT TO DRILL OR TO RE-OPEN OR PLUG BACK TO A DIFFERENT USE.)

OIL WELL ☒ GAS WELL ☐ OTHER ☐

Name of Operator
Carl A. Schellinger /

Address of Operator
P.O. Box 447, Roswell, New Mexico 88201

Location of Well
UNIT LETTER M 660 FEET FROM THE South LINE AND 660 FEET FROM
THE West LINE, SECTION 34 TOWNSHIP 8-S RANGE 27-E N.M.P.M.

15. Elevation (Show whether DF, RT, GR, etc.)
3871 GR 3882' KB

5a. Indicate Type of Lease
State ☒ Fee ☐

5. State Oil & Gas Lease No.
L-5347

7. Unit Agreement Name
Campbell Station Unit

8. Farm or Lease Name
Campbell Station Unit

9. Well No.
1

10. Field and Pool, or Wildcat
Wildcat

12. County
Chaves

Check Appropriate Box To Indicate Nature of Notice, Report or Other Data

NOTICE OF INTENTION TO:

PERFORM REMEDIAL WORK ☐ PLUG AND ABANDON ☐ REMEDIAL WORK ☐ ALTERING CASING ☐

TEMPORARILY ABANDON ☐ CHANGE PLANS ☐ COMMENCE DRILLING OPNS. ☒ PLUG AND ABANDONMENT ☐

WELL OR ALTER CASING ☐ OTHER ☐ CASING TEST AND CEMENT JOBS ☒

OTHER ☐

SUBSEQUENT REPORT OF:

7. Describe Proposed or Completed Operations (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work) SEE RULE 1103.

3/31/81: Osbourn Drilling Company, Rigged-up Cable Tools, Spudded 3:17 P.M.

4/14/81: TD 150', Moved off Cable Tools at 4:00 P.M.

5/4/81: TD 150' Reamed hole to 26" to depth of 42', Ran 40 feet of 20" conductor pipe, cemented to surface with 3 yards ready mix.

5/12/81: TD 345'; Bantam Drilling Company Rig No. 2 started operations @ 7:00 A.M. on 5/10/81, Drilled to 345', Ran 13 3/8" 48# casing to 345', Cemented with 365 sx Class C Cement, 1/4# Flo Cel, 2% CaCl; Circulated to surface, Plug down 3:45 P.M. 5/11/81, WOC, 18 hrs. pressured up to 500#, 1 hr. held OK. Prep to drill.

(NOTE: Blowout Preventer Diagram attached.)

I, hereby certify that the information above is true and complete to the best of my knowledge and belief.


APPROVED BY W.A. Gussitt TITLE Operator DATE 6/10/81

APPROVED BY W.A. Gussitt TITLE SUPERVISOR, DISTRICT II DATE JUL 16 1981

CONDITIONS OF APPROVAL, IF ANY:

BLOWOUT PREVENTER DIAGRAM

Shaffer Manual double 8" X 900 Series, 3000 WP
Regan Hydriil 10" Annular Preventer

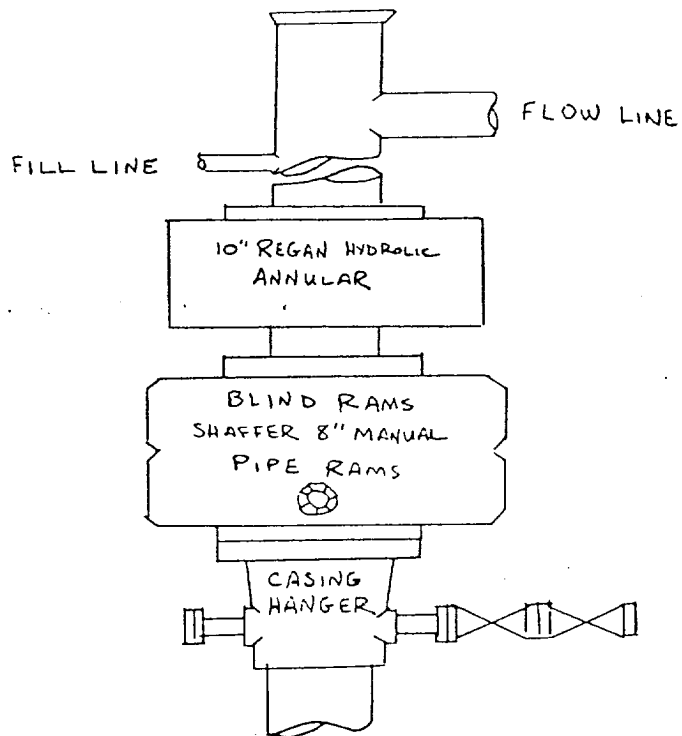

BANTAM DRILLING COMPANY, INC.

RIG No. 2
