

DISTRICT I
P.O. Box 1980, Hobbs, NM 88240

DISTRICT II
P.O. Drawer DD, Artesia, NM 88210

OIL CONSERVATION DIVISION
P.O. Box 2088
Santa Fe, New Mexico 87504-2088

INSTRUCTIONS ON REVERSE
SIDE

This form is not to be used for
reporting packer leakage tests in
Northwest New Mexico

SOUTHEAST NEW MEXICO PACKER LEAKAGE TEST

| | | | | | | | |
|---|----------------------|------------|--------------------------------|-----------------------------------|-------------------------------|---------------|--|
| Operator Yates Petroleum Corporation | | | Lease Siegenthaler "IS" Com | | | Well No. 1 | |
| Location of Well | Unit I | Sec. 21 | Twp 17 | Rge 26 | County Eddy | | |
| Name of Reservoir or Pool | | | Type of Prod. (Oil or Gas) | Method of Prod. Flow, Art Lift | Prod. Medium (Tbg. or Csg) | Choke Size | |
| Upper Compl | Kennedy Farms Atoka | | None | | CSG | | |
| Lower Compl | Kennedy Farms Morrow | | Gas | Compressor | TBG | | |

FLOW TEST NO. 1


Both zones shut-in at (hour, date): 08/12/2002 11:20am

Well opened at (hour, date): 08/13/2002 11:20am

| | Upper Completion | Lower Completion |
|--|---|---------------------|
| Indicate by (X) the zone producing..... | | XXX |
| Pressure at beginning of test..... | 412# | 340# |
| Stabilized? (Yes or No)..... | Yes | Yes |
| Maximum pressure during test..... | 413# | 340# |
| Minimum pressure during test..... | 390# | 20# |
| Pressure at conclusion of test..... | 392# | 23# |
| Pressure change during test (Maximum minus Minimum)..... | 23# | 320# |
| Was pressure change an increase or a decrease?..... | Decrease | Decrease |
| Well closed at (hour, date): 08/14/2002 11:20am | Total Time On Production 24 hours | |
| Oil Production During Test: 0 bbls; Grav. _____ | Gas Production During Test 87.5 MCF; GOR _____ | |
| Remarks Atoka not hooked up - Zone is not producing | | |

FLOW TEST NO. 2

| | Upper Completion | Lower Completion |
|--|--|---------------------|
| Well opened at (hour, date): _____ | | |
| Indicate by (X) the zone producing..... | | |
| Pressure at beginning of test..... | | |
| Stabilized? (Yes or No)..... | | |
| Maximum pressure during test..... | | |
| Minimum pressure during test..... | | |
| Pressure at conclusion of test..... | | |
| Pressure change during test (Maximum minus Minimum)..... | | |
| Was pressure change an increase or a decrease?..... | | |
| Well closed at (hour, date) _____ | Total time on Production _____ | |
| Oil production During Test: _____ bbls; Grav. _____ | Gas Production During Test _____ MCF; GOR _____ | |
| Remarks _____ | | |



OPERATOR CERTIFICATE OF COMPLIANCE

I hereby certify that the information contained herein is true
and completed to the best of my knowledge

Yates Petroleum Corporation

Operator

Signature

Don Norman/Wildcat Measurement Ser.

Printed Name

Title

08/22/2002

1-888-421-9453

Date

Telephone No.

OIL CONSERVATION DIVISION

Date Approved AUG 27 2002

By

Title

INSTRUCTIONS FOR SOUTHEAST NEW MEXICO PACKER LEAKAGE TEST


1. A packer leakage test shall be commenced on each multiply completed well within seven days after actual completion of the well, and annually thereafter as prescribed by the order authorizing the multiple completion. Such test shall also be commenced on all multiple completions within seven days following recompletion and/or chemical or fracture treatment, and whenever remedial work has been done on a well during which the packer or the tubing have been disturbed. Tests shall also be taken at any time that communication is suspected or when requested by the Division.
2. At least 72 hours prior to the commencement of any packer leakage test, the operator shall notify the Division in writing of the exact time the test is to be commenced. Offset operators shall also be so notified.
3. The packer leakage test shall commence when both zones of the dual completion are shut-in for pressure stabilization. Both zones shall remain shut-in until the well-head pressure in each has stabilized and for minimum of two hours thereafter, provided, however, that they need not remain shut-in more than 24 hours.
4. For Flow Test No. 1, one zone of the dual completion shall be produced at the normal rate of production while the other zone remains shut-in. Such test shall be continued until the flowing wellhead pressure has become stabilized and for minimum of two hours thereafter, provided however, that the flow test need not continue for more than 24 hours.
5. Following completion of Flow Test No. 1, the well shall again be shut-in, in accordance with Paragraph 3 above.
6. Flow Test No. 2 shall be conducted even though no leak was indicated during Flow Test No. 1. Procedure for Flow Test No. 2 is to be the same as for Flow Test No. 1 except that the previously produced zone shall remain shut-in while the previously shut-in zone is produced.
7. All pressures, throughout the entire test, shall be continuously measured and recorded with recording pressure gauges, the accuracy of which must be checked with deadweight tester at least twice, once at the beginning and once at the end, of each flow test.
8. The results of the above-described tests shall be filed in triplicate within 15 days after completion of the test. Tests shall be filed with the appropriate District Office of the New Mexico Oil Conservation Division on Southeast New Mexico Packer Leakage Test Form Revised 1-1-89, together with the original pressure recording gauge charts with all the deadweight pressures which were taken indicated thereon. In lieu of filing the aforesaid charts, the operator may construct a pressure versus time curve from each zone of each test, indicating thereon all pressure changes which may be reflected by the gauge charts as well as all deadweight pressure readings which were taken. If the pressure curve is submitted, the original chart must be permanently filed in the operator's office. Form C-116 shall also accompany the Packer Leakage Test Form when the test period coincides with a gas-oil ratio test period.

450
400
350
300
250
200
150
100
50

450
400
350
300
250
200
150
100
50

27.1 mF
1000*-Red 500*Blue
Red Lower 430.00
Blue 077.1
8-13-2002 8-14-2002
11:20 AM 11:20 AM
SIEGENTHALER IS COM #1
Flow-Lower
PACKER LEAKAGE TEST

05
001
150
005
050
300
350
400
450

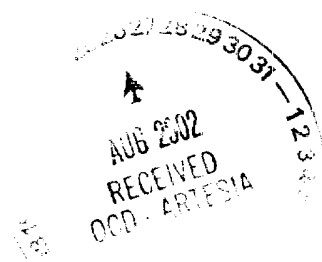

450
400
350
300
250
200
150
100
50

450
400
350
300
250
200
150
100
50

450
400
350
300
250
200
150
100
50

8

9

450

400

350

300

250

200

150

100

50

1000* RED 500* BLUE

RED LOWER

BLUE UPPER

8-12-2002

8-13-2002

11:20 AM

11:18 AM

SIEGENTHREE IS ON

SHUT IN

PAPER, ENGINE TEST

