

EOG MIDLAND

	DATE	TIME	TO/FROM	MODE	MIN/SEC	PGS	JOB#	STATUS
06	08/23	16:22	G. C. Timmermann	G3--S	01'27"	003	092	OK

EOG RESOURCES, INC.
1140' FNL & 1650' FWL
Sec.19-T17S-R28E

STARBUCK "19" FEDERAL COM. NO. 1
EDDY CO., NEW MEXICO
DECEMBER 13, 2000

WELLBORE SCHEMATIC

Spud: 11/24/00

- 14-3/4" Hole
 11-3/4" 42# H-40 ST&C @ 448'
 • 280sx Premium Plus/Econolite Cmt.
 • Circulate 87sx of cement to pit

TOC @ 3990.

- 11" Hole
 8-5/8" 32# J-55 ST&C @ 1,945'
 • 585sx Prem. Plus/Interfill Cmt.
 • Circulate 15sx of cement to pit


PLS packer w/on-off tool
 @ 6,711', SN @ 6,727'
 EOT @ 6,727'

- 7-7/8" Hole
 5-1/2" 17# N-80 LT&C @ 9,975'
 • 1125sx Econolite/Prem. 50/50 POZ Cmt.

	Lengths	Tops
1-Float Shoe	1.60'	9,973.40'
2-Shoe Jts.	92.32'	9,881.08'
1-Float Collar	1.40'	9,879.68'
221-5-1/2" Jts.	9,891.58'	(11.90)'
1-Cut-Off	28.38'	16.48'
KB	16.48'	0.00'

Marker Joint: 22.18' in length from 9,742' to 9,720'

TD @ 9,975' PBTD @ 9,742' (WL)

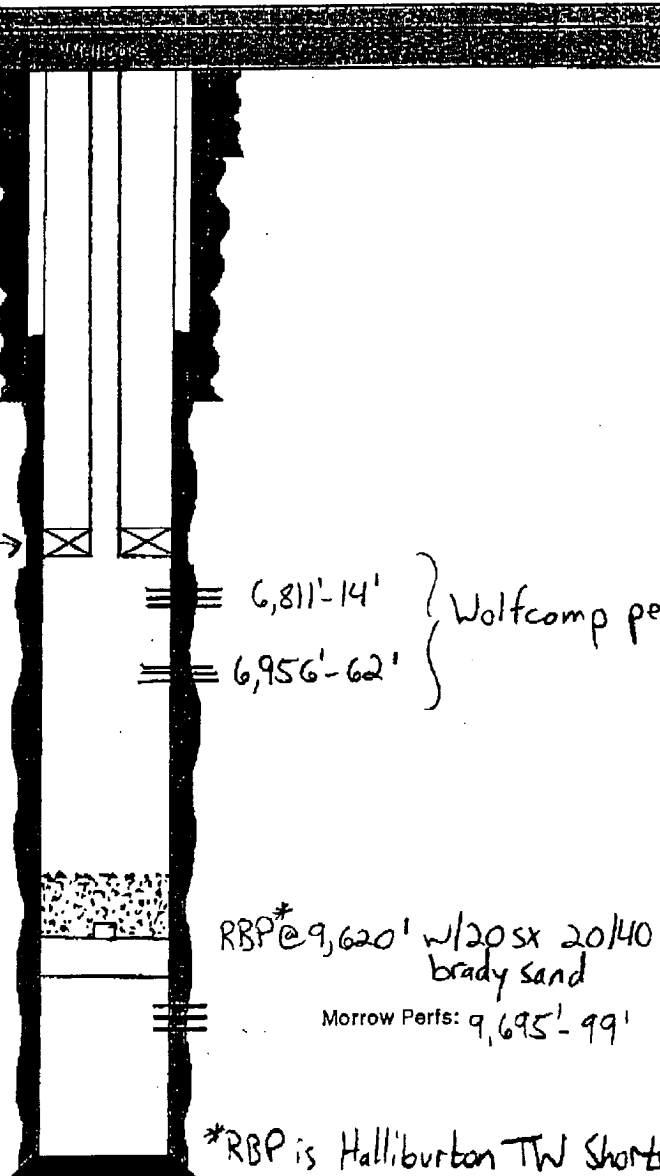

RBP @ 9,620' w/20sx 20/40
 brady sand

Morrow Perfs: 9,695'-99'

*RBP is Halliburton TW Shorty
 set on wireline
