


ACTUAL PLUG AND ABANDONMENT 11/1/95

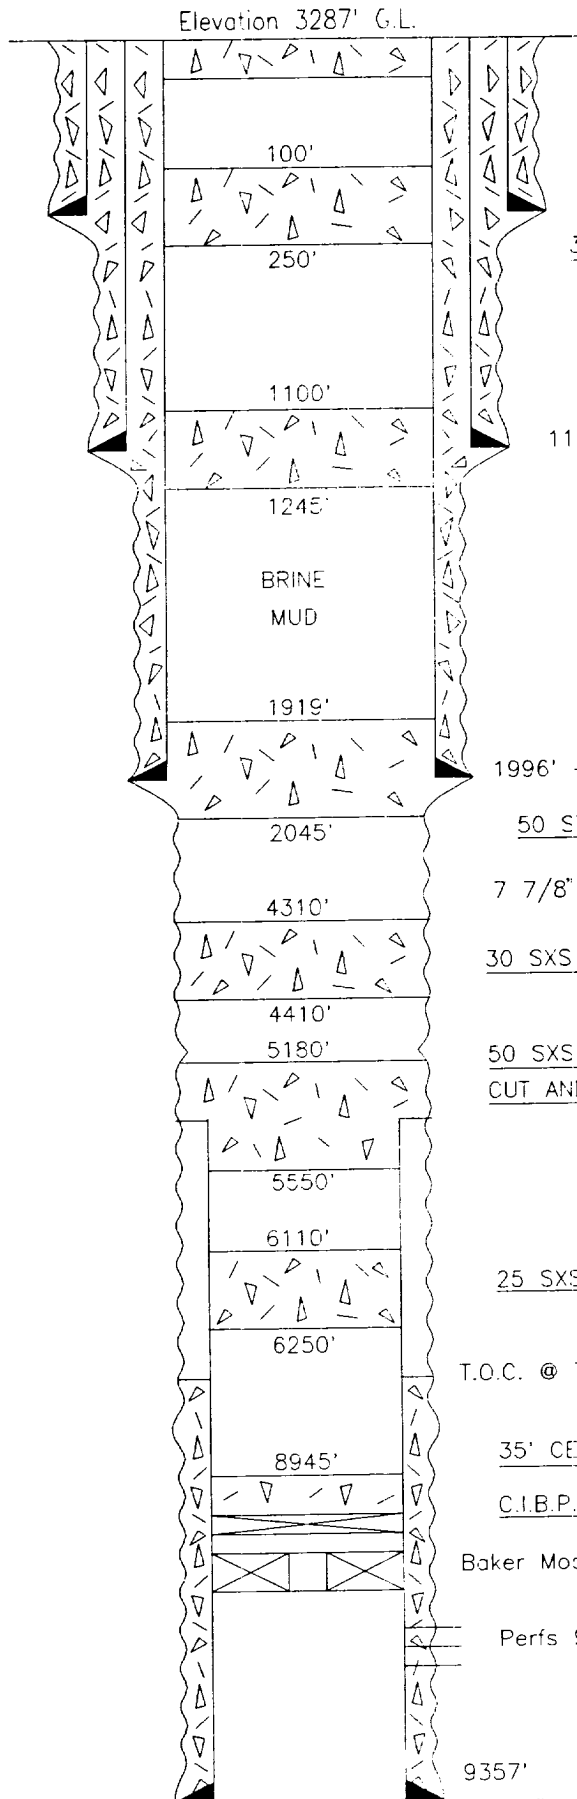

10 SXS SURFACE PLUG

201' - 16" csg. Cemented w/300 sxs Circ. to surface
30 SXS CEMENT 250'-100'

1192' - 11 3/4" csg. Cemented w/900 sxs Circ. to surface
30 SXS CEMENT 1245'-1100'

1996' - 8 5/8" csg. Cemented w/450 sxs Circ. to surface
50 SXS CEMENT 2045'-1919' (TAGGED)

7 7/8" Hole

30 SXS CEMENT 4310'-4410'

50 SXS CEMENT STUB PLUG 5550'-5180' (TAGGED)
CUT AND PULLED 5 1/2" CSG. AT 5500'

25 SXS CEMENT 6250'-6110'

T.O.C. @ 7610' (Temp. Sur.)

35' CEMENT 8980'-8945'

C.I.B.P. @ 8980'

Baker Model "D" Packer at 8997' w/on off tool

Perfs 9094'-9193'

9357'

5 1/2" 15.5# and 17# K-55 and N-80

LYNX PETROLEUM
Kaiser Com. No. 1
660' FNL & 2020' FWL
5 1/2" 15.5# and 17# K-55 and N-80
