


DEVON ENERGY CORPORATION WELLBORE SCHEMATIC

WELL NAME: State BW Com. # 1			Field: Turkey Track, North (Morrow)			
Location: Section 27, T18S, R28E			COUNTY: EDDY			STATE: NM
ELEVATION: GL=3528' KB=3549'			SPUD DATE: 12/4/81		COMP DATE: 3/9/82	
API # 30-015-23996		PREPARED BY: W. M. Frank			DATE: 9/27/01	
TUBULARS	DEPTH	SIZE	WEIGHT	GRADE	THREAD	HOLE SIZE
CASING:	0' - 405'	13 3/8"	54.5	K-55		17 1/2"
CASING:	0' - 2,684'	8 5/8"	28	S-80		11"
CASING:	0' - 11,116'	5 1/2"	17	L-80		7 7/8"
TUBING:	0' - 10,766'	2 3/8"	4.7	N-80	8rd	



CURRENT

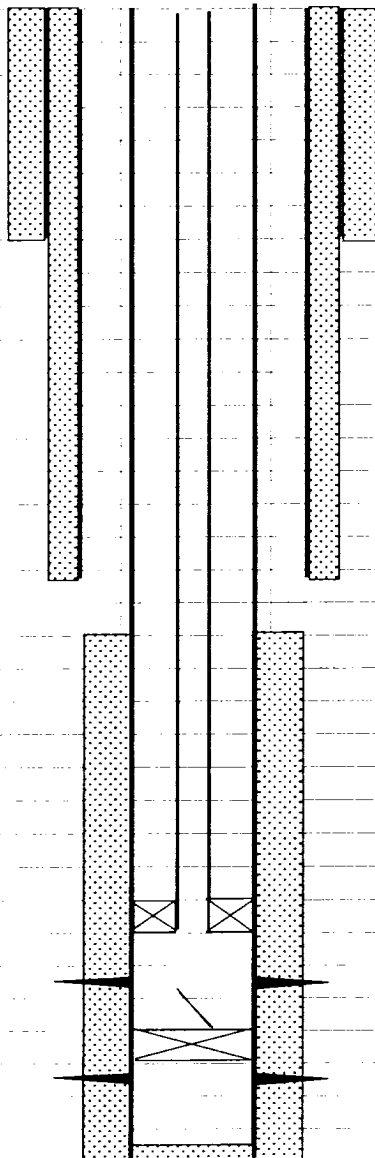

PROPOSED

Casing pressure tested to 1000 psig on 2/3/93

13 3/8" casing. Cemented w/500 sxs. Circ. Cement to surface.

Tubing String Detail:

351 jts 2 3/8", N-80, 8rd tubing

Baker On/Off tool w/1.78" profile nipple

Baker Lok-set Packer @ 10,766'.

8 5/8" casing. Cemented w/1700 sxs. Circulate cement to surface.

5 1/2" DV tool @ 7477'. Stage 2 cemented w/1,050 sxs. Did not circ cmt.

Baker Lok-Set packer @ 10,766'

Tagged w/wireline @ 10,849' On 2/9/01 (probably tagged paraffin knife fish).

Morrow Perfs 10,852 - 862' (4 spf)

Re-perf on 12/11/92 f/10,850 -864' (4 spf)

CIBP @ 10,885'. Paraffin cutter knocked to bottom on

Morrow Perfs perf'd on 12/11/92 f/10,910 - 918' (4 spf)

PBTD @ 11,066'

5 1/2" @ 11,116'. Stage 1 cemented w/700 sxs. Circ. 90 sxs when DV opened

TD @ 11,614'
