


Parkway West Unit #11
 760' FNL & 860' FEL
 Sec. 20, T-19-S, R-29-E
 Eddy Co., NM
 Elevation: 3340' GL, 3357' KB

Current Completion

Spud Date: 8/1/00
 Completion Date: 10/5/00

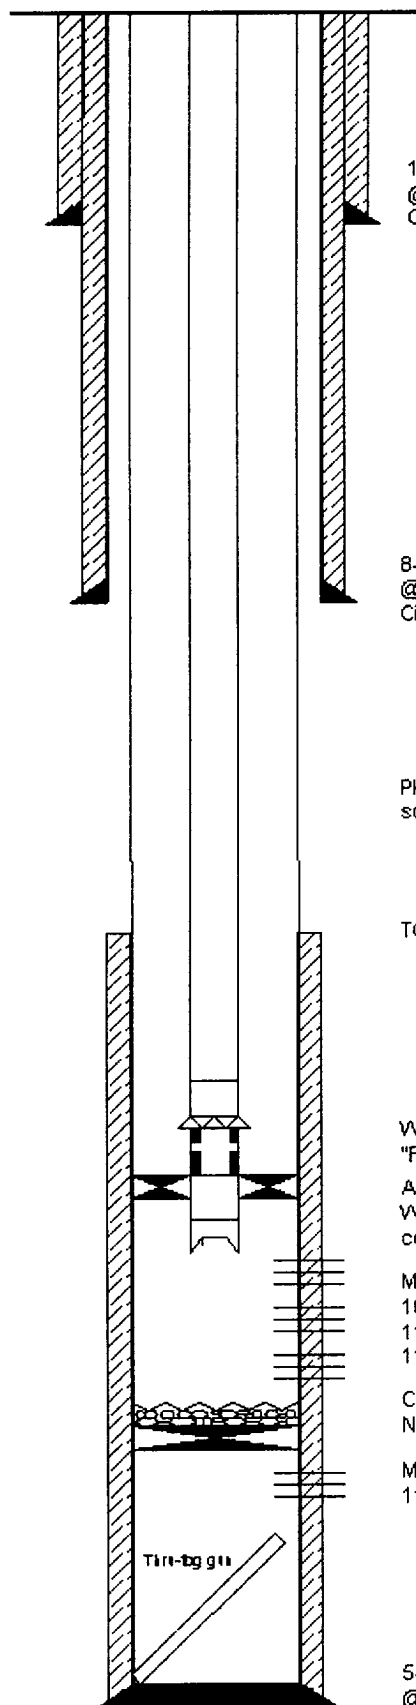

13-3/8", 46#, H-40 ST&C
 @ 350' Cmt'd w/400sx
 Circ'd to surface.

8-5/8", 32#, N-80 LT&C
 @ 3195' Cmt'd w/1325 sx
 Circ'd to surface.

Pkr Fluid: 2% KCl water with O2
 scavenger and inhibitor

TOC - 8514' (CBL)

Weatherford T-2 On/Off tool w/1.875"
 "F" profile @10,824'

Arrowset IX Packer @ 10,825' w/4' pup &
 VL entry guide @ 10,837' (set in 14 pts
 compression)

Morrow Perfs (5 spf):
 10,896-98', 10,970-72', 10,985-86',
 11,072-74', 11,081-82', 11,124-26',
 11,213-14'

CIBP @11,310' w/35' cmt on top
 New PBTD 11,275'

Morrow Perfs:
 11,336-42' & 11,350-56'

5-1/2", 17# L-80 & S-95
 @ 11,500' Cmt'd w/ 640
 sx

TD: 11,500'
 PBTD: 11,450'
 (CBL)

Completion

10/5/00 -- Perforated Morrow 11,336-42' and 11,350-56' using a 1-11/16" EnerJet thru-tubing gun loaded 6 spf, 45 degree phasing. Press. increased to 1200 psi in 2 minutes. Pulled out of rope socket while POOH w/guns. Drove guns down w/blind box on slick line. Left rope socket, torpedo tube, CCL tool, GR tool and XO for strip gun in hole (Schlumberger). PWOL. AOF 10.0 MMcfpd.

1/2/02 -- Morrow completion watered out. Abandoned Morrow 11,336-42' & 11,350-56' w/CIBP @ 11,310' w/35' cmt on top. Perf'd Morrow 10,896-98', 10,970-72', 10,985-86', 11,072-74', 11,081-82', 11,124-26', 11,213-14'. All intervals 5 spf. Acidized w/3000 gals of 7-1/2% HCL (Morrow acid) using PPI packers. Flowed back ARO 900 Mcf/d after recovering load. Frac'd down csg w/155,600 gals of binary foam carrying 182,000 lbs of 20/40 Interprop. Flowed back load. Ran production tbg. IP 4.0 MMcfpd FTP - 1200 psi.

Tubing Detail:

2-3/8", 4.7# L-80 EUE 8rd landing jt
 10' & 6' pup jts
 331 jts 2-3/8", 4.7# L-80 EUE 8rd tbg
 Weatherford T-2 on/off tool w/1.875" "F" profile @ 10,824'
 Arrowset 1-X packer w/carbide slips @ 10,825'
 4' pup jt
 VL entry guide @ 10,837'
