


TIME	CUM. HRS. / MIN.	P.S.I. @ 11,506 FEET.
9:15 A.M. 7-7-72	00HRS. 00 MIN.	4319 GAUGE REACHED 11,506 FEET.
10:15	01 00	START FIRST RATE
10:30	01 15	3990
11:15	02 00	4004 END FIRST RATE
11:30	02 15	3650
12:15 P.M.	03 00	3654 END SECOND RATE
12:30	03 15	3230
1:15	04 00	3216 END THIRD RATE
1:30	04 15	2940
2:15	05 00	2930 END FOURTH RATE SHUT-IN START BUILD-UP
3:15	06 00	4309
4:15	07 00	4312
5:15	08 00	4312
8:00 A.M. 7-8-72	22 45	4316 GAUGE OUT END TEST.
		TEST DATE: JULY 7&8, 1972
		TEST DEPTH: 11,506 FEET.
		ELEMENT NO. 7542 - N
		RANGE: 0 - 6950#
		CLOCK NO. 10835
		RANGE 0 - 36 HOURS.
		TEST OPERATOR: DON TYSON

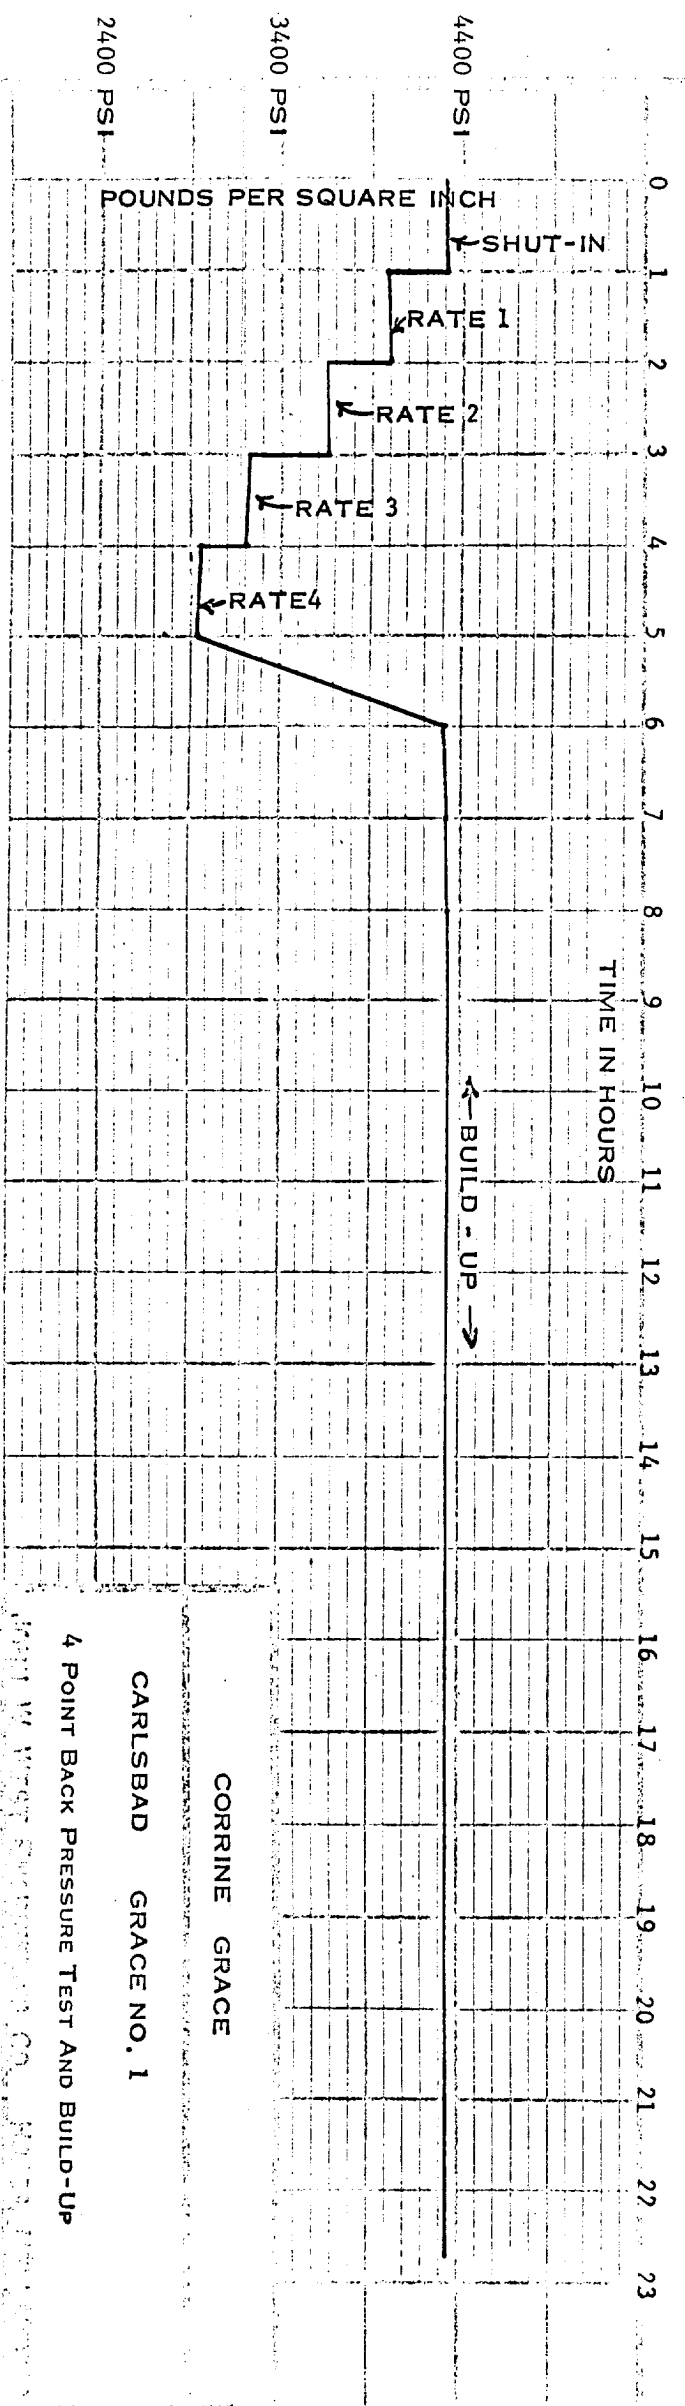

CORRINE GRACE

CARLSBAD GRACE NO. 1

4 POINT BACK PRESSURE TEST AND BUILD-UP

7-7-72 D.A.T.
