


COQUINA OIL CORPORATION

YATES - STATE NO. 1

PROPOSED COMPLETION

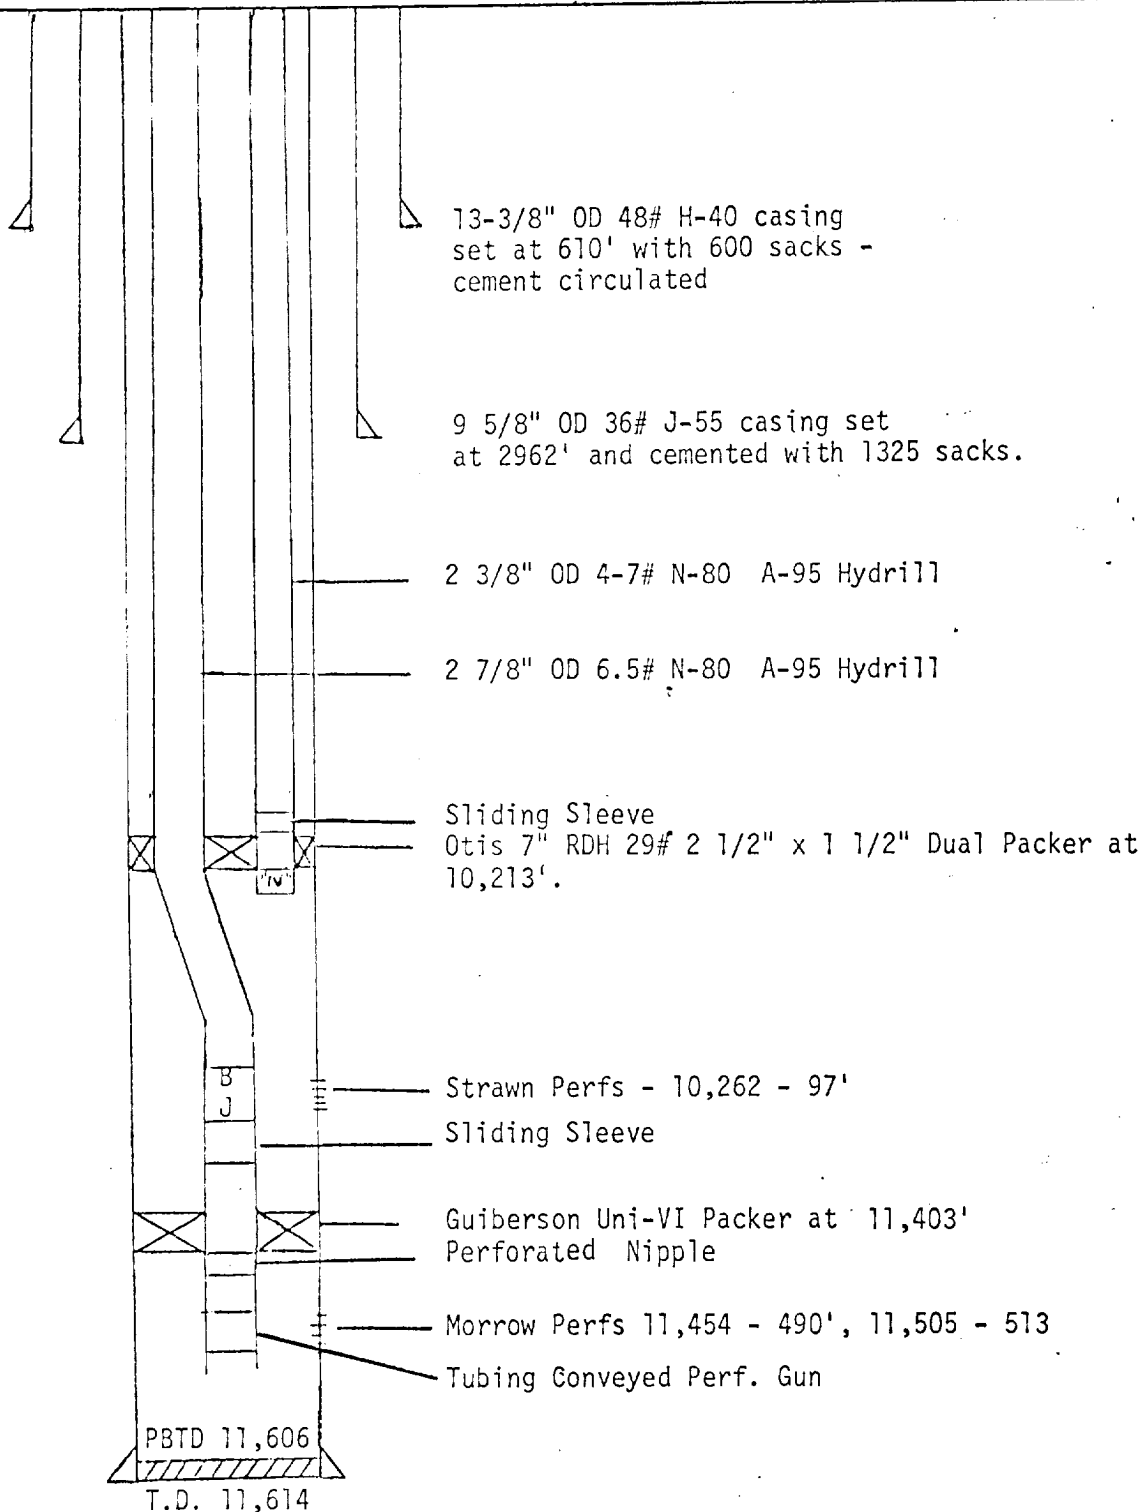

Casing-Bottom Up: 2683' 7" 29#
 3448' 7" 26#
 3615' 7" 23#
 1888' 7" 26#

Cemented with 350 sacks Class H 50-50 Poz followed by 250 sacks Class H + 4% Gel.
 Cement top 11,540' via temperature survey
