



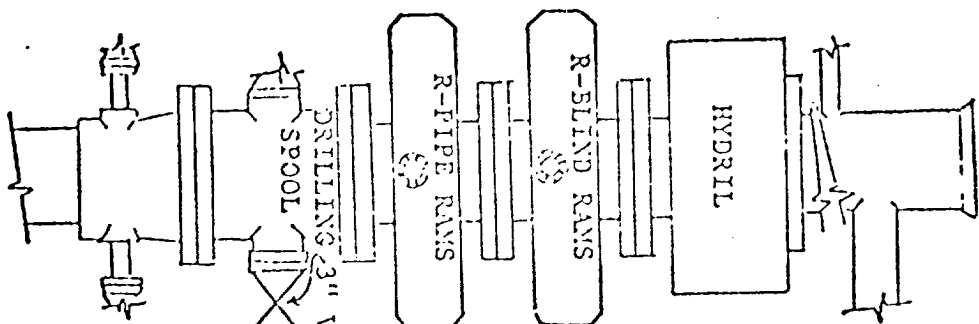

Drill Head installed here after setting 8 5/8"

BLOW OUT PREVENTION EQUIPMENT
 10" 900s ALL FLANGED CONNECTIONS
 3,000# WORKING PRESSURE - 6,000# TEST

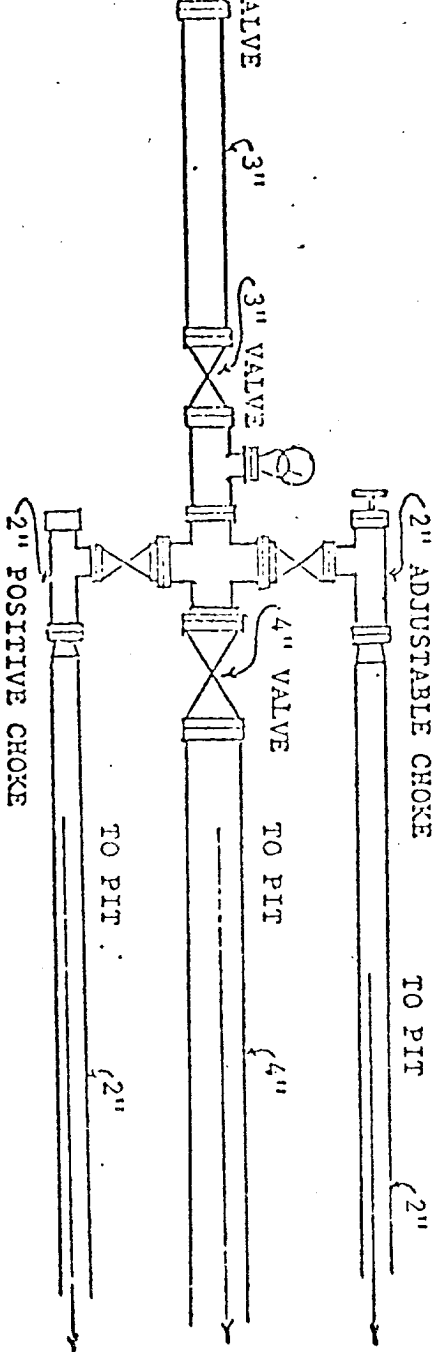

Sketch of BOP
 Southland Royalty Company
 State "2" Com. No. 1

ATTACHMENT TO FORM C-101

Sec. 2, T-20-S, R-37-E
 Eddy County, New Mexico

Contractor: Hondo Rig No. 5
