

Details of bop test

Phillips Petroleum Company


West Falls "A" #1

11/27/73

Contractor: Big West Drlg. Rig 17

Test by Yellow Jacket Tools and Services, Inc.

=====Transposition of the pressure recorder charts=====

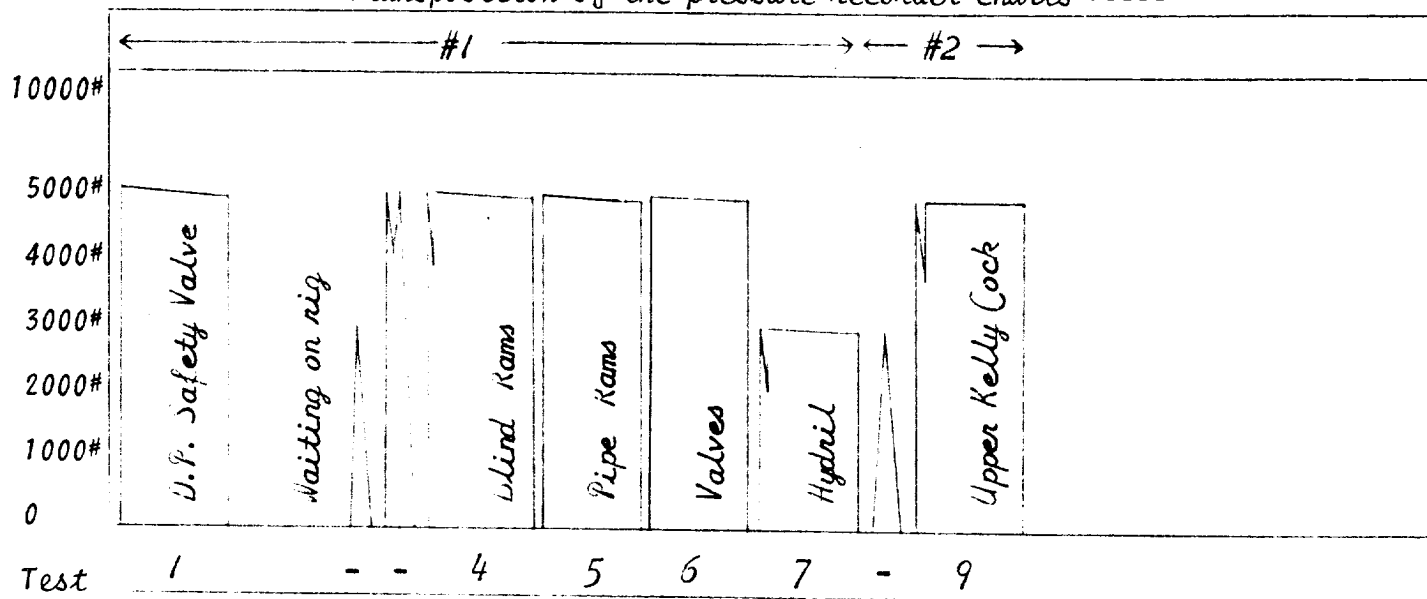

The above is a transposition of the pressure recorder charts covering test to the blowout control equipment in service on your well drilling in the Carlsbad Area, Hobbs District, New Mexico. Test was made with test plug landed in casing head with the following test results:

Arrived location - rig nipping up.

TESTING: Drill Pipe Safety Valve (Dart) - loose on rig floor.

Test #1 Pressured to 5000# with loss of approximately 200# during first twelve minutes then leveling out for remaining one minute of test.

NO VISIBLE LEAK. PRESSURE LEVELING OUT TOWARDS APPROXIMATELY 4800#.

Waiting on rig.
