

Details of bop test

Mobil Oil Corporation


Bindell Commission #1

4/13/74

Contractor: Marcum Drlg. Rig 3

Test by Yellow Jacket Tools and Services, Inc.

=====Transposition of the pressure recorder chart=====

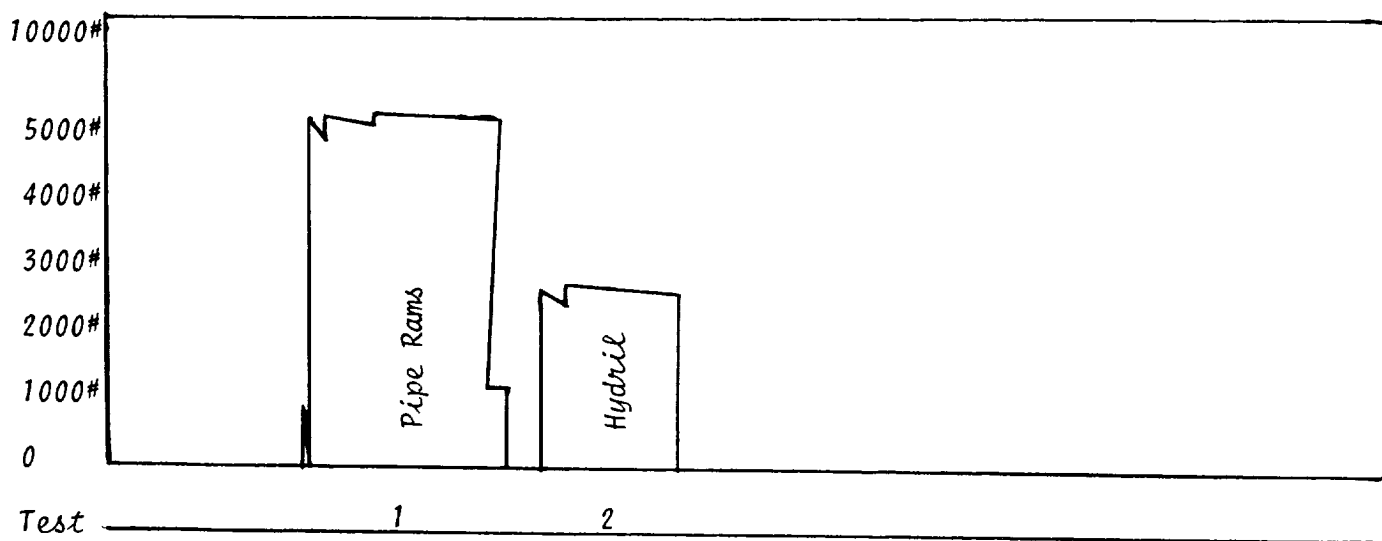

The above is a transposition of the pressure recorder chart covering test to the blowout control equipment in service on your well drilling in the Carlsbad Area, Hobbs District, New Mexico. Test was made with test packer landed in top of casing with the following test results:

-----

TESTING: Pipe Rams with valve closed next to stack on kill line, valve closed off casing spool, and all valves closed off choke-manifold cross - pressure applied down drill pipe.

Test #1 Pressured to 800# and released air; repressured to 5000# with loss of pressure; repressured to 5000# with loss of pressure; repressured to 5000# with loss of approximately 100# during first fifteen minutes then leveling out for remaining one minute of test. Released pressure to 1000# and closed Hydril and opened rams.

NO VISIBLE LEAK. PRESSURE LEVELING OUT TOWARDS APPROXIMATELY 4900#.

-----
