

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

SOIL CONSERVATION DIV
844 G-101
ARTESIA, N.M. 88210-2834

Form approved.

APPLICATION FOR PERMIT TO DRILL OR DEEPEN

1a TYPE OF WORK: DRILL ☒ DEEPEN ☐

b TYPE OF WELL:

OIL WELL ☒ GAS WELL ☐ Other ☐ SINGLE ZONE ☐ MULTIPLE ZONE ☐

2 NAME OF OPERATOR
DEVON ENERGY CORPORATION (NEVADA) 6137

3 ADDRESS AND TELEPHONE NO.
20 N. BROADWAY, SUITE 1500, OKC, OK 73102 (405) 235-3611

4 LOCATION OF WELL (Report location clearly and in accordance with any State requirements)*
At surface 990' FNL & 990' FEL

At top proposed prod. zone (SAME) Unit A

14.DISTANCE IN MILES AND DIRECTION FROM NEAREST TOWN OR POST OFFICE*
35 miles WNW of Jal, New Mexico

15.DISTANCE FROM PROPOSED LOCATION TO NEAREST PROPERTY OR LEASE LINE, FT. 990'
(Also to nearest dty. unit line if any)

16.NO. OF ACRES IN LEASE 1440

17.NO. OF ACRES ASSIGNED TO THIS WELL 40

18.DISTANCE FROM PROPOSED LOCATION* TO NEAREST WELL, DRILLING, COMPLETED, OR APPLIED FOR, ON THIS LEASE, FT. 1400'

19.PROPOSED DEPTH 8750'

20.ROTARY OR CABLE TOOLS* Rotary

21.ELEVATIONS (Show whether DF, RT, GR, etc.) GL 3515'

22. APPROX. DATE WORK WILL START* July 1, 1996

23. PROPOSED CASING AND CEMENTING PROGRAM

24. APPROX. DATE WORK WILL START* July 1, 1996

25. APPROX. DATE WORK WILL START* July 1, 1996

26. APPROX. DATE WORK WILL START* July 1, 1996

27. APPROX. DATE WORK WILL START* July 1, 1996

28. APPROX. DATE WORK WILL START* July 1, 1996

29. APPROX. DATE WORK WILL START* July 1, 1996

30. APPROX. DATE WORK WILL START* July 1, 1996

31. APPROX. DATE WORK WILL START* July 1, 1996

32. APPROX. DATE WORK WILL START* July 1, 1996

33. APPROX. DATE WORK WILL START* July 1, 1996

34. APPROX. DATE WORK WILL START* July 1, 1996

35. APPROX. DATE WORK WILL START* July 1, 1996

36. APPROX. DATE WORK WILL START* July 1, 1996

37. APPROX. DATE WORK WILL START* July 1, 1996

38. APPROX. DATE WORK WILL START* July 1, 1996

39. APPROX. DATE WORK WILL START* July 1, 1996

40. APPROX. DATE WORK WILL START* July 1, 1996

41. APPROX. DATE WORK WILL START* July 1, 1996

42. APPROX. DATE WORK WILL START* July 1, 1996

43. APPROX. DATE WORK WILL START* July 1, 1996

44. APPROX. DATE WORK WILL START* July 1, 1996

45. APPROX. DATE WORK WILL START* July 1, 1996

46. APPROX. DATE WORK WILL START* July 1, 1996

47. APPROX. DATE WORK WILL START* July 1, 1996

48. APPROX. DATE WORK WILL START* July 1, 1996

49. APPROX. DATE WORK WILL START* July 1, 1996

50. APPROX. DATE WORK WILL START* July 1, 1996

51. APPROX. DATE WORK WILL START* July 1, 1996

52. APPROX. DATE WORK WILL START* July 1, 1996

53. APPROX. DATE WORK WILL START* July 1, 1996

54. APPROX. DATE WORK WILL START* July 1, 1996

5. LEASE DESIGNATION AND SERIAL NO.
NM-NM-0404441
6. IF INDIAN, ALLOTTEE OR TRIBE NAME
N/A
7. UNIT AGREEMENT NAME
N/A
8. FARM OR LEASE NAME, WELL NO.
Todd "13A" Federal #1 18770
9. API WELL NO.
30-015-28903
10. FIELD AND POOL, OR WILDCAT
Ingle Wells (Delaware) 33745
11. SEC., T., R., M., OR BLOCK AND SURVEY OR AREA
Section 13-T23S-R31E, Unit A

12. COUNTY OR PARISH
Eddy
13. STATE
New Mexico

14. DISTANCE IN MILES AND DIRECTION FROM NEAREST TOWN OR POST OFFICE*
35 miles WNW of Jal, New Mexico

15. DISTANCE FROM PROPOSED LOCATION TO NEAREST PROPERTY OR LEASE LINE, FT. 990'
(Also to nearest dty. unit line if any)

16. NO. OF ACRES IN LEASE 1440

17. NO. OF ACRES ASSIGNED TO THIS WELL 40

18. DISTANCE FROM PROPOSED LOCATION* TO NEAREST WELL, DRILLING, COMPLETED, OR APPLIED FOR, ON THIS LEASE, FT. 1400'

19. PROPOSED DEPTH 8750'

20. ROTARY OR CABLE TOOLS* Rotary

21. ELEVATIONS (Show whether DF, RT, GR, etc.) GL 3515'

22. APPROX. DATE WORK WILL START* July 1, 1996

23. PROPOSED CASING AND CEMENTING PROGRAM

24. APPROX. DATE WORK WILL START* July 1, 1996

25. APPROX. DATE WORK WILL START* July 1, 1996

26. APPROX. DATE WORK WILL START* July 1, 1996

27. APPROX. DATE WORK WILL START* July 1, 1996

28. APPROX. DATE WORK WILL START* July 1, 1996

29. APPROX. DATE WORK WILL START* July 1, 1996

30. APPROX. DATE WORK WILL START* July 1, 1996

31. APPROX. DATE WORK WILL START* July 1, 1996

32. APPROX. DATE WORK WILL START* July 1, 1996

33. APPROX. DATE WORK WILL START* July 1, 1996

34. APPROX. DATE WORK WILL START* July 1, 1996

35. APPROX. DATE WORK WILL START* July 1, 1996

36. APPROX. DATE WORK WILL START* July 1, 1996

37. APPROX. DATE WORK WILL START* July 1, 1996

38. APPROX. DATE WORK WILL START* July 1, 1996

39. APPROX. DATE WORK WILL START* July 1, 1996

40. APPROX. DATE WORK WILL START* July 1, 1996

41. APPROX. DATE WORK WILL START* July 1, 1996

42. APPROX. DATE WORK WILL START* July 1, 1996

43. APPROX. DATE WORK WILL START* July 1, 1996

44. APPROX. DATE WORK WILL START* July 1, 1996

45. APPROX. DATE WORK WILL START* July 1, 1996

46. APPROX. DATE WORK WILL START* July 1, 1996

47. APPROX. DATE WORK WILL START* July 1, 1996

48. APPROX. DATE WORK WILL START* July 1, 1996

49. APPROX. DATE WORK WILL START* July 1, 1996

50. APPROX. DATE WORK WILL START* July 1, 1996

51. APPROX. DATE WORK WILL START* July 1, 1996

52. APPROX. DATE WORK WILL START* July 1, 1996

53. APPROX. DATE WORK WILL START* July 1, 1996

Devon Energy proposes to drill to approximately 8750' to test the Delaware for commercial quantities of oil. If the Delaware is deemed non-commercial, the wellbore will be plugged and abandoned as per Federal regulations. Programs to adhere to onshore oil and gas regulations are outlined in the following exhibits and attachments.

Drilling Program:

Surface Use and Operating Plan
Exhibit #1/1-A - Blowout Prevention Equipment
Exhibit #2 - Location and Elevation Plat
Exhibit #3 - Planned Access Roads
Exhibit #4 - Wells Within One Mile Radius
Exhibit #5 - Production Facilities Plat
Exhibit #6 - Rotary Rig Layout

Exhibit #7 - Casing Program
Evidence of Bond Coverage
Bond Coverage: Nationwide
BLM Bond No.: CO-1104

IN ABOVE SPACE DESCRIBE PROPOSED PROGRAM: If proposal is to deepen, give data on present productive zone and proposed new productive zone. If proposal is to drill or deepen directionally, give pertinent data on subsurface locations and measured and true vertical depths. Give blowout preventer program, if any.

24.

SIGNED

Gerald T. Pepper

TITLE District Engineer

Gerald T. Pepper

DATE January 17, 1996

(This space for Federal or State office use)

PERMIT NO. APPROVAL DATE

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon. CONDITIONS OF APPROVAL, IF ANY:

APPROVED BY *5/6/96 J. Lucero* TITLE *Acting State Director* DATE *3-20-96*

See Instructions On Reverse Side

Title 18 U.S.C. Section 1001, makes it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction

APPROVAL SUBJECT TO
GENERAL REQUIREMENTS AND
SPECIAL STIPULATIONS

DISTRICT I
P. O. Box 1980
Hobbs, NM 88241-1980

State of New Mexico
Energy, Minerals, and Natural Resources Department

EXHIBIT 2

Form C-102
Revised 02-10-94

Instructions on back

DISTRICT II
P. O. Drawer DD
Artesia, NM 88211-0719

DISTRICT III
1000 Rio Brazos Rd.
Aztec, NM 87410

DISTRICT IV
P. O. Box 2088
Santa Fe, NM 87507-2088

OIL CONSERVATION DIVISION

P. O. Box 2088
Santa Fe, New Mexico 87504-2088

Submit to the Appropriate
District Office
State Lease - 4 copies
Fee Lease - 3 copies

☐ AMENDED REPORT

WELL LOCATION AND ACREAGE DEDICATION PLAT

1 API Number 30-015-28903		2 Pool Code 33745		3 Pool Name UNDER INGLE WELLS (DELAWARE)					
4 Property Code		5 Property Name TODD '13' A FEDERAL						6 Well Number 1	
7 OGRID No. 6137		8 Operator Name DEVON ENERGY CORPORATION (NEVADA)						9 Elevation 3515'	
10 SURFACE LOCATION									
UL or lot no. A	Section 13	Township 23 SOUTH	Range 31 EAST, N.M.P.M.	Lot Ida	Feet from the 990'	North/South line NORTH	Feet from the 990'	East/West line EAST	County EDDY
11 BOTTOM HOLE LOCATION IF DIFFERENT FROM SURFACE									
UL or lot no.	Section	Township	Range	Lot Ida	Feet from the	North/South line	Feet from the	East/West line	County
12 Dedicated Acres 40		13 Joint or Infill		14 Consolidation Code		15 Order No.			

NO ALLOWABLE WELL BE ASSIGNED TO THIS COMPLETION UNTIL ALL INTERESTS HAVE BEEN
CONSOLIDATED OR A NON-STANDARD UNIT HAS BEEN APPROVED BY THE DIVISION

--	--	--	--	--	--	--	--	--	--

OPERATOR CERTIFICATION

I hereby certify that the information
contained herein is true and complete
to the best of my knowledge and belief.

Signature

Printed Name

Gerald T. Pepper

Title

District Engineer

Date

January 17, 1996


SURVEYOR CERTIFICATION

I hereby certify that the well
location shown on this plat was
plotted from field notes of actual
surveys made by me or under
my supervision, and that the
same is true and correct to the
best of my belief.

Date of Survey

NOVEMBER 17, 1995

Signature of Surveyor
Professional Seal




Certification No.


V. L. BEZNER R.P.S. #7920

JOB #42471-1 / 47 SW / V.H.B.

BOPE SCHEMATIC

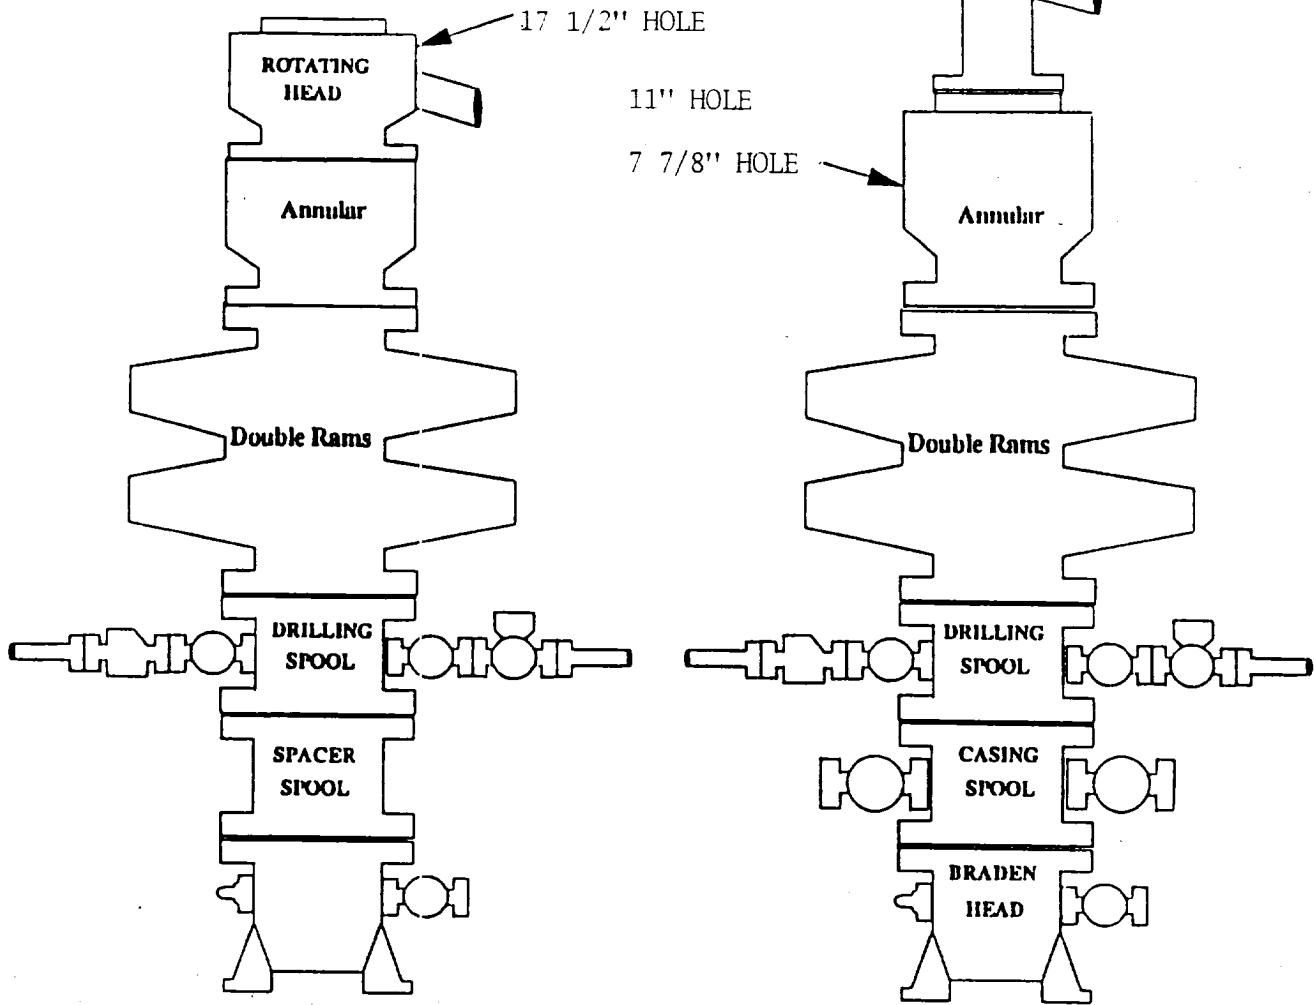

Choke Manifold Requirement (3000 psi WP)

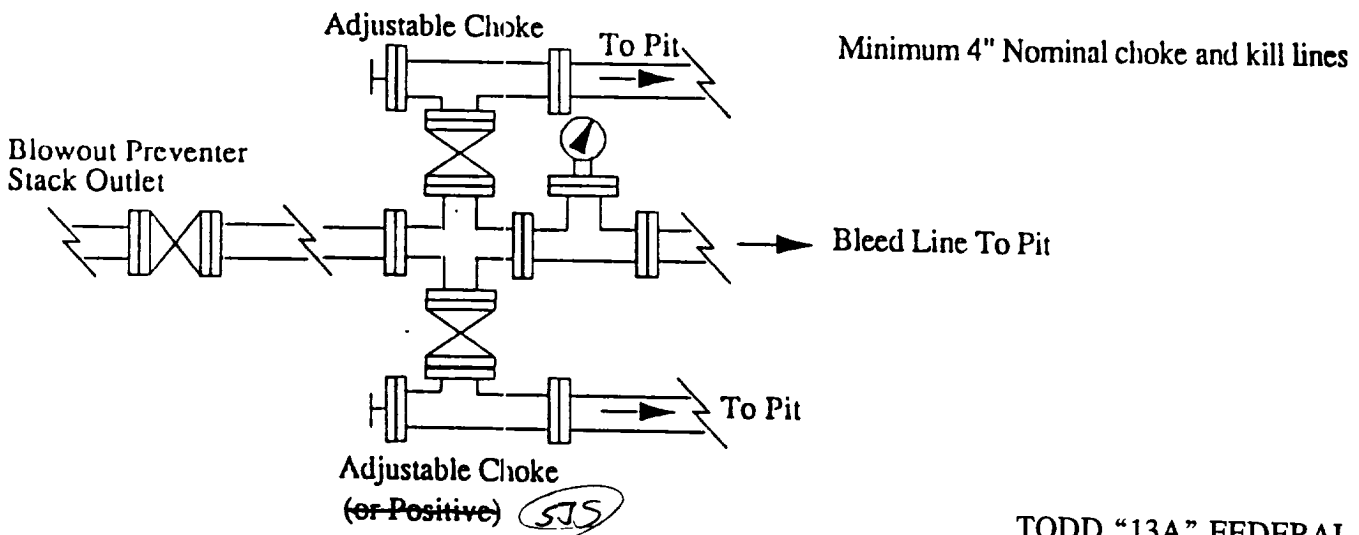

TODD "13A" FEDERAL #1
Eddy County, New Mexico
Exhibit #1

Exhibit #1A
NOTES REGARDING BLOWOUT PREVENTERS
Devon Energy Corporation (Nevada)
TODD "13A" FEDERAL #1
990' FNL & 990' FEL
Section 13-T23S-R31E, Unit A
Eddy County, New Mexico

1. Drilling nipple will be constructed so it can be removed mechanically without the aid of a welder. The minimum internal diameter will equal BOP bore.
2. Wear ring will be properly installed in head.
3. Blowout preventer and all associated fittings will be in operable condition to withstand a minimum 3000 psi working pressure.
4. All fittings will be flanged.
5. A full bore safety valve tested to a minimum 3000 psi WP with proper thread connections will be available on the rotary rig floor at all times.
6. All choke lines will be anchored to prevent movement.
7. All BOP equipment will be equal to or larger in bore than the internal diameter of the last casing string.
8. Will maintain a kelly cock attached to the kelly.
9. Hand wheels and wrenches will be properly installed and tested for safe operation.
10. Hydraulic floor control for blowout preventer will be located as near in proximity to driller's controls as possible.
11. All BOP equipment will meet API standards and include a minimum 40 gallon accumulator having two independent means of power to initiate closing operation.

MINIMUM BLOWOUT PREVENTER REQUIREMENT

3,000 psi Working Pressure

3 MWP

TODD "13A" FEDERAL #1
Eddy County, New Mexico
Exhibit #1-B


STACK REQUIREMENTS

No	Item	Min. I.D.	Min. Nominal
1	Flowline		
2	Fill up line		2"
3	Drilling nipple		
4	Annular preventer		
5	Two single or one dual hydraulically operated rams		
6a	Drilling spool with 2" min. kill line and 3" min choke line outlets		
6b	2" min. kill line and 3" min. choke line outlets in ram. (Alternate to 6a above.)		
7	Valve Gate <input type="checkbox"/> Plug <input type="checkbox"/>	3-1/8"	
8	Gate valve—power operated	3-1/8"	
9	Line to choke manifold		3"
10	Valves Gate <input type="checkbox"/> Plug <input type="checkbox"/>	2-1/16"	
11	Check valve	2-1/16"	
12	Casing head		
13	Valve Gate <input type="checkbox"/> Plug <input type="checkbox"/>	1-13/16"	
14	Pressure gauge with needle valve		
15	Kill line to rig mud pump manifold		2"

OPTIONAL

16	Flanged valve	1-13/16"	
----	---------------	----------	--

CONFIGURATION A

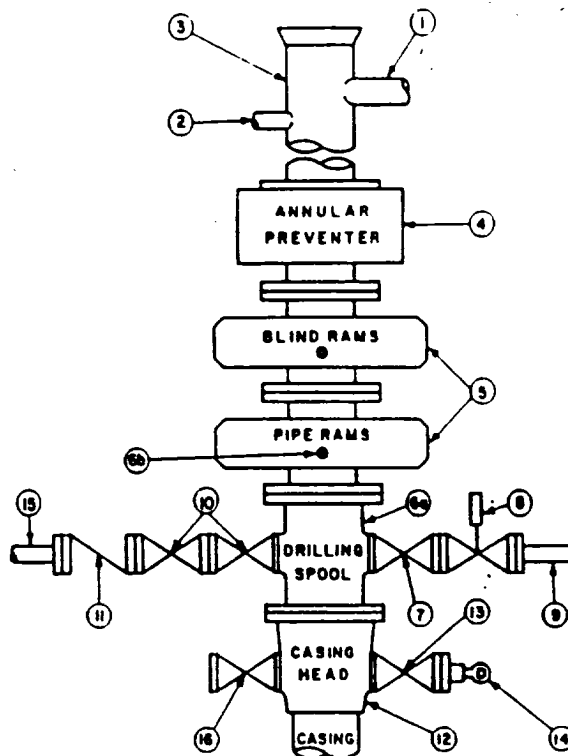

CONTRACTOR'S OPTION TO FURNISH:

1. All equipment and connections above bradenhead or casinghead. Working pressure of preventers to be 3,000 psi, minimum.
2. Automatic accumulator (80 gallon, minimum) capable of closing BOP in 30 seconds or less and, holding them closed against full rated working pressure.
3. BOP controls, to be located near drillers position.
4. Kelly equipped with Kelly cock.
5. Inside blowout preventer or its equivalent on derrick floor at all times with proper threads to fit pipe being used.
6. Kelly saver-sub equipped with rubber casing protector at all times.
7. Plug type blowout preventer tester.
8. Extra set pipe rams to fit drill pipe in use on location at all times.
9. Type RX ring gaskets in place of Type R.

MEC TO FURNISH:

1. Bradenhead or casinghead and side valves.
2. Wear bushing, if required.

GENERAL NOTES:


1. Deviations from this drawing may be made only with the express permission of MEC's Drilling Manager.
2. All connections, valves, fittings, piping, etc., subject to well or pump pressure must be flanged (suitable clamp connections acceptable) and have minimum working pressure equal to rated working pressure of preventers up through choke. Valves must be full opening and suitable for high pressure mud service.
3. Controls to be of standard design and each marked, showing opening and closing position.
4. Chokes will be positioned so as not to hamper or delay changing of choke beans. Replaceable parts for adjustable choke, other bean sizes, retainers, and choke wrenches to be conveniently located for immediate use.
5. All valves to be equipped with handwheels or handles ready for immediate use.
6. Choke lines must be suitably anchored.

7. Handwheels and extensions to be connected and ready for use.
8. Valves adjacent to drilling spool to be kept open. Use outside valves except for emergency.
9. All seamless steel control piping (3000 psi working pressure) to have flexible joints to avoid stress. Hoses will be permitted.
10. Casinghead connections shall not be used except in case of emergency.
11. Do not use kill line for routine fill-up operations.

**MINIMUM CHOKE MANIFOLD
3,000, 5,000 and 10,000 PSI Working Pressure**

3 MWP - 5 MWP - 10 MWP

**TODD "13A" FEDERAL #1
Eddy County, New Mexico
Exhibit #1-C**

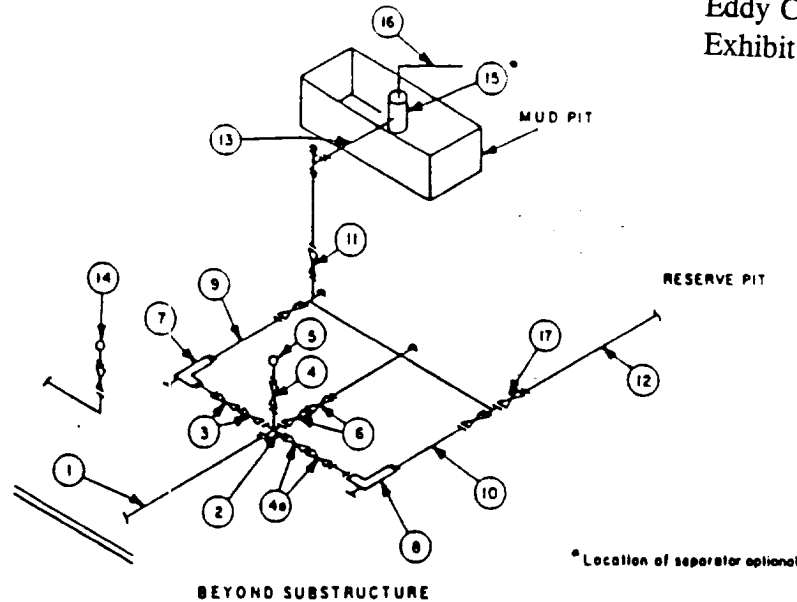

MINIMUM REQUIREMENTS										
No		3,000 MWP			5,000 MWP			10,000 MWP		
		I.D.	NOMINAL	RATING	I.D.	NOMINAL	RATING	I.D.	NOMINAL	RATING
1	Line from drilling spool		3"	3,000		3"	5,000		3"	10,000
2	Cross 3"x3"x3"x2"			3,000			5,000			
	Cross 3"x3"x3"x3"									10,000
3	Valves (1) Gate <input type="checkbox"/> Plug <input type="checkbox"/> (2)	3-1/8"		3,000	3-1/8"		5,000	3-1/8"		10,000
4	Valve Gate <input type="checkbox"/> Plug <input type="checkbox"/> (2)	1-13/16"		3,000	1-13/16"		5,000	1-13/16"		10,000
4a	Valves (1)	2-1/16"		3,000	2-1/16"		5,000	3-1/8"		10,000
5	Pressure Gauge			3,000			5,000			10,000
6	Valves Gate <input type="checkbox"/> Plug <input type="checkbox"/> (2)	3-1/8"		3,000	3-1/8"		5,000	3-1/8"		10,000
7	Adjustable Choke(3)	2"		3,000	2"		5,000	2"		10,000
8	Adjustable Choke	"		3,000	1"		5,000	2"		10,000
9	Line		3"	3,000		3"	5,000		3"	10,000
10	Line		2"	3,000		2"	5,000		3"	10,000
11	Valves Gate <input type="checkbox"/> Plug <input type="checkbox"/> (2)	3-1/8"		3,000	3-1/8"		5,000	3-1/8"		10,000
12	Lines		3"	1,000		3"	1,000		3"	2,000
13	Lines		3"	1,000		3"	1,000		3"	2,000
14	Remote reading compound standpipe pressure gauge			3,000			5,000			10,000
15	Gas Separator		2'x5'			2'x5'			2'x5'	
16	Line		4"	1,000		4"	1,000		4"	2,000
17	Valves Gate <input type="checkbox"/> Plug <input type="checkbox"/> (2)	3-1/8"		3,000	3-1/8"		5,000	3-1/8"		10,000

- (1) Only one required in Class 3M.
 (2) Gate valves only shall be used for Class 10M.
 (3) Remote operated hydraulic choke required on 5,000 psi and 10,000 psi for drilling.

EQUIPMENT SPECIFICATIONS AND INSTALLATION INSTRUCTIONS

- All connections in choke manifold shall be welded, studded, flanged or Cameron clamp of comparable rating.
- All flanges shall be API 6B or 6BX and ring gaskets shall be API RX or BX. Use only BX for 10 MWP.
- All lines shall be securely anchored.
- Chokes shall be equipped with tungsten carbide seats and needles, and replacements shall be available.
- Choke manifold pressure and standpipe pressure gauges shall be available at the choke manifold to assist in regulating chokes. As an alternate with automatic chokes, a choke manifold pressure gauge shall be located on the rig floor in conjunction with the standpipe pressure gauge.
- Line from drilling spool to choke manifold should be as straight as possible. Lines downstream from chokes shall make turns by large bends or 90° bends using bull plugged tees.
- Discharge lines from chokes, choke bypass and from top of gas separator should vent as far as practical from the well.
