Form 3160 -3 (April 2004)

UNITED STATES

DEPARTMENT OF THE INTERIOR

BUREAU OF LAND MANAGEMENT OF

4		FORM A OMB No Expires M	. 1004-0)
2000	2 15	Lease Serial No.		_

Lease	Serial No.
Jicar	illa C

APPLICATION FOR PERMIT TO	DRILL OR REENTER	in i	Jicarilla Apaci		
la. Type of work: ✓ DRILL REENT.	ER CONTRACTOR		7 If Unit or CA Agree	ement, Name a	ind No.
			8. Lease Name and V	Vell No.	
Ib. Type of Well:Oil Well Gas WellOther	Single Zone Multi	ple Zone	Jic Apache C #	8F	
2. Name of Operator CDX RIO, LLC			9. API Well No.	39-2	<u> 184</u>
3a. Address 4801 N. Butler, Suite 2000	3b. Phone No. (include area code)		10. Field and Pool, or E		
Farmington, NM 87401	505-326-3003		Blanco MV/La	pacito GP/B	asin DK
4. Location of Well (Report location clearly and in accordance with at At surface 2355' FNL and 2635' FEL	ny State requirements.*)		11. Sec., T. R. M. or Bl	Ψ.	or Area WCB4
At proposed prod. zone Same			G Sec 13, T26N-	R 5W	
14. Distance in miles and direction from nearest town or post office*			12. County or Parish	13.	State
8 Miles East and 20 Miles North of Counselor, New Mexi	ce		Rio Arriba		NM
15. Distance from proposed* 1750' location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any)	16. No. of acres in lease 2560.00	3	ng Unit dedicated to this well One of the property of the pro		
18. Distance from proposed location*	19. Proposed Depth	20. BLM/	BIA Bond No. on file		
to nearest well, drilling, completed, applied for, on this lease, ft.	8577'		23. Estimated duration		
21. Elevations (Show whether DF, KDB, RT, GL, etc.) 7232' GL	22 Approximate date work will sta 08/01/2004	ut*			
	24. Attachments				
The following, completed in accordance with the requirements of Onsho	re Oil and Gas Order No.1, shall be a	ttached to th	is form:		
 Well plat certified by a registered surveyor. A Drilling Plan. 	4. Bond to cover t Item 20 above).	he operatio	ns unless covered by an	existing bond	on file (see
3. A Surface Use Plan (if the location is on National Forest System SUPO shall be filed with the appropriate Forest Service Office).		specific infe	ormation and/or plans as	may be requir	ed by the
25. Signature	Name (Printed Typed)			Date	
Charles XIII SI	Charles Hanson, A	gent		06/16/20	004
Title HLPermitting Inc. P.O. Box 6684 Farmington,	NM 87499				
Approved by (Signature) /s/ David R. Sitzler	Name (Printed/Typed)			Date JUL	3 8 500
Assistant Field Manager	Office	*****			
Application approval does not warrant or certify that the applicant hole conduct operations thereon. Conditions of approval, if any, are attached.	ls legal or equitable title to those righ	its in the sub	ject lease which would en	ntitle the applic	cant to
Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a c States any false, fictitious or fraudulent statements or representations as	rime for any person knowingly and to any matter within its jurisdiction.	willfully to m	ake to any department or	r agency of the	United

*(Instructions on page 2)

NSL 6090 HOLD C184 FOR NGL in Maricus

1625 N. French Dr., Hobbs, N.M. 88240

DISTRICT II 1301 Y. Grand Ave., Artesia, N.M. 88210

DISTRICT III 1000 Rio Brazos Rd., Aztec, N.M. 87410 State of New Mexico
Energy, Minerals & Natural Resources Department

OIL CONSERVATION DIVISION 1220 South St. Francis Dr. Santa Fe, NM 87505


Form C-10. Revised June 10, 2003

Submit to Appropriate District Offic State Lease - 4 Copie Fee Lease - 3 Copie

I AMENDED REPORT

	1220 South St. Fran	icis Dr.,	Santa Fe, N	M 87505	-						MDED METO
			7	VELL L	OCATIO	N AND			ICATION P		
	30-033	7-2	7840	972	Pool Code 90/723	3.	NC B	asin Man	Pool Name Blauco Mes	a Verde - Bas	IN DAKOTA
	Property Cod	ie - 7	240	1		*Prop	erty Name RILLA C				ell Number 8F
	OGRED No.		JYV			*Operz	tor Name				Elevation
	222374	/			•	CDX	RIO, LL	C .			7232
	-		<u>,</u>			10 Surfa					
	UL or lot no.	Section 13	Township 26-N	Range 5-W	Lot Idn	Feet from the 2355	- 1	th/South line NORTH	Feet from the 2635	Rast/Vest line EAST	RIO ARRIBA
	<u> </u>		<u> </u>	¹¹ Bott	om Hole	Location	ı H Difi	ferent Fro	om Surface	•	
	UL or lot no.	Section	Township	Range	Lot Idn	Feet from th		th/South line	Feet from the	East/West line	County
	12 Dedicated Acres	16	o Marce	Joint or	l Infill	¹⁴ Consolidatio	n Code		²⁶ Order No.		L
	320 - MES		_ ,								
4			LL BE A	SSIGNEL	TO THI	S COMPLE	TION U	LLA LITV	NTERESTS H	AVE BEEN CO	NSOLIDATED
=	18		OR A N	ON-STA	NDARD U	NIT HAS	BEEN A	PPROVED	BY THE DIVI	SION	
7	ec. Corner D. Stone w/ /8 Rebar		N8872.	3'46'W	5438.2	2' (c)		EC. CORNÉ CALC'D B OP. METHO	D I hereby cer	PERATOR CEF tify that the information complete to the best of	m contained herein
			<u>.</u>	1	2355'	EST 28 29 3				ines Cocc	oran)_
	:			1	10 oil	25050 10 .0060 0 .0060 6	7.07	(0) '85 87'	Printed Na	ines Caece Managel -16-04	
	LAT. = 3629 LONG. = 107					2635	<u> </u>	· ic	Date 6	-16-04	
	-		·			-	•	S00.24'44"W	I hereby certify	VEYOR CERT that the well locations field notes of actual	shown on this plat
			•		-			· · · · · · · · · · · · · · · · · · ·	- S. S.	MEGAT	
									Service and	14831) und 15	
		ł	•			1	5FC	CORNER	14	ruj (1

SEC. CORNER

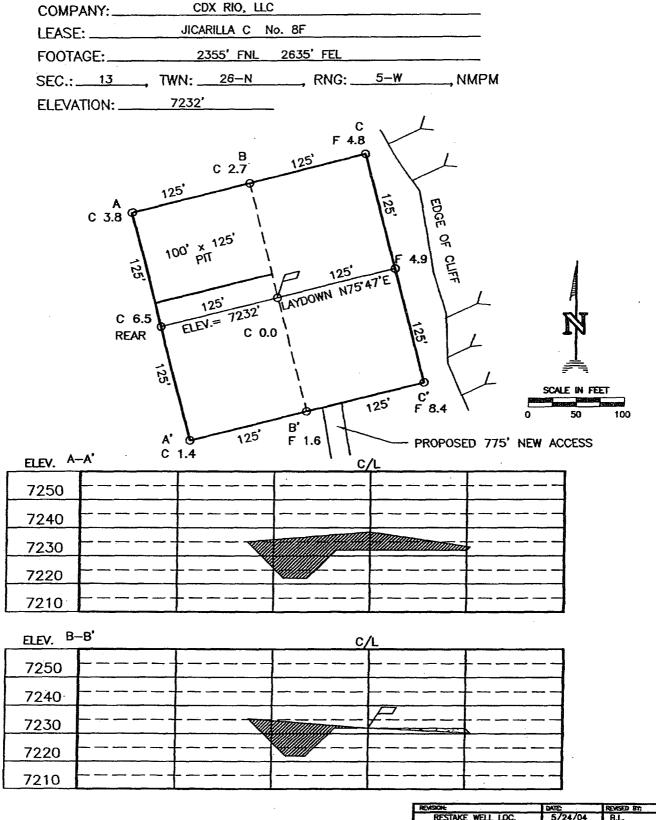

NOTE:

DAGGETT ENTERPRISES, INC. IS NOT LIABLE FOR UNDERGROUND UTILITIES OR PIPELINES. NEW MEXICO ONE CALL TO BE NOTIFIED 48 HOURS PRIOR TO EXCAVATION OR CONSTRUCTION.



Daggett Enterprises, Inc. Surveying and Oil Field Services P. O. Box 15068 - Farmington, NM 87401 Phone (505) 326–1772 - Fox (505) 326–6019

DRAWN BY: A.G.	CADFILE: CDXGAS059CF8
ROW#: CDXGAS059	DATE: 04/18/04



ONSHORE OIL & GAS ORDER NO. 1 Approval of Operations on Onshore Federal and Indian Oil and Gas Leases

Jicarilla C - #8F 2355 FNL & 2635 FEL, Sec 13, T26N - R5W

Drilling Plan

All lease and/or unit operations will be conducted in such a manner that full compliance is made with applicable laws, regulations (43 CFR 3100), Onshore Oil and Gas Order No. 1, and the approved plan of operations. The operator is fully responsible for the actions of his subcontractors. A copy of these conditions will be furnished to the field representative to insure compliance.

- 1. Estimated Tops of Important Geologic Markers (and)
- 2. Anticipated Water, Oil, Gas, or Mineral Formations

Estimated KB Elev:

7244


Ground Elev:

7232

Formation	Depth SS	Depth KB	Rock Type	Comments
Quaternary Alluvium	Surface	0.0	Gravel	Water
San Jose	Surface	0.0	SS / SH	
Ojo Alamo	4,041.0	3,203.0	SS / SH	
Kirtland	3,828.0	3,416.0	SH	
Fruitland	3,566.0	3,678.0	Coal / SH / SS	Possible Lost Circulation
Pictured Cliffs	3,416.0	3,828.0	SS	Water / Gas
Lewis Shale	3,330.0	3,914.0	SH	Set Casing 200' below top
Huerfanito	2,938.0	4,306.0	SH	
Chacra	2,474.0	4,770.0	Siltstone	Water / Gas
Mesaverde	1,749.0	5,495.0	Coal / SH / SS	
Cliff House	1,749.0	5,495.0	SS	Water / Gas
Menefee	1,620.0	5,624.0	Coal / SH / SS	
Point Lookout	1,200.0	6,044.0	SS	Possible Lost Circulation
Mancos Shale	1,060.0	6,184.0	SH	
Gallup	16.0	7,228.0	SS / SH	GAS
Tocito	-313.0	7,557.0	SS	
Juan Lopez	-421.0	7,665.0	SS	
Greenhorn	-723.0	7,967.0	LMST	
Graneros Shale	-786.0	8,030.0	SH	
Dakota Formation	-833.0	8,077.0	SS / SH / Coal	GAS
Morrison	-1,133.0	8,377.0	SH/SS	
TD	-1,233.0	8,477.0		TD 100' into Morrison

All fresh water and prospectively valuable minerals encountered during drilling and will be recorded by depth and adequately protected.

3. Pressure Control Equipment, CDX Minimum Specifications:

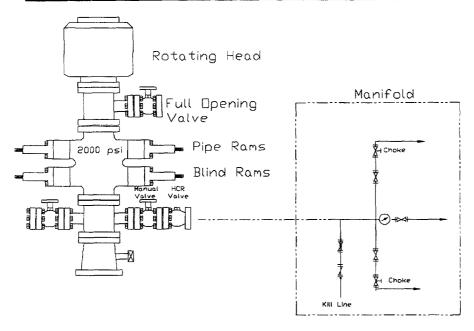

- A. BOP will consist of 2000-psi double ram BOP with a rotating head.
- B. Kill line and Choke line will be minimum 2" 2000 psi rating with pressure gauge on choke manifold.
- C. Ram type preventers and associated equipment shall be tested to approved stack working pressure if isolated by test plug or to 70 percent of internal yield pressure of casing. Pressure shall be maintained for at least 10 minutes or until requirements of test are met, whichever is longer. If a test plug is utilized, no bleed-off pressure is acceptable. For a test not utilizing a test plug, if a decline in pressure of more than 10 percent in 30 minutes occurs, the test shall be considered to have failed. Valve on casing head below test plug shall be open during test of BOP stack.
- D. Annular type preventers (if used) shall be tested to 50 percent of rated working pressure. Pressure shall be maintained for at least 10 minutes or until provisions of test are met, whichever is longer.
- E. As a minimum, the above test shall be performed:
 - 1. When initially installed
 - 2. Whenever any seal subject to test pressure is broken
 - 3. Following related repairs
 - 4. At 30-day intervals
- F. Valves shall be tested from working pressure side during BOP tests with all down stream valves open.
- G. When testing the kill line valve(s) the check valve shall be held open or the ball removed.
- H. Annular preventers shall be functionally operated at least weekly.
- 1. Pipe and blind rams shall be activated each trip, however, this function need not be performed more than once a day.
- J. A BOP pit level drill shall be conducted weekly for each drilling crew.
- K. Pressure tests shall apply to all related well control equipment.
- L. All of the above described tests and/or drills shall be recorded in the drilling log.

- Drilling Plan
 - M. BOP systems shall be consistent with API RP53. Pressure tests will be conducted before drilling out from under casing strings which have been set and cemented in place. Blowout preventer controls will be installed prior to drilling the surface casing plug and will remain in use until well is completed or abandoned. Preventers will be inspected and operated at least daily to ensure good mechanical working order, and this inspection will be recorded on the daily drilling report. Preventers will be pressure tested before drilling casing cement plugs.
 - N. The District Office should be notified, with sufficient lead-time, in order to have the BLM representative on location during pressure testing.
 - 1. The size and rating of the BOP stack is shown on the attached diagram. Although a rig has not been chosen to drill this well, most of the equipment for this depth of hole in the area uses a 2000-psi working pressure blowout preventer.
 - 2. A choke line and a kill line are to be properly installed. The kill line is <u>not</u> to be used as a fill-up line.
 - 3. The accumulator system shall have a pressure capacity to provide for repeated operation of hydraulic preventers.
 - 4. Drill string safety valve(s), to fit <u>all</u> tools in the drill string, are to be maintained on the rig floor while drilling operations are in progress.

4. Proposed Casing Program:

The proposed casing and cementing program shall be conducted as approved to protect and/or isolate all usable water zones, potentially productive zones, lost circulation zones, abnormally pressured zones, and any prospectively valuable deposits of minerals. Any isolating medium other than cement shall receive approval prior to use. The casing setting depth shall be calculated to position the casing seat opposite a competent formation, which will contain the maximum pressure to which it will be exposed during normal drilling operations. Determination of casing setting depth shall be based on all relevant factors, including; presence/absence of hydrocarbons; fracture gradients; usable water zones; formation pressures; lost circulation zones; other minerals; or other unusual characteristics. All indications of usable water shall be reported.

SURFACE

Setting	Depth								
TVD	MD	Length	Size	Weight	Grade	Threads	ID	Drift	Conn OD
300.0 ft	300.0 ft	300.0 ft	9.625 in	32.30 #/ft	H40	STC	9.0 in	8.8 in	10.6 in
			COLLAPSE						
	BURST		C	OLLAPSE			TENSILE		Optimum
Rated	BURST Load	S.F.	CO Rated	DLLAPSE Load	S.F.	Rated	TENSILE Load	S.F.	Optimum Torque

Intermediate

Setting	Depth									
TVD	MD	Length	Size	Weight	Grade	Threads	ID	Drift	Conn OD	
4,115.0 ft	4,115.0 ft	4,115.0 ft	7.000 in	20.0 #/ft	J55	STC	6.5 in	6.3 in	7.656 in	
	BURST		C	OLLAPSE			TENSILE		Optimum	
Rated	Load	S.F.	Rated	Load	S.F.	Rated	Load	S.F.	Torque	
- reacco			raica	Loud	T T	14400	LOAG	3.1.	tvique	

Production Casing Design

Set	ting D	Pepth												
TVD		MD	Length		Size		Weight		Grade	Threads	ID		Drift	Conn OD
8,477.0	ft	8,477.0 ft	8,477.0	ft	4.500	in	11.60	#/ft	N80	LTC	4.0	in	3.9 in	5.000 in
	BURST				COLLAPSE					TENSILE				
		BURST				C	DLLAPSE				TENSILE			Optimum
Rated		BURST Load	S.F.		Rated		DLLAPSE Load		S.F.	Rated	TENSILE Load		S.F.	Optimum Torque

- A. Casing design shall assume formation pressure gradients of 0.44 to 0.50 psi per foot for exploratory wells (lacking better data).
- B. Casing design shall assume fracture gradients from 0.70 to 1.00 psi per foot for exploratory wells (lacking better data).
- C. Casing collars shall have a minimum clearance of 0.422 inches on all sides in the hole/casing annulus, with recognition that variances can be granted for justified exceptions.
- D. All waiting on cement times shall be adequate to achieve minimum of 500-psi compressive strength at the casing shoe prior to drilling out.
- E. All casing, except the conductor casing, shall be new or reconditioned and tested used casing that meets or exceeds API standards for new casing.
- F. The surface casing shall be cemented back to surface either during the primary cement job or by the remedial cementing.
- G. All indications of usable water shall be reported to the authorized officer prior to running the next string of casing or before plugging orders are requested, whichever occurs first.
- H. Centralizers will be run on the bottom three joints of the surface casing with a minimum of 1 centralizer per joint starting with the shoe joint.
- Top plugs shall be used to reduce contamination of cement by displacement fluid. A bottom
 plug or other acceptable technique, such as a suitable pre-flush fluid, inner string cement
 method, etc. shall be utilized to help isolate the cement from contamination by the mud fluid
 being displaced ahead of the cement slurry.
- J. All Casing strings below the conductor shall be pressure tested to 0.22 psi per foot of casing string length or 1500 psi, whichever is greater, but not to exceed 70 percent of the minimum internal yield. If pressure declines more than 10 percent in 30 minutes, corrective action shall be taken.
- K. On all exploratory wells, and on that portion of any well approved for a 5M BOP system or greater, a pressure integrity test of each casing shoe shall be performed. Formation at the shoe shall be tested to a minimum of the mud weight equivalent anticipated to control the formation pressure to the next casing depth or at total depth of the well. This test shall be performed before drilling more than 20 feet of new hole.
- L. Casing design subject to revision based on geologic conditions encountered.

M. Proposed Cementing Program:

Surface Excess	0 125%	-	300	Tail	165 sx	Type III Omt + 2% CaO2 + 0.25 pps Celloflake	Yield Density	1.39 ft3/sx 14.6 ppg
Intermediate Excess	0 75%	-	4115	Lead 1	211 sx	Premium Lite FM +8% Gel + 3% CaOl2 + LOM	Yield Density	2.14 ft3/sx 12.1 ppg
				Tail 1	100 sx	Type III + 2% CaCl2 + 0.2% FL-52 + LCM	Yield Density	1.4 ft3/sx 14.6 ppg
				Tail 2	450 sx	Premium Lite FM +8% Gel + 3% CaCl2 + LCM	Yield Density	2.14 ft3/sx 12.1 ppg
Production Excess	3615 50%	-	8477	Lead	80 sx	Premium Lite HS+2% CaCl2 +0.75% FL52 +LCM		2.38 ft3/sx 11.9 ppg
				Tail	323 sx	Premium Lite HS+2% CaO2 +0.75% FL52 +LOM		2.02 ft3/sx 12.5 ppg

^{*}Actual volumes to be calculated from caliper log.

 Anticipated cement tops will be reported as to depth; not the expected number of sacks of cement to be used. The District Office should be notified, with sufficient lead time, in order to have a BLM representative on location while running all casing strings and cementing.

^{*}Depending on hole conditions Foam Cement may be run for production casing. If Foam cement is run the cement will be circulated to surface.

- 2. After cementing but before commencing any test, the casing string shall stand cemented until the cement has reached a compressive strength of at least 500 psi at the shoe. WOC time shall be recorded in the driller's log.
- N. The following report shall be filed with the District Manager within 30 days after the work is completed.
 - 1. Progress reports, Form 3160-5 (formerly 9-331) "Sundry Notices and Reports on Wells," must include complete information concerning:
 - Setting of each string of casing showing the size, grade, weight of casing set, hole size, setting depth, amount and type of cement used, whether cement circulated or the top of the cement behind the casing, depth of cementing tools used, casing test method and results, and the date work was done. Show the spud date on the first reports submitted.
 - 3. Temperature or bond logs must be submitted for each well where the casing cement was not circulated to the surface.

5. Mud Program:

Section	Interval	Mud Type	MW	PP
Surface	0 - 300	Fresh water gel and native clays	9.00	8.40
Intermediate	300 - 4115	Fresh water with polymer for reology. Mud up to LSNO system prior to Fruitland	8.5-9.0	8.40
Production	4115 - 8477	Air or Air/Mist. Mudding up to Fresh Water / Polymer system if hole conditions dictate.	<8.7	<8.5

- A. Sufficient quantities of mud materials will be maintained or readily accessible for the purpose of assuring well control during the course of drilling operations.
- B. A mud test shall be performed every 24 hours after mudding up to determine, as applicable: density, viscosity, gel strength, static filtration loss, and Ph.
- C. Mud monitoring equipment to be used is as follows:
 - Periodic checks of the mud system will be made each tour. The mud level will be checked visually.
 - No chromate additives will be used in the mud system on Federal and/or Indian lands without prior BLM approval to ensure adequate protection of fresh water aquifers.
 - 3. No chemicals subject to reporting under SARA Title III in an amount equal to or greater than 10,000 pounds will be used, produced, stored, transported, or disposed of annually in association with the drilling of this well. Furthermore, no extremely hazardous substances, as defined in 40 CFR 355, in threshold planning quantities, will be used, produced, stored, transported, or disposed of in association with the drilling of this well.
 - 4. The use of materials under BLM jurisdiction will conform to 43 CFR 3610.2-3.

6. Evaluation Program:

The anticipated type and amount of testing, logging and coring are as follows:

A. No drill stem tests are anticipated, however, if they are run the following will be adhered to... Initial opening of drill stem test tools shall be restricted to daylight hours unless specific approval to start during other hours is obtained from the authorized officer. However, DST's may be allowed to continue at night if the test was initiated during daylight hours and the rate of flow is stabilized and if adequate lighting is available (i.e. lighting which is adequate for visibility and vapor-proof for safe operations). Packers can be released, but tripping shall not begin before daylight, unless prior approval is obtained from the authorized officer. Closed chamber DST's may be accomplished day or night.
