


UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
OMB No. 1004-0136
Expires November 30, 2000

APPLICATION FOR PERMIT TO DRILL OR REENTER

1a. Type of Work: <input checked="" type="checkbox"/> DRILL <input type="checkbox"/> REENTER		5. Lease Serial No. SF-078343
1b. Type of Well: <input type="checkbox"/> Oil Well <input checked="" type="checkbox"/> Gas Well <input type="checkbox"/> Other <input checked="" type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone		6. If Indian, Allottee or Tribe Name
2. Name of Operator CONOCOPHILLIPS COMPANY Contact: VICKI WESTBY E-Mail: Vicki.R.Westby@conocophillips.com		7. If Unit or CA Agreement, Name and No.
3a. Address 4001 PENBROOK, SUITE 346 ODESSA, TX 79762		8. Lease Name and Well No. SAN JUAN 29-5 UNIT 18C
3b. Phone No. (include area code) Ph: 915.368.1352		9. API Well No. 30-039-29218
4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface NWNW 885FNL 835FWL At proposed prod. zone		10. Field and Pool, or Exploratory BLANCO MESAVERDE
14. Distance in miles and direction from nearest town or post office*		11. Sec., T., R., M., or Blk. and Survey or Area D Sec 5 T29N R5W Mer NMP
15. Distance from proposed location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any)	16. No. of Acres in Lease	12. County or Parish RIO ARRIBA ✓
18. Distance from proposed location to nearest well, drilling, completed, applied for, on this lease, ft.	19. Proposed Depth 6348 MD	13. State NM
21. Elevations (Show whether DF, KB, RT, GL, etc.) 6795 GL	22. Approximate date work will start	17. Spacing Unit dedicated to this well W/2



24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, shall be attached to this form:

- | | |
|---|--|
| 1. Well plat certified by a registered surveyor. | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above). |
| 2. A Drilling Plan. | 5. Operator certification |
| 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO shall be filed with the appropriate Forest Service Office). | 6. Such other site specific information and/or plans as may be required by the authorized officer. |

25. Signature (Electronic Submission)	Name (Printed/Typed) VICKI WESTBY	Date 08/27/2004
Title AGENT		
Approved by (Signature) <i>[Signature]</i>	Name (Printed/Typed)	Date 10-1-04
Title AFM		
Office FFO		

Application approval does not warrant or certify the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

Additional Operator Remarks (see next page)

Electronic Submission #35310 verified by the BLM Well Information System
For CONOCOPHILLIPS COMPANY, sent to the Farmington

DRILLING OPERATIONS AUTHORIZED ARE
SUBJECT TO COMPLIANCE WITH ATTACHED
"GENERAL REQUIREMENTS".

This action is subject to technical and
procedural review pursuant to 43 CFR 3165.3
and appeal pursuant to 43 CFR 3165.4



** OPERATOR-SUBMITTED ** OPERATOR-SUBMITTED ** OPERATOR-SUBMITTED **

NMOCD

District I
PO Box 1980, Hobbs, NM 88241-1980

District II
PO Drawer DD, Artesia, NM 88211-0719

District III
1000 Rio Brazos Rd., Aztec, NM 87410

District IV
PO Box 2088, Santa Fe, NM 87504-2088

State of New Mexico
Energy, Minerals & Natural Resources Department

OIL CONSERVATION DIVISION
PO Box 2088
Santa Fe, NM 87504-2088

Form C-102
Revised February 21, 1994
Instructions on back
Submit to Appropriate District Office
State Lease - 4 Copies
Fee Lease - 3 Copies

AMENDED REPORT

WELL LOCATION AND ACREAGE DEDICATION PLAT

*API Number 30-039-29218		*Pool Code 72319	*Pool Name BLANCO MESAVERDE
*Property Code 31325	*Property Name SAN JUAN 29-5 UNIT		*Well Number 18C
*OGRID No. 217817	*Operator Name CONOCOPHILLIPS COMPANY		*Elevation 6795'

¹⁰ Surface Location

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
D	5	29N	5W		885	NORTH	835	WEST	RIO ARriba

¹¹ Bottom Hole Location If Different From Surface

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County

¹² Dedicated Acres 321.0 Acres - W/2	¹³ Joint or Infill	¹⁴ Consolidation Code	¹⁵ Order No.
--	-------------------------------	----------------------------------	-------------------------

NO ALLOWABLE WILL BE ASSIGNED TO THIS COMPLETION UNTIL ALL INTERESTS HAVE BEEN CONSOLIDATED OR A NON-STANDARD UNIT HAS BEEN APPROVED BY THE DIVISION

¹⁶

¹⁷ OPERATOR CERTIFICATION

I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief

Vicki Westby (pf)
Signature
Vicki R. Westby
Printed Name
Sr. Analyst
Title
8/27/04
Date

¹⁸ SURVEYOR CERTIFICATION

I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief.

Date of Survey: JUNE 9, 2004

Signature and Seal of Professional Surveyor

JASON C. EDWARDS
Certificate Number 15269

Submit 3 Copies To Appropriate District Office
 District I
 1625 N. French Dr., Hobbs, NM 88240
 District II
 1301 W. Grand Ave., Artesia, NM 88210
 District III
 1000 Rio Brazos Rd., Aztec, NM 87410
 District IV
 1220 S. St. Francis Dr., Santa Fe, NM 87505

State of New Mexico
 Energy, Minerals and Natural Resources

Form C-103
 May 27, 2004

OIL CONSERVATION DIVISION
 1220 South St. Francis Dr.
 Santa Fe, NM 87505

SUNDRY NOTICES AND REPORTS ON WELLS (DO NOT USE THIS FORM FOR PROPOSALS TO DRILL OR TO DEEPEN OR PLUG BACK TO A DIFFERENT RESERVOIR. USE "APPLICATION FOR PERMIT" (FORM C-101) FOR SUCH PROPOSALS.)		WELL API NO.
1. Type of Well: Oil Well <input type="checkbox"/> Gas Well <input checked="" type="checkbox"/> Other <input type="checkbox"/>		5. Indicate Type of Lease STATE <input type="checkbox"/> FEE <input type="checkbox"/>
2. Name of Operator ConocoPhillips Company		6. State Oil & Gas Lease No.
3. Address of Operator 4001 Penbrook, Odessa, TX 79762		7. Lease Name or Unit Agreement Name <i>San Juan 29-5 unit</i>
4. Well Location Unit Letter <u>D</u> : <u>885</u> feet from the <u>North</u> line and <u>835</u> feet from the <u>West</u> line Section <u>5</u> Township <u>29N</u> Range <u>5W</u> NMPM <u>Rio Arriba</u> County		8. Well Number <u>18C</u>
11. Elevation (Show whether DR, RKB, RT, GR, etc.) <u>6795</u> GL		9. OGRID Number <u>217817</u>
Pit or Below-grade Tank Application <input type="checkbox"/> or Closure <input type="checkbox"/>		10. Pool name or Wildcat <u>Blanco Mesa Verde</u>
Pit type <u>Drill</u> Depth to Groundwater <u>50-100'</u> Distance from nearest fresh water well <u>>1000'</u> Distance from nearest surface water <u>200-1000'</u>		
Pit Liner Thickness: _____ mil Below-Grade Tank: Volume _____ bbls; Construction Material _____		

12. Check Appropriate Box to Indicate Nature of Notice, Report or Other Data

NOTICE OF INTENTION TO: PERFORM REMEDIAL WORK <input type="checkbox"/> PLUG AND ABANDON <input type="checkbox"/> TEMPORARILY ABANDON <input type="checkbox"/> CHANGE PLANS <input type="checkbox"/> PULL OR ALTER CASING <input type="checkbox"/> MULTIPLE COMPL <input type="checkbox"/>		SUBSEQUENT REPORT OF: REMEDIAL WORK <input type="checkbox"/> ALTERING CASING <input type="checkbox"/> COMMENCE DRILLING OPNS. <input type="checkbox"/> P AND A <input type="checkbox"/> CASING/CEMENT JOB <input type="checkbox"/>	
OTHER: Drill Pit Notification <input checked="" type="checkbox"/>		OTHER: <input type="checkbox"/>	

13. Describe proposed or completed operations. (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work). SEE RULE 1103. For Multiple Completions: Attach wellbore diagram of proposed completion or recompletion.

ConocoPhillips Company's Generic Pit Plan is on file at NMOCD in Aztec, NM. See the attached diagram that details the location of the pit in reference to the proposed wellhead. The drill pit will be lined. The drill pit will be closed after the well has been completed. The solids left after the water has been disposed of will be sampled and NMOCD approval will be obtained prior to closure of this pit.

I hereby certify that the information above is true and complete to the best of my knowledge and belief. I further certify that any pit or below-grade tank has been/will be constructed or closed according to NMOCD guidelines , a general permit or an (attached) alternative OCD-approved plan .


SIGNATURE Vicki Westby TITLE St. Analyst DATE 8/27/04

Type or print name Vicki Westby E-mail address: Vicki.R.Westby@ConocoPhillips.com Telephone No. 432-368-1352

APPROVED BY: [Signature] TITLE DEPUTY OIL & GAS INSPECTOR, DIST. #4 DATE OCT - 5 2004




Conditions of Approval (if any):

CONOCOPHILLIPS COMPANY SAN JUAN 29-5 UNIT #18C
885' FNL & 835' FWL, SECTION 5, T29N, R5W, NMPM
RIO ARRIBA COUNTY, NEW MEXICO ELEVATION: 6795'

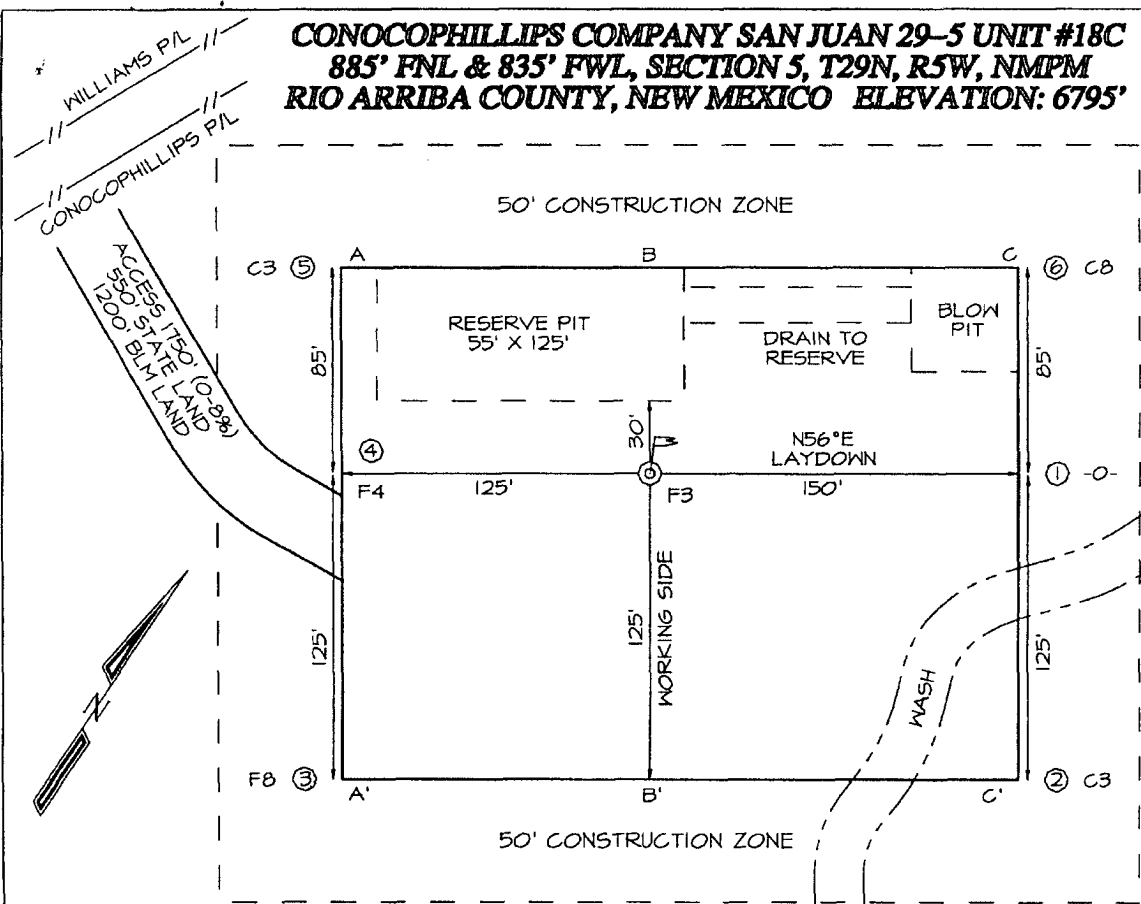

LATITUDE: 36.75946° N
LONGITUDE: 107.38631° W
 DATUM: NAD1927

PLAT NOTE:
 SURFACE OWNER
 Bureau of Land
 Management

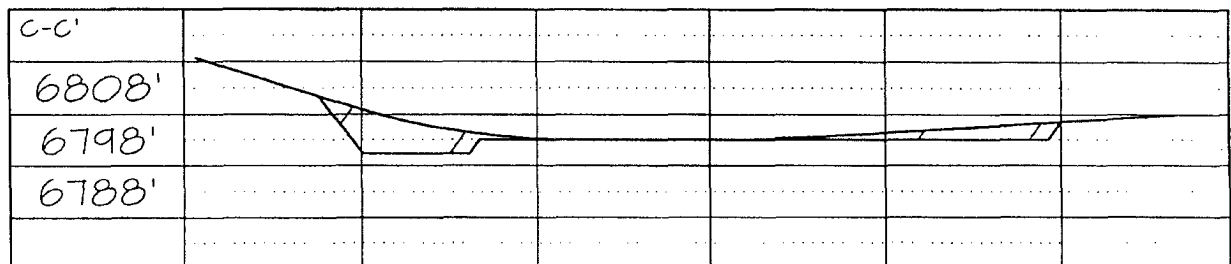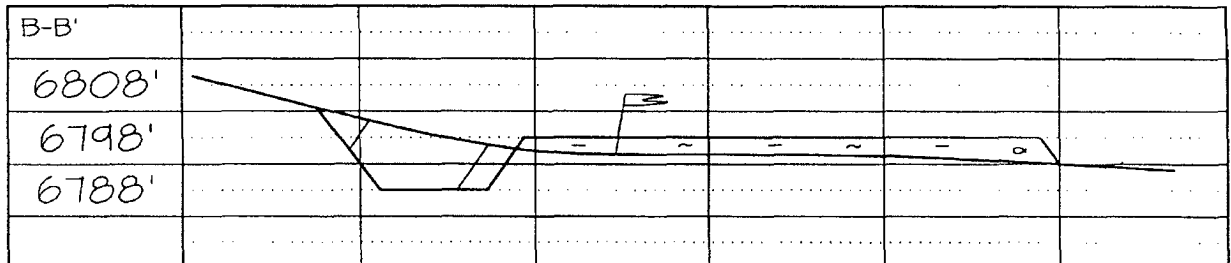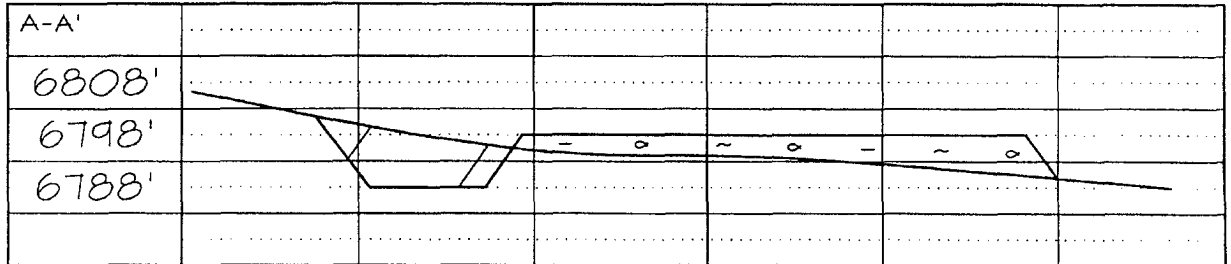

PROJECT PROPOSAL - New Drill / Sidetrack

SAN JUAN 29-5 18C

Lease:	AFE #: WAN.CNV.4135			AFE \$:
Field Name: hPHILLIPS 29-5	Rig: MACKLON Rig 3	State: NM	County: RIO ARRIBA	API #:
Geoscientist: Glaser, Terry J	Phone: (832)486-2332	Prod. Engineer: Moody, Craig E.	Phone: (281) 293 - 6559	
Res. Engineer: Johnson, Tom B.	Phone: (832)-486-2347	Proj. Field Lead: Franssen, Eric E.	Phone:	

Primary Objective (Zones):

Zone	Zone Name
RON	BLANCO MESAVERDE (PRORATED GAS)

Location: Surface **Straight Hole**

Latitude: 36.76	Longitude: -107.39	X:	Y:	Section: 5	Range: 5W
Footage X: 835 FWL	Footage Y: 885 FNL	Elevation: 6795 (FT)	Township: 29N		
Tolerance:					

Location Type: Summer Only	Start Date (Est.):	Completion Date:	Date In Operation:
Formation Data: Assume KB = 6808	Units = FT		

Formation Call & Casing Points	Depth (TVD in Ft)	SS (Ft)	Depletion (Yes/No)	BHP (PSIG)	BHT	Remarks
SURFACE CSG	213	6595	<input type="checkbox"/>			Severe Lost Circulation is possible. 12 1/4" Hole. 9 5/8" 32.3 ppf, H-40, STC casing. Circulate cement to surface.
NCMT	1518	5290	<input type="checkbox"/>			
OJAM	2953	3855	<input type="checkbox"/>			Possible water flows.
KRLD	3073	3735	<input type="checkbox"/>			
FRLD	3388	3420	<input type="checkbox"/>			Possible gas.
PCCF	3758	3050	<input type="checkbox"/>			
Intermediate Casing	3958	2850	<input type="checkbox"/>			8 3/4" Hole. 7", 20 ppf, J-55, STC Casing. Circulate cement to surface.
LEWS	4058	2750	<input type="checkbox"/>			
CHRA	4778	2030	<input type="checkbox"/>			
CLFH	5628	1180	<input type="checkbox"/>			Gas; possibly wet
MENF	5683	1125	<input type="checkbox"/>			Gas.
PTLK	5948	860	<input type="checkbox"/>	2000		Gas.
Total Depth	6348	460	<input type="checkbox"/>			6 1/4" Hole. 4 1/2", 10.5 ppf, J-55, LTC casing. Circulate cement a minimum of 100' inside the previous casing string. No open hole logs. Cased hole TDT with GR to surface.

Reference Wells:

Reference Type	Well Name	Comments

Logging Program:

Intermediate Logs: Log only if show GR/ILD Triple Combo


TD Logs: Triple Combo Dipmeter RFT Sonic VSP TDT

Additional Information:

Comments: General/Work Description -

Drilling Mud Program:
 Surface: spud mud
 Intermediate: fresh water mud with bentonite and polymer as needed
 Below Intermediate: air/nitrogen/mist drilling media with foamer, polymer, & corrosion inhibitor as needed

San Juan 29-5 # 18C



SURFACE CASING :

Drill Bit Diameter	12.25"	
Casing Outside Diameter	9.625"	Casing Inside Diam. 9.001"
Casing Weight	32.3	ppf
Casing Grade	H-40	
Shoe Depth	230'	
Cement Yield	1.21	cuft/sk
Excess Cement	125	%
Cement Required	147	sx

SHOE 230', 9.625", 32.3 ppf, H-40 STC

INTERMEDIATE CASING :

Drill Bit Diameter	8.75"	
Casing Outside Diameter	7"	Casing Inside Diam. 6.456"
Casing Weight	20	ppf
Casing Grade	J-55	
Shoe Depth	3958'	
Lead Cement Yield	2.88	cuft/sk
Lead Cement Excess	150	%
Tail Cement Length	791.6	'
Tail Cement Yield	1.33	cuft/sk
Tail Cement Excess	150	%
Lead Cement Required	397	sx
Tail Cement Required	231	sx

SHOE 3958', 7", 20 ppf, J-55 STC

PRODUCTION CASING :

Drill Bit Diameter	6.25"	
Casing Outside Diameter	4.5"	Casing Inside Diam. 4.000"
Casing Weight	11.6	ppf
Casing Grade	N-80	
Top of Cement	3758'	200' inside intermediate casing
Shoe Depth	6348'	
Cement Yield	1.45	cuft/sk
Cement Excess	50	%
Cement Required	270	sx

SHOE 6348', 4.5", 10.5 ppf, J-55 LTC

San Juan 29-5 # 18C			
	Surf. Csg	Int. Csg	Prod. Csg
OD	9.625	7	4.5
ID	9.001	6.456	4.000
Depth	230	3958	6348
Hole Diam	12.25	8.75	6.25
% Excess Lead		150	
% Excess Tail	125	150	50
Lead Yield		2.88	
Tail Yield	1.21	1.33	1.45
Ft of Tail Slurry	230	791.6	2590
Top of Tail Slurry	0	3166.4	3758
Top of Lead Slurry	N/A	0	N/A
Mud Wt (ppg)	8.9	9.0	air dril
Mud Type	WBM	WBM	air dril

Surface Casing						
	Ft	Cap	XS Factor	bbls	cuft	sx
Open Hole Annulus	230	0.055804	2.25	28.9	162.1	134.0
Shoe Track Volume	40	0.078735	1	3.1	17.7	13.3
Total				32.0	179.8	147.3

Intermediate Casing						
	Ft	Cap	XS Factor	bbls	cuft	sx
Lead Open Hole Annulus	2936.4	0.026786	2.5	196.6	1104.0	383.3
Lead Cased Hole Annulus	220	0.031116	1	6.8	38.4	13.3
Lead Total				203.5	1142.4	396.7
Tail Open Hole Annulus	791.6	0.026786	2.5	53.0	297.6	223.8
Tail Shoe Track Volume	42	0.040505	1	1.7	9.6	7.2
Tail Total				54.7	307.2	231.0

Production Casing						
	Ft	Cap	XS Factor	bbls	cuft	sx
Open Hole Annulus	2390	0.018282	1.5	65.5	368.0	253.8
Cased Hole Annulus	200	0.020826	1	4.2	23.4	16.1
Total				69.7	391.4	269.9

San Juan 29-5 # 18C		
9-5/8 Surface Casing		
Cement Recipe	Class C Standard Cement	
	+ 3% Calcium Chloride	
	+0.25 lb/sx Flocele	
Cement Volume	147	sx
Cement Yield	1.21	cuft/sx
Slurry Volume	179.8	cuft
	32.0	bbls
Cement Density	15.6	ppg
Water Required	5.29	gal/sx
Compressive Strength		
Sample cured at 60 deg F for 8 hrs		
4hrs 38 mins	50	psi
9hrs	250	psi


San Juan 29-5 # 18C

7" Intermediate Casing		
Lead Slurry		
Cement Recipe	Standard Cement	
	+ 3% Econolite (extender)	
	+ 10 lb/sx Pheno Seal	
Cement Required	397	sx
Cement Yield	2.88	cuft/sx
Slurry Volume	142.4	cuft
	203.5	bbls
Cement Density	11.5	ppg
Water Required	16.91	gal/sx
Compressive Strength		
Sample cured at 130 deg F for 24 hrs		
1 hr 47 min	50	psi
12 hr	350	psi
24 hr	450	psi


7" Intermediate Casing		
Tail Slurry		
Cement Slurry	50 / 50 POZ:Standard Cement	
	+ 2% Bentonite	
	+ 6 lb/sx Pheno Seal	
Cement Required	231	sx
Cement Yield	1.33	cuft/sx
Slurry Volume	307.2	cuft
	54.7	bbls
Cement Density	13.5	ppg
Water Required	5.52	gal/sx
Compressive Strength		
Sample cured at 130 deg F for 24 hrs		
2 hr 05 min	50	psi
4 hr 06 min	500	psi
12 hr	1250	psi
24 hr	1819	psi

San Juan 29-5 # 18C	
4-1/2" Production Casing	
Cement Recipe	50 / 50 POZ: Standard Cement
	+ 3% Bentonite
	+ 3.5 lb/sx PhenoSeal
	+ 0.2% CFR-3 Friction Reducer
	+ 0.1% HR-5 Retarder
	+ 0.8% Halad-9 Fluid Loss Additive
Cement Quantity	270 sx
Cement Yield	1.45 cuft/sx
Cement Volume	391.4 cuft
	69.7
Cement Density	13.1 ppg
Water Required	6.47 gal/sx
Compressive Strength	
Sample cured at 200 deg F for 23 hrs	
9 hr 50 min	50 psi
13 hr 45 min	500 psi
16 hr	1500 psi
23 hr	2525 psi

BLOWOUT PREVENTER ARRANGEMENT & PROGRAM
For Drilling to Intermediate Casing Point & Setting 7" Intermediate Casing

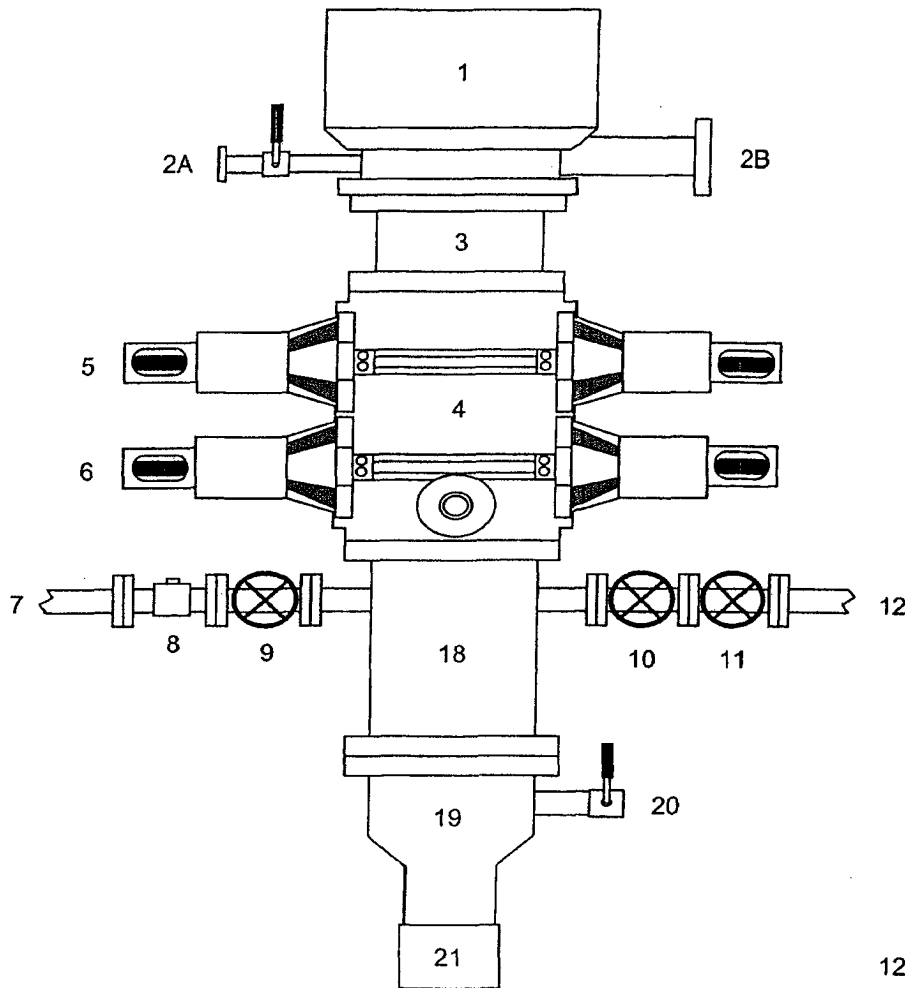

1. Rotating Head
- 2A. Fill-up Line & valve
- 2B. Flowline
3. Spacer Spool
4. Double Ram BOP (11", 3000 psi)
5. Pipe Rams
6. Blind Rams
7. Kill Line
8. Kill Line Check Valve
9. Kill Line Valve
10. Inner Choke Line Valve (3")
11. Outer Choke Line Valve (3")
12. Choke Line (3")
13. Variable Choke
14. Choke Line Valve (2")
15. Panic Line Valve (3")
16. Choke Manifold Pressure Gauge
17. Choke Line (2")
18. Mud Cross Spacer Spool
19. Casing Head "A" Section
20. Casing Head "A" Section 2" Valve
21. 9 5/8" Casing Collar

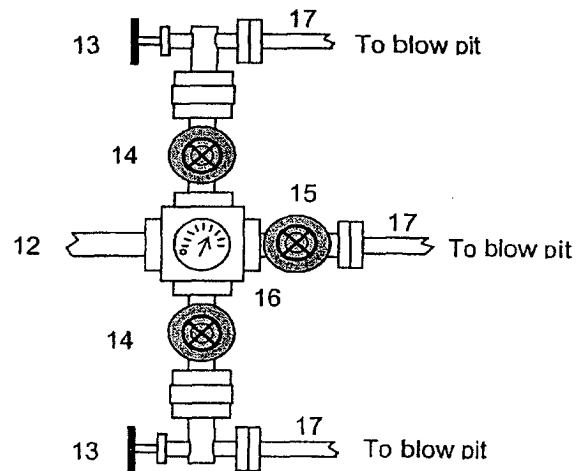


A 12-1/4" hole will be drilled to approximately 220' and the 9-5/8" surface casing will be run and cemented. The Casing Head "A" Section will be screwed onto the 9-5/8" surface casing stub. The BOP will be installed on the Casing Head "A" Section. A test plug will be set in the wellhead and the pipe rams and choke manifold will be tested to 200 psi to 300 psi (low pressure test) for 2-3 minutes and to 1000 psi (high pressure test) for 10 minutes. Then the test plug will be removed, and the 9-5/8" casing will be pressure tested against closed blind rams to 200 psi to 300 psi for 2-3 minutes and to 1000 psi for 30 minutes (this value is one 44% of the minimum internal yield pressure of the 9-5/8" casing). (Note: per regulatory requirements we will wait on cement at least 8 hrs after placement before testing the 9-5/8" surface casing). Then an 8-3/4" hole will be drilled to intermediate casing point and 7" intermediate casing will be run and cemented.

In addition to the equipment in the above diagram the following equipment will comprise the BOP system:


1. Upper Kelly cock Valve with handle
2. Stab-in TIW valve for all drillstrings in use

BLOWOUT PREVENTER ARRANGEMENT & PROGRAM

For Drilling to TD and Setting 4.5 inch Casing

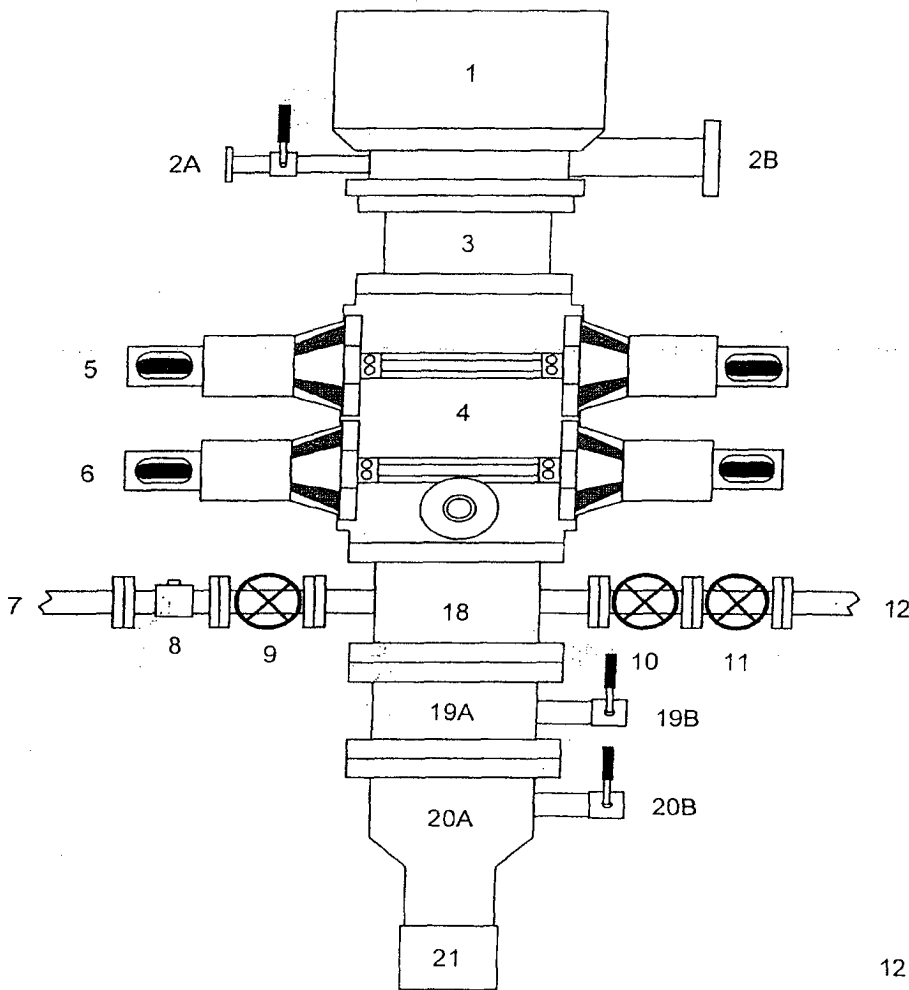

1. Rotating Head
- 2A. Fill-up Line & valve
- 2B. Bloeie Line (for Air Drilling)
3. Spacer Spool
4. Double Ram BOP (11", 3000 psi)
5. Pipe Rams
6. Blind Rams
7. Kill Line
8. Kill Line Check Valve
9. Kill Line Valve
10. Inner Choke Line Valve (3")
11. Outer Choke Line Valve (3")
12. Choke Line (3")
13. Variable Choke
14. Choke Line Valve (2")
15. Panic Line Valve (3")
16. Choke Manifold Pressure Gauge
17. Choke Line (2")
18. Mud Cross Spacer Spool
- 19A Csg Spool "B" Section (11", 3M)
- 19B "B" Section Csg Valve (2", 3M)
- 20A Csg-Head "A" Section (11", 3M)
- 20B "A" Section Csg Valve (2", 3M)
21. 9 5/8" Casing Collar

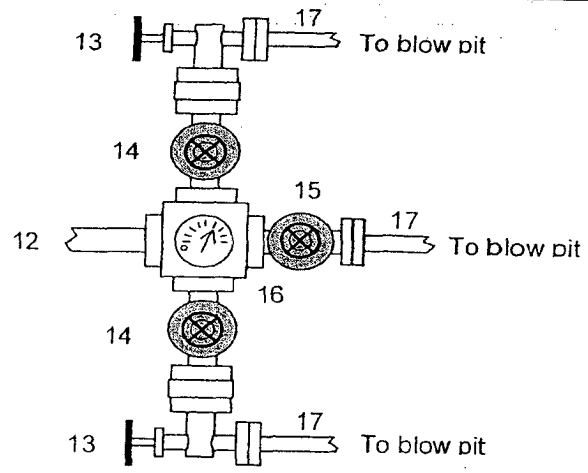

After the 7" intermediate casing has been run and cemented, the Casing Spool ("B" Section) will be installed on the wellhead ("A" Section) and the BOP will be installed on the Casing Spool. A test plug will be set in the wellhead and the pipe rams, blind rams, and choke manifold will be tested to 200 psi to 300 psi (low pressure test) for 2-3 minutes and to 3000 psi (high pressure test) for 10 minutes. Then the test plug will be removed and the 7" casing will be pressure tested against closed blind rams to 200 psi to 300 psi for 2-3 minutes and to 1800 psi for 30 minutes - this test pressure is 48% of the minimum internal yield strength of 3740 psi for the 7", 20#, J-55, STC casing. Then we will air drill the 6-1/4" hole to TD and run and cement the 4-1/2" casing.

In addition to the equipment in the above diagram the following equipment will comprise the BOP system:

1. Upper Kelly cock Valve with handle
2. Stab-in TIW valve for all drillstrings in use
