MC Com 8 #409H Basin Mancos/Lybrook Gallup (page 1)

Spud: 12/30/15


Completed: 3/18/16

SHL: 971' FSL & 2186' FWL SE/4 SW/4 Section 7 (N), T23N, R7W

BHL: 2326' FSL & 335' FWL NW/4 SW/4 Section 12 (L), T23N, R8W

Rio Arriba NM Elevation: 7307' API: 30-039-31337

Formation Name	MD		TVD
OJO ALAMO		1457	1447
KIRTLAND		1828	1810
PICTURE CLIFFS		2178	2153
LEWIS		2296	2269
CHACRA		2589	2556
CLIFF HOUSE		3677	3623
MENEFEE		3736	3681
PTLOOKOUT		4573	4501
MANCOS		4790	4714
GALLUP		5144	5061

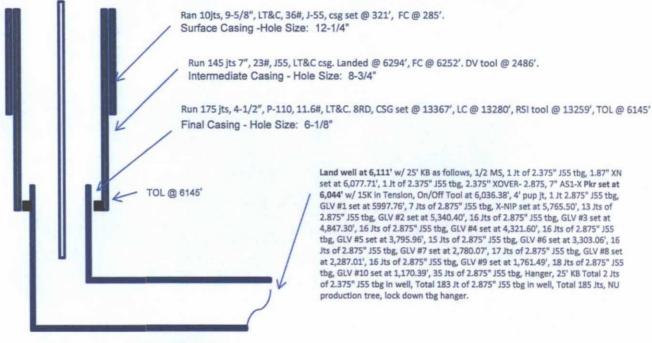

Land well at 6,111' w/ 25' KB as follows, 1/2 MS, 1 Jt of 2.375" J55 tbg, 1.87" XN set at 6,077.71', 1 Jt of 2.375" J55 tbg, 2.375" XOVER- 2.875, 7" AS1-X Pkr set at 6,044' w/ 15K in Tension, On/Off Tool at 6,036.38', 4' pup jt, 1 Jt 2.875" J55 tbg, GLV #1 set at 5997.76', 7 Jts of 2.875" J55 tbg, X-NIP set at 5,765.50', 13 Jts of 2.875" J55 tbg, GLV #2 set at 5,340.40', 16 Jts of 2.875" J55 tbg, GLV #3 set at 4,847.30', 16 Jts of 2.875" J55 tbg, GLV #4 set at 4,321.60', 16 Jts of 2.875" J55 tbg, GLV #5 set at 3,795.96', 15 Jts of 2.875" J55 tbg, GLV #6 set at 3,303.06', 16 Jts of 2.875" J55 tbg, GLV #7 set at 2,780.07', 17 Jts of 2.875" J55 tbg, GLV #8 set at 2,287.01', 16 Jts of 2.875" J55 tbg, GLV #9 set at 1,761.49', 18 Jts of 2.875" J55 tbg, GLV #10 set at 1,170.39', 35 Jts of 2.875" J55 tbg, Hanger, 25' KB Total 2 Jts of 2.375" J55 tbg in well, Total 183 Jt of 2.875" J55 tbg in well, Total 185 Jts, NU production tree, lock down tbg hanger.

TD: 13370' MD TVD: 5710' PBTD: 13280' MD

ft. Surface
it. Buildec
i.ft Surface
.ft. TOL 6145'
102011

OIL CONS. DIV DIST. 3 MAR 29 2016

Lg 3/21/16

