

RECEIVED

Form 3160-5  
(February 2005)UNITED STATES  
DEPARTMENT OF THE INTERIOR  
BUREAU OF LAND MANAGEMENT

OCT 05 2016

FORM APPROVED  
OMB No. 1004-0137  
Expires: March 31, 2007Farmington Field Office  
Bureau of Land Management

## SUNDRY NOTICES AND REPORTS ON WELLS

**Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.**

SUBMIT IN TRIPLICATE - Other instructions on page 2.

5. Lease Serial No.  
SP-078890

6. If Indian, Allottee or Tribe Name

7. If Unit of CA/Agreement, Name and/or No.  
Rosa Unit8. Well Name and No.  
Rosa Unit #389A9. API Well No.  
30-039-2950210. Field and Pool or Exploratory Area  
Basin Fruitland Coal11. Country or Parish, State  
Rio Arriba, NM

1. Type of Well

☐ Oil Well ☒ Gas Well ☐ Other

OIL CONS. DIV DIST. 3

OCT 07 2016

2. Name of Operator  
WPX Energy Production, LLC3a. Address  
PO Box 640 Aztec, NM 874103b. Phone No. (include area code)  
505-333-18164. Location of Well (Footage, Sec., T., R., M., or Survey Description)  
2450' FNL & 2380' FEL, Section 7, T31N, R 4W

## 12. CHECK THE APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, REPORT OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input checked="" type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input checked="" type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment Notice	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other MIT/TA
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug and Abandon	<input type="checkbox"/> Temporarily Abandon	
	<input type="checkbox"/> Convert to Injection	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	

13. Describe Proposed or Completed Operation: Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recompleat horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports must be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompleat in a new interval, a Form 3160-4 must be filed once testing has been completed. Final Abandonment Notices must be filed only after all requirements, including reclamation, have been completed and the operator has determined that the site is ready for final inspection.)

WPX requests to conduct a MIT in order to keep the well in TA status per attached procedure and wellbore diagram.

The last MIT was done on 10/28/11. WPX would like to save the well for possible future development.

**BLM'S APPROVAL OR ACCEPTANCE OF THIS ACTION DOES NOT RELIEVE THE LESSEE AND OPERATOR FROM OBTAINING ANY OTHER AUTHORIZATION REQUIRED FOR OPERATIONS ON FEDERAL AND INDIAN LANDS**

\* TA approved until 10/28/2017

14. I hereby certify that the foregoing is true and correct.

Name (Printed/Typed)

Lacey Granillo

Title Permitting Tech III

Signature

Date 10/5/16

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by

Title Petroleum Engineer

Date 10/6/2016

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Office FFO

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Instructions on page 2)

NMOCD

## Legacy MIT Procedure

**Well:** Rosa 389A

**API:** 30-039-29502

**Location:** Rio Arriba County, New Mexico

**S-T-R:** 7-31N-4W

**Date:** 4Oct16

**Objective:** Conduct Mechanical Integrity Test (MIT)

**AFE:** N/A

### EH&S Notes:

- ✓ Personnel Safety is the number one job, no exceptions.
- ✓ Please follow appropriate WPX Energy contractor protocols for this job plan. (Please see your WPX Energy Business Representative if you have any questions; Contractor protocols can be found in the WPX Energy Contractor Guide.)
- ✓ Continuous personal H2S monitoring is required. Any H2S alarms or other indications above 10 ppm will require work to stop and the situation to be evaluated
- ✓ A Safety meeting shall be held each morning before work and subsequent "tailgate" safety meetings are to be held during the day when operation objectives shift in nature and intent. Please ensure these are documented per the WPX Contractor Guide.

### Prior to Job:

- Notify BLM and NMOCD 24-48 hours prior to MIT such they can witness if they choose.
- Arrange for pump truck with chart recorder for MIT based on NMOCD witness availability.

**Current Wellbore Status:** Well is TA'd, CIBP @ 2,650'.

- Casing
  - 7" 23# J-55 LTC set @ 3,319'
  - Top of Cement @ surface.

### Procedure:

- Ensure BLM and NMOCD is present to witness or has given authorization to proceed with MIT w/o witness.
- Tie pump onto casing. Load hole as needed to perform MIT-hole should be full. Conduct 500-550 psi MIT for at least 30 minutes, recording pressure with a chart recorder per regulatory requirements. Turn chart into NMOCD as required.

### Notes:

- Ensure all JSA's, ECP's and Lockout procedures are in place for energized piping or equipment.



**ROSA UNIT #389A  
BASIN FRUITLAND COAL**

**Location:**

**SHL:** 2450' FNL and 2380' FEL  
SW/4 NE/4 Sec 07(G), T31N, R04W

**BHL:** 1028' FNL and 1074' FWL  
NW/4 NW/4 Sec 07(D), T31N, R04W  
Rio Arriba, New Mexico

**Elevation:** 6457' GR  
**API #** 30-039-29502

Spud date: 10/05/06

Completed: 11/09/06


1st Delivered: 11/20/06

Pump Install: 11/09/06

MIT: 10/28/11

Top	MD Depth
Ojo Alamo	2647'
Kirtland	2758'
Fruitland	3125'
Pictured Cliffs	3295'

Landed 95 jts 7", 23#, J-55, LT&C csg @ 3319'  
TMD, 3271' TVD. FC @ 3579' TMD, 3268'  
TVD. Cemented with 750 sx cmt.

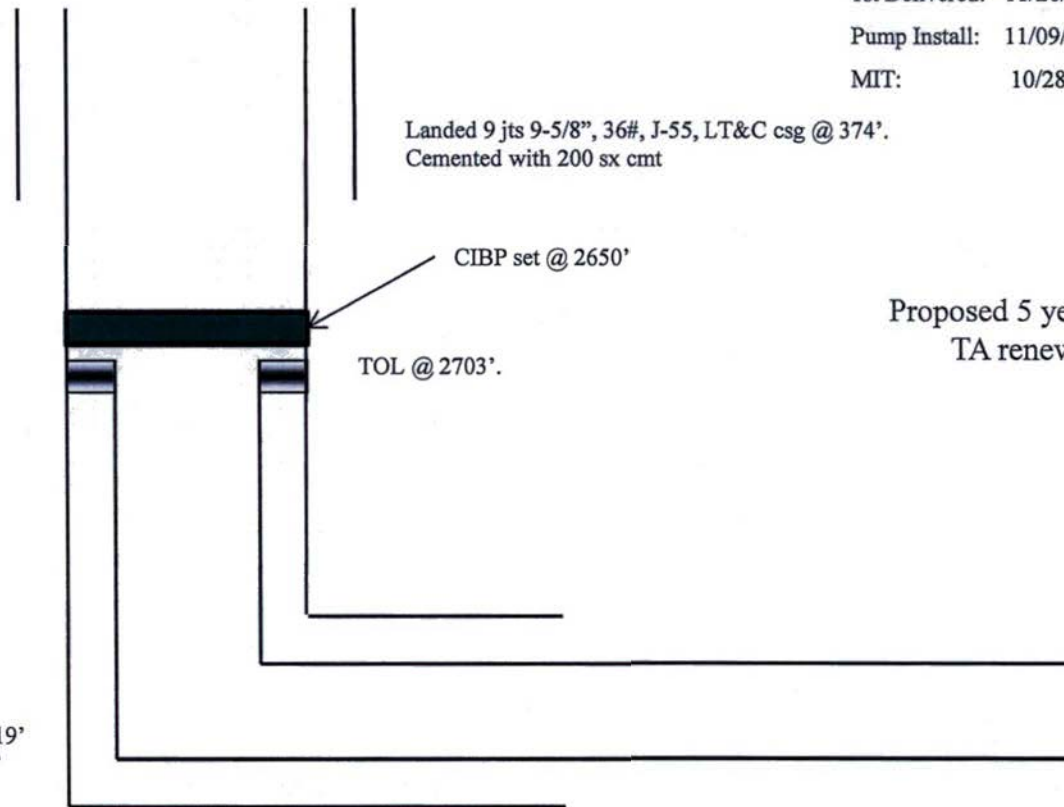

Landed 9 jts 9-5/8", 36#, J-55, LT&C csg @ 374'.  
Cemented with 200 sx cmt

CIBP set @ 2650'

TOL @ 2703'.

Proposed 5 year MIT  
TA renewal

TD @ 5163' TMD  
@ 3289' TVD

Landed 4-1/2" liner @ 5162' TMD, 3288' TVD, TOL @ 2703' as follows: liner hanger, 1 jt 4 1/2", 10.5#, J-55 non-perfed csg, 58 jts, 4 1/2", 11.6#, J-55 perfed csg & shoe on bottom. Liner perfs are from 2750' to 5160'. Total of 57,816 (0.50") holes.

Hole Size	Casing	Cement	Volume	Top of CMT
12-1/4"	9-5/8", 36#	200 sxs	280 cu.ft.	surface
8-3/4"	7", 23#	750 sxs	1464 cu.ft.	surface
6-1/4"	4-1/2", 11.6#	Did Not Cmt	N/A	N/A
