## KWU # 771H Kimbeto Wash Unit(page 1)

Spud: 5/19/16

Completed: 8/9/16


Amended TOL

SHL: 393' FSL & 1128' FEL SE/4 SE/4 Section 17(P), T23N, R9W

BHL: 334' FNL & 2193' FEL NW/4 NE/4 Section 18 (B), T23N, R9W

San Juan, NM Elevation: 6561' API: 30-045-35756

Formation	MD	TVD
PICTURE CLIFFS	802	802
LEWIS	924	923
CHACRA	1001	999
CLIFF HOUSE	2293	2217
MENEFEE	2309	2232
POINT LOOKOUT	3417	3258
MANCOS	3532	3364
GALLUP	3901	3706

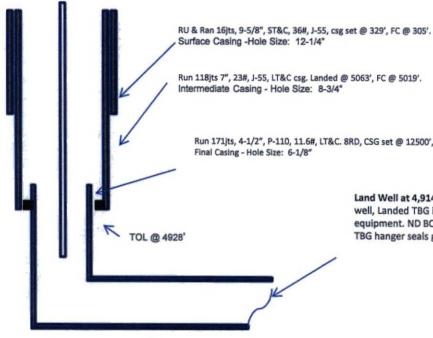

Run 118jts 7", 23#, J-55, LT&C csg. Landed @ 5063', FC @ 5019'.

Run 171jts, 4-1/2", P-110, 11.6#, LT&C. 8RD, CSG set @ 12500', LC @ 12406', RSI tool @ 12381', TOL @ 4928. .

Land Well at 4,914'. Total 163 Jt of 2.875" J55 tbg in well, Landed TBG in 10k Tension. RD rig floor and equipment. ND BOP stack and NU prod tree. Test TBG hanger seals good to 3000 psi.

TD: 12515' MD TVD: 4511' PBTD: 12406' MD

CASING	CEMENT	VOLUME	CMT TOP
9-5/8"	10 ls x	162cu.ft.	Surface
7"	780 sx	1260cu. ft.	Surface
4-1/2"	685 sx	932 cu. ft.	TOL 4928'
	7"	7" 780 sx	7" 780 sx 1260cu. ft.

LG 8/22/16

## **KWU # 771H** Kimbeto Wash Unit

MC 4th: •11609'-11765'-

(page 2 - lateral with completion)

