


Wellsite Data ALBUQUERQUE UNIT 101N

API / UWI 3004534408	Surface Legal Location 007-032N-006W-D	Field Name MV/DK COM	License No.	Well Configuration Type DEVIATED
Ground Elevation (ft) 6,243.00	Original KB/RT Elevation (ft) 6,258.00	KB-Ground Distance (ft) 15.00	KB-Casing Flange Distance (ft)	KB-Tubing Hanger Distance (ft) 6,258.00

DEVIATED - Original Hole, 10/16/2014 4:15:17 AM

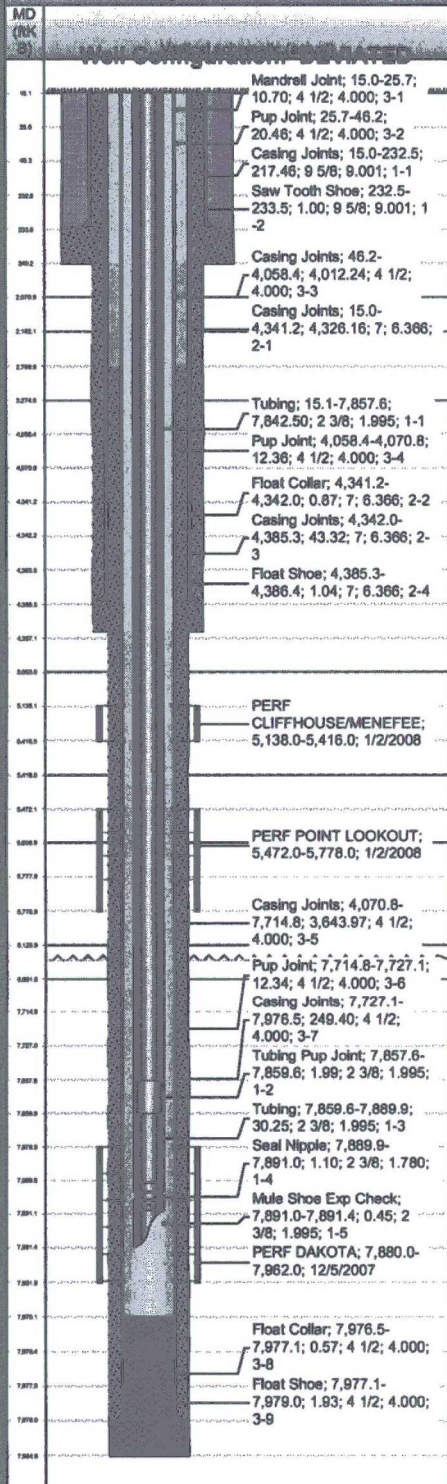

WELLHEADS

Type	Install Date

CASING STRINGS

String	OD (in)	WT/Lin (lb/ft)	Grade	Top Thread	Set Depth (ftKB)
Surface	9 5/8	32.30	H-40	STC	233.5
Intermediate	7	23.00	L-80	LT&C	4,386.4
Production	4 1/2	11.60	J-55	LT&C	7,979.0

PBTDs

Depth (ftKB)	KB MD (ftKB)	TD (max) (ftKB)
7,970.0		7,985.0

PERFORATIONS

Date	Top (ftKB)	Bot (ftKB)	Zone	Current Status
1/2/2008	5,138.0	5,416.0	BLANCO::MESAVERDE, Ori...	(5,138.0 - 5,416.0)
1/2/2008	5,472.0	5,778.0	BLANCO::MESAVERDE, Ori...	(5,472.0 - 5,778.0)
12/5/2007	7,880.0	7,962.0	BASIN::DAKOTA, Original Hole	

TUBING STRING

Tubing Description	Run Date	Pull Date	String Length (ft)	Set Depth (ftKB)
Tubing - Production	1/23/2008		7,876.29	7,891.4

Comment

Item	Item Desc	OD Nominal (in)	Nominal ID (in)	WT/Lin (lb/ft)	Grade	Make	Model	Len (ft)	Top (ftKB)
25	Tubing	2 3/8	1.995	4.70	L-80		T&C Upset	7,842.50	15.1
4	Tubing Pup Joint	2 3/8	1.995	4.70	L-80		T&C Upset	1.99	7,857.6
1	Tubing	2 3/8	1.995	4.70	L-80		T&C Upset	30.25	7,859.6
1	Seal Nipple	2 3/8	1.780				T&C Upset	1.10	7,889.9
1	Mule Shoe Exp Check	2 3/8	1.995					0.45	7,891.0
