

W LYBROOK UNIT #714H

Lybrook Mancos W

(page 1)

Spud: 2/22/17


Completed: 6/11/17

SHL: 2036' FNL & 2492' FWL
SE/4 NW/4 Section 13 (F), T23N, R9W

BHL: 2295' FSL & 1803' FWL
NE/4 SW/4 Section 11 (K), T23N, R9W

San Juan, NM
Elevation: 6700
API: 30-045-35802

	MD	TVD
OJO ALAMO	432	432
KIRTLAND	602	602
PICTURED CLIFFS	1083	1081
LEWIS	1280	1273
CHACRA	1504	1490
CLIFF HOUSE	2668	2560
MENEFEE	2724	2611
POINT LOOKOUT	3695	3492
MANCOS	3909	3685
GALLUP	4273	4028

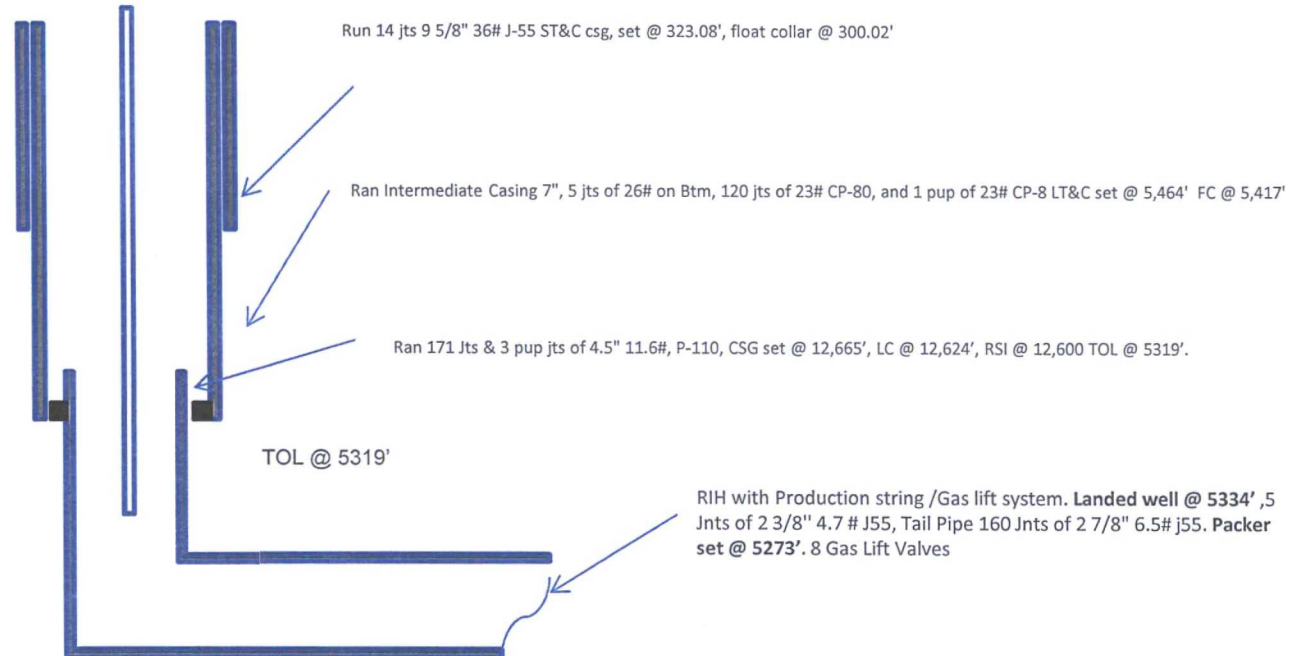

TD: 12665' MD
TVD: 4822'
PBTD: 12624' MD

Mancos Frac-

5592'-12600' w/ .32" diameter- 4 spf total

of 680 holes. w/ 35 stages 20/40 sand

total of 7,100,379#

HOLE SIZE	CASING	CEMENT	VOLUME	CMT TOP
12-1/4"	9-5/8"	101 sx	162 cu.ft.	Surface
8-3/4"	7"	845 sx	1325 cu. ft.	Surface
6-1/8"	4-1/2"	665sx	904 cu. ft.	5319' TOL

LG 6/28/17

Av

CONFIDENTIAL
