


CURRENT

WELL NAME: PINON UNIT 305H				SPOT: 1277' FSL, 288' FWL				OPERATOR: JREX				SPUD DATE: 9-May-17	
API NO: 30-045-35637				LOCATION: SEC. 16, T24N, R10W				ZONE: MANCOS				RR DATE: 2-Jun-17	
WI: 100%				FIELD: PINON UNIT				ELEVATION: 6,746' +14' KB				MICU: 15-Jul-17	
RI:				COUNTY: SAN JUAN				TD: 13,729'				COMPL DATE: 24-Jul-17	
				STATE: NEW MEXICO				PBTD: 13,659'				STATUS: PRODUCING	
PIPE RECORD								CEMENT & HOLE DATA					
CSG	OD	GRADE	THD	WT/FT	TOP	BTM	# JTS	BIT SIZE	DEPTH	SXS	TYPE	TOC	
Cond	9.625"	J-55	LTC	36.00#	0'	324'	16	12.250"	330'	101	Type I-II	Surface	
Surface	7.000"	J-55	LTC	23.00#	0'	5,471'	149	8.750"	5,480'	725	Hal-Cem	Surface	
Interm.	4.500"	P-110	LTC	11.60#	5274'	13,704'	204	6.125"	13,729'	770	Extendacem	5,275'	
Prod													
Tbg													
Tbg													
WELL HISTORY													
DATE	WORK DETAIL											PROD. RESULTS	
17-May-17	Already pre-set surface casing w/ Mo-Te to 324'. Spud well.												
19-May-17	Drilled pilot hole to 5,481'.												
22-May-17	Logged pilot hole w/ through bit triple combo												
15-Jul-17	MIRU WL unit, frac crew												
24-Jul-17	RDMO WL unit, frac crew												
15-Aug-17	MIRU WS rig. TOH w/ frac string												
16-Aug-17	TIH w/ 2 7/8" production tubing, packer & GLV's												

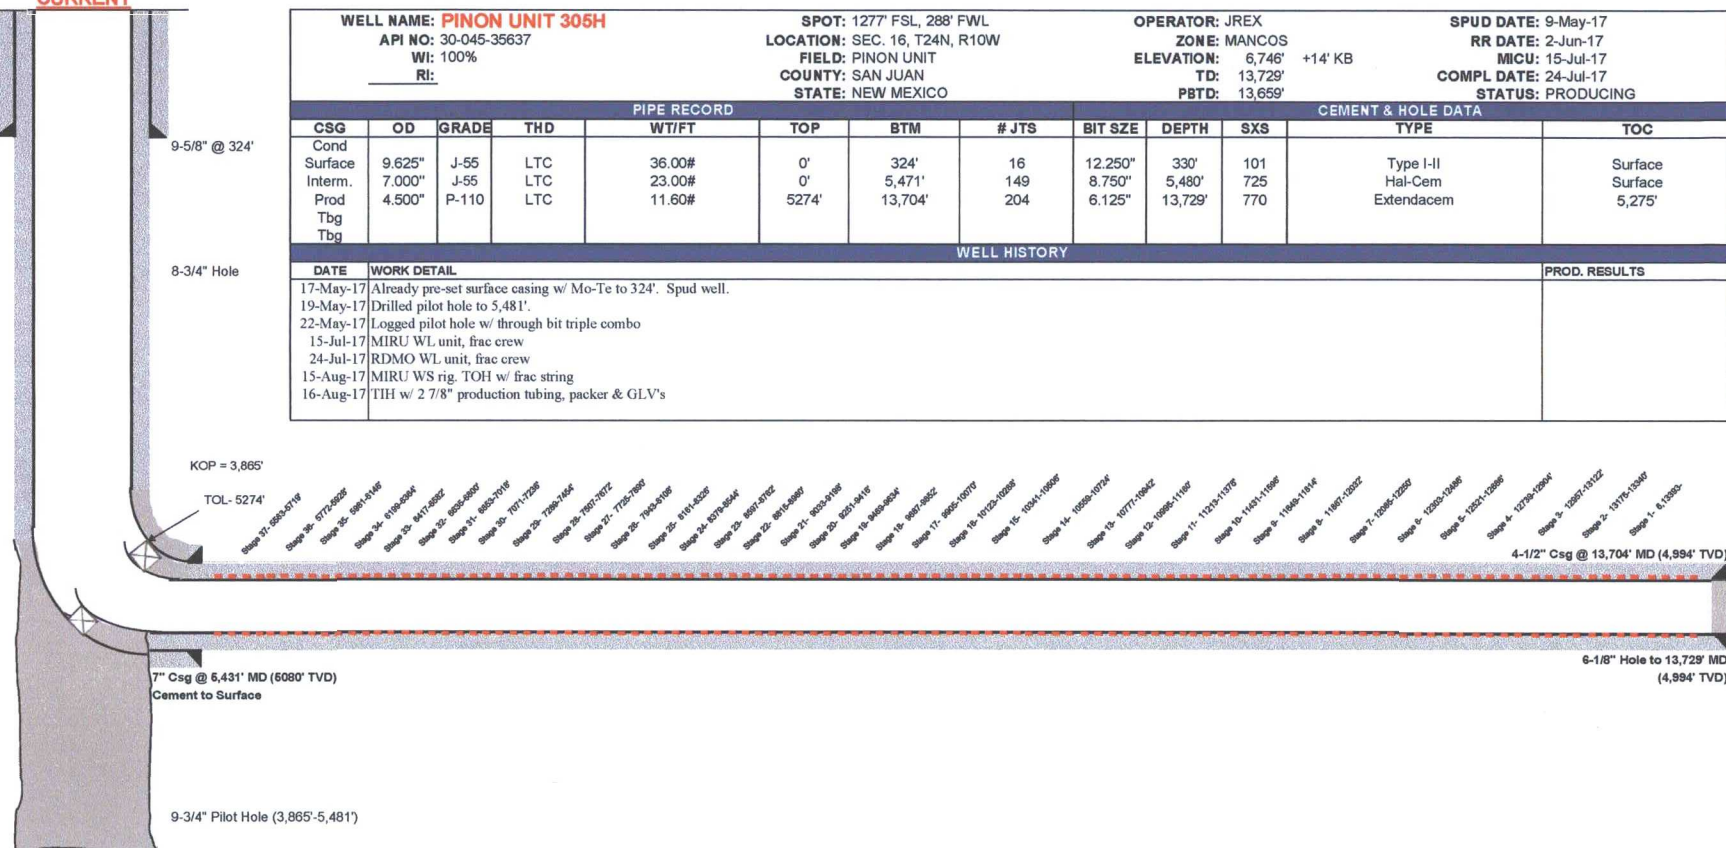

ANUCD Dec'd 9-22-17
AV
