

N Escavada Unit 314H

Escavada N; Mancos

(page 1)

Spud: 6/12/17


Completed: 8/26/17

SHL: 1900' FSL & 1275' FEL
NE/4 SE/4 Section 10 (I), T22N, R7W

BHL: 2264' FSL & 2358' FWL
NE/4 SW/4 Section 4 (K), T22N, R7W

Sandoval, NM
Elevation: 6944'
API: 30-043-21285

	MD	TVD
OJO ALAMO	996	993
KIRTLAND	1179	1172
PICTURED CLIFFS	1474	1462
LEWIS	1606	1592
CHACRA	1837	1818
CLIFF HOUSE	2966	2927
MENEFEE	3003	2963
POINT LOOKOUT	3885	3829
MANCOS	4034	3975
GALLUP	4372	4308

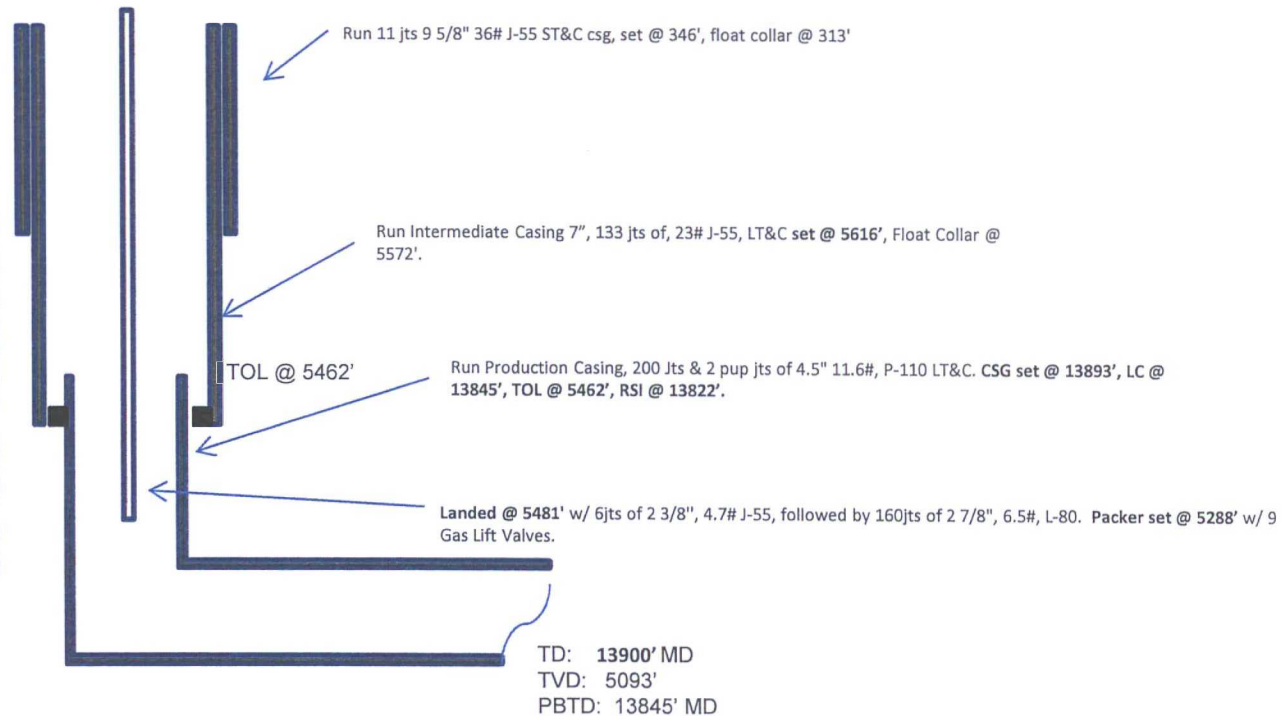

Mancos Frac-

5634'-13822' w/ .35" diameter- 4 spf total

of 788 holes. w/ 40 stages 20/40 sand

total of 8,010,8600#

LG 8/31/17

HOLE SIZE	CASING	CEMENT	VOLUME	CMT TOP
12-1/4"	9-5/8"	101 sx	162 cu.ft.	Surface
8-3/4"	7"	940 sx	1526 cu. ft.	Surface
6-1/8"	4-1/2"	795 sx	1078 cu. ft.	5462' TOL

CONFIDENTIAL
