

W LYBROOK UNIT #752H

Lybrook Mancos W

(page 1)

Spud: 2/23/17


Completed: 7/22/17

SHL: 2017' FNL & 2485' FWL
SE/4 NW/4 Section 13 (F), T23N, R9W

BHL: 342' FSL & 1580' FEL
SW/4 SE/4 Section 19 (O), T23N, R8W

San Juan, NM
Elevation: 6700'
API: 30-045-35805

	MD	TVD
OJO ALAMO	433	432
KIRTLAND	609	608
PICTURED CLIFFS	1086	1080
LEWIS	1285	1272
CHACRA	1518	1491
CLIFF HOUSE	2691	2551
MENEFEE	2731	2587
POINT LOOKOUT	3721	3482
MANCOS	3941	3682
GALLUP	4305	4025

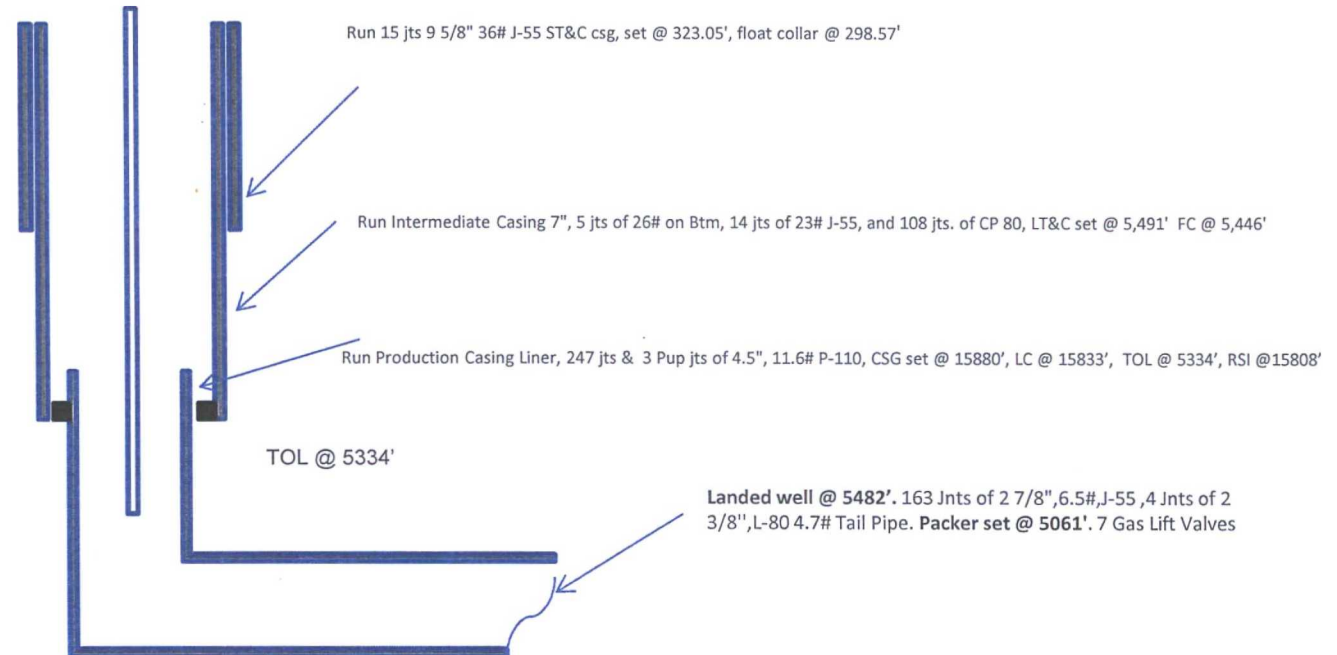

TD: 15886' MD
TVD: 4794'
PBTD: 15833' MD

Mancos Frac-

5504'-15808' 'w .35" diameter- 4 spf total

of 1008 holes. w/ 51 stages 20/40 sand

total of 10,334,300#

LG 8/10/17

HOLE SIZE	CASING	CEMENT	VOLUME	CMT TOP
12-1/4"	9-5/8"	101 sx	162 cu.ft.	Surface
8-3/4"	7"	845 sx	1314 cu. ft.	Surface
6-1/8"	4-1/2"	1020 sx	1387 cu. ft.	5334' TOL

CONFIDENTIAL
