


WellView

Schematic Components

Well Name: JICARILLA 103H

API/UWI 30-043-21202		County SANDOVAL		State/Province NEW MEXICO		Surface Legal Location Section 08, Twp 22N, Rng 05W, 23rd PM							
Spud Date 4/26/2014		On Production Date 8/1/2014		Abandon Date		Ground Elevation (ft) 6,961.00		Original KB Elevation (ft) 6,974.00		Total Depth (All) (ftKB) Original Hole - 10,766.0		PBTD (All) (ftKB) Original Hole - 10,720.0	

Horizontal, Original Hole, 3/7/2019 11:24:33 AM

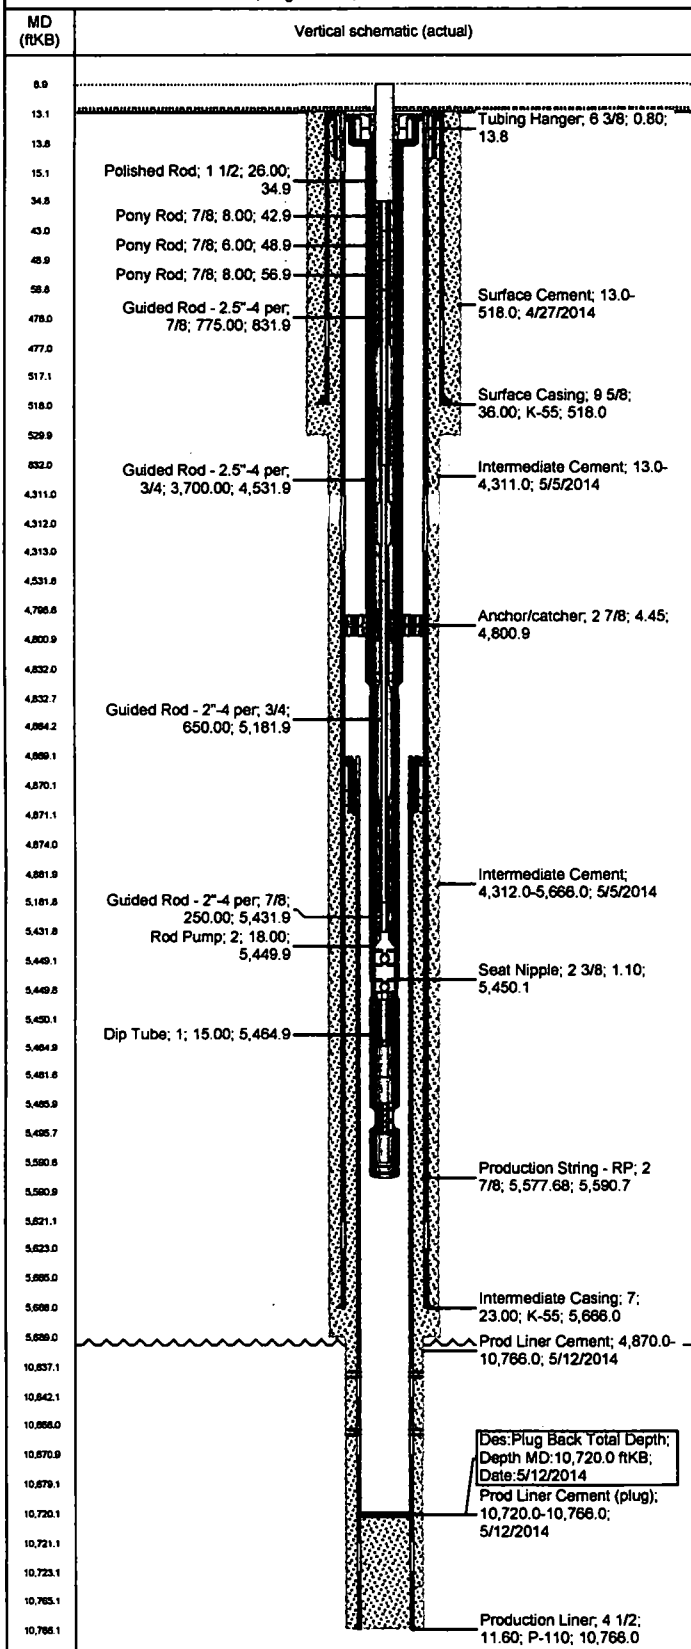

Other Strings

String Description	String Length (ft)	Set Depth (ftKB)	Run Date
--------------------	--------------------	------------------	----------

Rod Strings

Rod String #1 on 3/6/2019 17:30

Rod Description		String Length (ft)	Set Depth (ftKB)	Run Date	
Rod String #1		5,456.00	5,464.9	3/6/2019	
Jts	Item Des	OD (in)	Len (ft)	Top (ftKB)	Btm (ftKB)
	Polished Rod	1 1/2	26.00	8.9	34.9
2	Pony Rod	7/8	8.00	34.9	42.9
1	Pony Rod	7/8	6.00	42.9	48.9
1	Pony Rod	7/8	8.00	48.9	56.9
31	Guided Rod - 2.5"-4 per	7/8	775.00	56.9	831.9
148	Guided Rod - 2.5"-4 per	3/4	3,700.00	831.9	4,531.9
26	Guided Rod - 2"-4 per	3/4	650.00	4,531.9	5,181.9
10	Guided Rod - 2"-4 per	7/8	250.00	5,181.9	5,431.9
	Rod Pump	2	18.00	5,431.9	5,449.9
	Dip Tube	1	15.00	5,449.9	5,464.9

Tubing Strings

Production String - RP set at 5,590.7ftKB on 3/6/2019 10:30

Tubing Description		Len (ft)	Set Depth (f...)	Run Date	Cut/Pull Date	Depth C...	
Production String - RP		5,577.68	5,590.7	3/6/2019			
Jts	Item Des	OD (in)	Len (ft)	Top (ftKB)	Btm (ftKB)	Grade	Wt (lb/ft)
	Tubing Hanger	6 3/8	0.80	13.0	13.8	J-55	
14	Tubing	2 7/8	4,782.6	13.8	4,796.5	J-55	6.40
7			3				
	Anchor/catcher	2 7/8	4.45	4,796.5	4,800.9	J-55	
1	Tubing	2 7/8	31.18	4,800.9	4,832.1	J-55	6.40
	Cross Over	2 7/8	0.50	4,832.1	4,832.6	J-55	
1	Tubing	2 3/8	31.70	4,832.6	4,864.3	J-55	4.70
1	Tubing-Pup Jnt	2 3/8	9.80	4,864.3	4,874.1	J-55	4.70
1	Tubing-Pup Jnt	2 3/8	7.71	4,874.1	4,881.8	J-55	4.70
18	Tubing	2 3/8	567.20	4,881.8	5,449.0	J-55	4.70
	Seat Nipple	2 3/8	1.10	5,449.0	5,450.1	J-55	
1	Tubing	2 3/8	31.68	5,450.1	5,481.8	J-55	4.70
1	Tubing-Pup Jnt	2 3/8	4.00	5,481.8	5,485.8	J-55	4.70
	Desander - Cavins	2 3/8	10.10	5,485.8	5,495.9	J-55	
3	Tubing	2 3/8	94.53	5,495.9	5,590.4	J-55	4.70
	Bull Plug	2 3/8	0.30	5,590.4	5,590.7	J-55	

Other In Hole

Des	String	Top (ftKB)	Btm (ftKB)	Run Date
-----	--------	------------	------------	----------

Cement

Prod Liner Cement, Casing, 5/12/2014 14:00

Description	String	Cementing Start Date	Cementing End Date
Prod Liner Cement	Production Liner, 10,766.0ftKB	5/12/2014 14:00	5/12/2014 20:00

Cement Stages

Stg #	Top (ftKB)	Btm (ftKB)	Com
1	4,870.0	10,766.0	Lead: 40 sx Elastiseal, 290 sx Foamed Elastiseal. Tail: 100 sx Elastiseal

Intermediate Cement, Casing, 5/5/2014 14:00

Description	String	Cementing Start Date	Cementing End Date
Intermediate Cement	Intermediate Casing, 5,666.0ftKB	5/5/2014 14:00	5/5/2014 18:00

Cement Stages

Stg #	Top (ftKB)	Btm (ftKB)	Com
1	4,312.0	5,666.0	Lead: 110 sx Halcem Tail: 100 sx Halcem
2	13.0	4,311.0	Lead: 490 sx Halcem Tail: 50 sx Halcem
