

30-045-11134 4791

DATA SHEET FOR DEEP GROUND BED CATHODIC PROTECTION WELLS
NORTHWESTERN NEW MEXICO
(Submit 3 copies to OCD Aztec Office)

Operator MERIDIAN OIL Location: Unit SE Sec. 32 Twp 32 Rng 11

Name of Well/Wells or Pipeline Serviced SINCLAIR COM #1

cps 669w

Elevation 6295' Completion Date 6/4/64 Total Depth 220' Land Type* N/A

Casing, Sizes, Types & Depths N/A

If Casing is cemented, show amounts & types used N/A

If Cement or Bentonite Plugs have been placed, show depths & amounts used
N/A

Depths & thickness of water zones with description of water when possible:
Fresh, Clear, Salty, Sulphur, Etc. N/A

Depths gas encountered: N/A

Type & amount of coke breeze used: 2400 lbs.

Depths anodes placed: 170', 164', 148', 126', 120'

Depths vent pipes placed: N/A

Vent pipe perforations: N/A

Remarks: gb #1

Gib #1 & Gib #2

If any of the above data is unavailable, please indicate so. Copies of all logs, including Drillers Log, Water Analyses & Well Bore Schematics should be submitted when available. Unplugged abandoned wells are to be included.

*Land Type may be shown: F-Federal; I-Indian; S-State; P-Fee.
If Federal or Indian, add Lease Number.

RECEIVED
MAY 31 1991
OIL CON. DIV
DIST. 3

WELL CASING
CATHODIC PROTECTION CONSTRUCTION REPORT
DAILY LOG

Date: 6-4-64

Well Name Sinclair State No. 1			CPS No. 669-W		
Location SE 32-32-11			Work Order No. 52239		
Anode Hole Depth 220	Total Drilling Rig Time 8 Hrs.	Type & Size Bit Used 6 1/4 7491		No. Sacks Mud Used 3	
No. Sacks Lost Circulation Mat'l Used 0	Anode Depth				
	# 1 170	# 2 164	# 3 148	# 4 126	# 5 120
Total Lbs. Coke Used 2400 - (16 S KS)	Anode Output (Volts)				
	# 1 4.5	# 2 5.2	# 3 3.7	# 4 3.9	# 5 4.7
Total Circuit Resistance		No. Ft. Surface Cable Conduit			
Volts 12.0	Amps 11.2	Ohms 1.07	459		

Drilling Log (Attach H ere to) ☐

Remarks:


Static 9/5 74 R 600 E
PEM Rect. 40V12A Ser. 637352

All Construction Completed

[Signature]

(Signature)

GROUND BED LAYOUT SKETCH

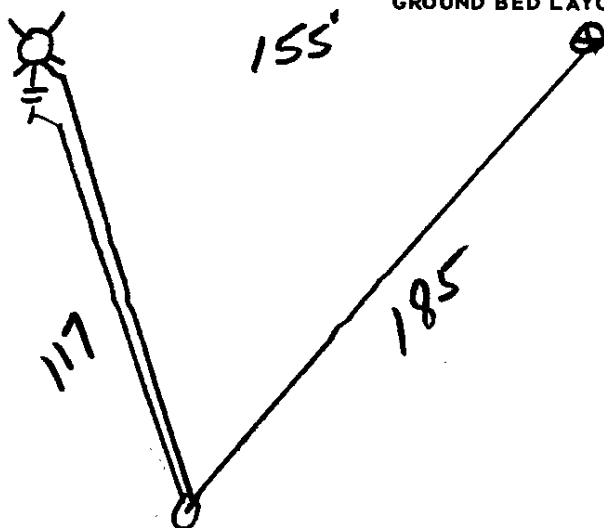

1187'



EL PASO NATURAL GAS COMPANY
DRILLING DEPARTMENT

DAILY DRILLING REPORT

LEASE SAN LAIR STATE WELL NO. 1 CONTRACTOR L.F. Wilson RIG NO. D-1 REPORT NO. 519-20 DATE 5-19-64 1964

MORNING

DAYLIGHT

EVENING

Driller <u>HAROLD</u>				Total Men In Crew				Driller				Total Men In Crew							
FROM	TO	WT-BIT	R.P.M.	FORMATION	TO	FROM	R.P.M.	FORMATION	TO	FROM	R.P.M.	FORMATION	TO	WT-BIT	R.P.M.				
0	30'			SAMP		210'		SS											
30'	110'			SA															
110'	160'			SS															
160'	220'			SA															
NO. DC				SIZE	NO. DC				SIZE	NO. DC				SIZE	NO. DC				SIZE
NO. DC				SIZE	NO. DC				SIZE	NO. DC				SIZE	NO. DC				SIZE
STANDS					STANDS					STANDS					STANDS				
SINGLES					SINGLES					SINGLES					SINGLES				
DOWN ON KELLY					DOWN ON KELLY					DOWN ON KELLY					DOWN ON KELLY				
TOTAL DEPTH				220	TOTAL DEPTH					TOTAL DEPTH					TOTAL DEPTH				
MUD, ADDITIVES USED AND RECEIVED					MUD, ADDITIVES USED AND RECEIVED					MUD, ADDITIVES USED AND RECEIVED					MUD, ADDITIVES USED AND RECEIVED				
MUD RECORD					MUD RECORD					MUD RECORD					MUD RECORD				
Time	Wt.	Vis.		Time	Wt.	Vis.		Time	Wt.	Vis.		Time	Wt.	Vis.					
30 MUD					RIG TIME 8 H														
TIME BREAKDOWN					TIME BREAKDOWN					TIME BREAKDOWN					TIME BREAKDOWN				
FROM	TO			FROM	TO			FROM	TO			FROM	TO						
5-19-64 FINISHED EAST HOLE AT 330 PM 1 1/2 HOURS				5-19-64 FINISHED EAST HOLE AT 330 PM 1 1/2 HOURS				5-19-64 FINISHED EAST HOLE AT 330 PM 1 1/2 HOURS				5-19-64 FINISHED EAST HOLE AT 330 PM 1 1/2 HOURS							
5-19-64 1 1/2 HOURS YARD AT 600 AM ARRIVED AT 1000 AM				5-19-64 1 1/2 HOURS YARD AT 600 AM ARRIVED AT 1000 AM				5-19-64 1 1/2 HOURS YARD AT 600 AM ARRIVED AT 1000 AM				5-19-64 1 1/2 HOURS YARD AT 600 AM ARRIVED AT 1000 AM							
REMARKS				REMARKS				REMARKS				REMARKS							
5-19-64 DRILLED FROM 0' TO 80' MUD IN LOOSE SAND				5-19-64 DRILLED FROM 0' TO 80' MUD IN LOOSE SAND				5-19-64 DRILLED FROM 0' TO 80' MUD IN LOOSE SAND				5-19-64 DRILLED FROM 0' TO 80' MUD IN LOOSE SAND							
5-19-64 DRILLED FROM 80' TO 220' FINISHED HOLE AT 130 PM				5-19-64 DRILLED FROM 80' TO 220' FINISHED HOLE AT 130 PM				5-19-64 DRILLED FROM 80' TO 220' FINISHED HOLE AT 130 PM				5-19-64 DRILLED FROM 80' TO 220' FINISHED HOLE AT 130 PM							
5-19-64 1 1/2 HOURS				5-19-64 1 1/2 HOURS				5-19-64 1 1/2 HOURS				5-19-64 1 1/2 HOURS							
5-19-64 1 1/2 HOURS				5-19-64 1 1/2 HOURS				5-19-64 1 1/2 HOURS				5-19-64 1 1/2 HOURS							

SIGNED: Toolpusher
