

30-045-21248

DATA SHEET FOR DEEP GROUND BED CATHODIC PROTECTION WELLS
NORTHWESTERN NEW MEXICO
(Submit 3 copies to OCD Aztec Office)

Operator MERIDIAN OIL Location: Unit NW Sec. 31 Twp 26 Rng 10

Name of Well/Wells or Pipeline Serviced HUERFANO UNIT #243

cps 996w

Elevation 6478' Completion Date 9/24/75 Total Depth 300' Land Type* N/A

Casing, Sizes, Types & Depths 24' STEEL CASING

If Casing is cemented, show amounts & types used N/A

If Cement or Bentonite Plugs have been placed, show depths & amounts used
N/A

Depths & thickness of water zones with description of water when possible:
Fresh, Clear, Salty, Sulphur, Etc. 100'

Depths gas encountered: N/A


Type & amount of coke breeze used: 3600 lbs.

Depths anodes placed: 240', 210', 200', 190', 180', 170', 160', 150', 140', 130'

Depths vent pipes placed: N/A

Vent pipe perforations: 220'

Remarks: qb #1



If any of the above data is unavailable, please indicate so. Copies of all logs, including Drillers Log, Water Analyses & Well Bore Schematics should be submitted when available. Unplugged abandoned wells are to be included.

*Land Type may be shown: F-Federal; I-Indian; S-State; P-Fee.
If Federal or Indian, add Lease Number.

WELL CASING
CATHODIC PROTECTION CONSTRUCTION REPORT
DAILY LOG

Drilling Log (Attach Hereto). ☐

Completion Date 9-24-75


Well Name Huerfano #243		Location NW 31-26-10		CPS No. 996W	
Type & Size Bit Used 6 3/4				Work Order No. 55526	
Anode Hole Depth 300	Total Drilling Rig Time	Total Lbs. Coke Used 3600	Lost Circulation Mat'l Used	No. Sacks Mud Used	
Anode Depth	# 1	# 2	# 3	# 4	# 5
	240	210	200	190	180
Anode Output (Amps)	# 1	# 2	# 3	# 4	# 5
	6.2	3.0	5.2	5.5	5.2
Anode Depth	# 6	# 7	# 8	# 9	# 10
	170	160	150	140	130
Anode Output (Amps)	# 6	# 7	# 8	# 9	# 10
	5.4	5.2	5.2	6.0	5.2
Anode Depth	# 11	# 12	# 13	# 14	# 15
Anode Output (Amps)	# 11	# 12	# 13	# 14	# 15
Total Circuit Resistance	Volts 10.0		Amps 22.0		Ohms 0.45
					No. 8 C.P. Cable Used 2145
					No. 2 C.P. Cable Used 0

Remarks: **Set 24' Steel Casing 8" (Sandy) - Moved original G.B. loc. Used 45' additional wire - Abandoned wire to original loc. in place**
Wet-Start Water injection at 100' - Drilled to 140' water Next A.M. at 115' Vent Perforated 220'
Slurry 36 coke

All Construction Completed

Danele
(Signature)

GROUND BED LAYOUT SKETCH

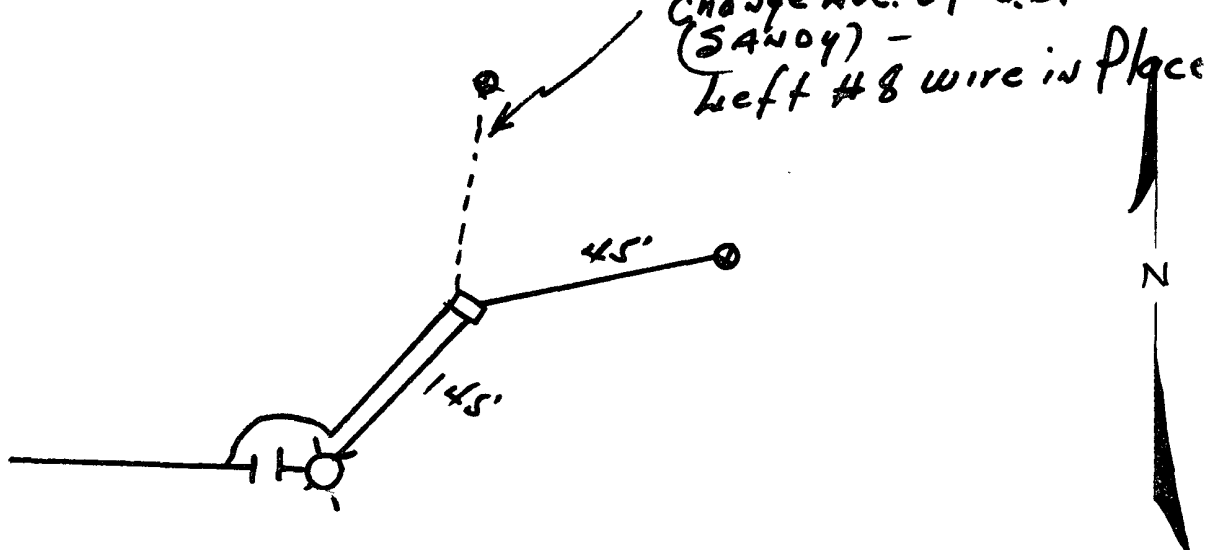

SIGNED: Toolpusher _____ Company Supervisor _____

