

30-039-07712

DATA SHEET FOR DEEP GROUND BED CATHODIC PROTECTION WELLS
NORTHWESTERN NEW MEXICO
(Submit 3 copies to OCD Aztec Office)

Operator MERIDIAN OIL Location: Unit SW Sec. 33 Twp 30 Rng 6

Name of Well/Wells or Pipeline Serviced SAN JUAN 30-6 UNIT #31

cps 176w

Elevation 6357' Completion Date 4/17/63 Total Depth 160' Land Type* N/A

Casing, Sizes, Types & Depths N/A

If Casing is cemented, show amounts & types used N/A

If Cement or Bentonite Plugs have been placed, show depths & amounts used

N/A

Depths & thickness of water zones with description of water when possible:

Fresh, Clear, Salty, Sulphur, Etc. N/A

Depths gas encountered: N/A

Type & amount of coke breeze used: 1190 lbs.

Depths anodes placed: 135', 129', 123', 117', 111'

Depths vent pipes placed: N/A

Vent pipe perforations: N/A

Remarks: qb #1

RECEIVED

MAY 31 1991

OIL CON. DIV

\ DIST. 3

If any of the above data is unavailable, please indicate so. Copies of all logs, including Drillers Log, Water Analyses & Well Bore Schematics should be submitted when available. Unplugged abandoned wells are to be included.

*Land Type may be shown: F-Federal; I-Indian; S-State; P-Fee.
If Federal or Indian, add Lease Number.

WELL CASING
CATHODIC PROTECTION CONSTRUCTION REPORT
DAILY LOG

DATE 17 April 1963

WELL NAME San Juan 30-6 Unit 31 CPS NO. 176W

LOCATION 5K1^A Sec. 33 T30 N R 6 W

WORK ORDER NUMBER 184-40542-50-02

ANODE HOLE DEPTH 160'

TOTAL DRILLING RIG TIME 10 Hrs.

DRILLING TIME FOR RECTIFIER POLE HOLE 0

TYPE AND SIZE BIT USED 6 1/4 Rock W.M. 3490 VMD 109 5X
76 84

NUMBER SACKS MUD USED 1

NUMBER SACKS LOST CIRCULATION MAT'L USED 1

ANODE DEPTHS #1 135, #2 129, #3 123, #4 117 #5 111

TOTAL LBS. COKE USED 1190 14 Sacks

ANODE OUTPUTS 12.4 VOLTS, #1 3.0, #2 3.0, #3 3.3, #4 3.2 #5 3.5

TOTAL CIRCUIT RESISTANCE: VOLTS 12.0 AMPERES 7.0 OHMS 1.71

NUMBER FEET SURFACE CABLE CONDUIT 840'

DRILLING LOG (ATTACH HERETO).

FORMATION LOG (ATTACH HERETO).

REMARKS: Static. C/s = .77 R 600 SW.

28 V 12A Rectifier Good All


Serial No. 62C 6220

EPNG Tag No. 176W

ALL CONSTRUCTION COMPLETED

O. Daniels
SIGNATURE

GROUND BED LAYOUT SKETCH

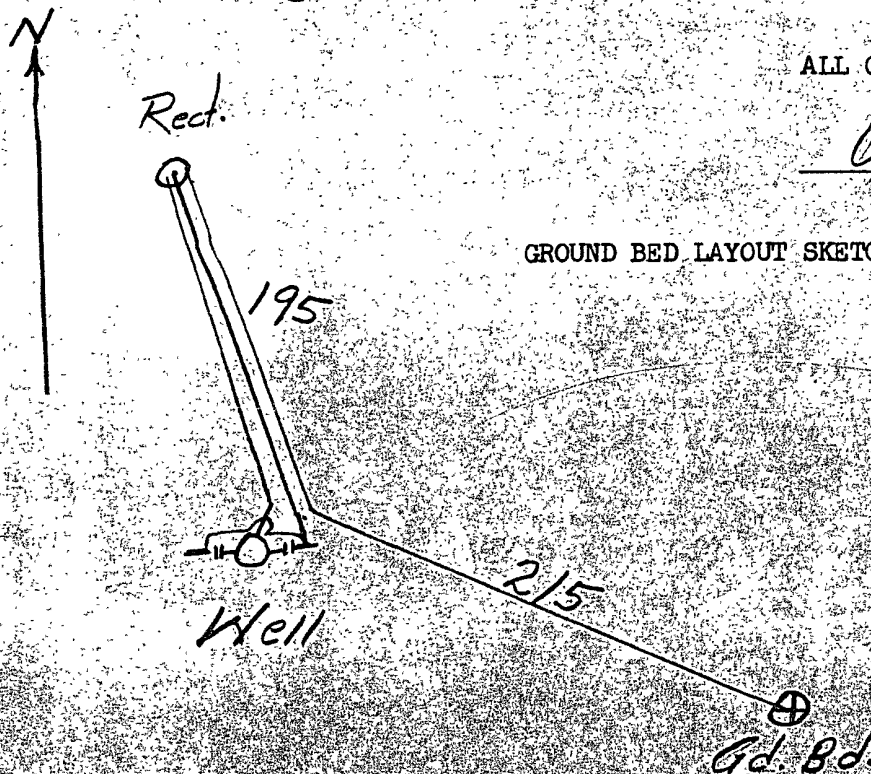

ORIGINAL & 1 COPY
ALL REPORTS

Sec. 33
T 30N R 6W

DAILY DRILLING REPORT

LEASES J 30-6 WELL NO. 31 CONTRACTOR *S. E. Wilson* RIG NO. *D-6* REPORT NO. DATE *April 16 & 17 1963*

MORNING										DAYLIGHT										EVENING									
Driller					Total Man In Crew					Driller					Total Man In Crew					Driller					Total Man In Crew				
FROM	TO	FORMATION	WT. BIT	LR. PM.	FROM	TO	FORMATION	WT. BIT	LR. PM.	FROM	TO	FORMATION	WT. BIT	LR. PM.	FROM	TO	FORMATION	WT. BIT	LR. PM.	FROM	TO	FORMATION	WT. BIT	LR. PM.					
0	20	Shale & sandstone	15		140	145	Shale & sandstone	15		140	145	Shale & sandstone	15																
20	40	Shale & sandstone	15		145	150	Shale & sandstone	15		145	150	Shale & sandstone	15																
40	100	Shale & sandstone	15		150	155	Shale & sandstone	15		150	155	Shale & sandstone	15																
100	105	Shale & sandstone	15																										
BIT NO.					NO. DC					NO. DC					NO. DC					NO. DC					NO. DC				
SERIAL NO.					SIZE					SIZE					SIZE					SIZE					SIZE				
TYPE					DOWN ON KELLY					DOWN ON KELLY					DOWN ON KELLY					DOWN ON KELLY					DOWN ON KELLY				
TOTAL DEPTH					TOTAL DEPTH					TOTAL DEPTH					TOTAL DEPTH					TOTAL DEPTH					TOTAL DEPTH				
MUD RECORD					MUD ADDITIVES USED AND RECEIVED					MUD RECORD					MUD ADDITIVES USED AND RECEIVED					MUD RECORD					MUD ADDITIVES USED AND RECEIVED				
TIME					TIME					TIME					TIME					TIME					TIME				
FROM					TO					FROM					TO					FROM					TO				
TIME BREAKDOWN					TIME BREAKDOWN					TIME BREAKDOWN					TIME BREAKDOWN					TIME BREAKDOWN					TIME BREAKDOWN				
REMARKS					REMARKS					REMARKS					REMARKS					REMARKS					REMARKS				
April 16 - Drilled 80' - sand & shale 1 1/2" bit 1 1/2" PM					April 17 - Drilled 80' - sand & shale 1 1/2" bit 1 1/2" PM					April 18 - Drilled 80' - sand & shale 1 1/2" bit 1 1/2" PM					April 19 - Drilled 80' - sand & shale 1 1/2" bit 1 1/2" PM					April 20 - Drilled 80' - sand & shale 1 1/2" bit 1 1/2" PM					April 21 - Drilled 80' - sand & shale 1 1/2" bit 1 1/2" PM				
10 hrs					10 hrs					10 hrs					10 hrs					10 hrs					10 hrs				
SIGNED: Toolpusher					SIGNED: Toolpusher					SIGNED: Toolpusher					SIGNED: Toolpusher					SIGNED: Toolpusher					SIGNED: Toolpusher				
Company Supervisor					Company Supervisor					Company Supervisor					Company Supervisor					Company Supervisor					Company Supervisor				

moving to new location
OT Hobbs
