

Form 3160-5
(November 1983)
(Formerly 9-311)

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

SUBMIT IN TRIPPLICATE*
(Other instructions on reverse side)

Form approved:
Budget Bureau No. 1004-0135
Expires August 31, 1985

3. LEASE DESIGNATION AND SERIAL NO.
SF-077966
5. IF INDIAN, ALLOTTEE OR TRIBE NAME

SUNDRY NOTICES AND REPORTS ON WELLS

(Do not use this form for proposals to drill or to deepen or plug back to a different reservoir.
Use "APPLICATION FOR PERMIT—" for such proposals.)

1. OIL WELL ☐ GAS WELL ☒ OTHER

2. NAME OF OPERATOR

Amoco Production Co.

3. ADDRESS OF OPERATOR

501 Airport Drive, Farmington, NM

4. LOCATION OF WELL (Report location clearly and in accordance with State requirements.
See also space 17 below.)
At surface

1510' FSL x 1525' FEL

BUREAU OF LAND MANAGEMENT
FARMINGTON RESOURCE AREA

14. PERMIT NO.

15. ELEVATIONS (Show whether OF, FT, GR, ETC.)

5989' GR

7. UNIT AGREEMENT NAME

Gallegos Canyon Unit

8. FARM OR LEASE NAME

9. WELL NO.

238E

10. FIELD AND POOL, OR WILDCAT

Basin Dakota

11. SEC., T., R., M., OR BLK. AND SURVEY OR AREA

NW/SE Sec 23, T28N, R13W

12. COUNTY OR PARISH

San Juan

13. STATE

NM

16. Check Appropriate Box To Indicate Nature of Notice, Report, or Other Data

NOTICE OF INTENTION TO:

ABANDONMENT REPORT OF:

STOP WORK

STOP WORK TREAT

SHOOT OR ACIDIZE

REPAIR WELL

(Other)

MULTIPLE COMPLETION

ABANDON*

CHANGE PLANS

STOP WORK

FRACURE TREATMENT

SHOOTING OR ACIDIZING

(Other) Spud and set casing

(NOTE: Report results of multiple completion on Well Completion or Recompletion Report and Log form.)

REPAIRING WELL

ALTERING CASING

ABANDONMENT*

17. DESCRIBE PROPOSED OR COMPLETED OPERATIONS (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work. If well is directionally drilled, give subsurface locations and measured and true vertical depths for all markers and zones pertinent to this work.) *

Spud a 12-1/4" on 5-14-85 at 1400 hrs. Drilled to 374'. Set 8-5/8" 28#, K55 casing at 374' and cemented with 325 cu. ft. class B Portland Circulated cement to surface. Pressure tested casing to 1000psi for 30 minutes. Drilled a 7-7/8" hole to a TD of 6470' on 5-26-85. Set 4-1/2", 11.6#, K55 casing at 6467'. Stage 1: cemented with 679 cu.ft. class B Portland and tailed in with 215 cu. ft. class B Portland. Stage 2: cemented with 789 cu. ft. class B Portland. Ran a temperature survey (attached) which indicated the top of the cement to be at 400'. The DV tool was set at 3240' and the rig was released on 5-27-85.

RECEIVED
JUL 29 1985
OIL CON. DIV.
DIST. 3

I hereby certify that the foregoing is true and correct

SIGNED

D. D. Lawson

TITLE District Adm. Supervisor

DATE

ACCEPTED FOR RECORD
7-16-85

(This space for Federal or State office use)

APPROVED BY

TITLE

DATE

CONDITIONS OF APPROVAL, IF ANY:

JUL 26 1985

FARMINGTON RESOURCE AREA
FARMINGTON, NEW MEXICO


*See Instructions on Reverse Side

NMOCC

BY

WF

WILSON				FORM 432-2	
SERVICE COMPANY					
TEMPERATURE SURVEY					
COMPANY <u>ANOCO Production</u>					
WELL <u>238-E</u>		LEASE <u>G. C. II.</u>			
COUNTY <u>San Juan</u>		STATE <u>New Mexico</u>			
SEC. <u>23</u>	TWP. <u>28N</u>	RGE. <u>13W</u>			
APPROX. TOP CEMENT <u>400'</u>					
Survey Begins at <u>100'</u>		Ft. Ends at <u>3250'</u>		Ft.	
Approx. Fill-Up		Max. Temp.			
Log Measured From <u>KB</u>		Run No. <u>1</u>			
Casing Size	Casing Depth	Diam. of Hole	Depth		
<u>4 1/2"</u> from	to	<u>7 7/8"</u> from	to		
from	to	from	to		
Date of Cementing <u>5-27-85</u>		Time <u>1:30 AM</u>			
Date of Survey <u>5-27-85</u>		Time <u>10:00 AM</u>			
Amount of Cement <u>As Per Report</u>					
Recorded by <u>Ebert</u>		Witnessed by			
REMARKS OR OTHER DATA					
<u>DV Tool @ 3261'</u>					
TEMPERATURE IN DEGREES FAHRENHEIT					

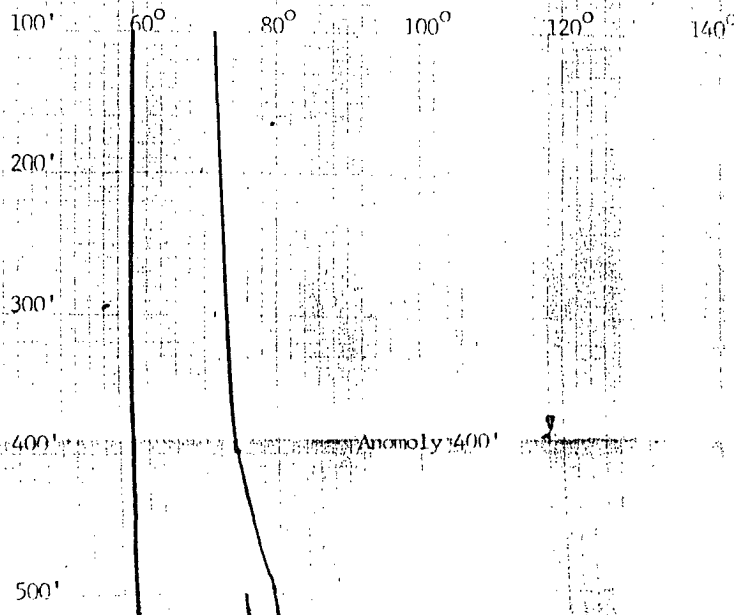

500'

600'

700'

800'

900'

1000'

1100'

1200'

1300'


1400'

1500'

1600'

1700'

1800'

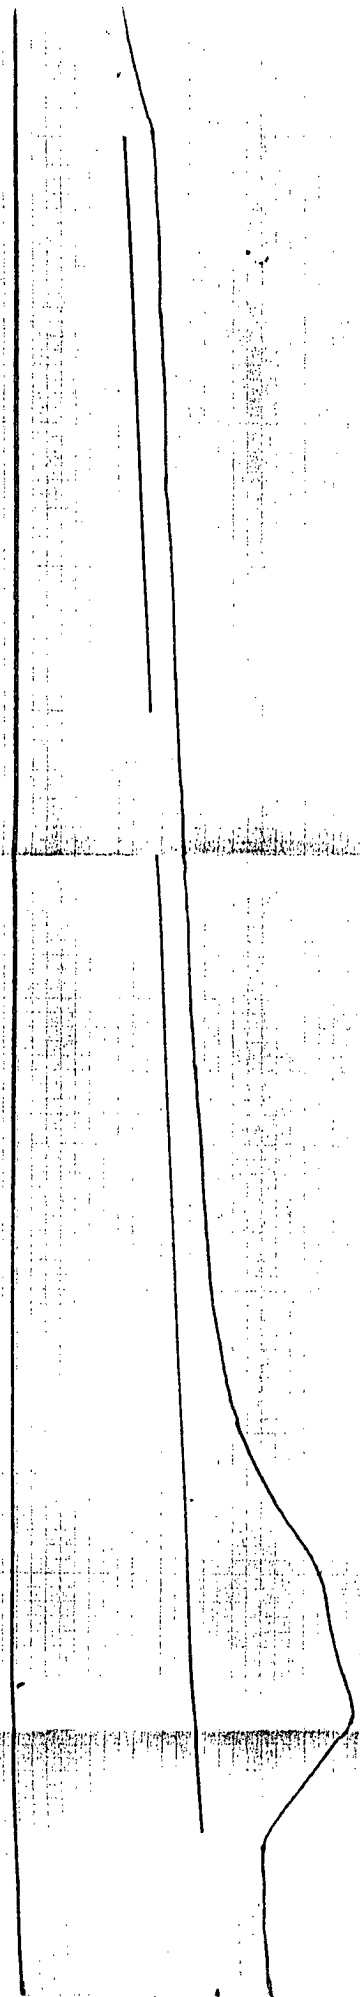

1700'

1800'

1900'

2000'

2100'

2200'

2300'

2400'

2500'


2600'

2700'

2800'

2900'

3000'

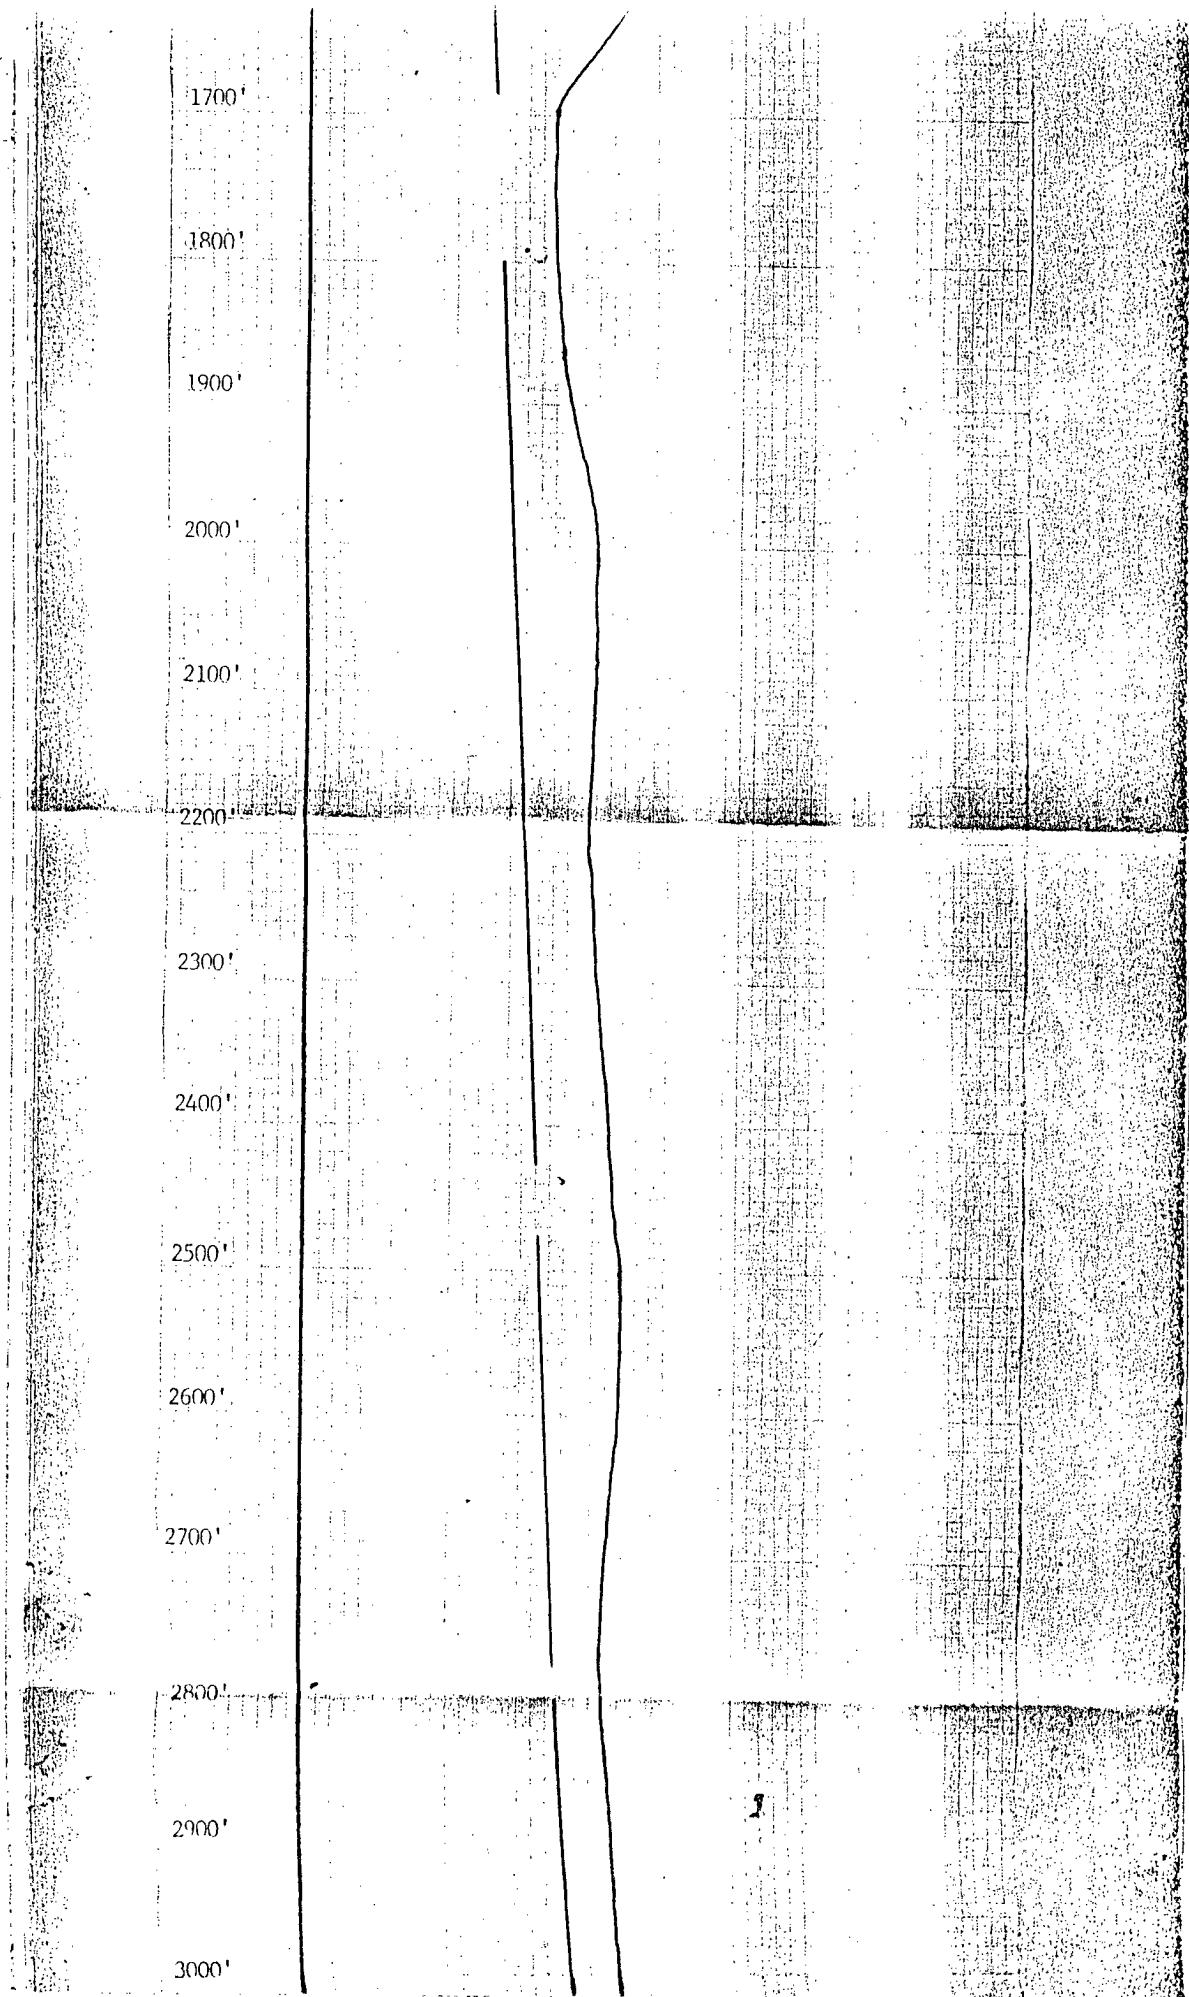

2500'

2600'

2700'

2800'

2900'

3000'

3100'

3200'

TD Surveyed 3250'
