

30-039-07833
30-039-24245

DATA SHEET FOR DEEP GROUND BED CATHODIC PROTECTION WELLS
NORTHWESTERN NEW MEXICO
(Submit 3 copies to OCD Aztec Office)

Operator MERIDIAN OIL Location: Unit SW Sec. 18 Twp 30 Rng 6

Name of Well/Wells or Pipeline Serviced SAN JUAN 30-6 UNIT #17, #455

cps 167w

Elevation 6630' Completion Date 4/9/63 Total Depth 120' Land Type* N/A

Casing, Sizes, Types & Depths N/A

If Casing is cemented, show amounts & types used N/A

If Cement or Bentonite Plugs have been placed, show depths & amounts used
N/A

Depths & thickness of water zones with description of water when possible:
Fresh, Clear, Salty, Sulphur, Etc. N/A

Depths gas encountered: N/A

Type & amount of coke breeze used: 850 lbs.

Depths anodes placed: 105', 99', 93', 87', 81'

Depths vent pipes placed: N/A

Vent pipe perforations: N/A

Remarks: gb #1

RECEIVED
MAY 31 1991
OIL CON. DIV
DIST. 3

If any of the above data is unavailable, please indicate so. Copies of all logs, including Drillers Log, Water Analyses & Well Bore Schematics should be submitted when available. Unplugged abandoned wells are to be included.

*Land Type may be shown: F-Federal; I-Indian; S-State; P-Fee.
If Federal or Indian, add Lease Number.

WELL CASING
CATHODIC PROTECTION CONSTRUCTION REPORT
DAILY LOG

DATE 9 April 63

WELL NAME San Juan 30-6 Unit No. 17 CPS NO. 167 W

LOCATION 5K1⁹ Sec. 18 T30N R6W

WORK ORDER NUMBER 184-40542-50-02

ANODE HOLE DEPTH 120

TOTAL DRILLING RIG TIME 4 Hrs.

DRILLING TIME FOR RECTIFIER POLE HOLE 0

TYPE AND SIZE BIT USED 6 1/4" Rock WM #1555

NUMBER SACKS MUD USED 2

NUMBER SACKS LOST CIRCULATION MAT'L USED 1

ANODE DEPTHS #1 105, #2 99, #3 93, #4 87 #5 81

TOTAL LBS. COKE USED 850

ANODE OUTPUTS 11.7 VOLTS, #1 4.2, #2 3.8, #3 3.6, #4 3.6 #5 3.0

TOTAL CIRCUIT RESISTANCE: VOLTS 11.3 AMPERES 8.0 OHMS 1.4

NUMBER FEET SURFACE CABLE CONDUIT 590'

DRILLING LOG (ATTACH HERETO).

FORMATION LOG (ATTACH HERETO).

REMARKS: Static % .66 R 600' W

Installed 28V 12A Rectifier


Good All Serial # 62C6287

Assigned Tag # 167 W

ALL CONSTRUCTION COMPLETED

Perrells
SIGNATURE

GROUND BED LAYOUT SKETCH

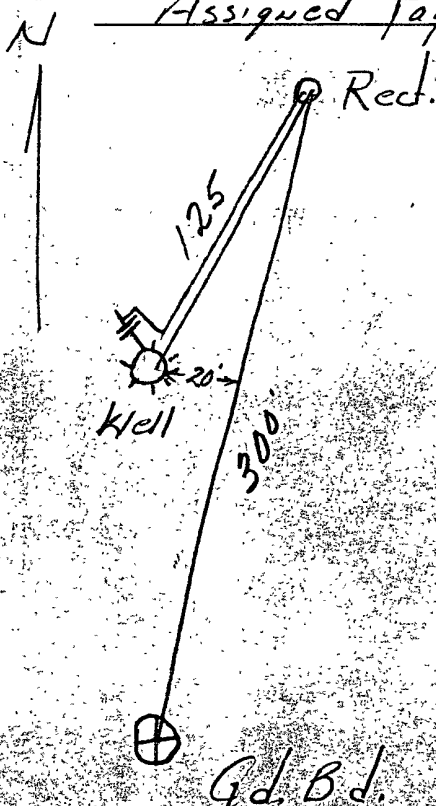

ORIGINAL & 1 COPY
ALL REPORTS

1135'

100

Wilson

REPORT NO.

一

CONTRACTOR	200
------------	-----

DAYLIGHT

[illegible]

卷之五

EVENING

NG

100

[illegible][illegible][illegible][illegible]

REMARKS

REMARKS:

April 9 - mailed 120 used 2 and 164 1/2 with and 4th time on 4.45.55

SIGNED: Toolpusher

Company Supervisor

James H. Power
