

139 - 30-039-06890

43 - 30-039-06887

DATA SHEET FOR DEEP GROUND BED CATHODIC PROTECTION WELLS
NORTHWESTERN NEW MEXICO
(Submit 3 copies to OCD Aztec Office)

Operator Union Oil Company of California Location: Unit Sec. 25 Twp 27N Rng 7W

Name of Well/Wells or Pipeline Serviced Rincon #139 DK Rincon #43 PC

Elevation 6647' Completion Date 10/29/65 Total Depth 310' Land Type* F

Casing, Sizes, Types & Depths None

If Casing is cemented, show amounts & types used None

If Cement or Bentonite Plugs have been placed, show depths & amounts used

None

Depths & thickness of water zones with description of water when possible:

Fresh, Clear, Salty, Sulphur, Etc. NA

RECEIVED
MAY 14 1990

Depths gas encountered: NA

OIL CON. DIV.
MAY 14 1990

Type & amount of coke breeze used: type unknown 4332 lbs

Depths anodes placed: 94' to 210'

Depths vent pipes placed: NA

Vent pipe perforations: NA

Remarks: El Paso Natural Gas Co. was the operator at the time this ground bed was installed.

First ground bed installed on this location.

If any of the above data is unavailable, please indicate so. Copies of all logs, including Drillers Log, Water Analyses & Well Bore Schematics should be submitted when available. Unplugged abandoned wells are to be included.

*Land Type may be shown: F-Federal; I-Indian; S-State; P-Fee.
If Federal or Indian, add Lease Number.

WELL CASING
CATHODIC PROTECTION CONSTRUCTION REPORT
DAILY LOG


#35 120' #9 Drag Bit 4 3/4"

Date 10-29-65

Well Name Rincon # 139 & #43			CPS No. 718W		
Location SW 25-27-7			Work Order No. (A) 184-52616 50-20		
Anode Hole Depth 310'	Total Drilling Rig Time 21 Hrs.	Type & Size Bit Used 7 1/8 Rock # 260240X	No. Sacks Mud Used 1		
No. Sacks Lost Circulation Mat'l Used 1 Mulls	Anode Depth #1 210'	#8 106	#9 100	#10 94	
Total Lbs. Coke Used 4332 lbs	Anode Output (Volts) #1 4.6	#2 4.9	#3 5.5	#4 5.0	
Total Circuit Resistance Volts 10.4	Amps 11.6	Ohms .896	No. Ft. Surface Cable Conduit 670' #8 Stranded		

Drilling Log (Attach Hereto). ☐

Remarks: Statics Rincon # 139 600' west = .66
Rincon # 43 600' west = .68
Installed 30/20 Goodall Rect. (4 Npg) Serial # 65C6703
4 lbs Chemical in Hand Bed.
1656 Feet #2 Stranded in Hand bed
100' 1/2" Hose in Hand Bed
11-1-65-Install CPS No. DeCal & Junction Box. QHS.

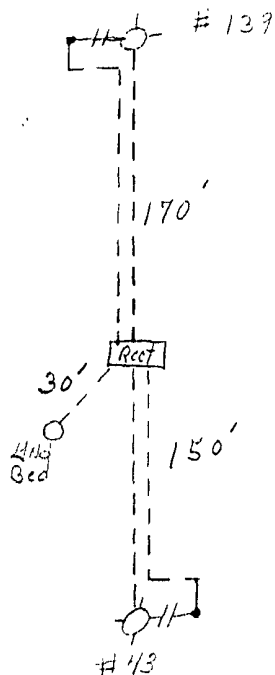

GROUND BED LAYOUT SKETCH

All Construction Completed

Phelps (QHS)
(Signature)

2326' #8 WIRE



DAILY DRILLING REPORT

LEASE *Wm #9 120'* WELL NO. *718W* CONTRACTOR *S. E. Wilson* RIG NO. *D-6* REPORT NO. DATE *10-27-1965*

MORNING					DAYLIGHT					EVENING				
Driller <i>Denver</i>		Total Men In Crew <i>2</i>			Driller		Total Men In Crew			Driller		Total Men In Crew		
FROM	TO	FORMATION	WT-BIT	R.P.M.	FROM	TO	FORMATION	WT-BIT	R.P.M.	FROM	TO	FORMATION	WT-BIT	R.P.M.
<i>0</i>	<i>20</i>	<i>Full</i>			<i>240</i>	<i>280</i>	<i>Sandy shale</i>							
<i>20</i>	<i>160</i>	<i>Shale</i>			<i>280</i>	<i>310</i>	<i>Sand</i>							
<i>160</i>	<i>190</i>	<i>Synstone</i>												
<i>190</i>	<i>240</i>	<i>Shale</i>												

BIT NO. <i>260240 X</i>		NO. DC	SIZE	LENG.	BIT NO.		NO. DC	SIZE	LENG.	BIT NO.		NO. DC	SIZE	LENG.
SERIAL NO.		STANDS			SERIAL NO.		STANDS			SERIAL NO.		STANDS		
SIZE		SINGLES			SIZE		SINGLES			SIZE		SINGLES		
TYPE		DOWN ON KELLY			TYPE		DOWN ON KELLY			TYPE		DOWN ON KELLY		
MAKE <i>310'</i>		TOTAL DEPTH			MAKE		TOTAL DEPTH			MAKE		TOTAL DEPTH		

MUD RECORD			MUD, ADDITIVES USED AND RECEIVED			MUD RECORD			MUD, ADDITIVES USED AND RECEIVED			MUD RECORD			MUD, ADDITIVES USED AND RECEIVED		
Time	Wt.	Vis.	<i>1 Mud</i>			Time	Wt.	Vis.				Time	Wt.	Vis.			

FROM	TO	TIME BREAKDOWN	FROM	TO	TIME BREAKDOWN	FROM	TO	TIME BREAKDOWN
			<i>Total rig time</i> <i>2 1 hr</i>					<i>10-27-65</i>
								<i>10-28-65</i>
								<i>10-29-65</i>

REMARKS -	REMARKS -	REMARKS -
<i>10-27-65</i>	<i>Left last loc. at 1000 morning. Drilled meter hole moved to ground level. Drilled 20' with 4 1/2".</i>	<i>Drilled meter hole.</i>
<i>10-28-65</i>	<i>Drilled 175' with 7 1/2". Left rig at 5:00.</i>	<i>Drilled 20' with 4 1/2".</i>
<i>10-29-65</i>	<i>Left yard at 600 arrived rig 7:45. Drilled from 175' to 300' down hole and logged when finished. Drilled to 300' with 4 1/2".</i>	<i>Drilled 20' with 4 1/2".</i>
	<i>Left rig at 5:00.</i>	
	<i>Left yard at 600 arrived rig 7:45. Drilled from 175' to 300' down hole and logged when finished. Drilled to 300' with 4 1/2".</i>	
	<i>Left rig at 1100.</i>	

SIGNED: Toolpusher

Company Supervisor
