

80 - 30-039-07086
159- 30-039-07071DATA SHEET FOR DEEP GROUND BED CATHODIC PROTECTION WELLS
NORTHWESTERN NEW MEXICO
(Submit 3 copies to OCD Aztec Office)Operator Union Oil Company of California Location: Unit Sec. 18 Twp 27N Rng 6WName of Well/Wells or Pipeline Serviced Rincon #80 MV & Rincon 159 DKElevation 6609 Completion Date 12/13/1965 Total Depth 275' Land Type* FCasing, Sizes, Types & Depths NAIf Casing is cemented, show amounts & types used NAIf Cement or Bentonite Plugs have been placed, show depths & amounts used
NADepths & thickness of water zones with description of water when possible:
Fresh, Clear, Salty, Sulphur, Etc. 105' - 120' 15' thickDepths gas encountered: NAType & amount of coke breeze used: 4255 lbsDepths anodes placed: 227'Depths vent pipes placed: 227'Vent pipe perforations: ?Remarks: El Paso Natural Gas was operator when this ground bed was installed.

If any of the above data is unavailable, please indicate so. Copies of all logs, including Drillers Log, Water Analyses & Well Bore Schematics should be submitted when available. Unplugged abandoned wells are to be included.

*Land Type may be shown: F-Federal; I-Indian; S-State; P-Fee.
If Federal or Indian, add Lease Number.

RECEIVED
MAY 03 1990
OIL CON. DIV.
DIST. 3


WELL CASING
CATHODIC PROTECTION CONSTRUCTION REPORT
DAILY LOG

Date 10-13-65

Well Name <u>Rincon #80 & #159</u>			CPS No. <u>687 W</u>		
Location <u>NE 18-27-6</u>			Work Order No. <u>52890 & 54108</u>		
Anode Hole Depth <u>275</u>	Total Drilling Rig Time <u>23 1/2 Hrs</u>	Type & Size Bit Used <u>7 7/8 - 398515 - 275</u>		No. Sacks Mud Used <u>1 -</u>	
No. Sacks Lost Circulation Mat'l Used <u>0</u>	Anode Depth <u>#1 227</u>	<u>#2 221</u>	<u>#3 215</u>	<u>#4 209</u>	<u>#5 203</u>
Total Lbs. Coke Used <u>4255</u>	Anode Output (Volts) <u>#1 2.5</u>	<u>#2 3.2</u>	<u>#3 3.1</u>	<u>#4 3.4</u>	<u>#5 3.6</u>
Total Circuit Resistance Volts <u>11.4</u>	Amps <u>9.2</u>	Ohms <u>1.24</u>	No. Ft. Surface Cable <u>1100</u>		

Drilling Log (Attach Hereto) ☐

Remarks: one notch (I) = #80 Cos. R% 600 S.W. = .74
Two Notch. (II) = #80 F.B.
Three Notch (III) = #159 Cos. R% 600 N.W. = .64
Install Good All Rectifier 30V 20A - 3 NEG. Term. Scr. #65C668
95' 3/4 Plastic Hosc. tied to Top Anode - Add 4lb. Chemical
Drilled 110' with air 9 3/4" Hole. Left overnite water level = 85'

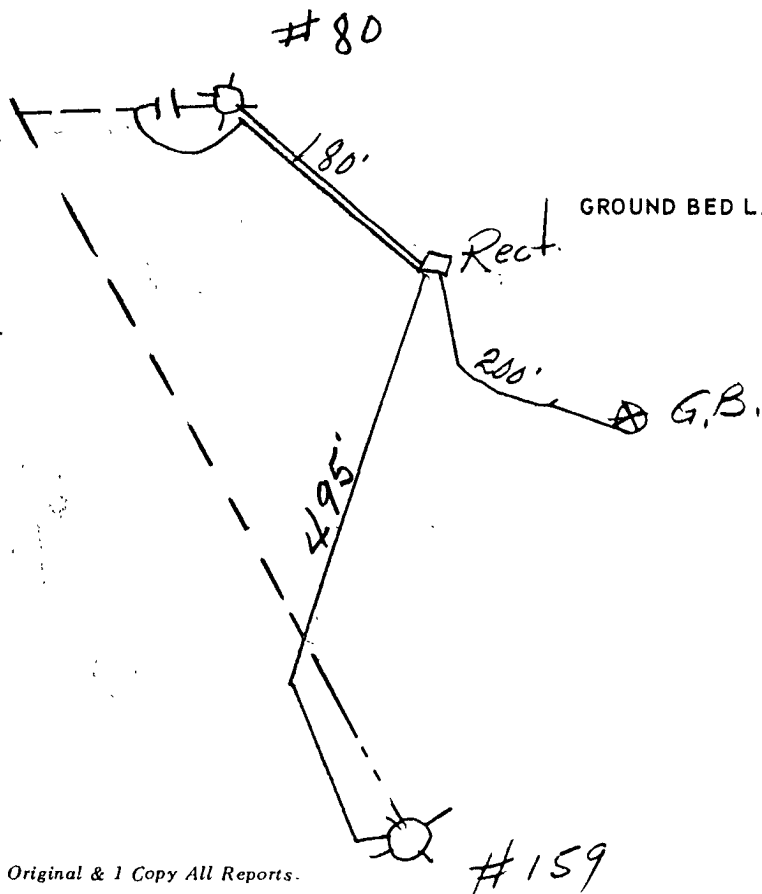

All Construction Completed

Sarrels
(Signature)

3108' #6 CABLE -

N
