District I

1625 N French Dr , Hobbs, NM 88240

District II

1301 W Grand Ave, Artesia, NM 88210

District III

 $1000\ Rio\ Brazos\ Rd$, Aztec, NM $\ 87410$

District IV

1220 S St Francis Dr , Santa Fe, NM 87505

State of New Mexico **Energy Minerals and Natural Resources**

Department Oil Conservation Division 1220 South St. Francis Dr. Santa Fe, NM 87505

July 21, 2008 For temporary pits, closed-loop sytems, and below-grade

Form C-144

tanks, submit to the appropriate NMOCD District Office

For permanent pits and exceptions submit to the Santa Fe Environmental Bureau office and provide a copy to the appropriate NMOCD District Office

Proposed Alternative Mathed Parmit on Cleaves Plan Application
Proposed Alternative Method Permit or Closure Plan Application
Type of action: X Permit of a pit, closed-loop system, below-grade tank, or proposed alternative method
Closure of a pit, closed-loop system, below-grade tank, or proposed alternative method Modification to an existing permit
Closure plan only submitted for an existing permitted or non-permitted pit, closed-loop system,
below-grade tank, or proposed alternative method
Instructions: Please submit one application (Form C-144) per individual pit, closed-loop system, below-grade tank or alternative request Please be advised that approval of this request does not relieve the operator of liability should operations result in pollution of surface water, ground water or the
environment. Nor does approval relieve the operator of its responsibility to comply with any other applicable governmental authority's rules, regulations or ordinances
Operator: ConocoPhillips Company OGRID#: 217817
Address: PO Box 4289, Farmington, NM 87499
Facility or well name: Michener 2P
API Number: 30-045- OCD Permit Number
U/L or Qtr/Qtr: G(SWNE) Section: 33 Township: 28N Range: 9W County: San Juan
Center of Proposed Design: Latitude: 36.61824' N Longitude: 107.79169' W NAD: 1927 X 1983 Surface Owner: X Federal State Private Tribal Trust or Indian Allotment
Surface Owner. A redefat State Frivate
2 X Pit: Subsection F or G of 19.15.17 11 NMAC
Temporary. X Drilling Workover
Permanent Emergency Cavitation P&A
X Lined Unlined Liner type Thickness 20 mil X LLDPE HDPE PVC Other
X String-Reinforced
Liner Seams. X Welded X Factory Other Volume 7000 bbl Dimensions L 120' x W 55' x D 12'
3
Closed-loop System: Subsection H of 19 15 17.11 NMAC
Type of Operation P&A Drilling a new well Workover or Drilling (Applies to activities which require prior approval of a permit or notice of intent)
Drying Pad Above Ground Steel Tanks Haul-off Bins Other
Lined Unlined Liner type: Thickness mil LLDPE HDPE PVD Other
Liner Seams Welded Factory Other
Secondary containment with leak detection Visible sidewalls, liner, 6-inch lift and automatic overflow shut-off Visible sidewalls and liner Visible sidewalls only Other
Volume: 120 bbl Type of fluid: Produced Water
Tank Construction material: Metal CONS. DW. D. CONS. DW. D. CONS.
Secondary containment with leak detection X Visible sidewalls, liner, 6-inch lift and automatic overflow shut-off
Visible sidewalls and liner Visible sidewalls only Other Visible sidewalls only Other
Liner Type. Thickness 45 mil HDPE PVC X Other LLDPE
5 Alternative Method:
Submittal of an exception request is required. Exceptions must be submitted to the Santa Fe Environmental Bureau office for consideration of approval.

Fencing: Subsection D of 19.15.17 11 NMAC (Applies to permanent pit, temporary pits, and below-grade tanks)									
Chain link, six feet in height, two strands of barbed wire at top (Required if located within 1000 feet of a permanent residence, school, hospital, inst	utution or chur	ch)							
Four foot height, four strands of barbed wire evenly spaced between one and four feet									
X Alternate Please specify 4' hogwire fence with a single strand of barbed wire on top.									
7									
Netting: Subsection E of 19.15.17.11 NMAC (Applies to permanent pits and permanent open top tanks)									
X Screen Netting Other Monthly inspections (If netting or screening is not physically feasible)									
8 Signs: Subsection C of 19.15.17.11 NMAC									
12" X 24", 2" lettering, providing Operator's name, site location, and emergency telephone numbers									
X Signed in compliance with 19.15.3.103 NMAC	=								
9									
Justifications and/or demonstrations of equivalency are required. Please refer to 19 15.17 NMAC for guidance.		ļ							
Please check a box if one or more of the following is requested, if not leave blank:									
Administrative approval(s): Requests must be submitted to the appropriate division district of the Santa Fe Environmental Bureau office for cons	ideration of ap	proval							
Exception(s): Requests must be submitted to the Santa Fe Environmental Bureau office for consideration of approval.									
10									
Siting Criteria (regarding permitting): 19.15.17.10 NMAC Instructions: The applicant must demonstrate compliance for each siting criteria below in the application. Recommendations of acceptable source material are provided below. Requests regarding changes to certain siting criteria may require administrative approval from the appropriate district office or may be considered an exception which must be submitted to the Santa Fe Environmental Bureau Office for consideration of approval. Applicant must attach justification for request. Please refer to 19.15.17.10 NMAC for guidance. Siting criteria									
does not apply to drying pads or above grade-tanks associated with a closed-loop system. Ground water is less than 50 feet below the bottom of the temporary pit, permanent pit, or below-grade tank.	Yes	XNo							
 NM Office of the State Engineer - iWATERS database search; USGS; Data obtained from nearby wells Within 300 feet of a continuously flowing watercourse, or 200 feet of any other watercourse, lakebed, sinkhole, or playa lake (measured from the ordinary high-water mark). Topographic map; Visual inspection (certification) of the proposed site 	Yes	XNo							
Within 300 feet from a permanent residence, school, hospital, institution, or church in existence at the time of initial application.	Yes	XNo							
(Applies to temporary, emergency, or cavitation pits and below-grade tanks)	□NA								
- Visual inspection (certification) of the proposed site; Aerial photo; Satellite image									
Within 1000 feet from a permanent residence, school, hospital, institution, or church in existence at the time of initial application.	Yes	No							
(Applied to permanent pits) Visual inspection (contification) of the proposed site. April photo: Setallite image	XNA								
 Visual inspection (certification) of the proposed site; Aerial photo; Satellite image Within 500 horizonal feet of a private, domestic fresh water well or spring that less than five households use for domestic or stock watering 	∏Yes	X No							
purposes, or within 1000 horizontal feet of any other fresh water well or spring, in existence at the time of initial application.		A							
- NM Office of the State Engineer - iWATERS database search; Visual inspection (certification) of the proposed site.									
Within incorporated municipal boundaries or within a defined municipal fresh water well field covered under a municipal ordinance adopted pursuant to NMSA 1978, Section 3-27-3, as amended	Yes	XNo							
- Written confirmation or verification from the municipality; Written approval obtained from the municipality Within 500 feet of a wetland. US Fish and Wildlyfa Wetland Identification man: Topographic man: Visual inspection (certification) of the proposed site.	Yes	XNo							
- US Fish and Wildlife Wetland Identification map; Topographic map; Visual inspection (certification) of the proposed site Witten confirmation or worffeeting or map from the NIM FANIED. Mining and	Yes	XNo							
- Written confirmation or verification or map from the NM EMNRD - Mining and Mineral Division Within an unstable area.	Yes	X No							
- Engineering measures incorporated into the design; NM Bureau of Geology & Mineral Resources; USGS; NM Geological Society; Topographic map	L15	Ano							
Within a 100-year floodplain - FEMA map	Yes	XNo							

Temporary Pits, Emergency Pits and Below-grade Tanks Permit Application Attachment Checklist: Subsection B of 19.15.17.9 NMAC
Instructions: Each of the following items must be attached to the application. Please indicate, by a check mark in the box, that the documents are attached X Hydrogeologic Report (Below-grade Tanks) - based upon the requirements of Paragraph (4) of Subsection B of 19.15.17 9 NMAC
X Hydrogeologic Report (Below-grade Tanks) - based upon the requirements of Paragraph (4) of Subsection B of 19.15.17 9 NMAC X Hydrogeologic Data (Temporary and Emergency Ptts) - based upon the requirements of Paragraph (2) of Subsection B of 19.15.17.9
X Siting Criteria Compliance Demonstrations - based upon the appropriate requirements of 19.15.17.10 NMAC
X Design Plan - based upon the appropriate requirements of 19.15.17.11 NMAC
X Operating and Maintenance Plan - based upon the appropriate requirements of 19 15.17 12 NMAC
X Closure Plan (Please complete Boxes 14 through 18, if applicable) - based upon the appropriate requirements of Subsection C of
19.15.17.9 NMAC and 19.15.17 13 NMAC
Previously Approved Design (attach copy of design) API or Permit
Closed-loop Systems Permit Application Attachment Checklist: Subsection B of 19.15.17.9 NMAC Instructions: Each of the following items must be attached to the application. Please indicate, by a check mark in the box, that the documents are attached. Geologic and Hydrogeologic Data (only for on-site closure) - based upon the requirements of Paragraph (3) of Subsection B of 19.15.17.9
Siting Criteria Compliance Demonstrations (only for on-site closure) - based upon the appropriate requirements of 19.15.17.10 NMAC
Design Plan - based upon the appropriate requirements of 19.15 17.11 NMAC
Operating and Maintenance Plan - based upon the appropriate requirements of 19.15.17.12 NMAC
Closure Plan (Please complete Boxes 14 through 18, if applicable) - based upon the appropriate requirements of Subsection C of 19.15 17.9
NMAC and 19 15 17 13 NMAC
Previously Approved Design (attach copy of design) API
Previously Approved Operating and Maintenance Plan API
13
Permanent Pits Permit Application Checklist: Subsection B of 19.15.17.9 NMAC
Instructions: Each of the following items must be attached to the application. Please indicate, by a check mark in the box, that the documents are attached.
Hydrogeologic Report - based upon the requirements of Paragraph (I) of Subsection B of 19.15.17.9 NMAC
Siting Criteria Compliance Demonstrations - based upon the appropriate requirements of 19.15 17.10 NMAC
Climatological Factors Assessment
Certified Engineering Design Plans - based upon the appropriate requirements of 19.15.17 11 NMAC Dike Protection and Structural Integrity Design: based upon the appropriate requirements of 19.15.17.11 NMAC
Leak Detection Design - based upon the appropriate requirements of 19.15.17.11 NMAC
Liner Specifications and Compatibility Assessment - based upon the appropriate requirements of 19.15.17 11 NMAC
Quality Control/Quality Assurance Construction and Installation Plan
Operating and Maintenance Plan - based upon the appropriate requirements of 19.15.17.12 NMAC
Freeboard and Overtopping Prevention Plan - based upon the appropriate requirements of 19.15.17.11 NMAC
Nuisance or Hazardous Odors, including H2S, Prevention Plan
Emergency Response Plan
Oil Field Waste Stream Characterization
Monitoring and Inspection Plan
☐ Erosion Control Plan ☐ Closure Plan - based upon the appropriate requirements of Subsection C of 19.15.17.9 NMAC and 19.15.17.13 NMAC
Proposed Closure: 19.15.17.13 NMAC
Instructions: Please complete the applicable boxes, Boxes 14 through 18, in regards to the proposed closure plan.
Type: X Drilling Workover Emergency Cavitation P&A Permanent Pit X Below-grade Tank Closed-loop System Alternative
Proposed Closure Method: X Waste Excavation and Removal (Below-Grade Tank)
Waste Removal (Closed-loop systems only)
X On-site Closure Method (only for temporary pits and closed-loop systems)
X In-place Burial On-site Trench
Alternative Closure Method (Exceptions must be submitted to the Santa Fe Environmental Bureau for consideration)
Waste Excavation and Removal Closure Plan Checklist: (19.15.17.13 NMAC) Instructions: Each of the following items must be attached to the closure plan.
Please indicate, by a check mark in the box, that the documents are attached. V Protocole and Procedures based upon the appropriate requirements of 10.15.17.13 NMAC
X Protocols and Procedures - based upon the appropriate requirements of 19.15.17 13 NMAC X Confirmation Sampling Plan (if applicable) - based upon the appropriate requirements of Subsection F of 19.15.17.13 NMAC
X Confirmation Sampling Plan (if applicable) - based upon the appropriate requirements of Subsection F of 19.13.17.13 NMAC X Disposal Facility Name and Permit Number (for liquids, drilling fluids and drill cuttings)
X Soil Backfill and Cover Design Specifications - based upon the appropriate requirements of Subsection H of 19.15.17.13 NMAC
X Re-vegetation Plan - based upon the appropriate requirements of Subsection I of 19.15.17.13 NMAC
X Site Reclamation Plan - based upon the appropriate requirements of Subsection G of 19.15.17.13 NMAC

Form C-144 Oil Conservation Division Page 3 of 5

16 Wasta Ramayal Clasura For Classel loan Systems That Hillia Above Cround S	Steel Tonks or Houl off Bins Only (10 15 17 13 D NIMAC)										
Waste Removal Closure For Closed-loop Systems That Utilize Above Ground S Instructions Please identify the facility or facilities for the disposal of liquids, drilli		acilities									
Disposal Facility Name:	Disposal Facility Permit #-										
Disposal Facility Name	Disposal Facility Permit #: Disposal Facility Permit #.										
Will any of the proposed closed-loop system operations and associated activi	Will any of the proposed closed-loop system operations and associated activities occur on or in areas that will not be used for future service and operations? Yes (If yes, please provide the information No										
Required for impacted areas which will not be used for future service and operation Soil Backfill and Cover Design Specification - based upon the appropriate requirements of Sub Re-vegetation Plan - based upon the appropriate requirements of Sub Site Reclamation Plan - based upon the appropriate requirements of Sub	oriate requirements of Subsection H of 19.15.17.13 NMA6 section I of 19.15.17.13 NMAC	2									
17 Siting Criteria (Regarding on-site closure methods only: 19.15.17.10 NM Instructions. Each siting criteria requires a demonstration of compliance in the closure play certain siting criteria may require administrative approval from the appropriate district office for consideration of approval. Justifications and/or demonstrations of equivalency are required.	 Recommendations of acceptable source material are provided beloce or may be considered an exception which must be submitted to the 										
Ground water is less than 50 feet below the bottom of the buried waste.		Yes X No									
- NM Office of the State Engineer - iWATERS database search; USGS: Data of	btained from nearby wells	∐N/A									
Ground water is between 50 and 100 feet below the bottom of the buried wa	ste	Yes X No									
- NM Office of the State Engineer - 1WATERS database search; USGS; Data of	btained from nearby wells	□N/A									
Ground water is more than 100 feet below the bottom of the buried waste		X Yes No									
- NM Office of the State Engineer - tWATERS database search; USGS; Data of	btained from nearby wells	□N/A									
Within 300 feet of a continuously flowing watercourse, or 200 feet of any other sign (measured from the ordinary high-water mark).	uficant watercourse or lakebed, sinkhole, or playa lake	Yes XNo									
- Topographic map; Visual inspection (certification) of the proposed site											
Within 300 feet from a permanent residence, school, hospital, institution, or church - Visual inspection (certification) of the proposed site; Aerial photo; satellite ima	∐Yes X No										
	Yes X No										
Within 500 horizontal feet of a private, domestic fresh water well or spring that less purposes, or within 1000 horizontal fee of any other fresh water well or spring, in ex - NM Office of the State Engineer - iWATERS database; Visual inspection (cert	sistence at the time of the initial application.										
Within incorporated municipal boundaries or within a defined municipal fresh water pursuant to NMSA 1978, Section 3-27-3, as amended.	·	Yes X No									
 Written confirmation or verification from the municipality, Written approval of Within 500 feet of a wetland 	obtained from the municipality	Yes X No									
- US Fish and Wildlife Wetland Identification map; Topographic map, Visual ii	nspection (certification) of the proposed site	163 2110									
Within the area overlying a subsurface mine.		Yes X No									
- Written confiramtion or verification or map from the NM EMNRD-Mining and	d Mineral Division	; 									
Within an unstable area. - Engineering measures incorporated into the design; NM Bureau of Geology & Topographic map	Mmeral Resources; USGS; NM Geological Society;	Yes XNo									
Within a 100-year floodplain - FEMA map		Yes X No									
On-Site Closure Plan Checklist: (19.15.17 13 NMAC) Instructions: Each by a check mark in the box, that the documents are attached.	ch of the following items must bee attached to the closur	e plan. Please indicate,									
X Siting Criteria Compliance Demonstrations - based upon the appropri	rate requirements of 19.15.17.10 NMAC										
X Proof of Surface Owner Notice - based upon the appropriate requiren											
Construction/Design Plan of Burial Trench (if applicable) based upor											
Construction/Design Plan of Temporary Pit (for in place burial of a d	••••	9.15.17.11 NMAC									
X Protocols and Procedures - based upon the appropriate requirements		-									
Confirmation Sampling Plan (if applicable) - based upon the appropri	ate requirements of Subsection F of 19.15 17.13 NMAC										
X Waste Material Sampling Plan - based upon the appropriate requirem	ents of Subsection F of 19.15 17 13 NMAC										
X Disposal Facility Name and Permit Number (for liquids, drilling fluid	s and drill cuttings or in case on-site closure standards car	nnot be achieved)									
X Soil Cover Design - based upon the appropriate requirements of Subs											
X Re-vegetation Plan - based upon the appropriate requirements of Sub-	X Re-vegetation Plan - based upon the appropriate requirements of Subsection I of 19.15.17.13 NMAC										

19	n Contiliantian.
Operator Application I hereby certify that the	information submitted with this application is true, accurate and complete to the best of my knowledge and belief.
Name (Print):	Crystal Tafoya Title Regulatory Technician
Signature:	Caratal Taloua Date: 10/10/08
e-mail address:	crystal.tafoya@conocophillibs.com Telephone: 505-326-9837
c-man address.	or justicity of a contract of the contract of
20 OCD Approval:	Permit Application (including closure plan) Closure Plan (only) OCD Conditions (see attachment)
OCD Representative	
Title:	Emiso Spec OCD Permit Number:
Title.	2003: 875fec Gertini Amou.
Instructions Operators report is required to be	quired within 60 days of closure completion): Subsection K of 19 15 17 13 NMAC is are required to obtain an approved closure plan prior to implementing any closure activities and submitting the closure report. The closure submitted to the division within 60 days of the completion of the closure activities. Please do not complete this section of the form until an that been obtained and the closure activities have been completed Closure Completion Date:
22	
Closure Method: Waste Excavati	on and Removal On-site Closure Method Alternative Closure Method Waste Removal (Closed-loop systems only) n approved plan, please explain.
Instructions: Please identified were utilized. Disposal Facility National Disposal Facility National Facility National Page 1997.	
Yes (If yes, plea	ase demonstrate compliane to the items below) No
Site Reclamation	ted areas which will not be used for future service and operations: on (Photo Documentation) g and Cover Installation Application Rates and Seeding Technique
24	
Closure Report A the box, that the do Proof of Closu Proof of Deed Plot Plan (for Confirmation Waste Materia Disposal Facil Soil Backfillir Re-vegetation	Attachment Checklist: Instructions: Each of the following items must be attached to the closure report. Please indicate, by a check mark in cuments are attached. The Notice (surface owner and division) Notice (required for on-site closure) The Notice (required for on-site closure) The Notice (surface owner and division) Notice (required for on-site closure) The
25	
	Sertification: e information and attachments submitted with this closure report is ture, accurate and complete to the best of my knowledge and belief. I also certify that th all applicable closure requirements and conditions specified in the approved closure plan.
Name (Print):	Title:
Signature:	Date.
e-mail address:	Telephone:

New Mexico Office of the State Engineer POD Reports and Downloads

Township: 28N Rang	e: 09W Sections:									
NAD27 X: Y:	Zone:	Search Radius:	 - - -							
County: Bas	in:	Number:	Suffix:							
Owner Name: (First)	(Last)	Non-Domestic C	Domestic							
POD / Surface D	POD / Surface Data Report Avg Depth to Water Report Water Column Report									
Clear Form iWATERS Menu Help										
WATER COLUMN REPORT 10/13/2008										


	(quarter	s are	big	gge	st	to:	smallest)		Depth	Depth	Wat∈
POD Number	Tws	Rng	Sec	q	đ	q	Zone	x	Y	Well	Water	Colum
SJ 03746 POD1	28N	09W	20	1	2	3				190	40	15
SJ 00018	28N	09W	20	3	1	4				135	71	ϵ
SJ 02800	28N	09W	24	4	2	3				200		


Record Count: 3

New Mexico Office of the State Engineer POD Reports and Downloads

Township: 27N	Range: 09W	Sections:								
NAD27 X:	' Y:	Zone:		Search Radius:						
County:	Basin:			Number:	Suffix:					
Owner Name: (First)	(La	ast) All	j i	○ Non-Domesti	c ODomestic					
POD / Surface Data Report Avg Depth to Water Report Water Column Report										
Clear Form iWATERS Menu Help										
WATER COLUMN REPORT 10/13/2008										
· -	ers are 1=NW 2= ers are biggest : Rng Sec q q	to smallest	-	Dept Y Well	h Depth Wate Water Colum					

No Records found, try again

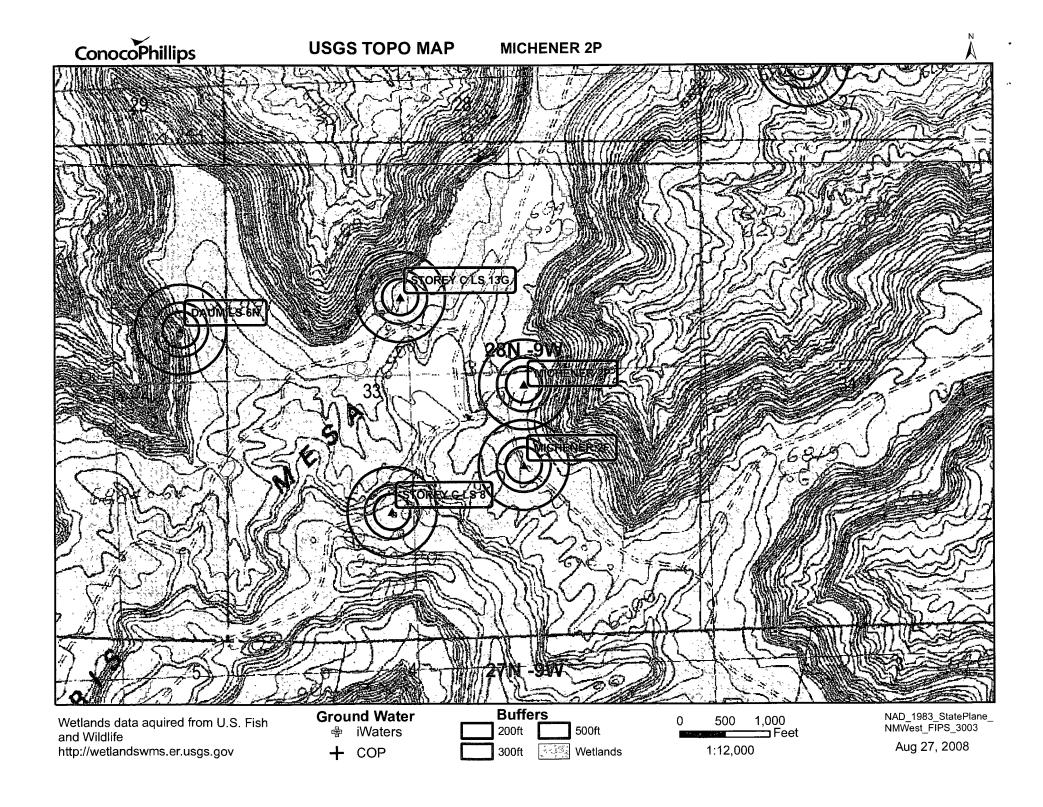

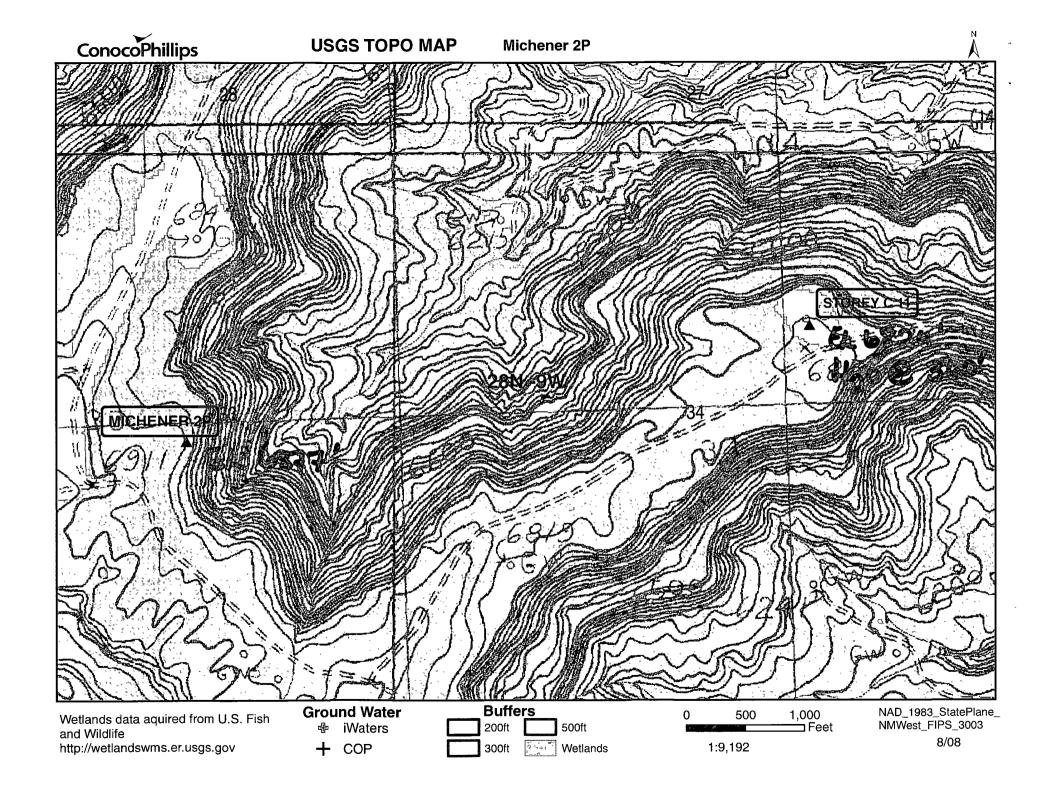

30-045-07028:

	-/0/01
DATE:	5/8/96

DATA SHEET FOR DEEP GROUND BED CATHODIC. PROTECTION WELLS NORTHWESTERN NEW MEXICO

Operator Mevidinu Oil INC. Location: Unit G Sec. 34 Twp 28 Rng 09
Name of Well/Wells or Pipeline Serviced
STOREY C#11
Elevation 6824 Completion Date 5/8/96 Total Depth 491 Jand Type F
Casing Strings, Sizes, Types & Depths 5/7 Set 59 of 8"PVC CAGING.
No GAS, WATER, OF BOULders Were ENCOUNTERED DUTING CASING.
If Casing Strings are cemented, show amounts & types used Cemented
WITH 15 SACKS
If Cement or Bentonite Plugs have been placed, show depths & amounts used
None "-
Depths & thickness of water zones with description of water: Fresh, Clear,
Salty, Sulphur, Etc. WIT Fresh WATER AT 360.
Depths gas encountered: None
Ground bed depth with type & amount of coke breeze used: 491 DepTH.
Used 130 SACKS OF ASbury 218R (6500#)
Depths anodes placed: 475, 465, 455, 445, 435, 425, 415, 405, 395, 365, 345, 326, 315, 230, +165
Depths vent pipes placed: Sufface To 491.
Vent pipe perforations: Bottom 360. DECEVED
Remarks:FEB 1 9 1997
OLL GON, DITY
DIST. 3

If any of the above data is unavailable, please indicate so. Copies of all logs, including Drillers Log, Water Analyses & Well Bore Schematics should be submitted when available. Unplugged abandoned wells are to be included.

Land Type may be shown: F-Federal; I-Indian; S-State; P-Fee. If Federal or Indian, add Lease Number.

	Crs Cadend Bed Clasiaut. Lia Workshamet											
29/	2915-W NOME (NUMBER () STOREY C#11											
	1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1										11/055	
A SE PRINCE	Drillet Reported DAMA AteAS AT											
70	70, 200, 260, AND WATER AT 360. INSTAILED 491' OF 1" PE											
VENT Pipe, WITH THE BOTTOM 360 PerforATEd. COKE												
Breeze To 115.												
CONTROL LOS LANGUETES DESCRIPTION OF LANGUE											-	
	ANGDE	-	 	-	-	İ	ANGER	-		AMODE	ANSSE.	
100	1		295		1	490	77.23	491	685			
105			300	1. 1.		495		1	690			
112			305	1.1		500]	695	-		
115			210	1.4		505			730		-	
1,20			315	. 2	1-13	510			AMERE	DEPTH	NES	FULLY
125		i	320	1.2		515			_ •		C014E	CBK. E
130	1 3		325	1.2	1-12	520			1	475	1.8	4.0
135	1 .3		330	1 2/		525			2	465	7.7	3.9
140	1.4		335	2		530			3	H55	1.7	4.0
145	14		340	1. 17		535			4	445	3.0	4.6
150	.4	1	345		- //	540			_ 5	#35	1.4	3.1
155	1.0	·	350	1	<u> </u>	545			5	425	1 1.3	2.8
160	1.3	-	355	1.4	-10	530		<u> </u>	7	415	1.2	127
165	1.3	- 15	360	1, 3		555		<u> </u>	8	405	1.6	13.1
170	1 - 9		355	7.2	ļ	550		- 	9	395	J. H	3.2
175	1		370	1	- 	<u> 555 </u>	ــــــــــــــــــــــــــــــــــــــ	-	10	255	1.3	3.6
180	1 , 3 , 3		375	1-22	-∤	570		┩——	11-11-	345	1.2	3.6
185	- 	-\	380	1.2	-}	575	 	-	12	1 225	1.3	2,2
190			385	1.2	-}	580	-	-}	13	1 215	1.5	3.2
195	- 	┥	390	1-3	-9	1 585	-}	-}	14	2/20	3.0	1.5.4
200	1 .3		395	1		598	- 	- 	 -12-	17.5	1-47	5.3
210	1-14	→	400	1 - 1 //		595			15	-}	- 	
215	1 00		410	1-12		605	-{			- 	┥	
220	1.0		415	-		610			18		-	
225			420			613	- 	┥	20	→	-	┥~~~
230	7.8	1-14	425	1.8		620	-	-∤	21	-	┥	┥
235	3.8	_	430	1.60		625		┪	22	~		-
240	1.2		435	1,4		630	┪──	_	23	_		-
245	1.2		440	1.6	7	635	-		24	┪		
250	1,0		445	3	#	640	_		25	Ta)	-	→
235	1.0		450	2.2		645			25	~ 		
260	1 1.7		455	1 - 4	j 3	650			27		<u> </u>	1-
265	1 /./		460	7, =		633			28		-	
270			465	1.6		<u> </u>			29			~
275			470	7. "/		665			30			
280	, 9		475	1 9		670						7
285	, 9	_!	480	12.7	4	673						
190	1, 7, 3)	485	,'.	<i>*</i>	680			1			
	1 / 1 - 7 1 - 2	!	1		<u> </u>	11	1 .	1	. 17_	•	1	1

SIBTRIBLITION - OPENSABLE - DEPRESENCE CREEK

NEW MEXICO OIL CONSERVATION COMMISSION Santa Fe, New Mexico


(Form C-104) Ravised 7/1/57

REQUEST FOR (OIL) - (GAS) ALLOWABLE


New Well


This form shall be submitted by the operator before an initial allowable will be assigned to any completed Oil or Gas well. Form C-104 is to be submitted in QUADRUPLICATE to the same District Office to which Form C-101 was sent. The allowable will be assigned effective 7:00 A.M. on date of completion or recompletion, provided this form is filed during calendar month of completion or recompletion. The completion date shall be that date in the case of an oil well when new oil is delivered into the stock tanks. Gas must be reported on 15.025 psia at 60° Fahrenheit.

					Farming	con, New	Mexico	July	y 23,	1958
					(Place)			•••••••••••••••••••••••••••••••••••••••	(Date)	•••••
E ARE	HEREBY RI	EQUESTI	NG AN ALLO	OWABLE FOR	R A WELL KNO	OWN AS:	SW		NE	
	ompany of One	rator)		(Iese)	, Well No		, in		•••••	1/4,
G`	Sec	34	_T 2811	9H	, NMPM.,	Blanco				D1
SACR T	Marian .									
Sa	n Juan		County. De	te Spudded	-18-58	Date Drill	ing Comple	ted 6.	-6-58	L
Ple	ase indicate k	ocation:	Elevation	6024	-18-58 Total I	Depth	(2,	KARAC.O.	• 543	# ·
		, , , ,	Top Oil/Gas	Pay 5248'	Perf.) Name of	Prod. Form.	Mesa V	Verde		
ן ע	CB	A	PRODUCING IN	TERVAL -						
[.,		Dan farrables	5248-5270	; 5 2 92-5312;	5338-535	0			
E	F G.	H	Perforations	None	Depth Casing	E),	71. D	epth ,	5388	
	X		Open Hole	MORRE	Casing	Shoe	T1	ubing	2300.	
-			OIL WELL TES	<u> -</u>						
L	KJ	I	Natural Prod	l. Test:	bbls.oil,	bbis wat	er in	hrs.	mín.	Choke
ŀ	ı				Treatment (after					_
X+	N O	1-5-						•	Choir	•
-			load oil use	·d) :bl	ols.oil,	bbls water i	n'hr	s,mi	n. Size	
		لل	GAS WELL TES	<u> -</u>						
1748	N, 1750'E		Natural Prod	l. Test:	MCF/Day	: Hours flow	ed	Choke Size	ρ	
uhtne Ge	aing and Gene	nting Rocci	_1		pack pressure, etc.					
Sipe	Fret	Sax		sering (priot,	50	45				3
-			Test After A	cid or Fracture	Treatment: 50		MCF/Day;	Hours flow	wed	
10 3/4	161	150	Choke Size_	Method	of Testing: Cale	CULA DEGL. A				
	1000	250	1 An d on Francis	ture Treatment	(Give amounts of m	atorials use	d. such as	acid, wate	er. oil.	and
7 5/8	3" 4916"	350			mater and 65,0				,,	
5 1/2	2" 644	200	sand): 65. Casing	Tubing (Date first no oil run to t	ew				
	53081		- Press.	Press.	to Natural Gar	anks	s Contest	A I km	<u></u>	
1 1/4'	1 3049		Oil Transpor	ter Ri	o Natural Gar Paso Natural (Gas Comme	nv	7\VE	—	
	Baken "B	LT' Per	Gas Transpor	ter				بسلا	0	
marks:	Dentit 19				and complete to the			~~~g~j9%)Q	. .
		••••	,			••••••••••	'يلاهٔ	العالم		
• • • • • • • • • • • • • • • • • • • •				•••••		······································		COL	3 /	<i>r</i>
I here	by certify the	at the info	rmation given	above is true	and complete to the	he best of m	y knowleds	re. DIS		
messed			July 28	, 1958	El Paso Na	tural Gas	Company	· ·		
proved				·····	•••••		or Operato			
^	II CONSED	VATION	COMMISSIO)N	By: Original	Signed D.	C. John	ictan		
						(Sig	gnature)	IO (UII		
Origi	inal Signed	l Emery	y C. Arnold	i	Title	oleum Eng	ineer			
	**************		*****************		Send (Communicat	ions regard	ling well t	to:	
ile Sup	ervisor Dist.	# 3				S. Oberl		-		
					Name					
					Box9	97, Farm	uington,	New Me	xico	

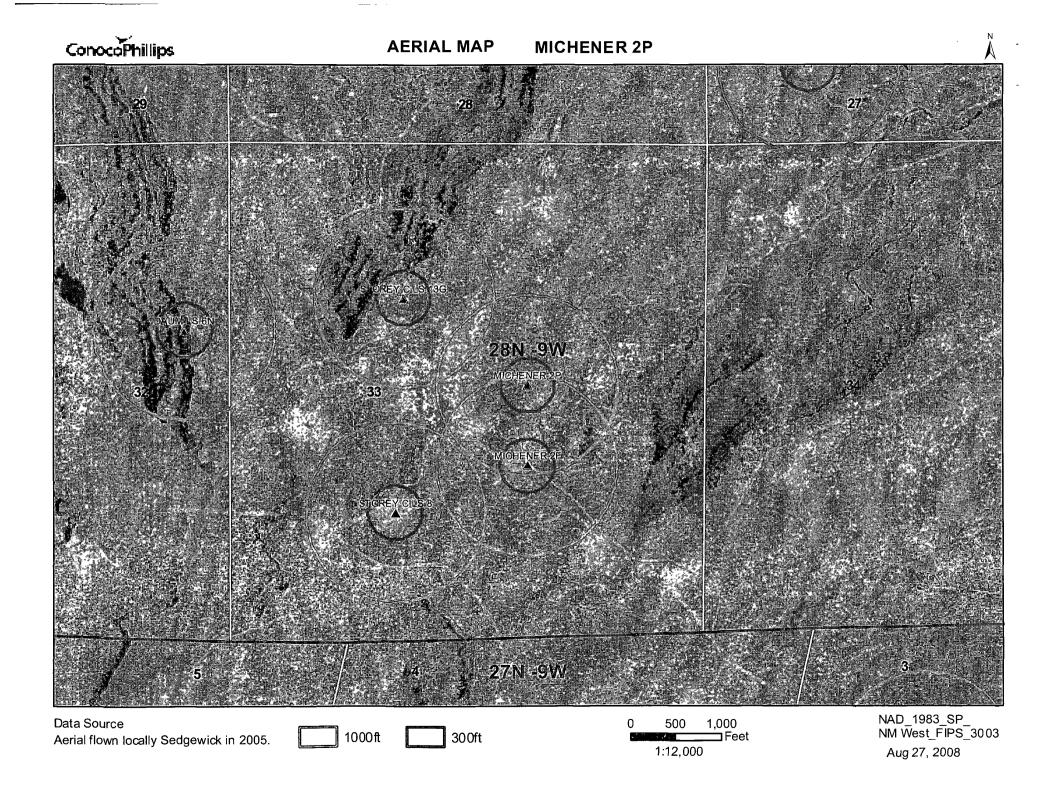


Michener 2P Mines, Mills and Quarries Web Map

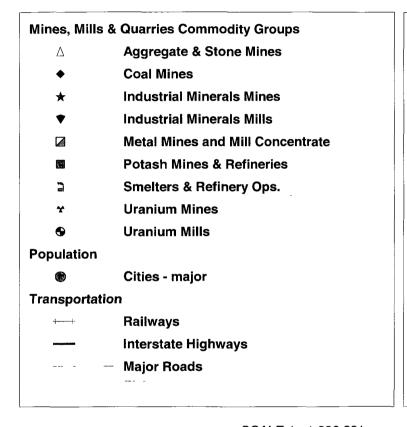

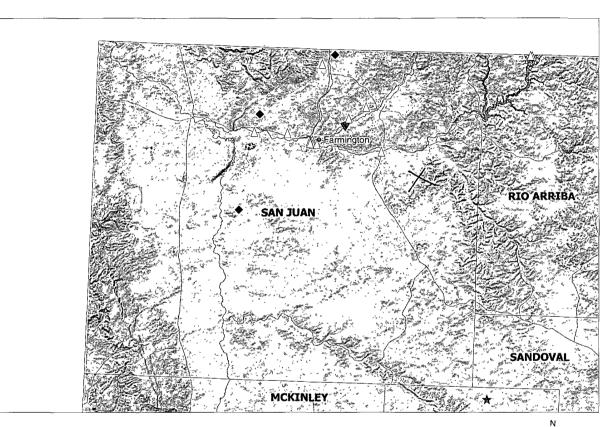





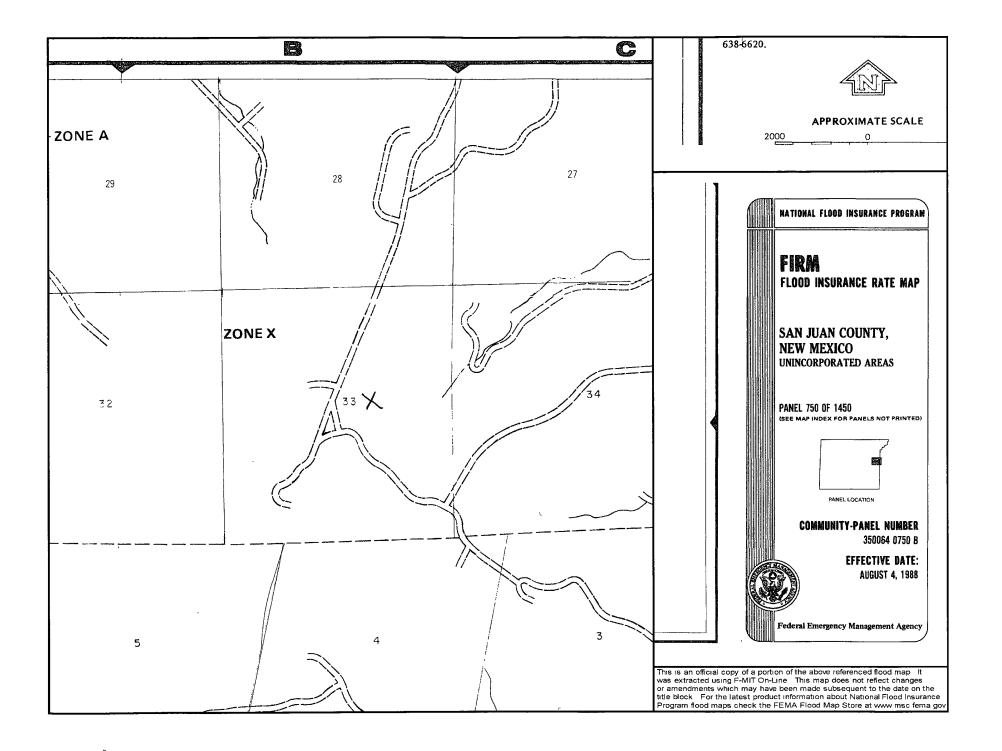

Hydrogeological report for Michener 2P

Regional Hydrogeological context:

The San Jose Formation of Eocene age occurs in New Mexico and Colorado, and its outcrop forms the land surface over much of the eastern half of the central basin. It overlies the Nacimiento Formation in the area generally south of the Colorado-New Mexico State line and overlies the Animas Formation in the area generally north of the State line.

The San Jose Formation was deposited in various fluvial-type environments. In general, the unit consists of an interbedded sequence of sandstone, siltstone, and variegated shale. Thickness of the San Jose Formation generally increases from west to east (200 feet in the west and south to almost 2,700 feet in the center of the structural basin). Ground water is associated with alluvial and fluvial sandstone aquifers. Thus, the occurrence of ground water is mainly controlled by the distribution of sandstone in the formation. The distribution of such sandstone is the result of original depositional extent plus any post-depositional modifications, namely erosion and structural deformation. Transmissivity data for San Jose Formation are minimal. Values of 40 and 120 feet squared per day were determined from two aquifer tests (Stone et al, 1983, table 5). The reported or measured discharge from 46 water wells completed in San Jose Formation ranges from 0.15 to 61 gallons per minute and the median is 5 gallons per minute. Most of the wells provide water for livestock and domestic use.

The San Jose Formation is a very suitable unit for recharge from precipitation because soils that form on the unit are sandy and highly permeable and therefore readily adsorb precipitation. However, low annual precipitation, relatively high transpiration and evaporation rates, and deep dissection of the San Jose Formation by the San Juan River and its tributaries all tend to reduce the effective recharge to the unit.

Stone et al., 1983, Hydrogeology and Water Resources of the San Juan Basin, New Mexico: Socorro, New Mexico Bureau of Mines and Mineral Resources Hydrologic Report 6, 70 p.

Siting Criteria Compliance Demonstration & Hydro Geologic Analysis

The Michener 2P is not located in an unstable area. The location is not over a mine and is not on the side of a hill as indicated on the Mines, Mills and Quarries Map and Topographic Map. The location of the excavated pit material will not be located within 300' of any continuously flowing watercourse or 200' from any other watercourse as indicated on the Topographic Map. The location is not within a 100-year floodplain area as indicated on the FEMA Map. The Cathodic well data from the Storey C 11 has an elevation of 6824' and groundwater depth of 360'. The subject well has an elevation of 6877' which is greater than the Storey C 11, therefore the groundwater depth is greater than 360'. There are no iWATERS data points located in the area as indicated on the TOPO Map. The hydro geologic analysis indicates the groundwater depth and the San Jose formation will create a stable area for this new location.

Tafoya, Crystal

From:

Tafoya, Crystal

Sent:

Wednesday, October 15, 2008 10:22 AM

To: Subject: 'mark_kelly@nm.blm.gov' Surface Owner Notification

The following locations will have the temporary pit closed on-site. Please let me know if you have any questions.

McClanahan 550S Lloyd B Com 100S Sunray F 1G Michener 2P Stanolind Gas Com 1M Huerfano Unit 304E

Thank you,

Crystal L. Tafoya Regulatory Technician *ConocoPhillips Company* San Juan Business Unit Phone: (505) 326-9837

Email: Crystal.Tafoya@conocophillips.com

DISTRICT I 1625 N. French Dr., Hobbs, N.M. 88240 State of New Mexico
Energy, Minerals & Natural Resources Department

Form C-102 Revised October 12, 2005

DISTRICT II 1301 W. Grand Avenue, Artesia, N.M. 88210

 DISTRICT III
 OIL CONS

 1000 Rio Brazos Rd., Aztec, N.M. 87410
 1220 S

OIL CONSERVATION DIVISION 1220 South St. Francis Dr. Santa Fe, NM 87505 Submit to Appropriate District Office State Lease - 4 Copies Fee Lease - 3 Copies

☐ AMENDED REPORT

DISTRICT IV 1220 S. St. Francis Dr., Santa Fe, NM 87505

WELL LOCATION AND ACREAGE DEDICATION PLAT

¹ API Number	⁴ Pool Code	*Pool Name BASIN DAKOTA/BLANCO MESAVERDE
Property Code	⁶ Property Name MICHENER	° Well Number 2 P
OGRID No.	Operator Name CONOCOPHILLIPS COMPAN	^o Elevation


¹⁰ Surface Location

ð	UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
	G	33	28N	9W		2725'	NORTH	1975'	EAST	SAN JUAN

¹¹ Bottom Hole Location If Different From Surface

bottom hole bocation in different From Surface									
UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
					ļ				
12 Dedicated Acres			18 Joint or	Infill	16 Consolidation C	ode	15 Order No.		
320.0 Ac	res - (E/2)							

NO ALLOWABLE WILL BE ASSIGNED TO THIS COMPLETION UNTIL ALL INTERESTS HAVE BEEN CONSOLIDATED
OR A NON-STANDARD UNIT HAS BEEN APPROVED BY THE DIVISION

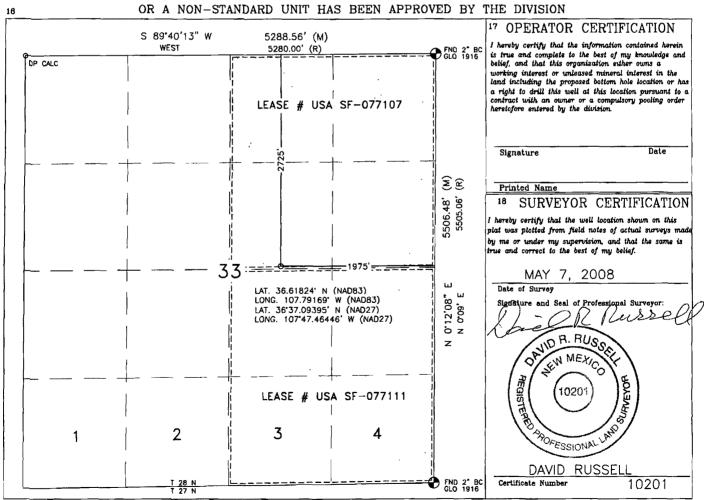

LATITUDE: 36.61824°N LONGITUDE: 107.79169°W DATUM: NAD 83

SLOPES TO BE CONSTRUCTED TO MATCH THE ORIGINAL CONTOURS AS CLOSE AS POSSIBLE.

CONOCOPHILLIPS COMPANY

MICHENER #2 P 2725' FNL & 1975' FEL


LOCATED IN THE SW/4 NE/4 OF SECTION 33,


T28N, R9W, N.M.P.M.,

SAN JUAN COUNTY, NEW MEXICO

GROUND ELEVATION: 6877', NAVD 88

FINISHED PAD ELEVATION: 6873.7', NAVD 88



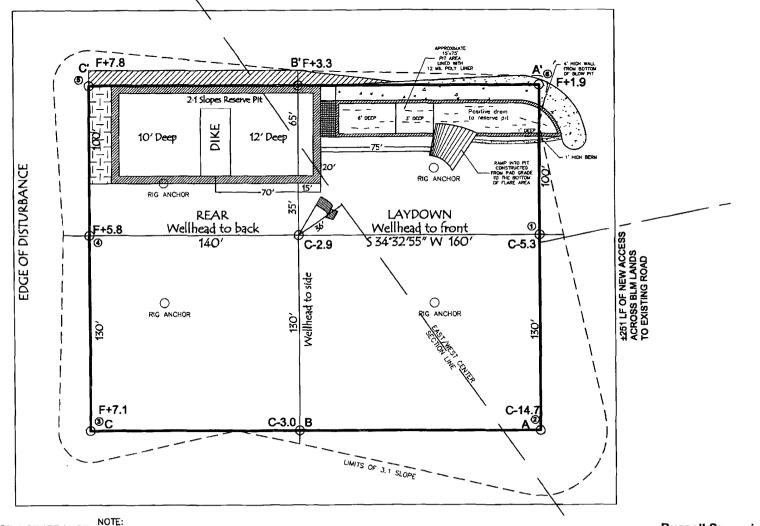

330' x 400' = 3.03 ACRES OF DISTURBANCE


SCALE: 1" = 60' JOB No.: COPC181 DATE: 05/21/08 RESERVE PIT DIKE: TO BE 8' ABOVE DEEP SIDE (OVERFLOW - 3' WIDE AND 1' ABOVE SHALLOW SIDE).
RUSSELL SURVEYING, INC. IS NOT LIABLE FOR UNDERGROUND UTILITIES OR PIPELINES.
CONTRACTOR SHOULD CALL ONE-CALL FOR LOCATION OF ANY MARKED OR UNMARKED, BURIED PIPELINES OR
CABLES ON WELL PAD, IN CONSTRUCTION ZONE AND/OR ACCESS ROAD AT LEAST TWO (2) WORKING DAYS PRIOR
TO CONSTRUCTION.



Russell Surveying 1409 W. Aztec Blvd. #2 Aztec, New Mexico 87410 (505) 334-8637 LATITUDE: 36.61824°N LONGITUDE: 107.79169°W DATUM: NAD 83

CONOCOPHILLIPS COMPANY

MICHENER #2 P 2725' FNL & 1975' FEL LOCATED IN THE SW/4 NE/4 OF SECTION 33, T28N, R9W, N.M.P.M., SAN JUAN COUNTY, NEW MEXICO GROUND ELEVATION. 6877', NAVD 88

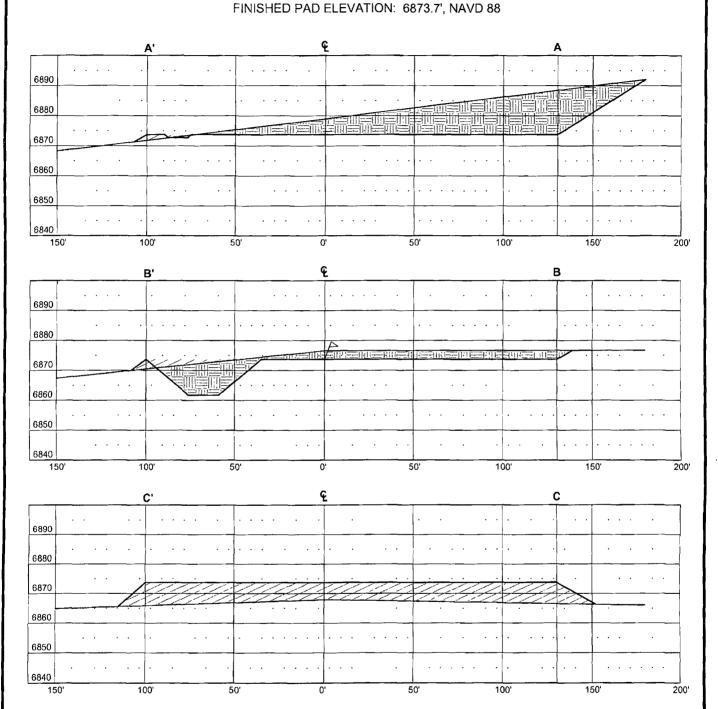

THIS DIAGRAM IS AN ESTIMATE OF DIRT BALANCE AND IS NOT INTENDED TO BE AN EXACT MEASURE OF VOLUME

VERT. SCALE: 1" = 30' HORZ. SCALE: 1" = 50' JOB No.: COPC181 DATE: 05/21/08





Russell Surveying 1409 W. Aztec Blvd. #2 Aztec, New Mexico 87410 (505) 334-8637

ConocoPhillips Company San Juan Basin Pit Design and Construction Plan

In accordance with Rule 19.15.17 the following information describes the design and construction of temporary pits on ConocoPhillips Company (COPC) locations. This is COPC's standard procedure for all temporary pits. A separate plan will be submitted for any temporary pit which does not conform to this plan.

- 1. COPC will design and construct a properly sized and approved temporary pit which will contain liquids and solids and should prevent contamination of fresh water and protect public health and environment.
- 2. Prior to constructing the pit, topsoil will be stockpiled in the construction zone for later use in restoration.
- 3. COPC will sign the well location in compliance with 19.15.3.103 NMAC.
- 4. COPC shall construct all new fences around the temporary pit utilizing 48" steel mesh field-fence (hogwire) on the bottom with a single strand of barbed wire on top. T-posts shall be installed every 12 feet and corners shall be anchored utilizing a secondary T-post. Temporary pits will be fenced at all times excluding drilling or workover operations, when the front side of the fence will be temporarily removed for operational purposes.
- 5. COPC shall construct the temporary pit so that the foundation and interior slopes are firm and free of rocks, debris, sharp edges or irregularities to prevent liner failure.
- COPC shall construct the pit so that the slopes are no steeper than two horizontal feet to one vertical foot.
- 7. Pit walls will be walked down by a crawler type tractor following construction.
- 8. All temporary pits will be lined with a 20-mil, string reinforced, LLDPE liner, complying with EPA SW-846 method 9090A requirements.
- Geotextile will be installed beneath the liner when rocks, debris, sharp edges or irregularities cannot be avoided.
- All liners will be anchored in the bottom of a compacted earth-filled trench at least 18 inches deep.
- 11. COPC will minimize liner seams and orient them up and down, not across a slope. Factory seams will be used whenever possible. COPC will ensure all field seams are welded by qualified personnel. Field seams will be overlapped four to six inches and will be oriented parallel to the line of maximum slope. COPC will minimize the number of field seams in corners and irregularly shaped areas.
- 12. The liner shall be protected from any fluid force or mechanical damage through the use of mud pit slides, or a manifold system.
- 13. The pit shall be protected from run-off by constructing and maintaining diversion ditches around the location or around the perimeter of the pit in some cases.
- 14. The volume of the pit shall not exceed 10 acre-feet, including freeboard.
- 15. Temporary blow pits will be constructed to allow gravity flow to discharge into lined drill pit.
- 16. The lower half of the blow pit (nearest lined pit) will be lined with a 20-mil, string reinforced, LLDPE liner. The upper half of the blow pit will remain unlined as allowed in Rule 19.15.17.11 F.11.
- 17. COPC will not allow freestanding liquids to remain on the unlined portion of a temporary blow pit.

ConocoPhillips Company San Juan Basin Maintenance and Operating Plan

In accordance with Rule 19.15.17 the following information describes the operation and maintenance of temporary pits on ConocoPhillips Company (COPC) locations. This is COPC's standard procedure for all temporary pits. A separate plan will be submitted for any temporary pit which does not conform to this plan.

- COPC will operate and maintain a temporary pit to contain liquids and solids and maintain the integrity of the liner and liner system to prevent contamination of fresh water and protect public health and environment.
- 2. COPC will conserve drilling fluids by transferring liquids to pits ahead of the rigs whenever possible. All other drilling fluids will be disposed at Basin Disposal Inc., permit # NM-01-005.
- 3. COPC will not discharge or store any hazardous waste in any temporary pit.
- 4. If any pit liner's integrity is compromised, or if any penetration of the liner occurs above the liquid's surface, then COPC shall notify the Aztec Division office by phone or email within 48 hours of the discovery and repair the damage or replace the liner.
- 5. If a leak develops below the liquid's level, COPC shall remove all liquids above the damaged liner within 48 hours and repair the damage or replace the liner. COPC shall notify the Aztec Division office by phone or email within 48 hours of the discovery for leaks less than 25 barrels. COPC shall notify the Aztec Division office as required pursuant to Subsection B of 19.15.3.116 NMAC shall be reported within twenty-four (24) hours of discovery of leaks greater than 25 barrels. In addition, immediate verbal notification pursuant to Subsection B, Paragraph (1), and Subparagraph (d) of 19.15.3.116 NMAC shall be reported to the division's Environmental Bureau Chief.
- 6. The liner shall be protected from any fluid force or mechanical damage through the use of mud pit slides, or a manifold system.
- 7. The pit shall be protected from run-off by constructing and maintaining diversion ditches around the location or around the perimeter of the pit in some cases.
- 8. COPC shall immediately remove any visible layer of oil from the surface of the temporary pit after cessation of a drilling or workover operation. Oil absorbent booms will be utilized to contain and remove oil from the pit's surface. An oil absorbent boom will stored on-site until closure of pit.
- Only fluids generated during the drilling or workover process may be discharged into a temporary pit.
- 10. COPC will maintain the temporary pit free of miscellaneous solid waste or debris.
- 11. During drilling operations, COPC will inspect the temporary pit at least once daily to ensure compliance with this plan. Inspections will be logged in the IADC reports. COPC will file this log with the Aztec Division office upon closure of the pit.
- 12. After drilling operations, COPC will inspect the temporary pit weekly so long as liquids remain in the temporary pit. A log of the inspections will be stored at COPC's office electronically and will be filed with the Aztec Division office upon closure of the pit.
- 13. COPC shall maintain at least two feet of freeboard for a temporary pit.
- 14. COPC shall remove all free liquids from a temporary pit within 30 days from the date the operator releases the drilling rig.
- 15. COPC shall remove all free liquids from a cavitation pit within 48 hours after completing cavitation. COPC may request additional time to remove liquids from the Aztec Division office if it is not feasible to remove liquids within 48 hours.

ConocoPhillips Company San Juan Basin Closure Plan

In accordance with Rule 19.15.17.12 NMAC the following information describes the closure requirements of temporary pits on ConocoPhillips Company (COPC) locations. This is COPC's standard procedure for all temporary pits. A separate plan will be submitted for any temporary pit which does not conform to this plan.

All closure activities will include proper documentation and be available for review upon request and will be submitted to OCD within 60 days of closure of pit closure. Closure report will be filed on C-144 and incorporate the following:

- Details on Capping and Covering, where applicable.
- Plot Plan (Pit Diagram)
- Inspection Reports
- Sampling Results
- C-105
- Copy of Deed Notice will be filed with County Clerk

- All free standing liquids will be removed at the start of the pit closure process from the pit and disposed of in a division—approved facility or recycle, reuse or reclaim the liquids in a manner that the appropriate division district office approves. The facilities to be used will be Basin Disposal (Permit #NM-01-005) and Envirotech Land Farm (Permit #NM-01-011).
- 2. The preferred method of closure for all temporary pits will be on-site burial, assuming that all the criteria listed in sub-section (B) of 19.15.17.13 are met.
- 3. The surface owner shall be notified of COPC's closing of the temporary pit prior to closure as per the approved closure plan via certified mail, return receipt requested.
- 4. Within 6 months of the Rig Off status occurring COPC will ensure that temporary pits are closed, re-contoured, and reseeded.
- 5. Notice of Closure will be given prior to closure to the Aztec Division office between 72 hours and one week via email, or verbally. The notification of closure will include the following:
 - i. Operator's name
 - Location by Unit Letter, Section, Township, and Range. Well name and API number.
- 6. Liner of temporary pit shall be removed above "mud level" after stabilization. Removal of liner will consist of manually or mechanically cutting liner at mud level and removing all remaining liner. Care will be taken to remove "All" of the liner i.e., edges of liner entrenched or buried. All excessive liner will be disposed of at the San Juan County Landfill located on CR 3100.
- 7. Pit contents shall be mixed with non-waste containing, earthen material in order to achieve the solidification process. The solidification process will be accomplished using a combination of natural drying and mechanically mixing. Pit contents will be mixed with non-waste, earthen material to a consistency that is deemed a safe and stable. The mixing ratio shall not exceed 3 parts clean soil to 1 part pit contents.
- 8. A five point composite sample will be taken of the pit using sampling tools and all samples tested per Subsection B of 19.15.17.13(B)(1)(b). In the event that the criteria are not met, all contents will be handled per Subparagraph (a) of Paragraph (1) of Subsection B of 19.15.17.13 i.e., Dig and haul.

Components	Tests Method	Limit (mg/Kg)
Benzene	EPA SW-846 8021B or 8260B	0.2
BTEX	EPA SW-846 8021B or 8260B	50
TPH	EPA SW-846 418.1	2500
GRO/DRO	EPA SW-846 8015M	5 00
Chlorides	EPA 300.1	(1000)500

- 9. Upon completion of solidification and testing standards being passed, the pit area will be backfilled with compacted, non-waste containing, earthen material. A minimum of four feet of cover shall be achieved and the cover shall include one foot of suitable material to establish vegetation at the site, or the background thickness of topsoil, whichever is greater. If standard testing fails COPC will dig and haul all contents pursuant to 19.15.17.13.i.a. After doing such, confirmation sampling will be conducted to ensure a release has not occurred.
- 10. During the stabilization process if the liner is ripped by equipment the Aztec OCD office will be notified within 48 hours and the liner will be repaired if possible. If the liner can not be repaired then all contents will be excavated and removed.
- 11. Dig and Haul Material will be transported to the Envirotech Land Farm located 16 miles south of Bloomfield on Angel Peak Road, CR 7175. Permit # NM010011
- 12. Re-contouring of location will match fit, shape, line, form and texture of the surrounding. Reshaping will include drainage control, prevent ponding, and prevent erosion. Natural drainages will be unimpeded and water bars and/or silt traps will be place in areas where needed to prevent erosion on a large scale. Final re-contour shall have a uniform appearance with smooth surface, fitting the natural landscape.
- 13. Notification will be sent to OCD when the reclaimed area is seeded.
- 14. COPC shall seed the disturbed areas the first growing season after the operator closes the pit. Seeding will be accomplished via drilling on the contour whenever practical or by other division-approved methods. BLM or Forest Service stipulated seed mixes will used on federal lands. Vegetative cover will equal 70% of the native perennial vegetative cover (unimpacted) consisting of at least three native plant species, including at least one grass, but not including noxious weeds, and maintain that cover through two successive growing seasons. Repeat seeding or planting will be continued until successful vegetative growth occurs.

Туре	Variety or Cultivator	PLS/A
Western wheatgrass	Arriba	3.0
Indian ricegrass	Paloma or Rimrock	3.0
Slender wheatgrass	San Luis	2.0
Crested wheatgrass	Hy-crest	3.0
Bottlebrush Squirreltail	Unknown	2.0
Four-wing Saltbrush	Delar	.25

Species shall be planted in pounds of pure live seed per acre: Present Pure Live Seed (PLS) = Purity X Germination/100 Two lots of seed can be compared on the basis of PLS as follows:

Source No. One (poor quality)

Purity

50 percent

Germination

40 percent

Percent PLS

20 percent

Percent PLS

Source No. two (better quality)

Purity

80 percent

Germination

63 percent

Percent PLS

50 percent

5 lb. bulk seed required to make 2 lb. bulk seed required to make

1 lb. PLS 1 lb. PLS

15. The temporary pit will be located with a steel marker, no less than four inches in diameter, cemented in a hole three feet deep in the center of the onsite burial upon the abandonment of all the wells on the pad. The marker will be flush with the ground to allow access of the active well pad and for safety concerns. The marker will include a threaded collar to be used for future abandonment. The top of the marker will contain a welded steel 12" square plate that indicates the onsite burial of the temporary pit. The plate will be easily removable and a four foot tall riser will be threaded into the top of the collar marker and welded around the base with the operator's information at the time of all wells on the pad are abandoned. The operator's information will include the following: Operator Name, Lease Name, Well Name and number, Unit Number, Section, Township, Range and an indicator that the marker is an onsite burial location.

ConocoPhillips Company San Juan Basin Below Grade Tank Design and Construction

In accordance with NMAC 19.15.17 the following information describes the design and construction of below grade tanks on ConocoPhillips Company (COPC) locations. This is COPC's standard procedure for all below grade tanks (BGT). A separate plan will be submitted for any BGT which does not conform to this plan.


- COPC will design and construct a properly sized and approved BGT which will
 contain liquids and should prevent contamination of fresh water to protect the
 public health and environment.
- 2. COPC will sign the well location in compliance with 19.15.3.103 NMAC.
- 3. COPC shall construct fencing around the BGT using 4 foot hog wire fencing topped with two strands of barbed wire, or with a pipe top rail. A six foot chain link fence topped with three strands of barbed wire will be use if the well location is within 1000 feet of permanent residence, school, hospital, institution or church.
- COPC will construct a screened, expanded metal covering, on the top of the BGT.
- 5. COPC shall ensure that a below-grade tank is constructed of materials resistant to the below-grade tank's particular contents and resistant to damage from sunlight.
- The COPC below-grade tank system shall have a properly constructed foundation consisting of a level base free of rocks, debris, sharp edges or irregularities to prevent punctures, cracks or indentations of the liner or tank bottom.
- 7. COPC shall construct a below-grade tank to prevent overflow and the collection of surface water run-on.
- 8. COPC will construct and use a below-grade tank that does not have double walls. The below-grade tank's side walls will be open for visual inspection for leaks, the below-grade tank's bottom is elevated a minimum of six inches above the underlying ground surface and the below-grade tank is underlain with a geomembrane liner to divert leaked liquid to a location that can be visually inspected.
- 9. COPC has equipped the below-grade tanks with the ability to detect high level in the tank and provide alarm notification and shutdown process streams into the tank. Once high level is detected RTU logic closes the inlet separator sales valve and does not permit vent valve to open. This shutdown of the sales valve and gagging of the vent valves prevents any hydrocarbon process streams from entering the pit tank once a high level is detected. Furthermore, an electronic page is sent to the COPC MSO for that well site and to the designated contract

drain line is in place to capture any collected rain water or spilled lubricants from our compressor skids. The swab drain line is a manually operated drain and by normal operating procedures is in the closed position. The tank drain line is also a manually operated drain and during normal operations it is in the closed position.

- 10. The geomembrane liner consists of a 45-mil flexible LLDPE material manufactured by Raven Industries as DURA-SKRIM J-45 which includes a 20 year warranty provided by said manufacturer. This product provides a level of UV and harsh weather conditions protection. It is rated to a Low temperature impact failure of -94°F. It exceeds ASTMD3083 standard by 10%. It is typically used in Brine Pond, Oilfield Pit liner and other industrial applications. The manufacture specific sheet is attached.
- 11. The general specification for design and construction are attached in the BR document.

MANUAL OPERATIONS PRODUCTION TANKS DRAINLINE SWABLINE DRAIN LINE ENVIROMENTAL DRAIN LINE FROM COMPRESSOR SKID

AUTOMATED OPERATION VENT VALVE DRAIN LINE DUMP LINE FROM SEPARATORS

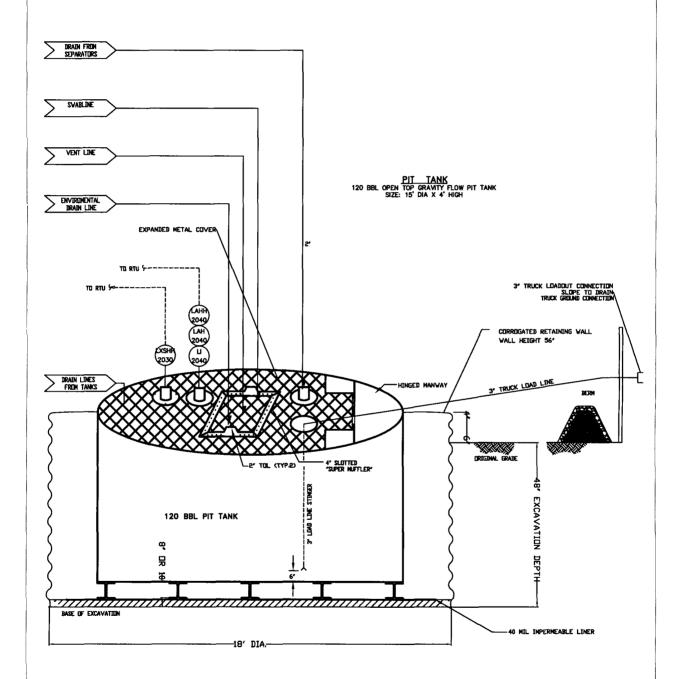

ConocoPhillips San Juan Business Unit

DURA-SKRM®

BOJBGEJAE

PROPERTIES !	TEST METHOD	J3	OBB .	J36	BB.	J45	BB)
		Min. Roll Averages	Typical Roll Averages	Min. Roll Averages	Typical Roll Averages	Mın Roll Averages	Typical Roll Averages
Appearance		Black/Black		Black/Black		Black/Black	
Thickness	ASTM D 5199	27 mil	30 mil	32 mil	36 mil	40 mil	45 mil
Weight Lbs Per MSF (oz/yd²)	ASTM D 5261	126 lbs (18.14)	140 lbs (20.16)	151 lbs (21.74)	168 lbs (24.19)	189 lbs (27.21)	210 lbs (30.24)
Construction		**Extr	usion laminated	with encapsula	ed tri-direction	al scrim reinforc	ement
Ply Adhesion	ASTM D 413	16 lbs	20 lbs	19 lbs	24 lbs	25 lbs	31 lbs
1" Tensile Strength	ASTM D 7003	88 lbf MD 63 lbf DD	110 lbf MD 79 lbf DD	90 lbf MD 70 lbf DD	113 lbf MD 87 lbf DD	110 lbf MD 84 lbf DD	138 lbf MD 105 lbf DD
1" Tensile Elongation @ Break % (Film Break)	ASTM D 7003	550 MD 550 DD	750 MD 750 DD	550 MD 550 DD	750 MD 750 DD	550 MD 550 DD	750 MD 750 DD
1. Tensile Elongation @ Peak % (Scrim Break)	ASTM D 7003	20 MD 20 DD	33 MD 33 DD	20 MD 20 DD	30 MD 31DD	20 MD 20 DD	36 MD 36 DD
Tongue Tear Strength	ASTM D 5884	75 lbf MD 75 lbf DD	97 lbf MD 90 lbf DD	75 lbf MD 75 lbf DD	104 lbf MD 92 lbf DD	100 lbf MD 100 lbf DD	117 lbf MD 118 lbf DD
Grab Tensile	ASTM D 7004	180 lbf MD 180 lbf DD	218 lbf MD 210 lbf DD	180 lbf MD 180 lbf DD	222 lbf MD 223 lbf DD	220 lbf MD 220 lbf DD	257 lbf MD 258 lbf DD
Trapezoid Tear	ASTM D 4533	120 lbf MD 120 lbf DD	146 lbf MD 141 lbf DD	130 lbf MD 130 lbf DD	189 lbf MD 172 lbf DD	160 lbf MD 160 lbf DD	193 lbf MD 191 lbf DD
* Dimensional Stability	ASTM D 1204	<1	<0.5	<1	<0.5	<1	<0.5
Puncture Resistance	ASTM D 4833	50 lbf	64 lbf	65 lbf	83 lbf	80 lbf	99 lbf
Maximum Use Temperature		180° F					
Minimum Use Temperature		-70° F					

MD = Machine Direction DD = Diagonal Directions



Note: Minimum Roll Averages are set to take into account product variability in addition to testing variability between laboratories.

*Dimensional Stability Maximum Value

**DURA-SKRIM J30BB, J36BB & J45BB are a four layer reinforced laminate containing no adhesives. The outer layers consist of a high strength polyethylene film manufactured using virgin grade resins and stabilizers for UV resistance in exposed applications. DURA-SKRIM J30BB, J36BB & J45BB are reinforced with a 1300 denier (minimum) tri-directional scrim reinforcement.

Note: RAVEN INDUSTRIES MAKES NO WARRANTIES AS TO THE FITNESS FOR A SPECIFIC USE OR MERCHANTABILITY OF PRODUCTS REFERRED TO, no guarantee of satisfactory results from reliance upon contained information or recommendations and disclaims all liability for resulting loss or damage.

PLANT FOCATION

SALES OFFICE

RAVEN Industries Sioux Falls, South Dakota

P.O. Box 5107 Sioux Falls, SD 57117-5107 (605) 335-0174 (605) 331-0333 FAX **800-635-3456**

08/06

ConocoPhillips Company San Juan Basin Below Grade Tank Maintenance and Operating Plan

In accordance with Rule 19.15.17 the following information describes the operation and maintenance of Below Grade Tank (BGT) on ConocoPhillips Company (COPC) locations. This is COPC's standard procedure for all BGT. A separate plan will be submitted for any BGT which does not conform to this plan.

- COPC will operate and maintain a BGT to contain liquids and solids and maintain the integrity of the liner, liner system and secondary containment system to prevent contamination of fresh water and protect public health and environment.
- 2. COPC will not discharge into or store any hazardous waste in the BGT.
- 3. COPC shall operate and install the below-grade tank to prevent the collection of surface water run-on. COPC shall not allow a below-grade tank to overflow or allow surface water run-on to enter the below-grade tank.
- COPC shall continuously remove any visible or measurable layer of oil from the fluid surface of a below-grade tank in an effort to prevent significant accumulation of oil overtime.
- 5. COPC shall inspect the below-grade tank at least monthly and maintain a written record of each inspection for five years.
- 6. COPC shall maintain adequate freeboard to prevent overtopping of the below-grade tank.
- 7. If a leak develops below the liquid's level, COPC shall remove all liquids within 48 hours and repair the damage or replace the below-grade tank. COPC shall notify the Aztec Division office by phone or email within 48 hours of the discovery for leaks less than 25 barrels. COPC shall notify the Aztec Division office as required pursuant to Subsection B of 19.15.3.116 NMAC shall be reported within twenty-four (24) hours of discovery of leaks greater than 25 barrels. In addition, immediate verbal notification pursuant to Subsection B, Paragraph (1), and Subparagraph (d) of 19.15.3.116 NMAC shall be reported to the division's Environmental Bureau Chief.

ConocoPhillips Company San Juan Basin Below Grade Tank Closure Plan

In accordance with Rule 19.15.17.13 NMAC the following information describes the closure requirements of Below Grade Tanks (BGTs) on ConocoPhillips Company locations hereinafter known as COPC locations. This is COPC's standard procedure for all BGTs. A separate plan will be submitted for any BGT which does not conform to this plan.

General Requirements:

- 1. COPC shall close a below-grade tank within the time periods provided in 19.15.17.13 NMAC, or by an earlier date that the division requires because of imminent danger to fresh water, public health or the environment.
- 2. COPC shall close a permitted below-grade tank within 60 days of cessation of the below-grade tank's operation. The closure report will be filed on C-144
- 3. COPC shall remove liquids and sludge from a below-grade tank prior to implementing a closure method and shall dispose of the liquids and sludge in a division-approved facility. The facilities to be used will be Basin Disposal (Permit #NM-01-005) and Envirotech Land Farm (Permit #NM-01-011). The liner will be disposed of at the San Juan County Landfill located on CR 3100.
- 4. COPC will receive prior approval to remove the below-grade tank and dispose of it in a division-approved facility or recycle, reuse, or reclaim it in a manner that the appropriate division district office approves. Documentation of how the below-grade tank was disposed of or recycled will be provided in the closure report.
- If there is any on-site equipment associated with a below-grade tank, then BR shall remove the equipment, unless the equipment is required for some other purpose.
- 6. COPC shall test the soils beneath the below-grade tank to determine whether a release has occurred. COPC shall collect, at a minimum, a five point, composite sample; collect individual grab samples from any area that is wet, discolored or showing other evidence of a release; and analyze for BTEX, TPH and chlorides to demonstrate that the benzene concentration, as determined by EPA SW-846 methods 8021B or 8260B or other EPA method that the division approves, does not exceed 0.2 mg/kg; total BTEX concentration, as determined by EPA SW-846 methods 8021B or 8260B or other EPA method that the division approves, does not exceed 50 mg/kg; the TPH concentration, as determined by EPA method 418.1 or other EPA method that the division approves, does not exceed 100 mg/kg; and the chloride concentration, as determined by EPA method 300.1 or other EPA method that the division approves, does not exceed 250 mg/kg, or the background concentration, whichever is greater. COPC shall notify the division of its results on form C-141.

- 7. If COPC or the division determines that a release has occurred, then COPC shall comply with 19.15.3.116 NMAC and 19.15.1.19 NMAC, as appropriate.
- 8. If the sampling program demonstrates that a release has not occurred or that any release does not exceed the concentrations specified in Paragraph (4) of Subsection E of 19.15.17.13 NMAC, then COPC shall backfill the excavation with compacted, non-waste containing, earthen material; construct a division-prescribed soil cover; recontour and re-vegetate the site.
- 9. Notice of Closure will be given prior to closure to the Aztec Division office between 72 hours and one week via email or verbally. The notification of closure will include the following:
 - i. Operator's name
 - ii. Location by Unit Letter, Section, Township, and Range. Well name and API number.
- 10. The surface owner shall be notified of COPC's closing of the below-grade tank prior to closure as per the approved closure plan via certified mail, return receipt requested.
- 11. Re-contouring of location will match fit, shape, line, form and texture of the surrounding. Re-shaping will include drainage control, prevent ponding, and prevent erosion. Natural drainages will be unimpeded and water bars and/or silt traps will be place in areas where needed to prevent erosion on a large scale. Final re-contour shall have a uniform appearance with smooth surface, fitting the natural landscape.
- 12. COPC shall seed the disturbed areas the first growing season after the operator closes the pit. Seeding will be accomplished via drilling on the contour whenever practical or by other division-approved methods. BLM or Forest Service stipulated seed mixes will used on federal lands. Vegetative cover will equal 70% of the native perennial vegetative cover (un-impacted) consisting of at least three native plant species, including at least one grass, but not including noxious weeds, and maintain that cover through two successive growing seasons. Repeat seeding or planting will be continued until successful vegetative growth occurs.
- 13. A minimum of four feet of cover shall be achieved and the cover shall include one foot of suitable material to establish vegetation at the site, or the background thickness of topsoil, whichever is greater.
- 14. All closure activities will include proper documentation and be available for review upon request and will be submitted to OCD within 60 days of closure of the below-grade tank. Closure report will be filed on C-144 and incorporate the following:
 - Soil Backfilling and Cover Installation
 - Re-vegetation application rates and seeding techniques
 - Photo documentation of the site reclamation
 - Confirmation Sampling Results
 - · Proof of closure notice
