

District I
1625 N. French Dr., Hobbs, NM 88240
District II
1301 W. Grand Avenue, Artesia, NM 88210
District III
1000 Rio Brazos Rd., Aztec, NM 87410
District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505

State of New Mexico
Energy, Minerals & Natural Resources

Form C-102
Revised October 12, 2005

OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505

Submit to Appropriate District Office
State Lease - 4 Copies
Fee Lease - 3 Copies

☐ AMENDED REPORT

WELL LOCATION AND ACREAGE DEDICATION PLAT

¹ API Number 30-039-30465		² Pool Code 71629		³ Pool Name Basin Fruitland Coal	
⁴ Property Code 35656		⁵ Property Name Carracas 16B			⁶ Well Number 1
⁷ OGRID No. 162928		⁸ Operator Name Energen Resources Corporation			⁹ Elevation 6860'

¹⁰ Surface Location

UL or lot no.	Section	Township	Range	Lot. Idn	Feet from the	North/South line	Feet from the	East/West line	County
F	16	32N	04W		1385	North	1525	West	Rio Arriba

¹¹ Bottom Hole Location If Different From Surface

UL or lot no.	Section	Township	Range	Lot. Idn	Feet from the	North/South line	Feet from the	East/West line	County
A	16	32N	04W		370	North	162	East	Rio Arriba


¹² Dedicated Acres 320 N/2	¹³ Joint or Infill	¹⁴ Consolidation Code	¹⁵ Order No. R13119 ^h
--	-------------------------------	----------------------------------	--

RCVD OCT 21 '09

OIL CONS. DIV.

DIST. 3

10/22/09
ALLOWABLE WILL BE ASSIGNED TO THIS COMPLETION UNTIL ALL INTERESTS HAVE BEEN CONSOLIDATED OR A NON-STANDARD UNIT HAS BEEN APPROVED BY THE DIVISION

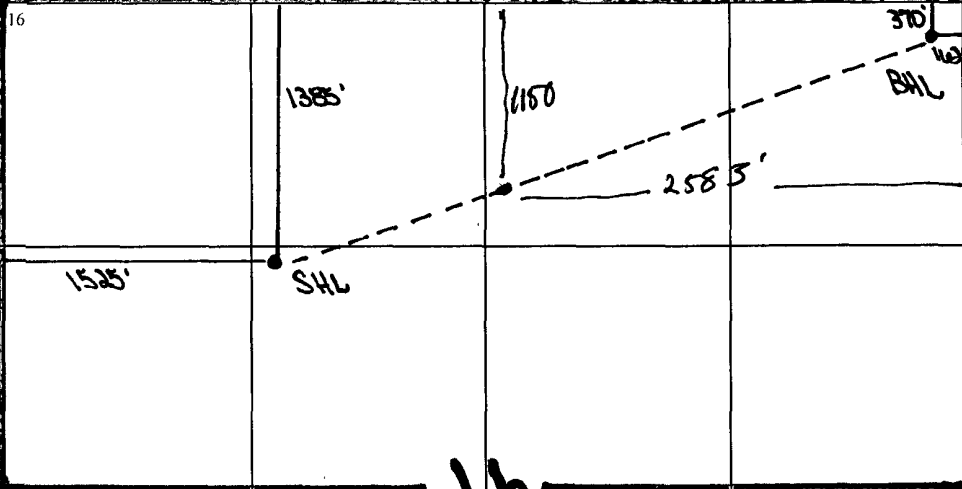				¹⁷ OPERATOR CERTIFICATION I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of such a mineral or working interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division <i>Vicki Donaghey</i> 10/19/09 Signature Date Vicki Donaghey Printed Name	
¹⁸ SURVEYOR CERTIFICATION I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief 10/24/07 Date of Survey Signature and Seal of Professional Surveyer original survey conducted and recorded by: David B. Russell 10201 Certificate Number					

RCVD OCT 21 '09
OIL CONS. DIV.
DIST. 3

Energen Resources

Rio Arriba County, NM
Sec. 16-T32N-R4W
Carracas 16B #1

Wellbore #2

Design: Actual field Surveys

Sperry Drilling Services Standard Report

04 September, 2009

Well Coordinates: 2,181,235.96 N, 1,344,308.61 E (36° 59' 24.04" N, 107° 15' 50.08" W)
Ground Level: 6,860.00 ft

Local Coordinate Origin:	Centered on Well Carracas 16B #1
Viewing Datum:	RKB @ 6877.00ft (Original Well Elev)
TVDs to System:	N
North Reference:	True
Unit System:	API- Alt
Geodetic Scale Factor Applied	
Version: 2003.16 Build: 431	

HALLIBURTON



Project: Rio Arriba County, NM
 Site: Sec. 16-T32N-R4W
 Well: Carracas 16B #1
 Wellbore: Wellbore #2
 Plan: Actual field Surveys

Energen Resources

HALLIBURTON
 Drilling and Formation
 Evaluation

WELLBORE TARGET DETAILS (LAT/LONG)

Name	TVD	+N/-S	+E/-W	Latitude	Longitude	Shape
400' FNL Hardline	0.00	985.00	0.00	36° 59' 33.775 N	107° 15' 50.076 W	Polygon
Carracas 16B #1 E 110' Setback	0.00	1275.00	3630.14	36° 59' 36.640 N	107° 15' 5.330 W	Polygon
Carracas 16B #1 N 110' Setback	0.00	1275.00	3630.14	36° 59' 36.640 N	107° 15' 5.330 W	Polygon
Carracas 16B #1 New Tgt.	3746.43	985.00	3632.00	36° 59' 33.773 N	107° 15' 5.307 W	Point

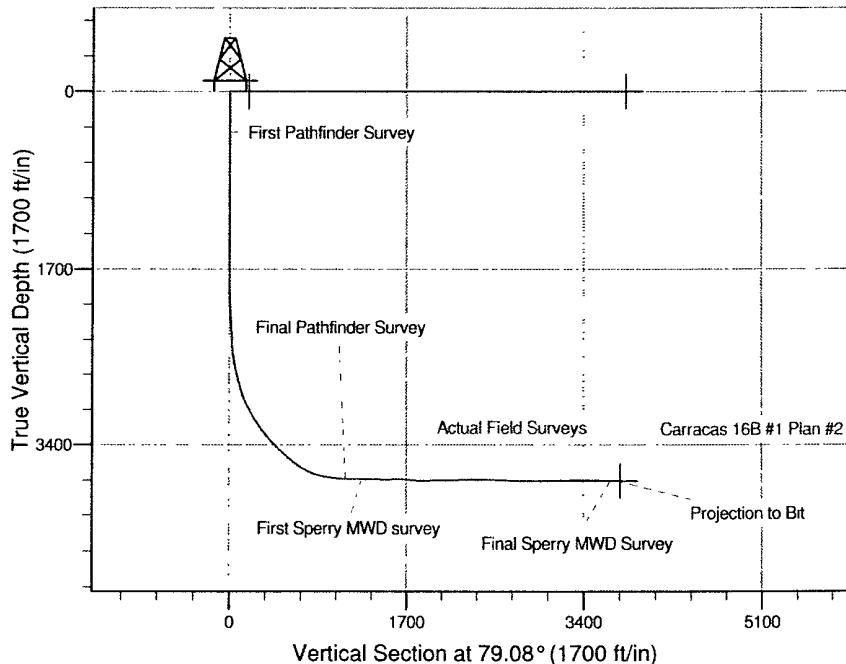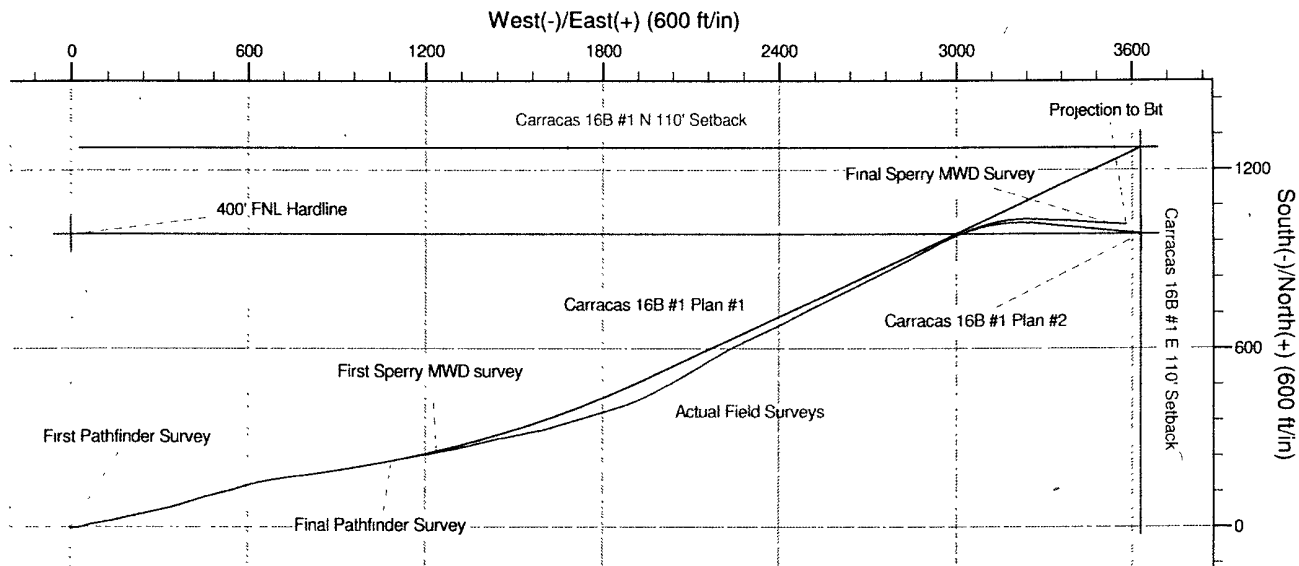

WELL DETAILS: Carracas 16B #1


+N/-S	+E/-W	Northing	Ground Level:	Easting	Latitude	Longitude
0.00	0.00	2181235.96	6860.00	1344308.61	36° 59' 24.036 N	107° 15' 50.076 W

Project: Rio Arriba County, NM
Site: Sec. 16-T32N-R4W
Well: Carracas 16B #1
Wellbore: Wellbore #2
Plan: Actual field Surveys

Energen Resources

HALLIBURTON

Drilling and Formation
Evaluation

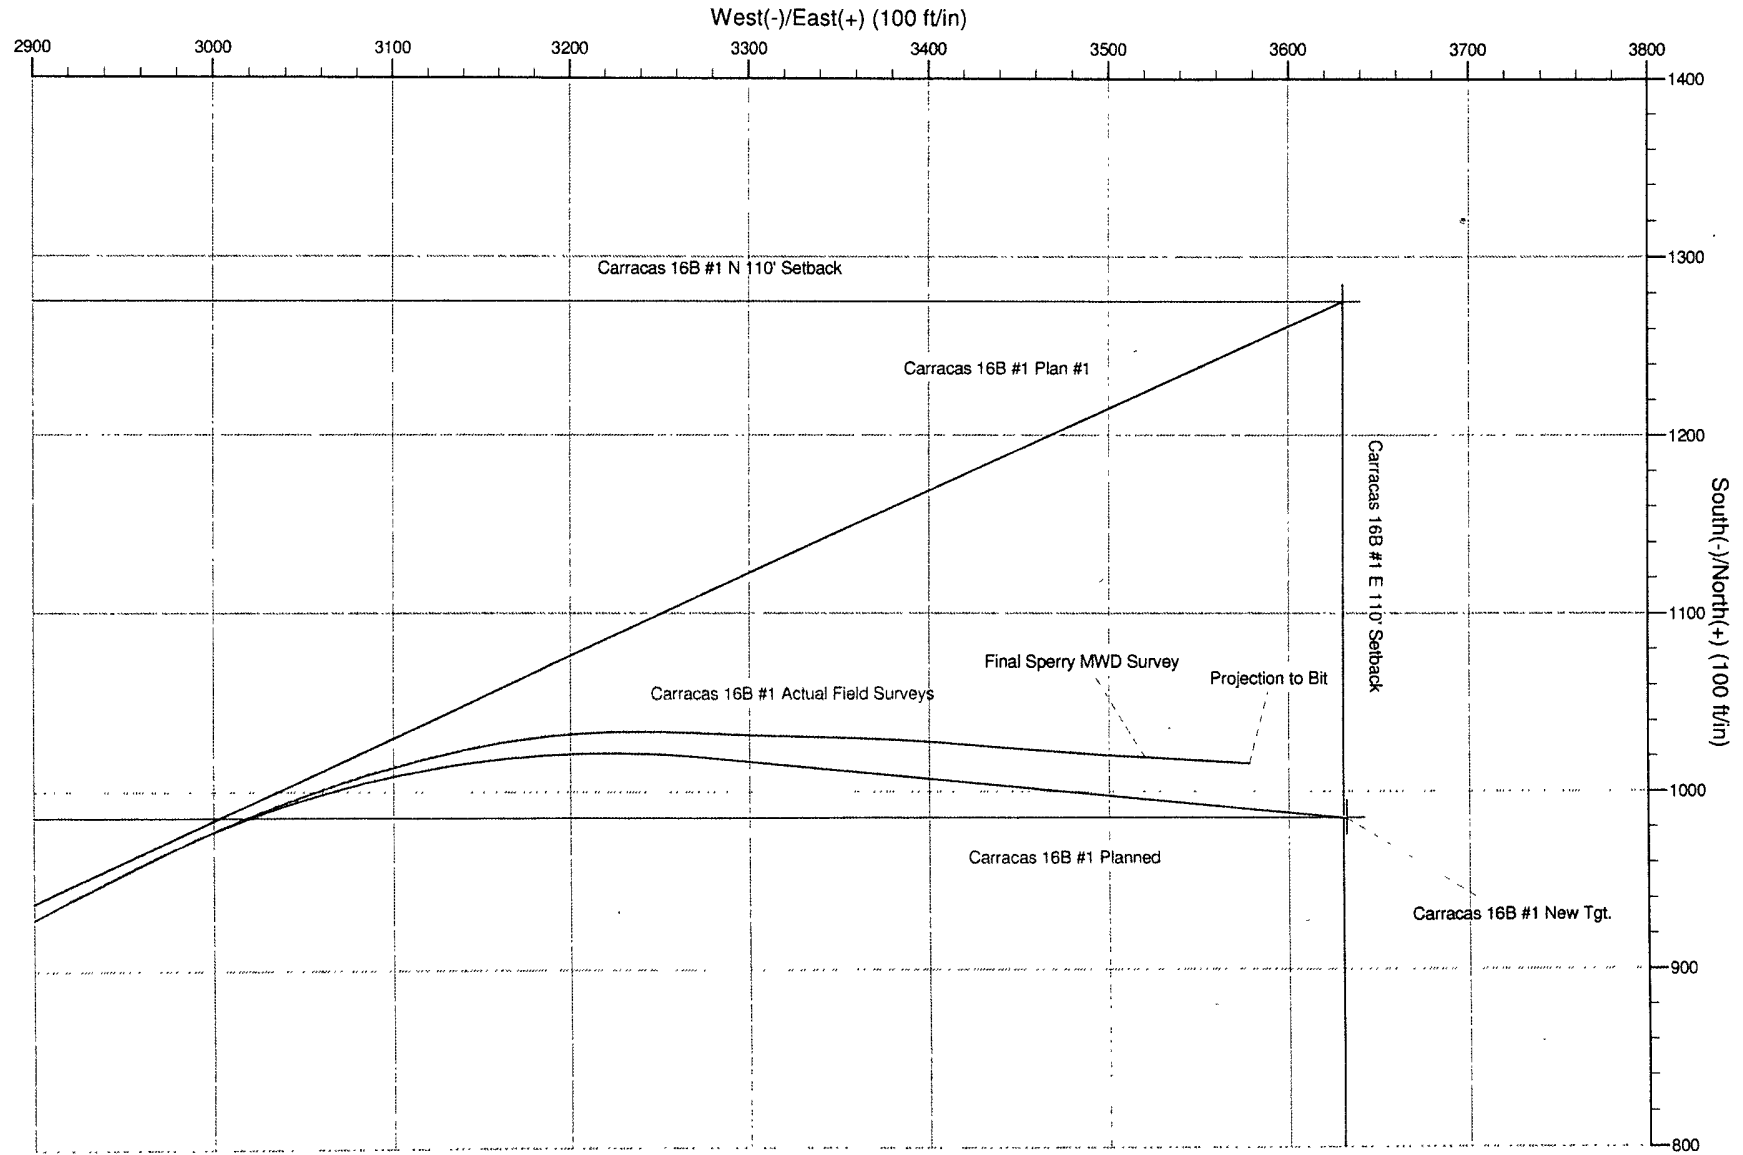

Design Report for Carracas 16B #1 - Actual field Surveys

Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)
0.00	0.00	0.000	0.00	0.00	0.00	0.00	0.00
400' FNL Hardline							
387.00	0.70	213.390	386.99	-1.97	-1.30	-1.65	0.18
First Pathfinder Survey							
478.00	0.09	21.900	477.99	-2.37	-1.58	-2.00	0.87
567.00	0.18	118.780	566.99	-2.37	-1.43	-1.86	0.24
658.00	0.09	199.720	657.99	-2.51	-1.33	-1.78	0.21
748.00	0.35	135.930	747.99	-2.77	-1.16	-1.67	0.36
838.00	0.09	173.640	837.99	-3.04	-0.96	-1.52	0.32
936.00	0.09	27.800	935.99	-3.05	-0.92	-1.48	0.18
1,059.00	0.09	356.550	1,058.99	-2.87	-0.88	-1.41	0.04
1,119.00	0.09	110.920	1,118.99	-2.84	-0.84	-1.36	0.25
1,210.00	0.26	38.890	1,209.99	-2.70	-0.64	-1.14	0.27
1,300.00	0.09	126.110	1,299.99	-2.59	-0.46	-0.94	0.30
1,389.00	0.26	279.010	1,388.99	-2.60	-0.60	-1.08	0.38
1,479.00	0.18	183.950	1,478.98	-2.70	-0.81	-1.31	0.37
1,569.00	0.26	126.840	1,568.98	-2.97	-0.66	-1.21	0.25
1,661.00	0.09	303.160	1,660.98	-3.05	-0.55	-1.12	0.38
1,749.00	0.09	176.490	1,748.98	-3.08	-0.61	-1.18	0.18
1,840.00	0.09	159.480	1,839.98	-3.22	-0.58	-1.18	0.03
1,932.00	1.93	109.450	1,931.97	-3.81	0.91	0.17	2.04
2,024.00	2.99	86.510	2,023.88	-4.18	4.77	3.89	1.55
2,119.00	3.17	86.320	2,118.74	-3.86	9.86	8.95	0.19
2,214.00	2.73	84.410	2,213.62	-3.47	14.73	13.81	0.47
2,309.00	2.81	87.670	2,308.51	-3.15	19.31	18.37	0.19
2,404.00	2.64	81.650	2,403.40	-2.74	23.80	22.85	0.35
2,436.00	3.43	78.440	2,435.36	-2.44	25.47	24.55	2.52
2,468.00	5.01	79.390	2,467.27	-1.99	27.78	26.90	4.94
2,500.00	6.51	78.740	2,499.11	-1.38	30.93	30.11	4.69
2,531.00	7.39	77.160	2,529.88	-0.59	34.60	33.86	2.90
2,562.00	8.44	74.870	2,560.58	0.44	38.74	38.12	3.54
2,594.00	9.32	72.970	2,592.20	1.81	43.49	43.04	2.90
2,625.00	10.38	72.530	2,622.74	3.39	48.55	48.31	3.43
2,656.00	11.26	73.120	2,653.19	5.10	54.11	54.10	2.86
2,688.00	12.31	74.410	2,684.51	6.93	60.39	60.61	3.38
2,719.00	13.01	76.680	2,714.76	8.62	66.97	67.39	2.77
2,751.00	13.81	79.170	2,745.89	10.17	74.22	74.80	3.08
2,783.00	14.77	80.960	2,776.90	11.53	82.00	82.70	3.30
2,815.00	15.48	81.970	2,807.79	12.76	90.26	91.04	2.37
2,847.00	16.18	81.720	2,838.57	14.00	98.90	99.76	2.20
2,878.00	16.97	80.320	2,868.29	15.39	107.63	108.60	2.86
2,910.00	18.29	79.150	2,898.78	17.12	117.17	118.29	4.27
2,942.00	19.87	78.450	2,929.02	19.15	127.43	128.75	4.99
2,973.00	21.54	77.880	2,958.02	21.40	138.15	139.71	5.43
3,005.00	22.95	77.480	2,987.64	23.99	149.99	151.82	4.43
3,036.00	24.45	77.620	3,016.02	26.67	162.16	164.27	4.84
3,067.00	25.50	77.730	3,044.12	29.47	174.94	177.36	3.39
3,099.00	27.00	77.840	3,072.82	32.46	188.78	191.51	4.69
3,130.00	28.40	77.950	3,100.27	35.48	202.87	205.91	4.52
3,162.00	29.81	77.800	3,128.23	38.75	218.08	221.47	4.41

Design Report for Carracas 16B #1 - Actual field Surveys

Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)
3,193.00	31.92	77.660	3,154.84	42.13	233.62	237.37	6.81
3,211.00	32.89	78.540	3,170.03	44.12	243.06	247.02	5.99
3,242.00	34.29	78.200	3,195.86	47.58	259.86	264.17	4.56
3,272.00	35.26	77.200	3,220.50	51.22	276.58	281.27	3.75
3,303.00	36.49	76.840	3,245.62	55.31	294.28	299.43	4.03
3,333.00	37.37	76.570	3,269.60	59.45	311.82	317.44	2.98
3,364.00	38.34	75.820	3,294.07	63.99	330.29	336.43	3.46
3,394.00	39.04	74.720	3,317.49	68.76	348.43	355.15	3.27
3,425.00	40.10	73.130	3,341.39	74.23	367.40	374.81	4.73
3,455.00	41.94	72.290	3,364.02	80.09	386.20	394.38	6.40
3,484.00	44.41	72.400	3,385.17	86.10	405.11	414.08	8.52
3,515.00	45.37	73.020	3,407.13	92.60	426.00	435.82	3.40
3,545.00	45.90	73.880	3,428.11	98.71	446.55	457.17	2.71
3,576.00	45.81	75.240	3,449.70	104.63	467.99	479.34	3.16
3,606.00	46.43	75.790	3,470.49	110.04	488.93	500.92	2.45
3,636.00	47.48	76.390	3,490.97	115.31	510.21	522.82	3.79
3,666.00	48.01	75.810	3,511.14	120.65	531.77	544.99	2.27
3,693.00	49.33	74.270	3,528.97	125.88	551.35	565.22	6.50
3,725.00	51.00	73.030	3,549.47	132.80	574.93	589.68	6.01
3,756.00	53.29	74.220	3,568.49	139.70	598.41	614.04	7.98
3,788.00	54.69	76.210	3,587.31	146.30	623.44	639.86	6.67
3,820.00	56.28	78.490	3,605.44	152.07	649.16	666.21	7.69
3,851.00	58.48	79.700	3,622.15	157.00	674.80	692.32	7.82
3,883.00	61.03	81.140	3,638.27	161.60	702.05	719.96	8.87
3,915.00	63.66	81.930	3,653.12	165.77	730.09	748.27	8.50
3,945.00	66.83	82.840	3,665.68	169.38	757.09	775.47	10.92
3,977.00	69.82	82.840	3,677.50	173.08	786.59	805.14	9.34
4,008.00	72.98	82.790	3,687.39	176.76	815.74	834.45	10.19
4,040.00	76.24	81.840	3,695.88	180.88	846.31	865.25	10.58
4,072.00	79.40	81.240	3,702.63	185.49	877.24	896.50	10.04
4,104.00	81.60	80.900	3,707.91	190.39	908.42	928.04	6.95
4,135.00	81.78	80.590	3,712.39	195.32	938.69	958.70	1.15
4,167.00	82.13	80.220	3,716.87	200.60	969.94	990.37	1.58
4,199.00	82.48	79.890	3,721.15	206.08	1,001.17	1,022.08	1.50
4,230.00	84.15	79.340	3,724.76	211.63	1,031.45	1,052.87	5.67
4,262.00	87.41	79.020	3,727.12	217.62	1,062.80	1,084.78	10.24
4,287.00	90.04	79.080	3,727.67	222.36	1,087.33	1,109.77	10.52
Final Pathfinder Survey			3728	235	1167		
4,440.00	89.01	79.540	3,728.94	250.74	1,237.67	1,262.76	0.74
First Sperry MWD survey							
4,472.00	87.90	79.180	3,729.80	256.65	1,269.11	1,294.75	3.65
4,504.00	89.57	78.660	3,730.51	262.80	1,300.50	1,326.74	5.47
4,535.00	90.62	77.930	3,730.46	269.09	1,330.86	1,357.73	4.13
4,567.00	88.83	76.360	3,730.61	276.21	1,362.05	1,389.71	7.44
4,599.00	88.33	76.030	3,731.41	283.84	1,393.12	1,421.66	1.87
4,631.00	88.33	76.940	3,732.34	291.31	1,424.22	1,453.62	2.84
4,663.00	90.25	78.470	3,732.74	298.13	1,455.48	1,485.60	7.67
4,694.00	90.31	79.980	3,732.58	303.92	1,485.93	1,516.60	4.87
4,726.00	90.56	79.380	3,732.34	309.66	1,517.41	1,548.60	2.03
4,758.00	90.87	78.440	3,731.94	315.81	1,548.81	1,580.59	3.09
4,790.00	91.36	78.260	3,731.32	322.27	1,580.15	1,612.59	1.63

Design Report for Carracas 16B #1 - Actual field Surveys

Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)
4,821.00	88.77	75.530	3,731.28	329.30	1,610.33	1,643.56	12.14
4,853.00	84.87	73.210	3,733.06	337.90	1,641.10	1,675.39	14.17
4,884.00	85.05	72.490	3,735.78	347.01	1,670.60	1,706.09	2.39
4,916.00	86.29	72.550	3,738.20	356.59	1,701.04	1,737.79	3.88
4,947.00	86.04	73.160	3,740.27	365.71	1,730.59	1,768.54	2.12
4,979.00	86.17	73.400	3,742.44	374.90	1,761.17	1,800.30	0.85
5,010.00	87.16	73.570	3,744.25	383.69	1,790.84	1,831.10	3.24
5,041.00	89.88	73.940	3,745.05	392.36	1,820.59	1,861.95	8.85
5,073.00	92.16	73.390	3,744.48	401.36	1,851.29	1,893.80	7.33
5,105.00	92.40	71.020	3,743.21	411.13	1,881.73	1,925.54	7.44
5,136.00	91.73	68.040	3,742.09	421.96	1,910.75	1,956.09	9.85
5,167.00	90.80	65.200	3,741.40	434.26	1,939.20	1,986.35	9.64
5,199.00	89.81	63.570	3,741.23	448.09	1,968.05	2,017.30	5.96
5,231.00	89.69	62.460	3,741.37	462.61	1,996.57	2,048.05	3.49
5,262.00	90.25	62.290	3,741.39	476.99	2,024.03	2,077.74	1.89
5,294.00	90.74	61.020	3,741.11	492.18	2,052.19	2,108.27	4.25
5,325.00	91.05	60.200	3,740.63	507.39	2,079.20	2,137.67	2.83
5,357.00	92.10	60.700	3,739.75	523.17	2,107.03	2,167.98	3.63
5,389.00	92.47	59.690	3,738.47	539.06	2,134.77	2,198.24	3.36
5,420.00	92.97	59.100	3,737.00	554.82	2,161.42	2,227.39	2.49
5,452.00	92.41	59.710	3,735.50	571.09	2,188.94	2,257.49	2.59
5,483.00	91.17	60.270	3,734.53	586.59	2,215.77	2,286.77	4.39
5,514.00	90.86	62.420	3,733.98	601.45	2,242.97	2,316.29	7.01
5,545.00	89.75	63.670	3,733.82	615.50	2,270.60	2,346.08	5.39
5,577.00	89.44	64.690	3,734.04	629.44	2,299.40	2,377.01	3.33
5,609.00	89.94	64.960	3,734.22	643.05	2,328.36	2,408.02	1.78
5,640.00	90.99	65.050	3,733.97	656.15	2,356.46	2,438.09	3.40
5,672.00	89.14	64.490	3,733.93	669.79	2,385.40	2,469.09	6.04
5,704.00	87.47	63.070	3,734.88	683.92	2,414.10	2,499.94	6.85
5,735.00	87.29	62.320	3,736.29	698.13	2,441.61	2,529.65	2.49
5,767.00	87.16	62.350	3,737.84	712.97	2,469.92	2,560.26	0.42
5,799.00	87.59	63.100	3,739.31	727.62	2,498.33	2,590.93	2.70
5,830.00	87.78	63.470	3,740.56	741.54	2,526.00	2,620.74	1.34
5,861.00	87.59	63.770	3,741.81	755.30	2,553.75	2,650.59	1.14
5,893.00	87.72	63.670	3,743.12	769.46	2,582.42	2,681.42	0.51
5,925.00	87.58	63.740	3,744.43	783.62	2,611.08	2,712.25	0.49
5,956.00	87.59	64.120	3,745.74	797.23	2,638.90	2,742.15	1.23
5,988.00	88.15	64.160	3,746.93	811.18	2,667.68	2,773.04	1.75
6,020.00	88.70	63.690	3,747.81	825.24	2,696.41	2,803.92	2.26
6,051.00	89.01	63.150	3,748.43	839.11	2,724.13	2,833.76	2.01
6,083.00	90.12	63.410	3,748.67	853.50	2,752.71	2,864.55	3.56
6,115.00	90.80	63.050	3,748.41	867.91	2,781.28	2,895.33	2.40
6,146.00	90.93	62.980	3,747.95	881.98	2,808.90	2,925.12	0.48
6,178.00	90.86	61.970	3,747.45	896.76	2,837.28	2,955.78	3.16
6,209.00	91.11	63.170	3,746.91	911.04	2,864.79	2,985.50	3.95
6,238.00	90.80	63.580	3,746.43	924.03	2,890.71	3,013.41	1.77
6,270.00	90.37	63.040	3,746.10	938.41	2,919.30	3,044.21	2.16
6,302.00	91.54	62.960	3,745.57	952.93	2,947.80	3,074.95	3.66
6,333.00	92.16	64.470	3,744.57	966.65	2,975.58	3,104.82	5.26
6,365.00	91.79	66.680	3,743.47	979.88	3,004.70	3,135.92	7.00
6,396.00	90.56	68.840	3,742.83	991.61	3,033.39	3,166.31	8.02

Design Report for Carracas 16B #1 - Actual field Surveys

Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)
6,428.00	89.32	71.100	3,742.86	1,002.57	3,063.45	3,197.90	8.06
6,460.00	88.40	73.970	3,743.50	1,012.17	3,093.96	3,229.68	9.42
6,491.00	87.47	76.300	3,744.62	1,020.11	3,123.90	3,260.59	8.09
6,523.00	87.72	79.730	3,745.96	1,026.75	3,155.17	3,292.55	10.74
6,554.00	89.32	83.780	3,746.76	1,031.19	3,185.84	3,323.50	14.04
6,586.00	91.24	87.700	3,746.61	1,033.57	3,217.74	3,355.27	13.64
6,617.00	93.09	91.240	3,745.43	1,033.86	3,248.71	3,385.74	12.88
6,649.00	90.62	92.770	3,744.40	1,032.74	3,280.67	3,416.91	9.08
6,680.00	88.09	91.700	3,744.75	1,031.53	3,311.64	3,447.09	8.86
6,712.00	87.66	91.350	3,745.93	1,030.68	3,343.61	3,478.31	1.73
6,744.00	88.27	92.630	3,747.07	1,029.57	3,375.57	3,509.48	4.43
6,775.00	90.62	94.470	3,747.37	1,027.65	3,406.50	3,539.50	9.63
6,807.00	92.16	94.780	3,746.59	1,025.07	3,438.39	3,570.32	4.91
6,838.00	92.66	94.270	3,745.29	1,022.63	3,469.26	3,600.17	2.30
6,870.00	91.23	93.530	3,744.21	1,020.45	3,501.17	3,631.09	5.03
6,889.00	91.23	93.310	3,743.80	1,019.32	3,520.13	3,649.49	1.16
Final Sperry MWD Survey							
6,947.00	91.23	93.310	3,742.55	1,015.97	3,578.02	3,705.70	0.00
Projection to Bit - Carracas 16B #1 E 110' Setback - Carracas 16B #1 N 110' Setback - Carracas 16B #1 New Tgt.							

Design Annotations

Measured Depth (ft)	Vertical Depth (ft)	Local Coordinates		Comment
		+N/-S (ft)	+E/-W (ft)	
387.00	386.99	-1.97	-1.30	First Pathfinder Survey
4,287.00	3,727.67	222.36	1,087.33	Final Pathfinder Survey
4,440.00	3,728.94	250.74	1,237.67	First Sperry MWD survey
6,889.00	3,743.80	1,019.32	3,520.13	Final Sperry MWD Survey
6,947.00	3,742.55	1,015.97	3,578.02	Projection to Bit

Vertical Section Information

Angle Type	Target	Azimuth (°)	Origin Type	Origin		Start TVD (ft)
				+N/-S (ft)	+E/-W (ft)	
User	No Target (Freehand)	79.080	Slot	0.00	0.00	0.00

Survey tool program

From (ft)	To (ft)	Survey/Plan	Survey Tool
387.00	4,357.00	Pathfinder Surveys	MWD
4,440.00	6,947.00	Sperry MWD Surveys	MWD

Design Report for Carracas 16B #1 - Actual field Surveys

Targets

Target Name - hit/miss target - Shape	Dip Angle (°)	Dip Dir. (°)	TVD (ft)	+N/-S (ft)	+E/-W (ft)	Northing (ft)	Easting (ft)	Latitude	Longitude
Carracas 16B #1 E 111	0.00	0.00	0.00	1,275.00	3,630.14	2,182,472.24	1,347,952.12	36° 59' 36.640 N	107° 15' 5.330 W
- actual wellpath misses target center by 3751.87ft at 6947.00ft MD (3742.55 TVD, 1015.97 N, 3578.02 E)									
- Polygon									
Point 1				3,630.14	1,275.00	2,182,472.24	1,347,952.12		
Point 2				3,630.14	-25.00	2,181,172.31	1,347,938.28		
Carracas 16B #1 New	0.00	0.00	3,746.43	985.00	3,632.00	2,182,182.23	1,347,950.89	36° 59' 33.773 N	107° 15' 5.307 W
- actual wellpath misses target center by 62.35ft at 6947.00ft MD (3742.55 TVD, 1015.97 N, 3578.02 E)									
- Point									
Carracas 16B #1 N 111	0.00	0.00	0.00	1,275.00	3,630.14	2,182,472.24	1,347,952.12	36° 59' 36.640 N	107° 15' 5.330 W
- actual wellpath misses target center by 3751.87ft at 6947.00ft MD (3742.55 TVD, 1015.97 N, 3578.02 E)									
- Polygon									
Point 1				3,630.14	1,275.00	2,182,472.24	1,347,952.12		
Point 2				30.14	1,275.00	2,182,510.57	1,344,352.32		
400' FNL Hardline	0.00	0.00	0.00	985.00	0.00	2,182,220.91	1,344,319.10	36° 59' 33.775 N	107° 15' 50.076 W
- actual wellpath misses target center by 985.00ft at 0.00ft MD (0.00 TVD, 0.00 N, 0.00 E)									
- Polygon									
Point 1				3,632.00	985.00	2,182,182.23	1,347,950.89		
Point 2				0.00	985.00	2,182,220.91	1,344,319.10		
