District I

1625 N. French Dr., Hobbs, NM 88240

1301 W. Grand Ave., Artesia, NM 88210

1000 Rio Brazos Rd., Aztec, NM 87410

District IV

1220 S. St. Francis Dr., Santa Fe, NM 87505

State of New Mexico Energy Minerals and Natural Resources

Department Oil Conservation Division 1220 South St. Francis Dr. Santa Fe, NM 87505

July 21, 2008 For temporary pits, closed-loop sytems, and below-grade tanks, submit to the appropriate NMOCD District Office.

Form C-144

For permanent pits and exceptions submit to the Santa Fe Environmental Bureau office and provide a copy to the appropriate NMOCD District Office.

Pit, Closed-Loop System, Below-Grade Tank, or Proposed Alternative Method Permit or Closure Plan Application

Trop	osca Atternative Method Fernite of Closure Frant Application
Type of action:	Permit of a pit, closed-loop system, below-grade tank, or proposed alternative method
	X Closure of a pit, closed-loop system, below-grade tank, or proposed alternative method
	Modification to an existing permit
	Closure plan only submitted for an existing permitted or non-permitted pit, closed-loop system,
	below-grade tank, or proposed alternative method
Please submit one a	pplication (Form C-144) per individual pit, closed-loop system, below-grade tank or alternative reques
be advised that approval of	of this request does not relieve the operator of liability should operations result in pollution of surface water, ground water or the

Instructions: I

environment. Nor does approval relieve the operator of its responsibility to comply	with any other applicable governmental authority's rules, regulations or ordinances.
Operator: Burlington Resources Oil & Gas Company, LP	OGRID#: 14538
Address: P.O. Box 4289, Farmington, NM 87499	
Facility or well name: FARMINGTON COM 100	
API Number: 30-045-34574	OCD Permit Number:
U/L or Qtr/Qtr: L(NW/SW) Section: 36 Township: 31N	Range: 13W County: San Juan
Center of Proposed Design: Latitude: 36.855205 °N	Longitude: 108.16134 °W NAD: 1927 X 1983
Surface Owner: Federal X State Private T	ribal Trust or Indian Allotment
X Pit: Subsection F or G of 19.15.17.11 NMAC	X LLDPE
Closed-loop System: Subsection H of 19.15.17.11 NMAC Type of Operation: P&A Drilling a new well Workover of notice of in Drying Pad Above Ground Steel Tanks Haul-off Bins Lined Unlined Liner type: Thickness mil Liner Seams: Welded Factory Other	Other LLDPE HDPE PVD Other Other
	er, 6-inch lift and automatic overflow shut-off
5 Alternative Method: Submittal of an exception request is required. Exceptions must be submitted to	the Santa Fe Environmental Bureau office for consideration of approval.

6 🔑					
Fencing: Subsection D of 19.15.17.11 NMAC (Applies to permanent pit, temporary pits, and below-grade tanks) Chain link, six feet in height, two strands of barbed wire at top (Required if located within 1000 feet of a permanent residence, school, hospital, institution or church)					
Four foot height, four strands of barbed wire evenly spaced between one and four feet					
Alternate. Please specify					
Nesting: Subsection F of 10.15.17.11 NMAC (Applies to payment a pits and payment apart to payment					
Netting: Subsection E of 19.15.17.11 NMAC (Applies to permanent pits and permanent open top tanks) Screen Netting Other					
Monthly inspections (If netting or screening is not physically feasible)					
8					
Signs: Subsection C of 19.15.17.11 NMAC					
12" X 24", 2" lettering, providing Operator's name, site location, and emergency telephone numbers X Signed in compliance with 19.15.3.103 NMAC					
9 Administrative Approvals and Exceptions:					
Justifications and/or demonstrations of equivalency are required. Please refer to 19.15.17 NMAC for guidance.					
Please check a box if one or more of the following is requested, if not leave blank: Administrative approval(s): Requests must be submitted to the appropriate division district of the Santa Fe Environmental Bureau office for cons	ideration of ar	proval			
(Fencing/BGT Liner)	racramon or ap	pro rui.			
Exception(s): Requests must be submitted to the Santa Fe Environmental Bureau office for consideration of approval.					
10					
Siting Criteria (regarding permitting): 19.15.17.10 NMAC Instructions: The applicant must demonstrate compliance for each siting criteria below in the application. Recommendations of acceptable source material are provided below. Requests regarding changes to certain siting criteria may require administrative approval from the appropriate district office or may be considered an exception which must be submitted to the Santa Fe Environmental Bureau Office for consideration of approval. Applicant must attach justification for request. Please refer to 19.15.17.10 NMAC for guidance. Siting criteria does not apply to drying pads or above grade-tanks associated with a closed-loop system.					
Ground water is less than 50 feet below the bottom of the temporary pit, permanent pit, or below-grade tank. NM Office of the State Engineer - iWATERS database search; USGS; Data obtained from nearby wells	Yes	□No			
Within 300 feet of a continuously flowing watercourse, or 200 feet of any other watercourse, lakebed, sinkhole, or playa lake (measured from the ordinary high-water mark). - Topographic map; Visual inspection (certification) of the proposed site	Yes	□No			
Within 300 feet from a permanent residence, school, hospital, institution, or church in existence at the time of initial application.	Yes	□No			
(Applies to temporary, emergency, or cavitation pits and below-grade tanks)	□NA				
- Visual inspection (certification) of the proposed site; Aerial photo; Satellite image					
Within 1000 feet from a permanent residence, school, hospital, institution, or church in existence at the time of initial application.	Yes	∐No			
(Applied to permanent pits) - Visual inspection (certification) of the proposed site; Aerial photo; Satellite image	│ ∐ ^{NA}				
Within 500 horizonal feet of a private, domestic fresh water well or spring that less than five households use for domestic or stock watering purposes, or within 1000 horizontal feet of any other fresh water well or spring, in existence at the time of initial application.	Yes	□No			
- NM Office of the State Engineer - iWATERS database search; Visual inspection (certification) of the proposed site.					
Within incorporated municipal boundaries or within a defined municipal fresh water well field covered under a municipal ordinance adopted pursuant to NMSA 1978, Section 3-27-3, as amended Written confirmation or verification from the municipality. Written approval obtained from the municipality.	Yes	□No			
 Written confirmation or verification from the municipality; Written approval obtained from the municipality Within 500 feet of a wetland. US Fish and Wildlife Wetland Identification map; Topographic map; Visual inspection (certification) of the proposed site 					
Within the area overlying a subsurface mine.					
- Written confirmation or verification or map from the NM EMNRD - Mining and Mineral Division Within an unstable area.	∏Yes	□No			
- Engineering measures incorporated into the design; NM Bureau of Geology & Mineral Resources; USGS; NM Geological Society; Topographic map		⊔.			
Within a 100-year floodplain - FEMA map	Yes	□No			

Temporary Pits, Emergency Pits and Below-grade Tanks Permit Application Attachment Checklist: Subsection B of 19.15.17.9 NMAC Instructions: Each of the following items must be attached to the application. Please indicate, by a check mark in the box, that the documents are attached.				
Hydrogeologic Report (Below-grade Tanks) - based upon the requirements of Paragraph (4) of Subsection B of 19.15.17.9 NMAC				
Hydrogeologic Data (Temporary and Emergency Pits) - based upon the requirements of Paragraph (2) of Subsection B of 19.15.17.9				
Siting Criteria Compliance Demonstrations - based upon the appropriate requirements of 19.15.17.10 NMAC				
Design Plan - based upon the appropriate requirements of 19.15.17.11 NMAC				
Operating and Maintenance Plan - based upon the appropriate requirements of 19.15.17.12 NMAC				
Closure Plan (Please complete Boxes 14 through 18, if applicable) - based upon the appropriate requirements of Subsection C of 19.15.17.9 NMAC and 19.15.17.13 NMAC				
Previously Approved Design (attach copy of design) API				
Closed-loop Systems Permit Application Attachment Checklist: Subsection B of 19.15.17.9 NMAC Instructions: Each of the following items must be attached to the application. Please indicate, by a check mark in the box, that the documents are attached. Geologic and Hydrogeologic Data (only for on-site closure) - based upon the requirements of Paragraph (3) of Subsection B of 19.15.17.9				
Siting Criteria Compliance Demonstrations (only for on-site closure) - based upon the appropriate requirements of 19.15.17.10 NMAC				
Design Plan - based upon the appropriate requirements of 19.15.17.11 NMAC				
Operating and Maintenance Plan - based upon the appropriate requirements of 19.15.17.12 NMAC				
Closure Plan (Please complete Boxes 14 through 18, if applicable) - based upon the appropriate requirements of Subsection C of 19.15.17.9 NMAC and 19.15.17.13 NMAC				
Previously Approved Design (attach copy of design) API				
Previously Approved Operating and Maintenance Plan API				
Permanent Pits Permit Application Checklist: Subsection B of 19.15.17.9 NMAC				
Instructions: Each of the following items must be attached to the application. Please indicate, by a check mark in the box, that the documents are attached.				
Hydrogeologic Report - based upon the requirements of Paragraph (I) of Subsection B of 19.15.17.9 NMAC				
Siting Criteria Compliance Demonstrations - based upon the appropriate requirements of 19.15.17.10 NMAC				
Climatological Factors Assessment Cartified Engineering Design Plans, based upon the content of 10.15.17.11 NIMAC				
Certified Engineering Design Plans - based upon the appropriate requirements of 19.15.17.11 NMAC Dike Protection and Structural Integrity Design: based upon the appropriate requirements of 19.15.17.11 NMAC				
Leak Detection Design - based upon the appropriate requirements of 19.15.17.11 NMAC				
Liner Specifications and Compatibility Assessment - based upon the appropriate requirements of 19.15.17.11 NMAC				
Quality Control/Quality Assurance Construction and Installation Plan				
Operating and Maintenance Plan - based upon the appropriate requirements of 19.15.17.12 NMAC				
Freeboard and Overtopping Prevention Plan - based upon the appropriate requirements of 19.15.17.11 NMAC				
Nuisance or Hazardous Odors, including H2S, Prevention Plan				
Emergency Response Plan				
Oil Field Waste Stream Characterization				
Monitoring and Inspection Plan				
Erosion Control Plan Closure Plan - based upon the appropriate requirements of Subsection C of 19.15.17.9 NMAC and 19.15.17.13 NMAC				
Closure Fian - based upon the appropriate requirements of Subsection C of 19.13.17.9 NMAC and 19.13.17.13 NMAC				
Proposed Closure: 19.15.17.13 NMAC Instructions: Please complete the applicable boxes, Boxes 14 through 18, in regards to the proposed closure plan.				
Type: Drilling Workover Emergency Cavitation P&A Permanent Pit Below-grade Tank Closed-loop System Alternative				
Proposed Closure Method: Waste Excavation and Removal				
Waste Removal (Closed-loop systems only)				
On-site Closure Method (only for temporary pits and closed-loop systems)				
In-place Burial On-site Trench				
Alternative Closure Method (Exceptions must be submitted to the Santa Fe Environmental Bureau for consideration)				
Waste Excavation and Removal Closure Plan Checklist: (19.15.17.13 NMAC) Instructions: Each of the following items must be attached to the closure plan.				
Please indicate, by a check mark in the box, that the documents are attached.				
Protocols and Procedures - based upon the appropriate requirements of 19.15.17.13 NMAC				
Confirmation Sampling Plan (if applicable) - based upon the appropriate requirements of Subsection F of 19.15.17.13 NMAC				
Disposal Facility Name and Permit Number (for liquids, drilling fluids and drill cuttings)				
Soil Backfill and Cover Design Specifications - based upon the appropriate requirements of Subsection H of 19.15.17.13 NMAC				
Re-vegetation Plan - based upon the appropriate requirements of Subsection I of 19.15.17.13 NMAC				
Site Reclamation Plan - based upon the appropriate requirements of Subsection G of 19.15.17.13 NMAC				

16					
Waste Removal Closure For Closed-loop Systems That Utilize Above Ground Steel Tanks or Haul-off Bins Only: (19.15.17.13.D NMAC) Instructions: Please identify the facility or facilities for the disposal of liquids, drilling fluids and drill cuttings. Use attachment if more than two	n				
facilities are required.	•				
Disposal Facility Name: Disposal Facility Permit #:					
Disposal Facility Name: Disposal Facility Permit #:					
Will any of the proposed closed-loop system operations and associated activities occur on or in areas that will not be used for future Yes (If yes, please provide the information No					
Yes (If yes, please provide the information No Required for impacted areas which will not be used for future service and operations: Soil Backfill and Cover Design Specification - based upon the appropriate requirements of Subsection H of 19.15.17.13 NMAC Re-vegetation Plan - based upon the appropriate requirements of Subsection I of 19.15.17.13 NMAC Site Reclamation Plan - based upon the appropriate requirements of Subsection G of 19.15.17.13 NMAC					
17					
Siting Criteria (Regarding on-site closure methods only: 19.15.17.10 NMAC Instructions: Each siting criteria requires a demonstration of compliance in the closure plan. Recommendations of acceptable source material are provided certain siting criteria may require administrative approval from the appropriate district office or may be considered an exception which must be submitted to office for consideration of approval. Justifications and/or demonstrations of equivalency are required. Please refer to 19.15.17.10 NMAC for guidance.					
Ground water is less than 50 feet below the bottom of the buried waste.	Yes	No			
- NM Office of the State Engineer - iWATERS database search; USGS: Data obtained from nearby wells	□N/A				
Ground water is between 50 and 100 feet below the bottom of the buried waste	□Yes	□No			
- NM Office of the State Engineer - iWATERS database search; USGS; Data obtained from nearby wells	∏N/A				
Ground water is more than 100 feet below the bottom of the buried waste.	Yes	□No			
- NM Office of the State Engineer - iWATERS database search; USGS; Data obtained from nearby wells	∏ _{N/A}				
Within 300 feet of a continuously flowing watercourse, or 200 feet of any other significant watercourse or lakebed, sinkhole, or playa lake (measured from the ordinary high-water mark).	Yes	No			
- Topographic map; Visual inspection (certification) of the proposed site					
Within 300 feet from a permanent residence, school, hospital, institution, or church in existence at the time of initial application. - Visual inspection (certification) of the proposed site; Aerial photo; satellite image	Yes	No			
1(Yes	□No			
Within 500 horizontal feet of a private, domestic fresh water well or spring that less than five households use for domestic or stock watering purposes, or within 1000 horizontal fee of any other fresh water well or spring, in existence at the time of the initial application. - NM Office of the State Engineer - iWATERS database; Visual inspection (certification) of the proposed site					
Within incorporated municipal boundaries or within a defined municipal fresh water well field covered under a municipal ordinance adopted pursuant to NMSA 1978, Section 3-27-3, as amended.	Yes	□No			
- Written confirmation or verification from the municipality; Written approval obtained from the municipality					
Within 500 feet of a wetland - US Fish and Wildlife Wetland Identification map; Topographic map; Visual inspection (certification) of the proposed site	Yes	∐No			
Within the area overlying a subsurface mine.	Yes	□No			
- Written confiramtion or verification or map from the NM EMNRD-Mining and Mineral Division					
Within an unstable area.	Yes	No			
 Engineering measures incorporated into the design; NM Bureau of Geology & Mineral Resources; USGS; NM Geological Society; Topographic map 					
Within a 100-year floodplain FEMA map	Yes	□No			
18					
On-Site Closure Plan Checklist: (19.15.17.13 NMAC) Instructions: Each of the following items must bee attached to the clos by a check mark in the box, that the documents are attached.	ure plan. Plea	se indicate,			
Siting Criteria Compliance Demonstrations - based upon the appropriate requirements of 19.15.17.10 NMAC					
Proof of Surface Owner Notice - based upon the appropriate requirements of Subsection F of 19.15.17.13 NMAC					
Construction/Design Plan of Burial Trench (if applicable) based upon the appropriate requirements of 19.15.17.11 NMAC					
Construction/Design Plan of Temporary Pit (for in place burial of a drying pad) - based upon the appropriate requirements of	19.15.17.11 N	MAC			
Protocols and Procedures - based upon the appropriate requirements of 19.15.17.13 NMAC					
Confirmation Sampling Plan (if applicable) - based upon the appropriate requirements of Subsection F of 19.15.17.13 NMAC					
Waste Material Sampling Plan - based upon the appropriate requirements of Subsection F of 19.15.17.13 NMAC					
Disposal Facility Name and Permit Number (for liquids, drilling fluids and drill cuttings or in case on-site closure standards cannot be achieved)					
Soil Cover Design - based upon the appropriate requirements of Subsection H of 19.15.17.13 NMAC					
Re-vegetation Plan - based upon the appropriate requirements of Subsection I of 19.15.17.13 NMAC Site Reclamation Plan - based upon the appropriate requirements of Subsection G of 19.15.17.13 NMAC					

19 Occupation Application Contification
Operator Application Certification: I hereby certify that the information submitted with this application is true, accurate and complete to the best of my knowledge and belief.
Name (Print): Title:
Signature: Date:
e-mail address: Telephone:
20 OCD Approval: Permit Application (including closure plan) Closure Plan (only) OCD Conditions (see attachment)
OCD Representative Signature: 7 grand 7 les Approval Date: -20 10
Title:OCD Permit Number:
Title. 2001 / 342 OCE Termit Number.
Closure Report (required within 60 days of closure completion): Subsection K of 19.15.17.13 NMAC Instructions: Operators are required to obtain an approved closure plan prior to implementing any closure activities and submitting the closure report. The closure report is required to be submitted to the division within 60 days of the completion of the closure activities. Please do not complete this section of the form until an approved closure plan has been obtained and the closure activities have been completed. [X] Closure Completion Date: November 3, 2008
22
Closure Method:
Waste Excavation and Removal X On-site Closure Method Alternative Closure Method Waste Removal (Closed-loop systems only)
If different from approved plan, please explain.
23 <u>Closure Report Regarding Waste Removal Closure For Closed-loop Systems That Utilize Above Ground Steel Tanks or Haul-off Bins Only:</u> Instructions: Please identify the facility or facilities for where the liquids, drilling fluids and drill cuttings were disposed. Use attachment if more than two facilities were utilized.
Disposal Facility Name: Disposal Facility Permit Number:
Disposal Facility Name: Disposal Facility Permit Number:
Were the closed-loop system operations and associated activities performed on or in areas that will not be used for future service and operations?
Yes (If yes, please demonstrate complilane to the items below)
Required for impacted areas which will not be used for future service and operations:
Site Reclamation (Photo Documentation) Soil Backfilling and Cover Installation
Re-vegetation Application Rates and Seeding Technique
24
Closure Report Attachment Checklist: Instructions: Each of the following items must be attached to the closure report. Please indicate, by a check mark in
the box, that the documents are attached.
X Proof of Closure Notice (surface owner and division) X Proof of Deed Notice (required for on-site closure)
X Plot Plan (for on-site closures and temporary pits)
X Confirmation Sampling Analytical Results (if applicable)
Waste Material Sampling Analytical Results (if applicable)
X Disposal Facility Name and Permit Number
X Soil Backfilling and Cover Installation
X Re-vegetation Application Rates and Seeding Technique
X Site Reclamation (Photo Documentation) On-site Closure Location: Latitude: 36.855348 °N Longitude: 108.161507 °W NAD 1927 X 1983
On-site Closure Location: Latitude: <u>36.855348</u> <u>°N</u> Longitude: <u>108.161507</u> <u>°W</u> NAD [1927 [X 1983]
25
Operator Closure Certification: I hereby certify that the information and attachments submitted with this closure report is ture, accurate and complete to the best of my knowledge and belief. I also certify that the closure complies with all applicable closure requirements and conditions specified in the approved closure plan.
Name (Print): Crystal Tafoya Title: Regulatory Tech
212-1
Signature: Date: 1/19/20/0
e-mail address: crystal.tafoya@conocophillips.com Telephone: 505-326-9837

Burlington Resources Oil Gas Company, LP San Juan Basin Closure Report

Lease Name: Farmington Com 100

API No.: 30-045-34574

In accordance with Rule 19.15.17.13 NMAC the following information describes the closure of the temporary pit referenced above. All proper documentation regarding closure activities is being included with the C-144. The temporary pit for this location was constructed and location drilled before June 16, 2008 (effective date for Rule 19.15.17). While closure of the temporary pit did fall within the rule some dates for submittals are after the rig release date.

- Details on Capping and Covering, where applicable. (See report)
- Plot Plan (Pit Diagram) (Included as an attachment)
- Inspection Reports (Included as an attachment)
- Sampling Results (Included as an attachment)
- C-105 (Included as an attachment)
- Copy of Deed Notice will be filed with County Clerk (Not required on Federal, State, or Tribal land as stated by FAQ dated October 30, 2008)

General Plan:

1. All free standing liquids will be removed at the start of the pit closure process from the pit and disposed of in a division—approved facility or recycle, reuse or reclaim the liquids in a manner that the appropriate division district office approves.

All recovered liquids were disposed of at Basin Disposal (Permit #NM-01-005) and any sludge or soil required to be removed to facilitate closure was hauled to Envirotech Land Farm (Permit #NM-01-011) and JFJ Landfarm % IEI (Permit #NM-01-0010B).

2. The preferred method of closure for all temporary pits will be on-site burial, assuming that all the criteria listed in sub-section (B) of 19.15.17.13 are met.

The pit was closed using onsite burial.

3. The surface owner shall be notified of BR's closing of the temporary pit as per the approved closure plan using certified mail, return receipt requested.

The closure process notification to the landowner was sent via permit submittal. (See Attached)(Well located on State Land, certified mail is not required for Federal Land per BLM/OCD MOU.)

4. Within 6 months of the Rig Off status occurring BR will ensure that temporary pits are closed, re-contoured, and reseeded.

Provision 4 of the closure plan requirements were not met due to rig move off date as noted on C-105 which was prior to pit rule change. Burlington will ensure compliance with this rule in the future.

- 5. Notice of Closure will be given to the Aztec Division office between 72 hours and one week of closure via email, or verbally. The notification of closure will include the following:
 - i. Operator's name
 - ii. Location by Unit Letter, Section, Township, and Range. Well name and API number.

Notification is attached.

6. Liner of temporary pit shall be removed above "mud level" after stabilization. Removal of liner will consist of manually or mechanically cutting liner at mud level and removing all remaining liner. Care will be taken to remove "All" of the liner i.e., edges of liner entrenched or buried. All excessive liner will be disposed of at a licensed disposal facility.

Liner of temporary pit was removed above "mud level" after stabilization. Removal of the liner consisted of manually cutting liner at mud level and removing all remaining liner. Care was taken to remove "ALL" of the liner i.e., edges of liner entrenched or buried. All excessive liner was disposed of at a licensed disposal facility, (San Juan County Landfill).

7. Pit contents shall be mixed with non-waste containing, earthen material in order to achieve the solidification process. The solidification process will be accomplished using a combination of natural drying and mechanically mixing. Pit contents will be mixed with non-waste, earthen material to a consistency that is deemed a safe and stable. The mixing ratio shall not exceed 3 parts clean soil to 1 part pit contents.

Burlington mixed the Pit contents with non-waste containing, earthen material in order to achieve the solidification process. The solidification process was accomplished by using a combination of natural drying and mechanically mixing. Pit contents were mixed with non-waste, earthen material to a consistency that is deemed as safe and stable. The mixing ratio consisted of approximately 3 parts clean soil to 1 part pit contents.

8. A five point composite sample will be taken of the pit using sampling tools and all samples tested per Subsection B of 19.15.17.13(B)(1)(b). In the event that the criteria are not met, all contents will be handled per Subparagraph (a) of Paragraph (1) of Subsection B of 19.15.17.13 i.e., Dig and haul.

A five point composite sample was taken of the pit using sampling tools and all samples tested per Subsection B of 19.15.17.1 3(B)(1)(b). (Sample results attached).

Components	Tests Method	Limit (mg/Kg)	Results
Benzene	EPA SW-846 8021B or 8260B	0.2	ND ug/kg
BTEX	EPA SW-846 8021B or 8260B	50	ND ug/kG
TPH	EPA SW-846 418.1	2500	67.1mg/kg
GRO/DRO	EPA SW-846 8015M	500	3.5 mg/Kg
Chlorides	EPA 300.1	1000/500	800 mg/L

9. Upon completion of solidification and testing standards being passed, the pit area will be backfilled with compacted, non-waste containing, earthen material. A minimum of four feet of cover shall be achieved and the cover shall include one foot of suitable material to establish vegetation at the site, or the background thickness of topsoil, whichever is greater. If standard testing fails BR will dig and haul all contents pursuant to 19.15.17.13.i.a. After doing such, confirmation sampling will be conducted to ensure a release has not occurred.

The pit material passed solidification and testing standards. The pit area was then backfilled with compacted, non-waste containing, earthen material. More than four feet of cover was achieved and the cover included one foot of suitable material to establish vegetation at the site.

10. During the stabilization process if the liner is ripped by equipment the Aztec OCD office will be notified within 48 hours and the liner will be repaired if possible. If the liner can not be repaired then all contents will be excavated and removed.

The integrity of the liner was not damaged in the pit closure process.

11. Dig and Haul Material will be transported to the Envirotech Land Farm located 16 miles south of Bloomfield on Angel Peak Road, CR 7175. Permit # NM010011

Dig and Haul was not required.

12. Re-contouring of location will match fit, shape, line, form and texture of the surrounding. Re-shaping will include drainage control, prevent ponding, and prevent erosion. Natural drainages will be unimpeded and water bars and/or silt traps will be place in areas where needed to prevent erosion on a large scale. Final recontour shall have a uniform appearance with smooth surface, fitting the natural landscape.

The pit area was re-contoured to match fit, shape, line, form and texture of the surrounding area. Reshaping included drainage control, to prevent ponding and erosion. Natural drainages were unimpeded and water bars and/or silt traps were placed in areas where needed to prevent erosion on a large scale. Final recontour has a uniform appearance with smooth surface, fitting the natural landscape.

13. Notification will be sent to OCD when the reclaimed area is seeded.

Provision 13 was accomplished through complying with State seeding requirements as allowed by the BLM/OCD MOU.

14. BR shall seed the disturbed areas the first growing season after the operator closes the pit. Seeding will be accomplished via drilling on the contour whenever practical or by other division-approved methods. BLM or Forest Service stipulated seed mixes will used on federal lands. Vegetative cover will equal 70% of the native perennial vegetative cover (un-impacted) consisting of at least three native plant species, including at least one grass, but not including noxious weeds, and maintain that cover through two successive growing seasons. Repeat seeding or planting will be continued until successful vegetative growth occurs.

Provision 14 was accomplished through complying with State seeding requirements as allowed by the BLM/OCD MOU.

15. The temporary pit will be located with a steel marker, no less than four inches in diameter, cemented in a hole three feet deep in the center of the onsite burial upon the abandonment of all the wells on the pad. The marker will be flush with the ground to allow access of the active well pad and for safety concerns. The marker will include a threaded collar to be used for future abandonment. The top of the marker will contain a welded steel 12" square plate that indicates the onsite burial of the temporary pit. The plate will be easily removable and a four foot tall riser will be threaded into the top of the collar marker and welded around the base with the operator's information at the time of all wells on the pad are abandoned. The operator's information will include the following: Operator Name, Lease Name, Well Name and number, Unit Number, Section, Township, Range and an indicator that the marker is an onsite burial location.

Provision 15 was accomplished by installing a steel marker in the temporary pit, no less than four inches in diameter, cemented in a hole three feet deep in the center of the onsite burial. The marker is flush with the ground to allow access of the active well pad and for safety concerns. The top of the marker contains a welded steel 12" square plate that indicates the onsite burial of the temporary pit. The plate contains the following: Operator Name, Lease Name, Well Name and number, Unit Number, Section, Township, Range and an indicator that the marker is an onsite burial location.

The plate will be easily removable and a four foot tall riser will be threaded into the top of the collar marker and welded around the base with the following operator's information at the time of all wells on the pad are abandoned. The riser will be labeled: BR, State, Farmington Com 100, UL-L, Sec. 36, T 31N, R 13W, API # 30-045-34574

DISTRICT I 1625 N. French Dr., Hobbs, N.M. 68240

State of New Mexico
Energy, Minerals & Natural Resources Department

Form C-102 Revised October 12, 2005

DISTRICT H
1301 West Grand Avenue, Artesia, N.M. 88210

OIL CONSERVATION DIVISION 1220 South St. Francis Dr. Santa Fe, NM 87505

Submit to Appropriate District Office State Lease - 4 Copies Fee Lease - 3 Copies

DISTRICT III 1000 Rio Brazos Rd., Aztec, N.M. 87410

DISTRICT IV 1220 S. St. Francis Dr., Santa Fe, NM 87505


☐ AMENDED REPORT

¹API 1	Number		*1	Pool Code			Pool Nam. BASIN FRUITLAI	transfer of the second	3	
*Property Co	de				Property FARMINGTON				• Well Number 100	
OGRID No.			BURLIN	GTON RE	*Operator	Name AND GAS COMP	ANY LP		* Elevation 6107	1
	384				10 Surface	Location				
UL or lot no.	Section 36	Township 31—N	Range 13-W	Lot kin	Feet from the 2245'	North/South line SOUTH	Feet from the 1040'	East/West line WEST	County SAN JU	UAN
			11 Bottor	n Hole	Location J	f Different Fr	om Surface			3 1
UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	6 County	\$ 1 a a
Pedicated Acres FC 320.0 A		1/2	Joint or In	m	¹⁴ Consolidation	Code	¹⁵ Order No.			

OR A NON-STANDARD UNIT HAS BEEN APPROVED BY THE DIVISION

06-1649-1			17 OPERATOR CERTIFICATION I hereby certify that the information contained hirein is true and complete to the best of my knowledge and botief, and that this expanication either owns a working interest or unleased mineral interest in the land including the proposed bottom hale location or has a right to drill this well at this location pursuant to a contract with an owner of such a mineral er a working interest, or to a working interest of the division.
NEW MEXICO ST OF O	30 ST OF E-3150-11	6	Signature Printed Name 18 SURVEYOR CERTIFICATION
1040' 2245'	NEW MEXICO	LAT: 36'51.3122' N. LONG: 108'09.6426' V.	I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my behind. Dete of Survey. MEL Signature and Sign of Professional Surveyor. (15703)
	55° 06' B 6.30'	NAD 1927 LAT: 36.855205 N. LONG: 108.161340 V. NAD 1983	Certificate Number 15703

NOTE. VECTOR SURVEYS IS NOT LIABLE FOR UNDERGROUND UTILITIES OR UNMARKED BURIED
CONTRACTOR SHOULD CALL ONE-CALL FOR LOCATION OF ANY MARKED OR UNMARKED BURIED
CONTRACTOR SHOULD CALL ONE-CALL FOR LOCATION OF ANY MARKED OR UNMARKED BURIED
CONSTRUCTION.

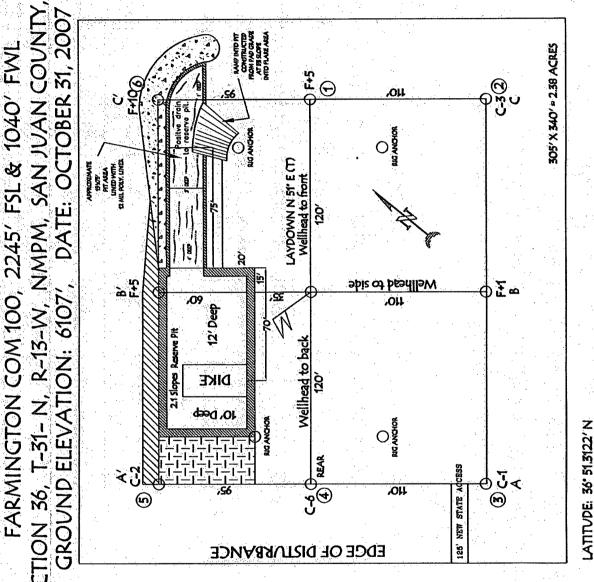

BURLINGTON RESOURCES OIL & GAS COMPANY LP

LATITUDE: 36° 51.3122′ N LONGITUDE: 108° 09.6426′ W NAD 27

REZERVE PIT DIKE. TO BE 8' ABOVE DEEP SIDE (OVERFLOW - 3' WIDE AND 1' ABOVE SHALLOW SIDE).



EPA METHOD 8015 Modified Nonhalogenated Volatile Organics Total Petroleum Hydrocarbons

Client:	ConocoPhillips	Project #:	96052-0026
Sample ID:	Farmington Com #100	Date Reported:	08-26-08
Laboratory Number:	46844	Date Sampled:	08-20-08
Chain of Custody No:	5058	Date Received:	08-21-08
Sample Matrix:	Soil	Date Extracted:	08-22-08
Preservative:	Cool	Date Analyzed:	08-25-08
Condition:	Intact	Analysis Requested:	8015 TPH

Parameter	Concentration (mg/Kg)	Det. Limit (mg/Kg)	
Gasoline Range (C5 - C10)	ND	0.2	
Diesel Range (C10 - C28)	3.5	0.1	
Total Petroleum Hydrocarbons	3.5	0.2	

ND - Parameter not detected at the stated detection limit.

References:

Method 8015B, Nonhalogenated Volatile Organics, Test Methods for Evaluating Solid Waste,

SW-846, USEPA, December 1996.

Comments:

Drilling Pit Sample

Analyst

Mater of Walter Beview

5796 U.S. Highway 64 • Farmington, NM 87401 • Tel 505-632-0615 • Fax 505-632-1865



EPA METHOD 8015 Modified Nonhalogenated Volatile Organics Total Petroleum Hydrocarbons

Client:	ConocoPhillips	Project #:	96052-0026
Sample ID:	Farmington Com #100 Background	Date Reported:	08-26-08
Laboratory Number:	46845	Date Sampled:	08-20-08
Chain of Custody No:	5058	Date Received:	08-21-08
Sample Matrix:	Soil	Date Extracted:	08-22-08
Preservative:	Cool	Date Analyzed:	08-25-08
Condition:	Intact	Analysis Requested:	8015 TPH

Parameter .	Concentration (mg/Kg)	Det. Limit (mg/Kg)	
Gasoline Range (C5 - C10)	ND	0.2	
Diesel Range (C10 - C28)	ND	0.1	
Total Petroleum Hydrocarbons	ND	0.2	

ND - Parameter not detected at the stated detection limit.

References:

Method 8015B, Nonhalogenated Volatile Organics, Test Methods for Evaluating Solid Waste,

SW-846, USEPA, December 1996.

Comments:

Drilling Pit Sample

Analyst

Muster of Weel

5796 U.S. Highway 64 • Farmington, NM 87401 • Tel 505-632-0615 • Fax 505-632-1865



EPA Method 8015 Modified Nonhalogenated Volatile Organics Total Petroleum Hydrocarbons

Quality Assurance Report

98.8%

97.2%

Christin on Waller Review

75 - 125%

75 - 125%

Client:	QA/QC		Project #:		N/A
Sample ID:	08-25-08 QA/	QC	Date Reported:		08-26-08
Laboratory Number:	46828		Date Sampled:		N/A
Sample Matrix:	Methylene Chlo	ride	Date Received:		N/A
Preservative:	N/A		Date Analyzed:		08-25-08
Condition:	N/A		Analysis Reques	ted:	TPH
	I-Cal/Date/	#Cal RF	©≟©alRF≅	% Difference	Accept Rang
Gasoline Range C5 - C10	05-07-07	1.0023E+003	1.0027E+003	0.04%	0 - 15%
Diesel Range C10 - C28	05-07-07	9.9987E+002	1.0003E+003	0.04%	0 - 15%
Blank Conc. (mg/L=mg/Kg)	Concentration		Detection Lim	it
Gasoline Range C5 - C10		ND		0.2	-
Diesel Range C10 - C28		ND		0.1	•
Total Petroleum Hydrocarbons		ND		0.2	
Duplicate Conc. (mg/Kg)	Sample	Duplicate	% Difference	Accept. Range	
Gasoline Range C5 - C10	ND	ND	0.0%	0 - 30%	·
Diesel Range C10 - C28	ND	ND	0.0%	0 - 30%	

Spike Conc. (mg/Kg) Sample Spike Added Spike Result % Recovery. Accept Range

250

250

ND - Parameter not detected at the stated detection limit.

References:

Gasoline Range C5 - C10

Diesel Range C10 - C28

Method 8015B, Nonhalogenated Volatile Organics, Test Methods for Evaluating Solid Waste,

247

243

SW-846, USEPA, December 1996.

ND

ND

Comments:

QA/QC for Samples 46828 - 46829, 46840 - 46845 and 46865.

Analyst



EPA METHOD 8021 AROMATIC VOLATILE ORGANICS

Client	ConocoPhillips	Project #:	96052-0026
Sample ID:	Farmington Com #100	Date Reported:	08-26-08
Laboratory Number:	46844	Date Sampled:	08-20-08
Chain of Custody:	5058	Date Received:	08-21-08
Sample Matrix:	Soīl	Date Analyzed:	08-25-08
Preservative:	Cool	Date Extracted:	08-22-08
Condition:	Intact	Analysis Requested:	BTEX

Parameter	Concentration (ug/Kg)	Det. Limit (ug/Kg)		
Benzene	ND	0.9		
Toluene	ND	1.0		
Ethylbenzene	ND	1.0	_	
p,m-Xylene	ND	1.2		
o-Xylene	ND	0.9		
Total BTEX	ND			

ND - Parameter not detected at the stated detection limit.

Surrogate Recoveries:	Parameter	Percent Recovery
	Fluorobenzene	99.0 %
	1,4-difluorobenzene	99.0 %
	Bromochlorobenzene	99.0 %

References:

Method 5030B, Purge-and-Trap, Test Methods for Evaluating Solid Waste, SW-846, USEPA,

December 1996.

Method 8021B, Aromatic Volatile Organics, Test Methods for Evaluating Solid Waste, SW-846,

USEPA, December 1996.

Comments:

Drilling Pit Sample

Analyst

Ahrsten Weeten
Review



EPA METHOD 8021 AROMATIC VOLATILE ORGANICS

Client	ConocoPhillips	Project #:	96052-0026
Sample ID:	Farmington Com #100 Background	Date Reported:	08-26-08
Laboratory Number:	46845	Date Sampled:	08-20-08
Chain of Custody:	5058	Date Received:	08-21-08
Sample Matrix:	Soil	Date Analyzed:	08-25-08
Preservative:	Cool	Date Extracted:	08-22-08
Condition:	Intact	Analysis Requested:	BTEX

	Concentration	Det. Limit	
Parameter	(ug/Kg)	(ug/Kg)	
Benzene	ND	0.9	
Toluene	ND	1.0	
Ethylbenzene	ND	1.0	-
p,m-Xylene o-Xylene	ND	1.2	
o-Xylene	ND	0.9	
Total BTEX	ND		

ND - Parameter not detected at the stated detection limit.

Surrogate Recoveries:	Parameter	Percent Recovery	
	Fluorobenzene	96.0 %	
	1,4-difluorobenzene	9 6 .0 %	
	Bromochlorobenzene	96.0 %	

References:

Method 5030B, Purge-and-Trap, Test Methods for Evaluating Solid Waste, SW-846, USEPA,

December 1996.

Method 8021B, Aromatic Volatile Organics, Test Methods for Evaluating Solid Waste, SW-846,

USEPA, December 1996.

Comments:

Drilling Pit Sample

Analyst

Moturn Daeter Review



EPA METHOD 8021 AROMATIC VOLATILE ORGANICS

Client:	N/A	Project #:	N/A
Sample ID:	08-25-BT QA/QC	Date Reported:	08-26-08
Laboratory Number:	46823	Date Sampled:	NA
Sample Matrix:	Soil	Date Received:	N/A
Preservative:	N/A	Date Analyzed:	08-25-08
Condition:	N/A	Analysis:	BTEX

Calibration and Detection Limits (ug/L)	l-Galirië	C-CallRF Accept Rand	%Diff je 0 = 15%	Blank Conc	Detect : Limit
Benzene	7.8668E+007	7.8826E+007	0.2%	ND	0.1
Toluene	5.9532E+007	5.9652E+007	0.2%	ND	0.1
Ethylbenzene	4.7030E+007	4.7124E+007	0.2%	ND	0.1
p,m-Xylene	9.5728E+007	9.5920E+007	0.2%	ND	0.1
o-Xylene	4.5003E+007	4.5093E+007	0.2%	ND	0.1

Duplicate Conc. (ug/Kg)	Sample D	uplicate	%Diff;	Accept Range	Defect Limit
Benzene	2.0	. 2.2	10.0%	0 - 30%	0.9
Toluene	4.7	5.0	6.4%	0 - 30%	1.0
Ethylbenzene	3.3	3.4	3.0%	0 - 30%	1.0
p,m-Xylene	18.1	18.7	3.3%	0 - 30%	1.2
o-Xylene	5.3	5.2	1.9%	0 - 30%	0.9

Spike Conc. (ug/Kg)	Sample , Amo	unt Spiked - Spik	ed Sample	% Recovery	Accept Range
Benzene	2.0	50.0	51.6	99.2%	39 - 150
Toluene	4.7	50.0	54.3	99.3%	46 - 148
Ethylbenzene	3.3	50.0	52.9	99.2%	- 32 - 160
p,m-Xylene	18.1	100	116	98.3%	46 - 148
o-Xylene	5.3	50.0	54.9	99.3%	46 - 148

ND - Parameter not detected at the stated detection limit.

References:

Method 5030B, Purge-and-Trap, Test Methods for Evaluating Solid Waste, SW-846, USEPA,

December 1996.

Method 8021B, Aromatic and Halogenated Volatiles by Gas Chromatography Using Photoionization and/or Electrolytic Conductivity Detectors, SW-846, USEPA December 1996.

Comments:

QA/QC for Samples 46823, 46828 - 46829, and 46840 - 46845.

Analyst

Muster MUcelan Review



TRACE METAL ANALYSIS

Client:	ConocoPhillips	Project #:	96052-0026
Sample ID:	Farmington Com #100	Date Reported:	08-28-08
Laboratory Number:	46844	Date Sampled:	08-20-08
Chain of Custody:	5058	Date Received:	08-21-08
Sample Matrix:	Soil	Date Analyzed:	08-25-08
Preservative:	Cool	Date Digested:	08-25-08
Condition:	Intact	Analysis Needed:	Total Metals

Parameter	Concentration (mg/Kg)	Det. Limit (mg/Kg)	TCLP Regulatory Level (mg/Kg)
Arsenic	0.115	0.001	5.0
Barium	2.75	0.001	100
Cadmium	ND	0.001	1.0
Chromium	0.435	0.001	5.0 -
Lead	0.235	0.001	5.0
Mercury	ND	0.001	0.2
Selenium	ND	0.001	1.0
Silver	ИD	0.001	5.0

ND - Parameter not detected at the stated detection limit.

References:

Method 3050B, Acid Digestion of Sediments, Sludges and Soils.

SW-846, USEPA, December 1996.

Method 6010B, Analysis of Metals by Inductively Coupled Plasma Atomic Emmision

Spectroscopy, SW-846, USEPA, December 1996.

Note:

Regulatory Limits based on 40 CFR part 261 subpart C

section 261.24, August 24, 1998.

Comments:

Drilling Pit Sample.

Anabet

Review



TRACE METAL ANALYSIS

Client:	ConocoPhillips	Project #:	96052-0026
Sample ID:	Farmington Com #100 Background	Date Reported:	08-28-08
Laboratory Number:	46845	Date Sampled:	08-20-08
Chain of Custody:	5058	Date Received:	08-21-08
Sample Matrix:	Soil	Date Analyzed:	08-25-08
Preservative:	Cool	Date Digested:	08-25-08
Condition:	Intact	Analysis Needed:	Total Metals

Parameter	Concentration (mg/Kg)	Det. Limit (mg/Kg)	TCLP Regulatory Level (mg/Kg)
Arsenic	0.347	0.001	5.0
Barium	0.464	0.001	100
Cadmium	ND	0.001	1.0
Chromium	0.166	0.001	5.0
Lead	0.290	0.001	5.0
Mercury	ND	0.001	0.2
Selenium	ND	0.001	1.0
Silver	ND	0.001	5.0

ND - Parameter not detected at the stated detection limit.

References:

Method 3050B, Acid Digestion of Sediments, Sludges and Soils.

SW-846, USEPA, December 1996.

Method 6010B, Analysis of Metals by Inductively Coupled Plasma Atomic Emmision

Spectroscopy, SW-846, USEPA, December 1996.

Note:

Regulatory Limits based on 40 CFR part 261 subpart C

section 261.24, August 24, 1998.

Comments:

Drilling Pit Sample.

Analyst

/hoste male acter



TRACE METAL ANALYSIS Quality Control / Quality Assurance Report

	QA/QC		Project #:			QA/QC
	08-25 TM QA/AC		Date Repo	orted:		08-28-08
	46818		Date Sam	pled:		N/A
	Soil·		Date Rece	eived:		N/A
	Total RCR	A Metals	Date Anal	yzed:		08-25-08
	N/A		Date Dige	sted:		08-25-08
THE RESERVE AND DESCRIPTIONS OF THE PARTY AND PERSONS ASSESSED.	Committee of the Commit	The first of the contract of t	n Sample	Duplicate	4	Acceptance
Contraction Contra	en tale to land the second	the the section of th			Commence of the second	Range
						0% - 30%
						0% - 30%
						0% - 30%
ND					6.5%	0% - 30%
ND	ND	0.001	1.49	1.54	3.6%	0% - 30%
ND	ND	0.001	ND	ND	0.0%	0% - 30%
ND	ND	0.001	0.029	0.027	6.6%	0% - 30%
ND	ND	0.001	ND	ND	0.0%	0% - 30%
	Spike	Sample				Acceptance
	Added		Sample	Recovery		Range
	0.250	0.081	0.298	90.2%		80% - 120%
	0.500	4.07	3.95	86.3%		80% - 120%
	0.250	0.014	0.264	100.2%		80% - 120%
	0.500	0.537	0.991	95.6%		80% - 120%
,	0.500	1.49	2.293	116%		80% - 120%
	0.100	ND	0.099	99.0%		80% - 120%
						-
	0.100	0.029	0.120	93.1%		80% - 120%
٠	mk (mg/K ND ND ND ND ND ND ND ND	08-25 TM 46818 Soil- Total RCR N/A Instrument Method Mk (mg/kg) Blank ND N	08-25 TM QA/AC 46818 Soil- Total RCRA Metals N/A Instrument Method Detection Mix (mg/Kg) Blank Limit ND ND 0.001 Spike Sample Added 0.250 0.081 0.500 4.07 0.250 0.014 0.500 0.537 0.500 1.49	08-25 TM QA/AC Date Report	08-25 TM QA/AC Date Reported: 46818 Date Sampled: Soil- Date Received: Total RCRA Metals Date Analyzed: N/A Date Digested: Instrument Method Detection Sample Duplicate Mik (mg/Rg) Blank Limit ND ND 0.001 0.081 0.085 ND ND 0.001 0.014 0.014 ND ND 0.001 0.537 0.572 ND ND 0.001 0.537 0.572 ND ND 0.001 1.49 1.54 ND ND 0.001 1.49 1.54 ND ND 0.001 0.029 0.027 ND ND 0.001 ND ND ND ND 0.001 ND ND ND ND 0.001 ND ND Spike Sample Spiked Percent Added Sample Recovery 0.250 0.081 0.298 90.2% 0.500 4.07 3.95 86.3% 0.250 0.014 0.264 100.2% 0.500 0.537 0.991 95.6% 0.500 1.49 2.293 116%	08-25 TM QA/AC Date Reported: 46818 Date Sampled: Soil- Date Received: Total RCRA Metals Date Analyzed: N/A Date Digested: Instrument Method Detection Sample Duplicate Sample Diff. ND ND 0.001 0.081 0.085 5.7% ND ND 0.001 4.07 4.04 0.7% ND ND 0.001 0.014 0.014 1.4% ND ND 0.001 0.537 0.572 6.5% ND ND 0.001 0.537 0.572 6.5% ND ND 0.001 1.49 1.54 3.6% ND ND 0.001 ND ND 0.0% ND ND 0.001 0.029 0.027 6.6% ND ND 0.001 ND ND 0.0% ND ND 0.001 ND ND 0.0% ND ND 0.001 ND ND 0.0% Spike Sample Spiked Percent Added Sample Recovery 0.250 0.081 0.298 90.2% 0.500 4.07 3.95 86.3% 0.250 0.014 0.264 100.2% 0.500 0.537 0.991 95.6% 0.500 1.49 2.293 116%

ND - Parameter not detected at the stated detection limit.

References:

Method 3050B, Acid Digestion of Sediments, Sludges and Soils.

SW-846, USEPA, December 1996.

Method 6010B, Analysis of Metals by Inductively Coupled Plasma Atomic Emmision

Spectorscopy, SW-846, USEPA, December 1996.

Comments:

QA/1QC for Sample 46818 and 46840 - 46847.

Analyst



EPA METHOD 418.1 TOTAL PETROLEUM HYDROCARBONS

Phristum Weeters

Client:	ConocoPhillips	Project #:	96052-0026
Sample ID:	Farmington Com #100	Date Reported:	08-29-08
Laboratory Number:	46844	Date Sampled:	08-20-08
Chain of Custody No:	5058	Date Received:	08-21-08
Sample Matrix:	Soil	Date Extracted:	08-25-08
Preservative:	Cool	Date Analyzed:	08-25-08
Condition:	intact	Analysis Needed:	TPH-418.1

		Det.
	Concentration	Limit
Parameter	(mg/kg)	(mg/kg)

Total Petroleum Hydrocarbons

67.1

5.0

ND = Parameter not detected at the stated detection limit.

References:

Method 418.1, Petroleum Hydrocarbons, Total Recoverable, Chemical Analysis of Water

and Waste, USEPA Storet No. 4551, 1978.

Comments:

Drilling Pit Sample.

Analyst



EPA METHOD 418.1 TOTAL PETROLEUM HYDROCARBONS

Client:	ConocoPhillips	Project #:	96052-0026
Sample ID:	Farmington Com #100	Date Reported:	08-29-08
Laboratory Number:	46845	Date Sampled:	08-20-08
Chain of Custody No:	5058	Date Received:	08-21-08
Sample Matrix:	Soil	Date Extracted:	08-25-08
Preservative:	Cool	Date Analyzed:	08-25-08
Condition:	Intact	Analysis Needed:	TPH-418.1

		Det.
	Concentration	Limit
Parameter	(mg/kg)	(mg/kg)

Total Petroleum Hydrocarbons

14.1

5.0

ND = Parameter not detected at the stated detection limit.

References:

Method 418.1, Petroleum Hydrocarbons, Total Recoverable, Chemical Analysis of Water

and Waste, USEPA Storet No. 4551, 1978.

Comments:

Drilling Pit Sample Background.

Analyst

huster of Weeters



EPA METHOD 418.1 TOTAL PETROLEUM HYROCARBONS QUALITY ASSURANCE REPORT

Client	QA/QC	Project #:	N/A
Sample ID:	QA/QC	Date Reported:	08-28-08
Laboratory Number:	08-25-TPH.QA/QC 46840	Date Sampled:	NA
Sample Matrix:	Freon-113	Date Analyzed:	08-25-08
Preservative:	N/A	Date Extracted:	08-25-08
Condition:	N/A	Analysis Needed:	TPH
		-	

Calibration	I-Cal Date	C-Cal Date	I-Cal RF:	C-Cal RF:	% Difference	Accept. Range
	08-22-08	08-25-08	1,680	1,610	4.2%	+/- 10%

Blank Conc. (mg/Kg) TPH	Concentration ND	Detection Limit 13.4

Duplicate Conc. (mg/Kg) TPH	Sample 83.3	Duplicate 80.6	% Difference 3.2%	Accept. Range +/- 30%

Spike Conc. (mg/Kg)	Sample	Spike Added	Spike Result	% Recovery	Accept Range
TPH	83.3	2,000	1,810		80 - 120%

ND = Parameter not detected at the stated detection limit.

References: Method 418.1, Petroleum Hydrocarbons, Total Recoverable, Chemical Analysis of Water

and Waste, USEPA Storet No. 4551, 1978.

Comments: QA/QC for Samples 46840 - 46847.

Analyst

Muster of Waller

ENVIROTECH LABS

CATION / ANION ANALYSIS

Client:	ConocoPhillips	Project #:	96052-0026
Sample ID:	Farmington Com #100	Date Reported:	08-29-08
Laboratory Number:	46844	Date Sampled:	08-20-08
Chain of Custody:	5058	Date Received:	08-21-08
Sample Matrix:	Soil Extract	Date Extracted:	08-21-08
Preservative:	Cool	Date Analyzed:	08-22-08
Condition:	Intact		

	Analytical			
Parameter	Result	Units		
рН	7.47	s.u.		
Conductivity @ 25° C	7,090	umhos/cm		
Total Dissolved Solids @ 180C	4,260	mg/L		
Total Dissolved Solids (Calc)	4,824	mg/L		
SAR	7.5	ratio		
Total Alkalinity as CaCO3	32.0	mg/L		
Total Hardness as CaCO3	1,850	mg/L		-
Bicarbonate as HCO3	32.0	mg/L	0.52	meq/L
Carbonate as CO3	<0.1	mg/L	0.00	meq/L
Hydroxide as OH	<0.1	mg/L	0.00	meq/L
Nitrate Nitrogen	<0.01	mg/L	0.00	meq/L
Nitrite Nitrogen	<0.01	mg/L	0.00	meq/L
Chloride	800	mg/L	22.57	meq/L
Fluoride	0.577	mg/L	0.03	meq/L
Phosphate	0.104	mg/L	0.00	meq/L
Sulfate	2,410	mg/L	50.18	meq/L
Iron	0.055	mg/L	0.00	` meq/L.
Calcium	620	mg/L	30.94	meq/L
Magnesium	73.6	mg/L	6.06	meq/L
Potassium	161	mg/L	4.12	meq/L
Sodium	739	mg/L	32.15	meq/L
Cations			73.26	meq/L
Anions			73.30	meq/L
Cation/Anion Difference			0.06%	•

Reference: U.S.E.P.A., 600/4-79-020, "Methods for Chemical Analysis of Water and Wastes", 1983. Standard Methods For The Examination of Water And Waste Water", 18th ed., 1992.

Comments: Drilling Pit Sample.

Analyst

Mustum Wester

ENVIROTECH LABS

CATION / ANION ANALYSIS

1			
Client	ConocoPhillips	Project #:	96052-0026
Sample ID:	Farmington Com #100 Background	Date Reported:	08-29-08
Laboratory Number:	46845	Date Sampled:	08-20-08
Chain of Custody:	5058	Date Received:	08-21-08
Sample Matrix:	Soil Extract	Date Extracted:	08-21-08
Preservative:	Cool	Date Analyzed:	08-22-08
Condition:	Intact		

	Analytical			
Parameter	Result	Units		
pH	7.63	s.u.		
Conductivity @ 25° C	4,400	umhos/cm		
Total Dissolved Solids @ 180C	2,110	mg/L		
Total Dissolved Solids (Calc)	2,340	mg/L		
SAR	0.1	ratio		
Total Alkalinity as CaCO3	24.0	mg/L		
Total Hardness as CaCO3	1,700	mg/L		-
Bicarbonate as HCO3	24.0	mg/L	0.39	meq/L
Carbonate as CO3	<0.1	mg/L	0.00	meq/L
Hydroxide as OH	<0.1	mg/L	0.00	meq/L
Nitrate Nitrogen	1.31	mg/L	0.02	meq/L
Nitrite Nitrogen	0.022	mg/L	0.00	meq/L
Chloride	0.702	mg/L	0.02	meq/L
Fluoride	0.428	mg/L	0.02	meq/L
Phosphate	0.020	mg/L	0.00	meq/L
Sulfate	1,632	mg/L	33.98	meq/L
iron	0.008	mg/L	0.00	` meq/L.
Calcium	675	mg/L	33.68	meq/L
Magnesium	3.06	mg/L	0.25	meq/L
Potassium	4.85	mg/L	0.12	meq/L
Sodium	7.70	mg/L	0.33	meq/L
Cations			34.39	meq/L
Anions			34.44	meq/L
Cation/Anion Difference			0.12%	

Reference: U.S.E.P.A., 600/4-79-020, "Methods for Chemical Analysis of Water and Wastes", 1983. Standard Methods For The Examination of Water And Waste Water", 18th ed., 1992.

Comments: Drilling Pit Sample.

Analyst

Review College

Submit To Appropr Two Copies District I					State of New Minerals and				es						m C-105 aly 17, 2008
1625 N. French Dr. District II 1301 W. Grand Ave										1. WELL 30-045-34:		O.			
District III 1000 Rio Brazos Re					Conservat					2. Type of L	ease				
District IV					Santa Fe, N			Л.		3. State Oil		FEE ease No	FED	D/INDI	AN
1220 S. St. Francis	Dr., Santa F	e, NIM 8/505			Santa I C, IV	VIVI C	,,,,,,,			OG-1649-	,				
		ETION (OR RE	COMPL	ETION REF	POR	T AN	D LOC	<u> </u>	THE REPORT OF THE PARTY.	湖湖			A HOUSE HE	THE B
4. Reason for fili		ADT (Eill in 1	ovec#1	through #21	for State and Eee	walla	only)			5. Lease Nam	GTON			e 	
(-						6. Well Num 100	ber:				
#33; attach this a	nd the plat								and/or	100					
] WORKOVE	R 🗆 D	EEPENING	□PLUGBACK		DIFFER	ENT RES	ERVOI	R OTHER					
8. Name of Opera		. 0". 0	<u> </u>	I D					-	9. OGRID 14538			3		
Burlington R		s Oil Gas	Compa	any, LP						11. Pool name	e or Wil	deat			<u> </u>
PO Box 4298, Fa		NM 87499										avat			
12.Location	Unit Ltr	Section	T	ownship	Range	Lot		Feet fr	om the	N/S Line	Feet 1	from the	E/W Lin	ie	County
Surface:						-									
BH:		1									†			-	
13. Date Spudded	d 14. Da	te T.D. Reach	ned	15. Date Rig 03/15/08	Released		10	6. Date Co	ompleted	d (Ready to Pro	duce)		Elevation G, GR, etc.		and RKB,
18. Total Measur	ed Depth o	of Well		19. Plug Bac	k Measured Dep	ith	20). Was D	irection	al Survey Made	?	21. Type	e Electric	and Oth	ier Logs Run
22. Producing Int	terval(s), o	f this complet	ion - Top	p, Bottom, Na	me	•	- _	-							· · · · · ·
23.	_			CAS	ING REC	ORI) (Rej	ort all	strin	gs set in w	rell)				· · · · · · ·
CASING SI	ZE	WEIGHT	LB./FT.		DEPTH SET			OLE SIZ		CEMENTIN		ORD	AMC	DUNT I	PULLED
					- 1/8										
						\dashv				_		<u> </u>			
									,						
SIZE	TOP		BOTTO		ER RECORD SACKS CEMI	ENT	SCREE	N	25	ZE		G RECO		ACKE	DCET
SIZE	101		BOTIN	OM_	SACKS CLIVII	LIVI	SCREE	.11	31.	ZC	DE	rmser		ACKL	KSEI
•															
26. Perforation	record (in	terval, size, a	nd numb	er)				CID, SH I INTER		ACTURE, CI AMOUNT					
			·												
28.				36.4.1.00				TION		1		~-			
Date First Produc	ction	Pi	oduction	n Method (File	owing, gas lift, pi	umping	g - Size a	nd type p	ump)	Well Statu	s (Prod.	or Shut-	in)		
Date of Test	Hours	Tested	Choke	e Size	Prod'n For Test Period		Oil - B	bl	Ga	s - MCF	War	ter - Bbl.		Gas - O	il Ratio
Flow Tubing Press.	Casing	Pressure	Calcul Hour I	lated 24- Rate	Oil - Bbl.		Ga	s - MCF		Water - Bbl.		Oil Grav	vity - API	- (Corr)
29. Disposition o	f Gas (Solo	d, used for fue	l, vented	l, etc.)					1		30. Te	est Witne	ssed By		
31. List Attachme	ents										Ь				
32. If a temporar	y pit was u	sed at the wel	l, attach	a plat with th	e location of the	tempo	rary pit.								
33. If an on-site b	ourial was i	used at the we	il, report	t the exact loc	ation of the on-s	ite bui	rial:								
		Latitude	36.8553	348°N Lor	ngitude 108.161	507°W	/ NAD	□ 1927	⊠ 1983						
I hereby certif	ر در	e informat	ion sho	wn on both Prir	n sides of this nted	form	is true	and co	mplete				_	belief	
Signature	/	1	/		ne Crystal T	агоуг	111	ic. Keg	guiator	y i ech l	Date: I	1/16/201	10		
E-mail Addre	ss crysta	11.1a10ya(<i>a</i>)	COHOCO	piiiiips.co	111										

ConocoPhillips

Pit Closure Form:	
Date: _11/3/09	
Well Name: Farmington Com #100	
Footages: 2445 FSL 1040 FWL	Unit Letter:
Section: 31, T-31-N, R-13-W, County: 34	State: New Mexica
Contractor Closing Pit: JD Riffer Construction	×
Construction Inspector: Johny R. McDonald Inspector Signature: Jamy R. M. Donald	Date: <u>11/3/08</u>

Jaramillo, Marie E

From:

Silverman, Jason M

Sent:

Thursday, October 23, 2008 1:06 PM

To:

Brandon.Powell@state.nm.us; Mark Kelly; Robert Switzer; Sherrie Landon

Cc:

Busse, Dollie L; 'jdritt@aol.com'; Faver Norm (faverconsulting@yahoo.com); Becker, Joey W; Bonilla, Amanda; Bowker, Terry D; Chavez, Virgil E; Green, Cary J; GRP:SJBU Production Leads; Kennedy, Jim R; Kramme, Jeff L; Larry Thacker; Lopez, Richard A; Loudermilk, Jerry L; Nelson, Terry J; O'Nan, Mike J.; Peace, James T; Poulson, Mark E; PTRRC; Richards,

Brian, Silverman, Jason M; Stamets, Stephan A; Work, James A

Subject:

Clean Up Notice Farmington COM 100

Attachments: Farmington Com 100.pdf

J.D. Ritter Construction will move a tractor to the Farmington COM 100 on **Thursday, October 30th, 2008** to start the reclamation process. Please contact Norman Faver (320-0670) in you have any questions or need additional information.

Thanks
Jason Silverman

Network#:

10210940

Operator:

Burlington Resources

Legals:

2245' FSL, 1040' FWL

Section 36, T31N. R13W Unit Letter 'L' (NW/SW) San Juan County, NM

Lease:

New Mexico ST of OG-1649-1

API #:

30-045-34574

Surface/Minerals:

State/State

Jason M. Silverman ConocoPhillips Construction Technician Phone: (505) 326-9821 San Juan Basin Unit

CorocoPhilips

Reclamation Form:
Date: 11/18/2006
Well Name: Farmington com 100
Footages: ZM45 FSL 1040 FWL Link Letter:
Section: 36, 7-31-N, Pr-13-W, County: 57 State: NM
Reclamation Contractor: <u>JD R:++</u>
Reclamation Date: 11/5/2008
Road Completion Date:
Seeding Date: 1\/ 18/2008
Construction Inspector: Norman Faver Date: 11/18/2008
Inspector Signature: 1/2mm ==









WELL PAD SAFETY AND ENVIRONMENTAL CHECK LIST

WELL NAME: Farmington Com #100

API#: 30-045-34574

DATE	INSPECTOR	SAFETY	LOCATION	PICTURES	COMMENTS
		CHECK	CHECK	TAKEN	
3/19/08	Eric Smith	×	×		Apron left on location, called MVCI to remove
4/25/08	Jared Chavez				BJ Frac crew is on location
, 5/29/08	Jared Chavez	×	×		A few minor holes, south corner needs keyed, blow pit needs keyed, called MVCI and Brandon with OCD
80/6/9	Jared Chavez	×	×		Pit and location in good condition
6/16/08	Jared Chavez	×	×		Pit and location in good condition
6/23/08	Jared Chavez	×	×		Pit in location in good condition
2/3/08	Jared Chavez	×			Key rig #15 is on location
7/21/08	Jared Chavez	×	×		Holes in the liner, contacted Crossfire for repairs
7/28/08	Jared Chavez	×	×		Pit and location in good condition
8/4/08	Jared Chavez	×	×		Pit and location in good condition
8/11/08	Jared Chavez	×	×		Pit and location in good condition
8/18/08	Jared Chavez	×	×		Pit and location in good condition
8/29/08	Jared Chavez	×	×		Pit and location in good condition
9/12/08	Jared Chavez	×	×		Pit and location in good condition

9/19/08	Jared Chavez	×	×	Pit and location in good condition
10/10/08	Jared Chavez	×	×	Pit and location in good condition
