

well file

Casper Division
Production United States



**Marathon
Oil Company**

P.O. Box 2659
Casper, Wyoming 82602
Telephone 307/577-1555

December 21, 1984

State of New Mexico Energy and Minerals Department
1000 Rio Brazos Road
Aztec, New Mexico 87410
Attention: Mr. Frank Chavez

Dear Mr. Chavez:

Re: Jicarilla Well 9E
 Section 28, T26N, R5W
 Rio Arriba County, New Mexico

As per your telephone conversation with our engineer, Bob Ferri, on December 13, 1984, please find herein the information that you requested.

We plan to test a downhole commingling of the Mesaverde and Graneros and Dakota Zones commencing on 12/21/84. This test will not exceed 30 days. A wellbore schematic and map are attached. Thank you for your cooperation.

Sincerely yours,

MARATHON OIL COMPANY

Doyle L. Jones
by J. B. O'Neal
Doyle L. Jones
District Operations Manager

DLJ:RPF:pjl
Attachments

RECEIVED
DEC 31 1984
OIL CON. DIV.
DIST. 3

RIO ARriba COUNTY, NEW MEXICO
R 5 W

T
26
N


CONTRACT # 154
HICARILLA APACHE TRIBE

T
26
N

JICARILLA APACHE #9-E

1040' FSL & 1685' FEL
Section 28-T26N-R5W
Rio Arriba County, New Mexico
Completed 3-3-82

6,697' KB
6,684' GL

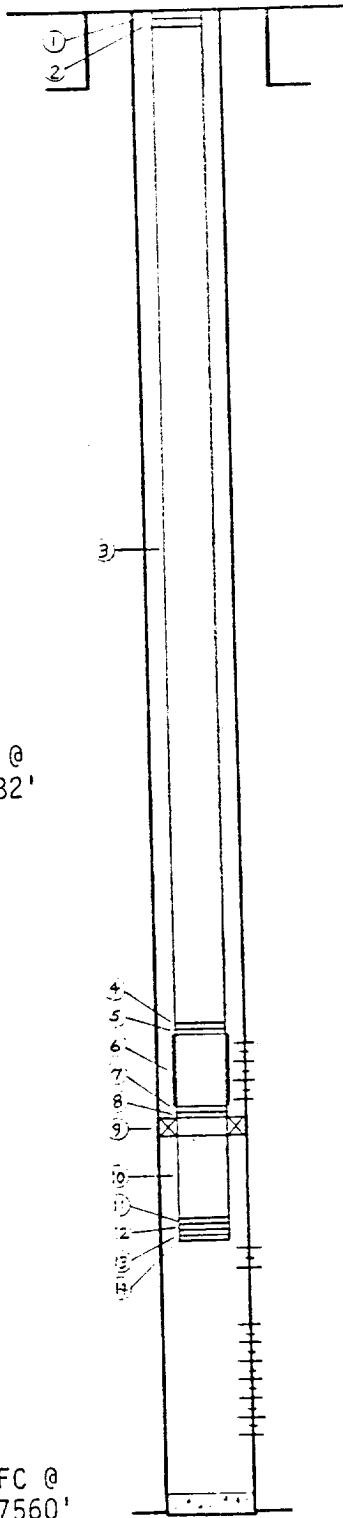

9-5/8", 36#, K-55 set @ 522' cemented w/450 sx

Tubing String (Top to Bottom):

<u>Description</u>	<u>Depth Set</u>
1. 1 jt 2-3/8" tbg	
2. 3' 2-3/8" sub	
3. 167 jts 2-3/8", 4.7#, J-55 tbg	
4. Baker Model L Sliding Sleeve	5207'
5. 8' & 6' 2-3/8" tbg subs	
6. 120' Blast Joints	
7. Baker Safety Joint	5344'
8. 8' 2-3/8" sub	
9. Baker Model FH Hydrostatic Packer	5353'
10. 59 jts 2-3/8", 4.7#, J-55 tbg	
11. 1.78" R Nipple	7193'
12. 1 jt 2-3/8", 4.7#, J-55 tbg	
13. Hydrotrip Pressure Sub	7225'
14. Expendable Check Valve	7226'

DV @
4082'

POINT LOOKOUT PERFS: 5233', 34', 35', 48', 49', 50', 51', 52',
88', 92', 94', 96', 98', 5300', 02', 04', 31', 33', & 35' w/1 SPF.
Reperfed 5232'-5236', 5246'-5254', 5281'-5310', 5329'-5336' w/4
SPF.

GRANEROS PERFS: 7237', 40', & 44' w/1 SPF. Reperfed 7234'-7246'
w/4 SPF. ~~Reperfed 7234'-7246' w/4 SPF.~~

DAKOTA PERFS: 7366', 68', 70', 72', 74', 76', 99', 7401', 09',
16', 52', 54', 56', 58', 60', & 62' w/1 SPF. Reperfed 7364'-7380',
7397'-7404', 7407'-7418', & 7450'-7466' w/4 SPF.

FC @
7560'

PBTD 7549'
TD 7611'

4-1/2" 10.5# & 11.6# K-55 set @ 7606' cemented w/
1st Stage: 825 sx BJ Lite followed w/180 sx Class B
2nd Stage: 800 sx 50-50 Poz

4-1/2" 10.5#, K-55 0 - 6470'
4-1/2" 11.6#, K-55 6470'-7605'
