

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

SUBMIT IN TRIPLICATE
(Other instructions on reverse side)

Budget Bureau No. 1004-0135
Expires August 31, 1985

SUNDRY NOTICES AND REPORTS ON WELLS

(Do not use this form for proposals to drill or to deepen or plug back or to otherwise alter or repair.
Use "APPLICATION FOR PERMIT—" for such proposals.)

RECEIVED

JAN 08 1986

1. OIL WELL ☒ CAR WELL ☐ OTHER ☐	2. NAME OF OPERATOR Amoco Production Co.	3. ADDRESS OF OPERATOR 501 Airport Drive, Farmington, N M 87401	4. LOCATION OF WELL (Report location clearly and in accordance with any State requirements. See also space 17 below.) At surface 765' FSL X 1120' FEL	5. LEASE DESIGNATION AND SERIAL NO. Jicarilla Apache A 118	6. IF INDIAN, ALLOTTEE OR TRIBE NAME Jicarilla Apache Tribe	7. UNIT AGREEMENT NAME	8. FARM OR LEASE NAME Jicarilla Apache A-118	9. WELL NO. 17	10. FIELD AND POOL, OR WILDCAT Ojito Gallup-Dakota	11. SEC., T., R., W., OR B.L. AND SURVEY OR AREA SE/SE Sec 26, T26N, R3W	12. COUNTY OR PARISH Rio Arriba	13. STATE New Mexico
14. PERMIT NO.	15. ELEVATIONS (Show whether DF, RT, GR, etc.) 7484' GR											

Check Appropriate Box To Indicate Nature of Notice, Report, or Other Data

NOTICE OF INTENTION TO:

TEST WATER SHUT-OFF

FRACTURE TREAT

SHOOT OR ACIDIZE

REPAIR WELL

(Other)

PULL OR ALTER CASING

MULTIPLE COMPLETION

ABANDON*

CHANGE PLANS

SUBSEQUENT REPORT OF:

WATER SHUT-OFF

FRACTURE TREATMENT

SHOOTING OR ACIDIZING

(Other) Spud and Set Casing

REPAIRING WELL

ALTERING CASING

ABANDONMENT*

(NOTE: Report results of multiple completion on Well Completion or Recompletion Report and Log form.)

17. DESCRIBE PROPOSED OR COMPLETED OPERATIONS (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work. If well is directionally drilled, give subsurface locations and measured and true vertical depths for all markers and zones pertinent to this work.)

Spud a 12 1/4" hole on 12-5-85 at 1900 hours. Drilled to 456'. Set 8 5/8", 24#, K-55 casing at 450' and cemented with 330 cu. ft. Class B. Circulated cement to surface. Pressure tested casing with 1000 psi for 30 minutes. Drilled a 7 7/8" hole to a TD of 8525' on 12-23-85. Set 5 1/2", 17.0# and 15.5#, K-55 casing at 8525'. Stage 1: cemented with 532 cu. ft. Class B 65:35 poz and tailed in with 616 cu. ft. Class B 50:50 poz. Stage 2: cemented with 1773 cu. ft. Class B 65:35 poz. Ran a temperature survey (attached) which indicates the top of the cement to be at 3800'. (See Temp Survey)
The DV tool was set at 1502' and the rig was released on 12-24-85.

RECEIVED
JAN 13 1986
OIL CON. DIV.
DIST. 3

I hereby certify that the foregoing is true and correct

SIGNED

BLS Shaw

TITLE Adm. Supervisor

(This space for Federal or State office use)

ACCEPTED FOR RECORD
DATE JAN 13 1986

APPROVED BY

CONDITIONS OF APPROVAL, IF ANY:

TITLE

DATE

FARMINGTON RESOURCE AREA

BY

*See Instructions on Reverse Side

NMOCC

RECEIVED

JAN 08 1986

BUREAU OF LAND MANAGEMENT
FARMINGTON RESOURCE AREA

WILSON SERVICE COMPANY

TEMPERATURE SURVEY

COMPANY.....Amoco Production.....

WELL.....#17.....LEASE.....Jicarilla 118.....

COUNTY.....Rio Arriba.....STATE.....New Mexico.....

SEC.....26.....TWP.....26N.....RGE.....3W.....

APPROX. TOP CEMENT.....3800'.....

Survey Begins at 2500'.....Ft. Ends at 5060'.....Ft.

Approx. Fill-Up.....Max. Temp.

Log Measured From KB.....Run No. 1.....

Casing Size	Casing Depth	Diam of Hole	Depth
5 1/2" from	to	from 7 7/8"	to
from	to	from	to

Date of Cementing.....12/24/85.....Time.....6:00 pm.....

Date of Survey.....12/25/85.....Time.....10:00 am.....


Amount of Cement.....As Per Report.....

Recorded by Bizzell.....Witnessed by.....

REMARKS OR OTHER DATA

DV Tool @ 5100'

TEMPERATURE IN DEGREES FAHRENHEIT

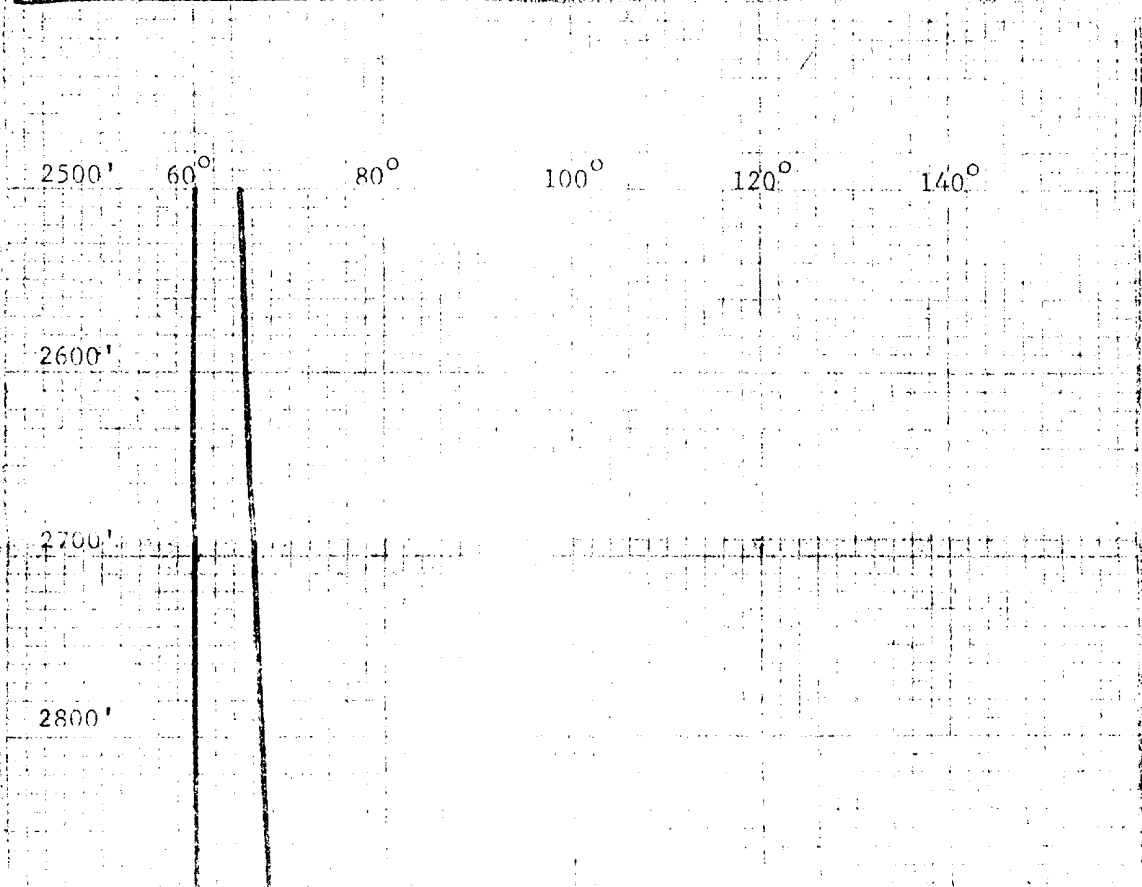

2600'

2700'

2800'

2900'

3000'

3100'

3200'

3300'

3400'

3500'

3600'

3700'

3800'

3900'

C/o Alamo from 3584' - 3800'
- Remedial Cementing Required

Anomaly at 3800'

3800'

Anomaly at 3800'

3900'

4000'

4100'

4200'

4300'

4400'

4500'

4600'

4700'

4800'

4900'

5000'

TD Surveyed at 5060'
