

Huerfano		1		Kay Kimbell		Lubbock, Texas	
LEASE NAME		WELL NO.		TEST NO.		LEASE OWNER	
OWNERS DISTRICT							
LOCATION Section 4 - TWP 25N - R10W		FIELD Wildcat		COUNTY San Juan		STATE New Mexico	
Date October 2, 1959 Ticket No. 189278 HOWCO DISTRICT Farmington, N. M. Kind of Job Open Hole Test		CONTRACTOR E. P. Campbell Drilling Company HOLE & TOOL DATA Elevation 6,708' G. L. Top Packer Depth 6,410' Total Depth 6,583' Bottom Packer Depth 6,415' Casing or Hole Size 8 3/4" Size & Type 7 3/4" ESA Liner or Rathole Size Bottom Choke 3/4" Casing Perforations Top Bottom Size Surface Choke 1" Interval Tested 168' ID & Lengths Air Chamber Formation Tested Dakota ID & Lengths Drill Collars 2 7/8" x 540' Est. Gauge Actual 190 Size Drill Pipe 3 1/2" I. F. MUD DATA Weight 9.1 Viscosity 70 All depths measured from Rotary Table No. Folders Reproduced 11 REMARKS: Tool opened with a fair blow decreasing to a weak blow at the end of the test. Gas to surface in 40 minutes.					
Initial Closed In Time Tool Open Flow Period Final Closed In Time		1st 2nd Minutes		120 Minutes			
Depth Top Gauge 6,420 Ft. BT P.R.D. No. 812 Pressure Readings Initial Hydro Mud Pressure 3,070 Initial Closed in Pres.		Blanked Off Yes 24/1747 Hr. Clock Office Corrected 3,124 104 176 1,458 3,039		Blanked Off Mr. Clock Office Corrected			
Initial Flow Pres. 100 Final Flow Pres. 175 Final Closed in Pres. 1,440 Final Hydro Mud Pressure 3,070		Field 3,124 104 176 1,458 3,039		Field Office Corrected			
Depth Center Gauge BT P.R.D. No. Pressure Readings Initial Hydro Mud Pressure Initial Closed in Pres. Initial Flow Pres. Final Closed in Pres. Final Hydro Mud Pressure		Ft. Mr. Clock Office Corrected Blanked Off Field Field Field Field Field		Blanked Off Mr. Clock Office Corrected Blanked Off Field Field Field Field Field			
Depth Bottom Gauge 6,580 Ft. BT P.R.D. No. 814 Pressure Readings Initial Hydro Mud Pressure 3,190 Initial Closed in Pres. Initial Flow Pres. 160 Final Flow Pres. 240 Final Closed in Pres. 1,515 Final Hydro Mud Pressure 3,190		Blanked Off Yes 12-1491 Hr. Clock Office Corrected 3,205 167 242 1,536 3,097		Blanked Off Mr. Clock Office Corrected Blanked Off Field Field Field Field Field			
Amount-Type of Casing		None				Witnessed By Mr. Ben Bungan Tester Mr. R. E. Moore	

← PRESSURE →

500
1000
1500
2000
2500
3000
3500





189278-812

TIME →

500
1000
1500
2000
2500
3000
3500

189278-814

EACH HORIZONTAL LINE EQUAL TO 1000 P.S.I.

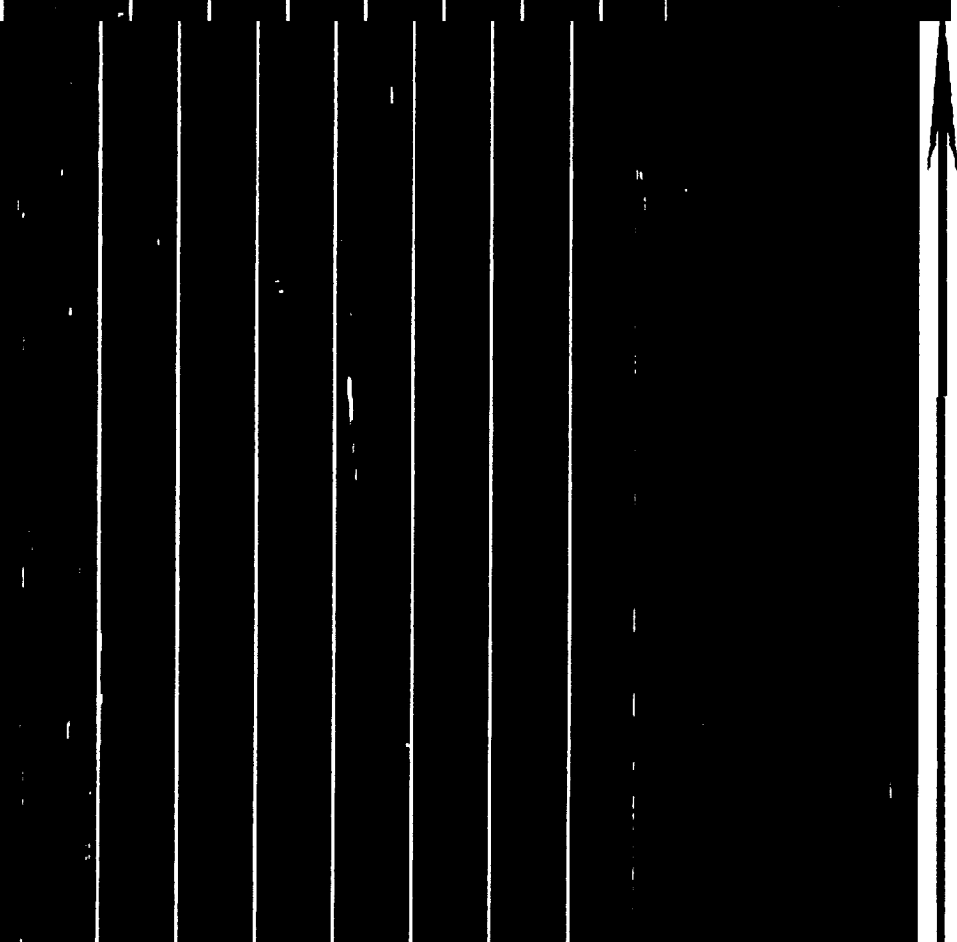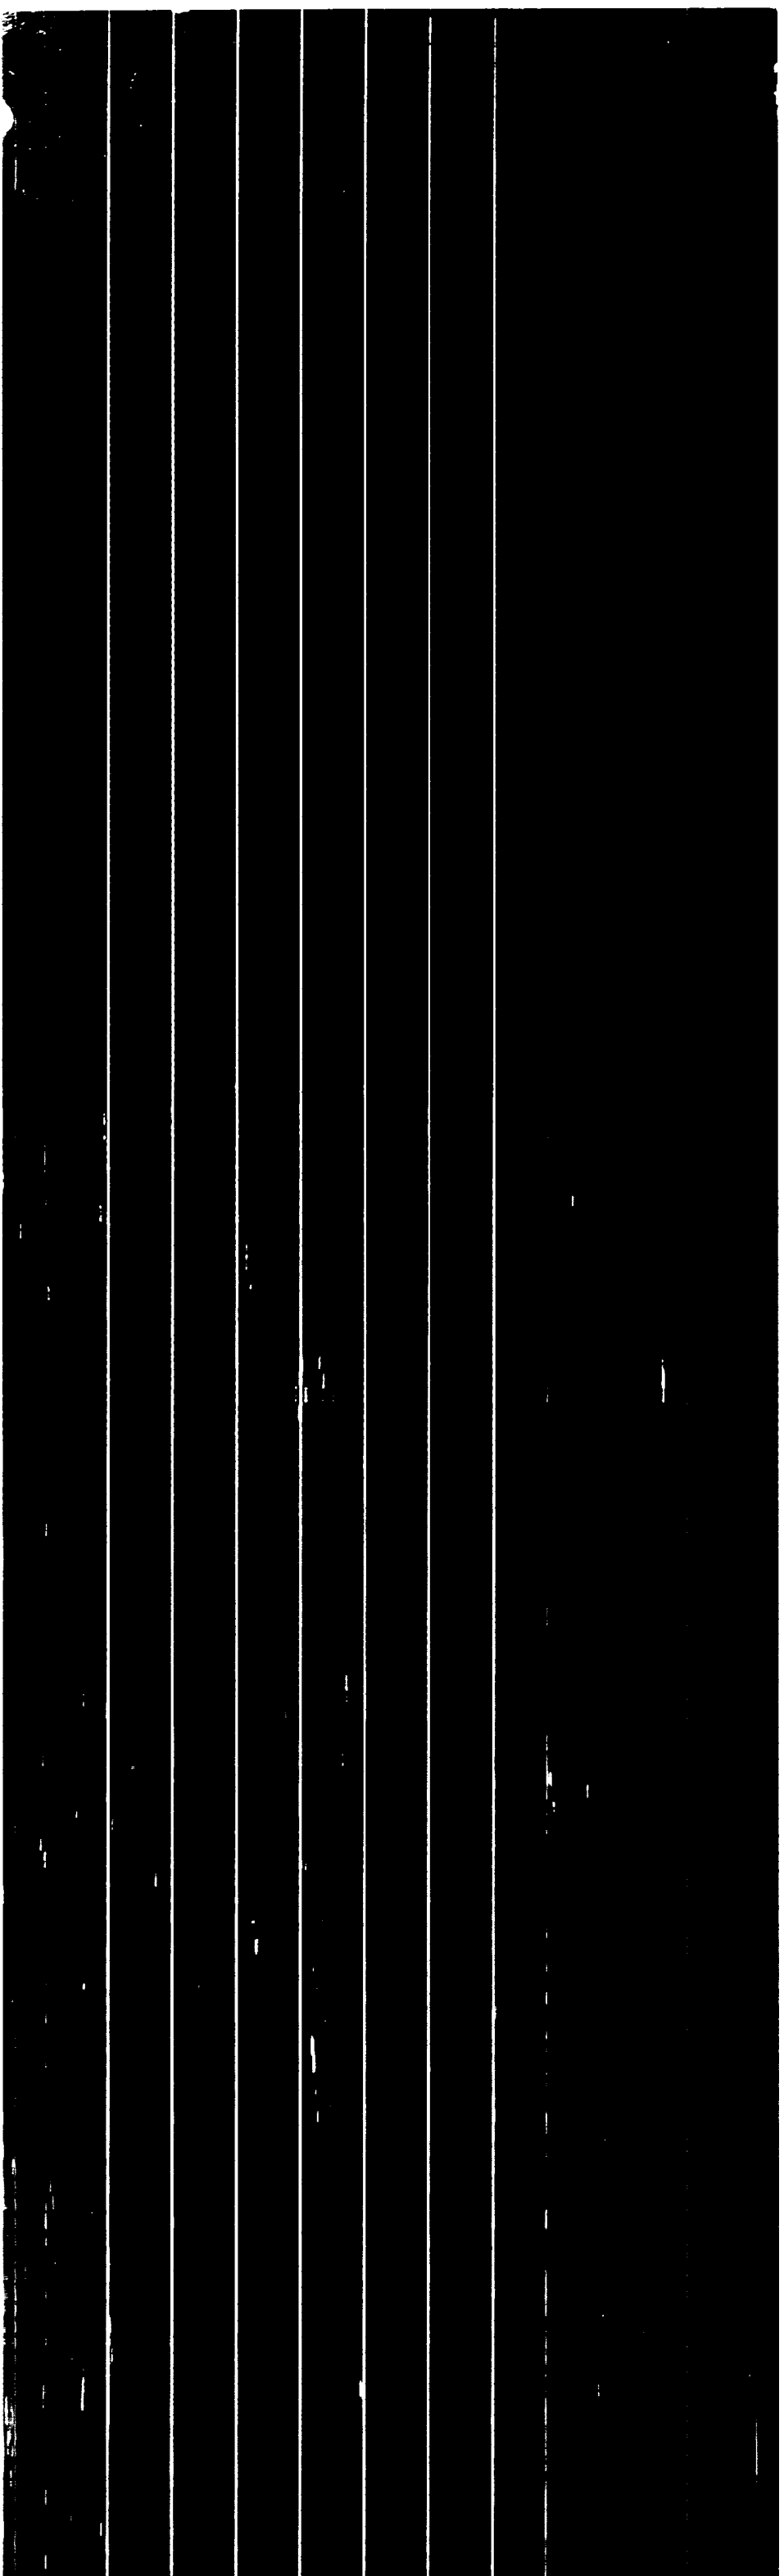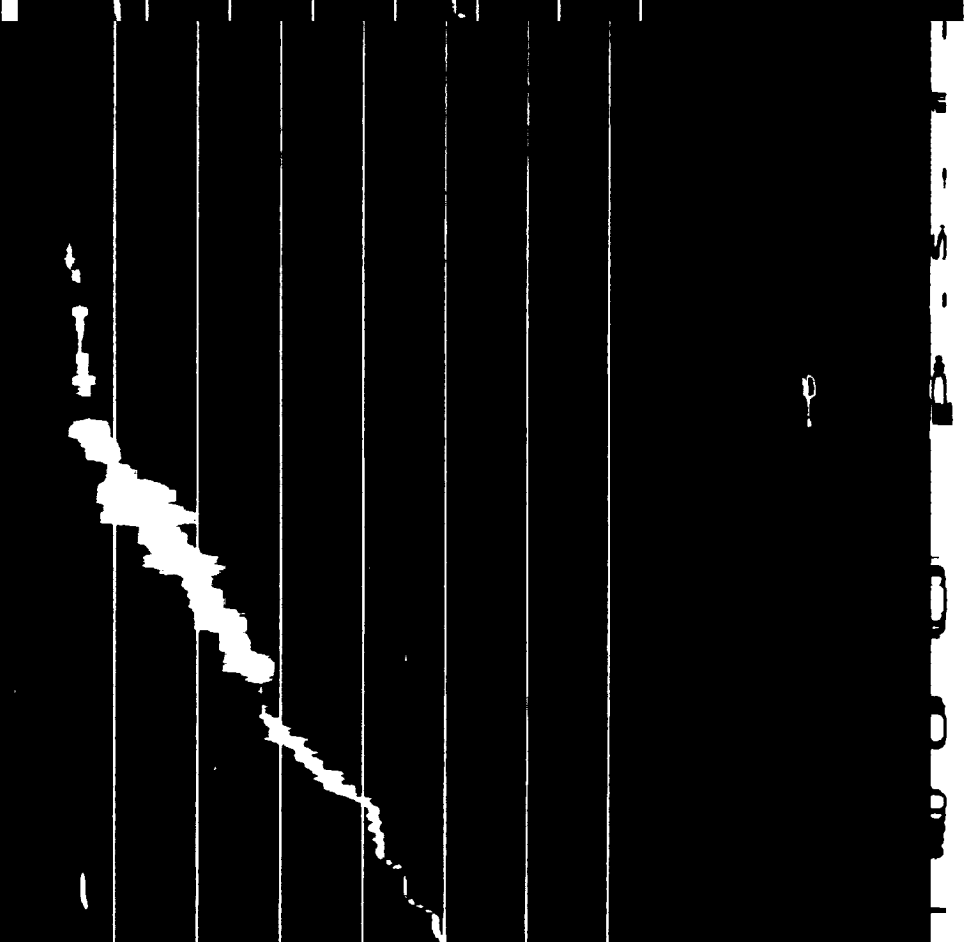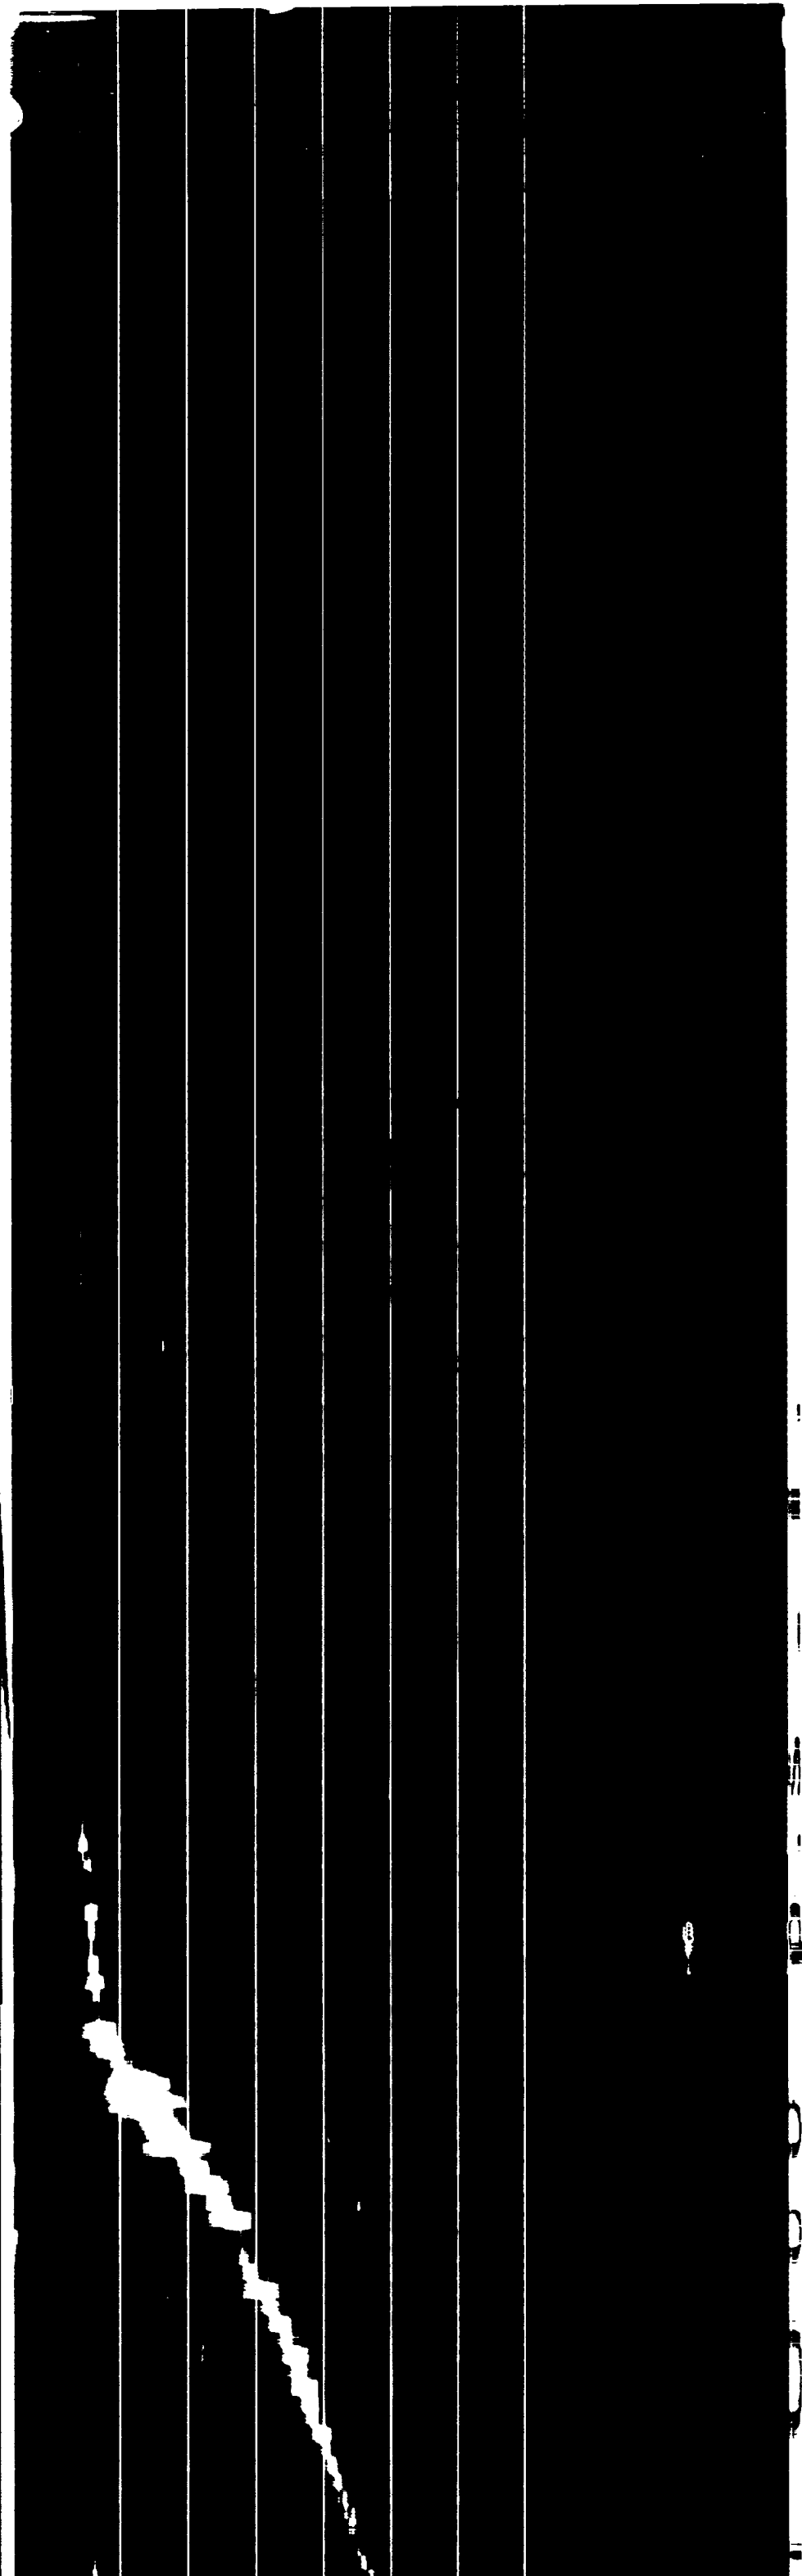

THE NEW.....

Formation Testing Service Report

