

Duplicate

UNITED STATES
DEPARTMENT OF THE INTERIOR
GEOLOGICAL SURVEY

APPLICATION FOR PERMIT TO DRILL, DEEPEN, OR PLUG BACK

1a. TYPE OF WORK
DRILL ☒ DEEPEN ☐ PLUG BACK ☐

b. TYPE OF WELL
OIL WELL ☐ GAS WELL ☒ OTHER ☐ SINGLE ZONE ☒ MULTIPLE ZONE ☐

2. NAME OF OPERATOR
Tenneco Oil Company

3. ADDRESS OF OPERATOR
. 720 So. Colorado Blvd., Denver, Colorado 80222

4. LOCATION OF WELL (Report location clearly and in accordance with any State requirements.)
At surface 790 FSL, 790 FWL

At proposed prod. zone
same as above

14. DISTANCE IN MILES AND DIRECTION FROM NEAREST TOWN OR POST OFFICE*
Approximately 2 miles NNW of Blanco, N.M.

15. DISTANCE FROM PROPOSED* LOCATION TO NEAREST PROPERTY OR LEASE LINE, FT.
(Also to nearest drilg. unit line, if any)

15. DISTANCE FROM PROPOSED* LOCATION TO NEAREST WELL DRILLING, COMPLETED, OR APPLIED FOR, ON THIS LEASE, FT.


21. ELEVATIONS (Show whether DF, RT, GR, etc.)
5884' GR

PROPOSED CASING AND CEMENTING PROGRAM

SIZE OF HOLE	SIZE OF CASING	WEIGHT PER FOOT	SETTING DEPTH	QUANTITY OF CEMENT
12 1/4"	9 5/8" new	36#	±250'	Circulate to surface
8 3/4"	7" new	23#	±2900'	Circulate to surface
6 1/4"	4 1/2" new	11.6#, 10.5#	±6950'	Circulate to liner top

See attached.

The gas is dedicated.



IN ABOVE SPACE DESCRIBE PROPOSED PROGRAM: If proposal is to deepen or plug back, give data on present productive zone and proposed new productive zone. If proposal is to drill or deepen directionally, give pertinent data on subsurface locations and measured and true vertical depths. Give blowout preventer program, if any.

24. SIGNED R. A. Mishler TITLE Sr. Production Analyst DATE Sept. 29, 1980

(This space for Federal or State office use)

PERMIT NO. APPROVED AS AMENDED APPROVAL DATE _____

APPROVED BY DEC 8 1980 TITLE _____ DATE _____
CONDITIONS OF APPROVAL James F. Sims
DISTRICT ENGINEER

*See Instructions On Reverse Side

**NEW MEXICO OIL CONSERVATION COMMISSION
WELL LOCATION AND ACREAGE DEDICATION PLAT**

OSM Form No. 100-2-1
Supersedes O-100
Effective 1-1-75

All distances must be from the outer boundaries of the Section


TENNECO OIL COMPANY			Lease: HOUCK		Well No. 1
Section 1	Township 29N	Range 10W	County San Juan		
Section 16000 Location of Well: 790 feet from the South line and 790 feet from the West line Ground Level Elev. 5834 Producing Formation Dakota Pool Basin Dakota Dedicated Acreage: 323 Acres					

1. Outline the acreage dedicated to the subject well by colored pencil or hatchure marks on the plat below.
2. If more than one lease is dedicated to the well, outline each and identify the ownership thereof (both as to working interest and royalty).
3. If more than one lease of different ownership is dedicated to the well, have the interests of all owners been consolidated by communitization, unitization, force-pooling, etc?

☒ Yes ☐ No If answer is "yes," type of consolidation Communitization is in progress.

If answer is "no," list the owners and tract descriptions which have actually been consolidated. (Use reverse side of this form if necessary.) _____

No allowable will be assigned to the well until all interests have been consolidated (by communitization, unitization, forced-pooling, or otherwise) or until a non-standard unit, eliminating such interests, has been approved by the Commission.

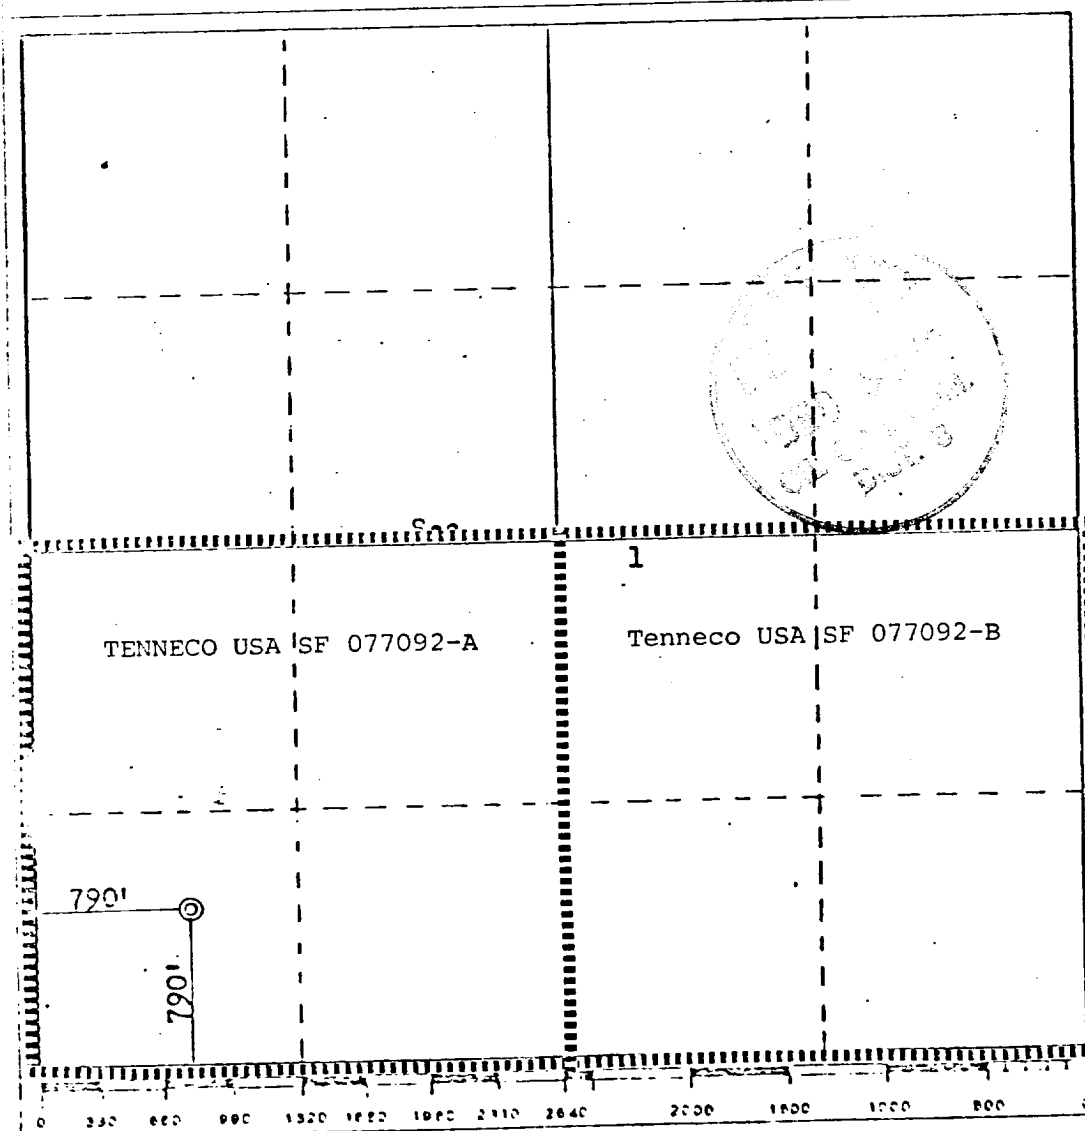

CERTIFICATION

I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief.

R. A. Mishler
Name

R. A. Mishler

Position

Sr. Production Analyst

Company

Tenneco Oil Company

Date

September 29, 1980

I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my knowledge and belief.

Date Surveyed

September 25, 1978

Registered Professional Surveyor and or Licensed Geologist

Fred B. Kerr, Jr.
Fred B. Kerr, Jr.

Continuation of Form O-100
3950

TECHNICAL OIL COMPANY
ROCKY MOUNTAIN DIVISION
PENTHOUSE, 720 SOUTH COLORADO BOULEVARD
DENVER, COLORADO 80222

DWILLING PROPERTIES

DATE: September 5, 1980

LEASE: Huck

WELL NO.: 1

LOCATION: 790 FSL, 790 FWE
Sec. 1, T29N, R10W
San Juan County, New Mexico

FIELD: Basin Dakota

ELEVATION: 5884, Est. G.L.

TOTAL DEPTH: 6950'

PROJECTED HORIZON: Dakota

SUBMITTED BY:

B.W. Harris

DATE:

9-8-80

APPROVED BY:

B. Barnes

DATE:

9/8/80

CC: Administration
DSB Well File
Field File

ESTIMATED FORMATION TOPS

Ojo

Fruitland

Pictured Cliffs

2360'

Gas

Lewis

2440'

Shale

Cliff House

4015'

Gas

M. ...

Point Lookout

4615'

Gas

Mancos

Shale

Gallup

5870'

Gas/Oil

Greenhorn

6610'

Limestone

Dakota

6725'

Gas

T.D.

DRILLING, CASING AND CEMENTING PROGRAM.

1. MIRURT
2. Drill a 12 $\frac{1}{4}$ " Hole to \pm 250' with Gel-Water Mud.
3. RU and run 9 5/8" 36# K-55 ST&C casing to TD. Cement with Class B + 2% CaCl_2 in sufficient quantity to circulate cement to surface. WOC 12 hours.
4. Screw on 9 5/8 8rd x 11-3000 casing head, NU BOPS. Pressure test casing, lines and blinds to 1000 PSI for 30 minutes. GIH with drill pipe and test pipe rams to 1000 PSI for 30 minutes. Record all tests on IADC Report.
5. Drill out using an 8 3/4" Bit and clear water. Drill to 2900'. Mud up prior to reaching intd. TD.
6. RU and run 7" 23# K-55 ST&C casing to bottom. Cement with 50:50 Pozmix, 4% Gel; tailed with 150 sx Class B + 2% CaCl_2 . Circulate cement to surface. WOC 18 hours.
7. Set slips and cut-off casing. GIH with 6 $\frac{1}{2}$ " Bit and 3 $\frac{1}{2}$ " drilling assembly. Pressure test to 1000 PSI for 30 minutes. Record tests on IADC Report.
8. RU to Gas Drill. Drill to within 5' of shoe with water, unload hole with N_2 . Drill a few feet of new formation and blow with gas until dusting.
9. Drill a 6 $\frac{1}{2}$ " hole to TD with gas. Log open hole as directed by G.E. Department.
10. Run 4 $\frac{1}{2}$ " 11.6 and 10.50# K-55 ST&C as designed as a liner. Have 150' overlap inside the 7" casing. Cement with 50:50 Pozmix, 4% Gel; tailed by 100 sx of Class B. Use a fluid loss additive in the lead slurry and circ cement to liner top.
11. Circulate out excess cement, LDDP and MORT.
12. Install tree and fence reserve pit.
13. If non-productive, P & A as required by the USGS.

Casing Program

<u>Interval</u>	<u>Length</u>	<u>Size</u>	<u>Weight</u>	<u>Grade</u>	<u>Coupling</u>
0-250	250	9 5/8	36#	K-55	STC
0-2900	2900	7	23#	K-55	STC
2700-6950	4250	4 1/2	10.5#	K-55	STC

MUD PROGRAM

- 0-250 Spud mud.
- 250-2900 Low solid, fresh water mud. (Water and Benex.) Mud up prior to running casing.
- 2900-TD Gas.

EVALUATION

Cores and DST's: None.

Deviation Surveys:

1. Survey surface hole at 100' intervals. Maximum allowable deviation at 500' is $1\frac{1}{2}^{\circ}$.
3. From surface to total depth, deviation surveys must be taken every 500' on each trip, whichever is first. This may entail running the TOTCO on wire line. Record each survey on the IADC Drilling Report Sheet. Maximum allowable change in deviation is 1° per 100'. Maximum deviation allowable is 5° .

Samples: As requested by Wellsite Geological Engineer.

Logs: 1. GR/IND FDC-GR-Cal TD to MW

BLOWOUT EQUIPMENT

11" - 3000 BOP with rotating head to comply with TOC requirements as shown in BOE arrangement, Figure C. Preventers must be checked for operation every 24 hours with each check recorded on the IADC Drilling Report Sheet.

REPORTS

Drilling reports for the past 24 hours will include depth, footage, time distribution, activity breakdown, mud properties, bit record, bottom hole assembly, daily and cumulative mud costs, plus any other pertinent information, will be called into Tenneco Oil Company, Denver, Colorado, between 7:30 a.m. and 8:00 a.m.

1. 303-758-7130 (Office) Don Barnes
303-93-7287 (Office) Don Barnes' private line, Monday-Friday (before 7:45 a.m.)
303-93-0704 (Home) Don Barnes, weekends and holidays.
2. John Owen (Home) 303-795-0221

The yellow sheet of the IADC Report is to be filled out completely. The original copy of the drilling time recorder, and copies of any invoices for this well, signed and received for Tenneco Oil Company, will be mailed daily to:

TENNECO OIL COMPANY
ROCKY MOUNTAIN DIVISION
PENTHOUSE, 720 SOUTH COLORADO BOULEVARD
DENVER, COLORADO 80222

ATTENTION: Drilling Department

IN CASE OF EMERGENCY, NOTIFY THE FOLLOWING:

1. Mr. Don Barnes, Division Drilling Engineer.
2. Mr. John W. Owen, Project Drilling Engineer.
3. Mr. Mike Lacey, Division Production Manager (Home 303-979-0509).

TENNECO OIL COMPANY - 10 POINT PLAN

1. The geological name of the surface formation: Tertiary San Jose
- 2 & 3. Estimated Formation Tops:


(See Attached Drilling Procedure)
4. Proposed Casing Program:

(See Attached Drilling Procedure)
5. Blowout Preventors:
Hydraulic double ram. One set of rams will be provided each size drill pipe in the hole. One set of blind rams at all times. Fill line will be 2", kill line will be 2", choke relief line will be 2". BOP's, drills and tests will be recorded in the driller's log. BOP will be tested every 24 hours and recorded in IADC Log.
6. Mud Program: (Sufficient quantity of mud and weight material will be available on location).

(See Attached Drilling Procedure.)
7. Auxiliary Equipment:
 - a. Kelly cock will be in use at all times.
 - b. Stabbing valve to fit drill pipe will be present on floor at all times.
 - c. Mud monitoring will be visual. No abnormal pressures are anticipated.
 - d. Floats at bits.
 - e. Drill string safety valve(s) to fit all pipe in drill string will be maintained on the rig floor while drilling operations are in progress.
8. Coring, Logging, and Testing Program:

(See Attached Drilling Procedure)
9. No abnormal pressures, temperatures or potential hazards such as H₂S are expected to be encountered.
10. The drilling of this well will start approximately (Feb. 1981) and continue for 10 to 12 days.

Your office will be notified of spudding in sufficient time to witness cementing operations. Immediate notice will be given on blowouts, fires, spills, and accidents involving life threatening injuries or loss of life. Prior approval will be obtained before appreciably changing drilling program or commencing plugging operations, plug back work, casing repair work or corrective cementing operations.

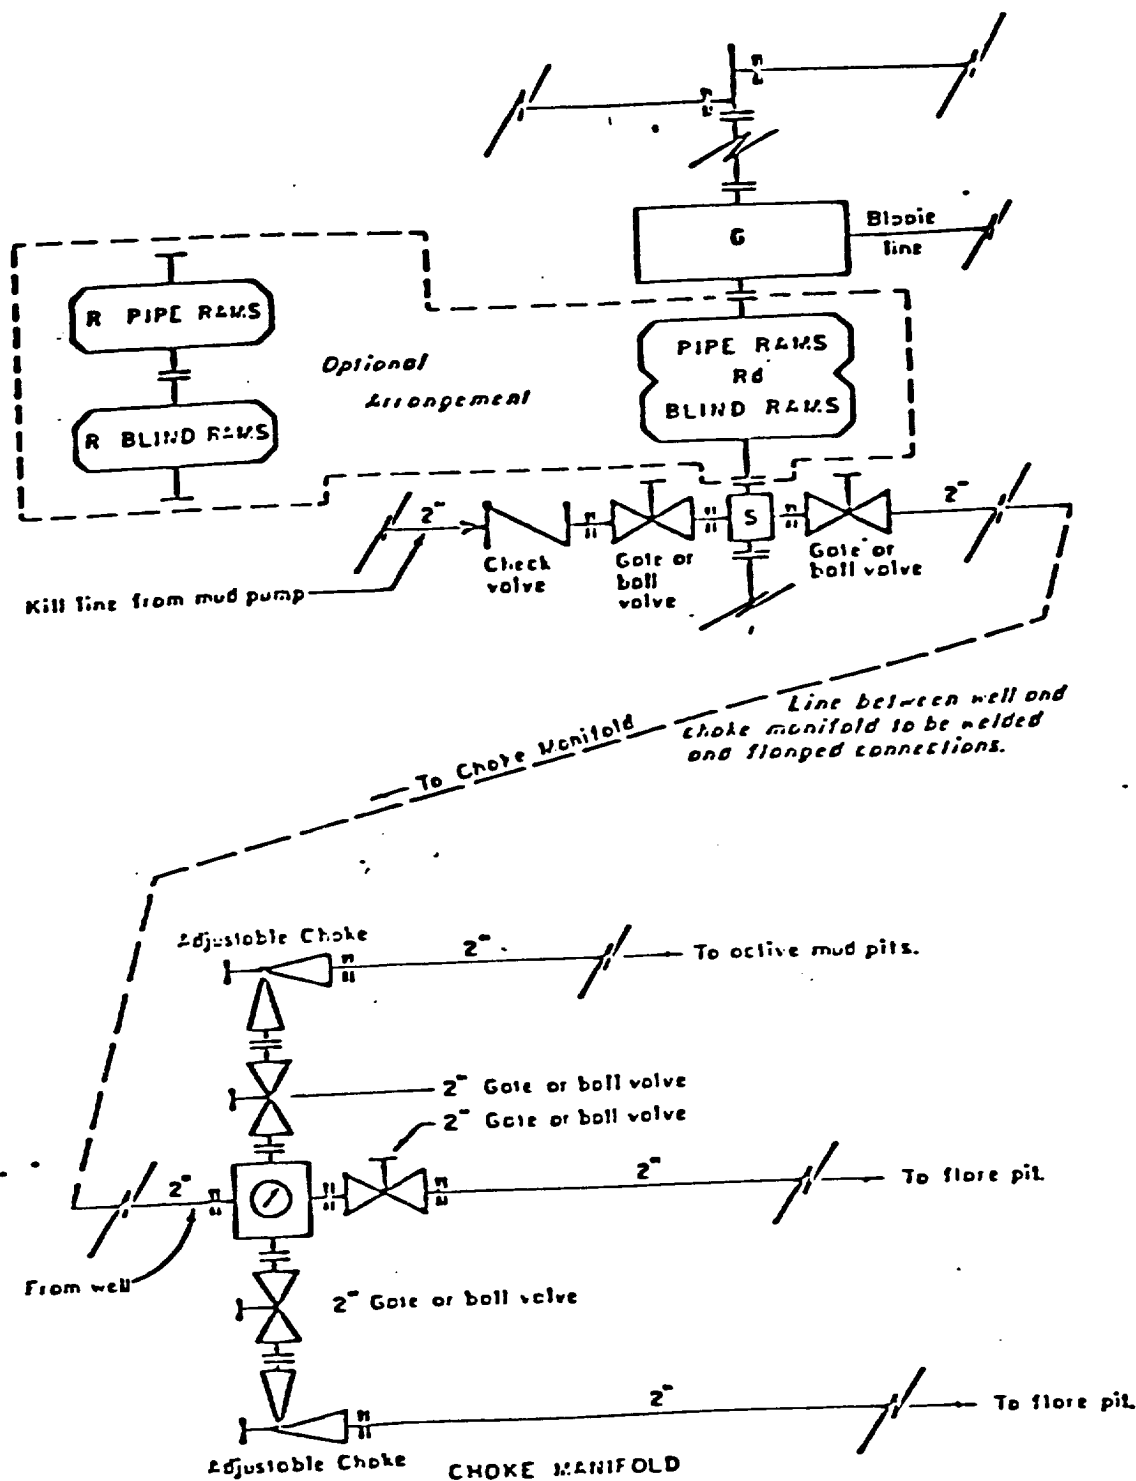

- All equipment to be 3,000 psi working pressure except as noted.
- Rd Double ram type preventer with two sets of rams.
 - R Single ram type preventer with one set of rams.
 - S Drilling spool with side outlet connections for choke and kill lines.
 - G Rotating head 150 psi working pressure minimum


ARRANGEMENT C

TENNECO OIL COMPANY
ROCKY MOUNTAIN DIVISION
REQUIRED MINIMUM
BLOWOUT PREVENTER AND
CHOKE MANIFOLD

J. MAGILL 10-26-78 EVI

1. Existing Road - Please refer to Map No. 1 which shows the existing roads. New roads which will be required have been marked on this map. All existing and new roads will be properly maintained during the duration of this project.
2. Planned Access Roads - Please refer to Map No. 1. The grade of the access roads will be consistent with that of the local terrain. The road surface will not exceed twenty feet (20') in width. Upon completion of the project, the access road will be adequately drained to control soil erosion. Drainage facilities may include ditches, water bars, culverts or any other measure deemed necessary by trained Company personnel to insure proper drainage. Gates and/or cattleguards will be installed if necessary.
3. Location of Existing Wells - Please refer to Map No. 2.
4. Location of Tank Batteries, Production Facilities, and Production Gathering and Service Lines - Please refer to Maps No. 1 and No. 2. Map No. 2 shows the existing roads and new proposed access roads. All known production facilities are shown on these two maps.
5. Location and Type of Water Supply - Water for the proposed project will be obtained from a private source.
6. Source of Construction Materials - No additional materials will be required to build either the access road or the proposed location.
7. Methods of Handling Waste Materials - All garbage and trash materials will be put into a burn pit shown on the attached Location Plat No. 1. When clean-up operations are begun on the proposed project, the burn pit with its refuse will be buried to a depth of at least three feet (3'). A latrine, the location of which is also shown on Plat No. 1. will be provided for human waste. If large amounts of liquids are left in the reserve pit after completion of the project, the pit will be fenced until the liquids have had adequate time to dry. The location clean-up will not take place until such time as the reserve pit can be properly covered over to prevent run-off from carrying any of these materials into the watershed. No earthen pit will be located on natural drainage; all earthen pits will be so constructed as to prevent leakage from occurring.

8. Ancillary Facilities - No camps or airstrips will be associated with this project.
9. Wellsite Layout - Please refer to the attached Plat No. 1.
10. Plans for Restoration of the Surface - After completion of the proposed project the location will be cleaned and leveled. The location will be left in such a condition that will enable reseeding operations to be carried out. Seed mixture as designated by the responsible government agency will be used. The reseeding operation will be performed during the time period set forth by the regulatory body. The location production equipment will be painted as designated by the responsible government agency.
11. Other Information - The proposed site is on a relatively flat area approximately $1\frac{1}{2}$ miles west of the San Juan River. Some large rock formations are present.
12. Operator's Representative - See drilling prognosis.
13. Certification -
I hereby certify that I, or persons under my direct supervision, have inspected the proposed drillsite and access route; that I am familiar with the conditions which presently exist; that the statements made in this plan are, to the best of my knowledge, true and correct; and that the work associated with the operations proposed herein will be performed by Tenneco Oil Company and its contractors and sub-contractors in conformity with this plan and the terms and conditions under which it is approved.



R. A. Mishler
Sr. Production Analyst


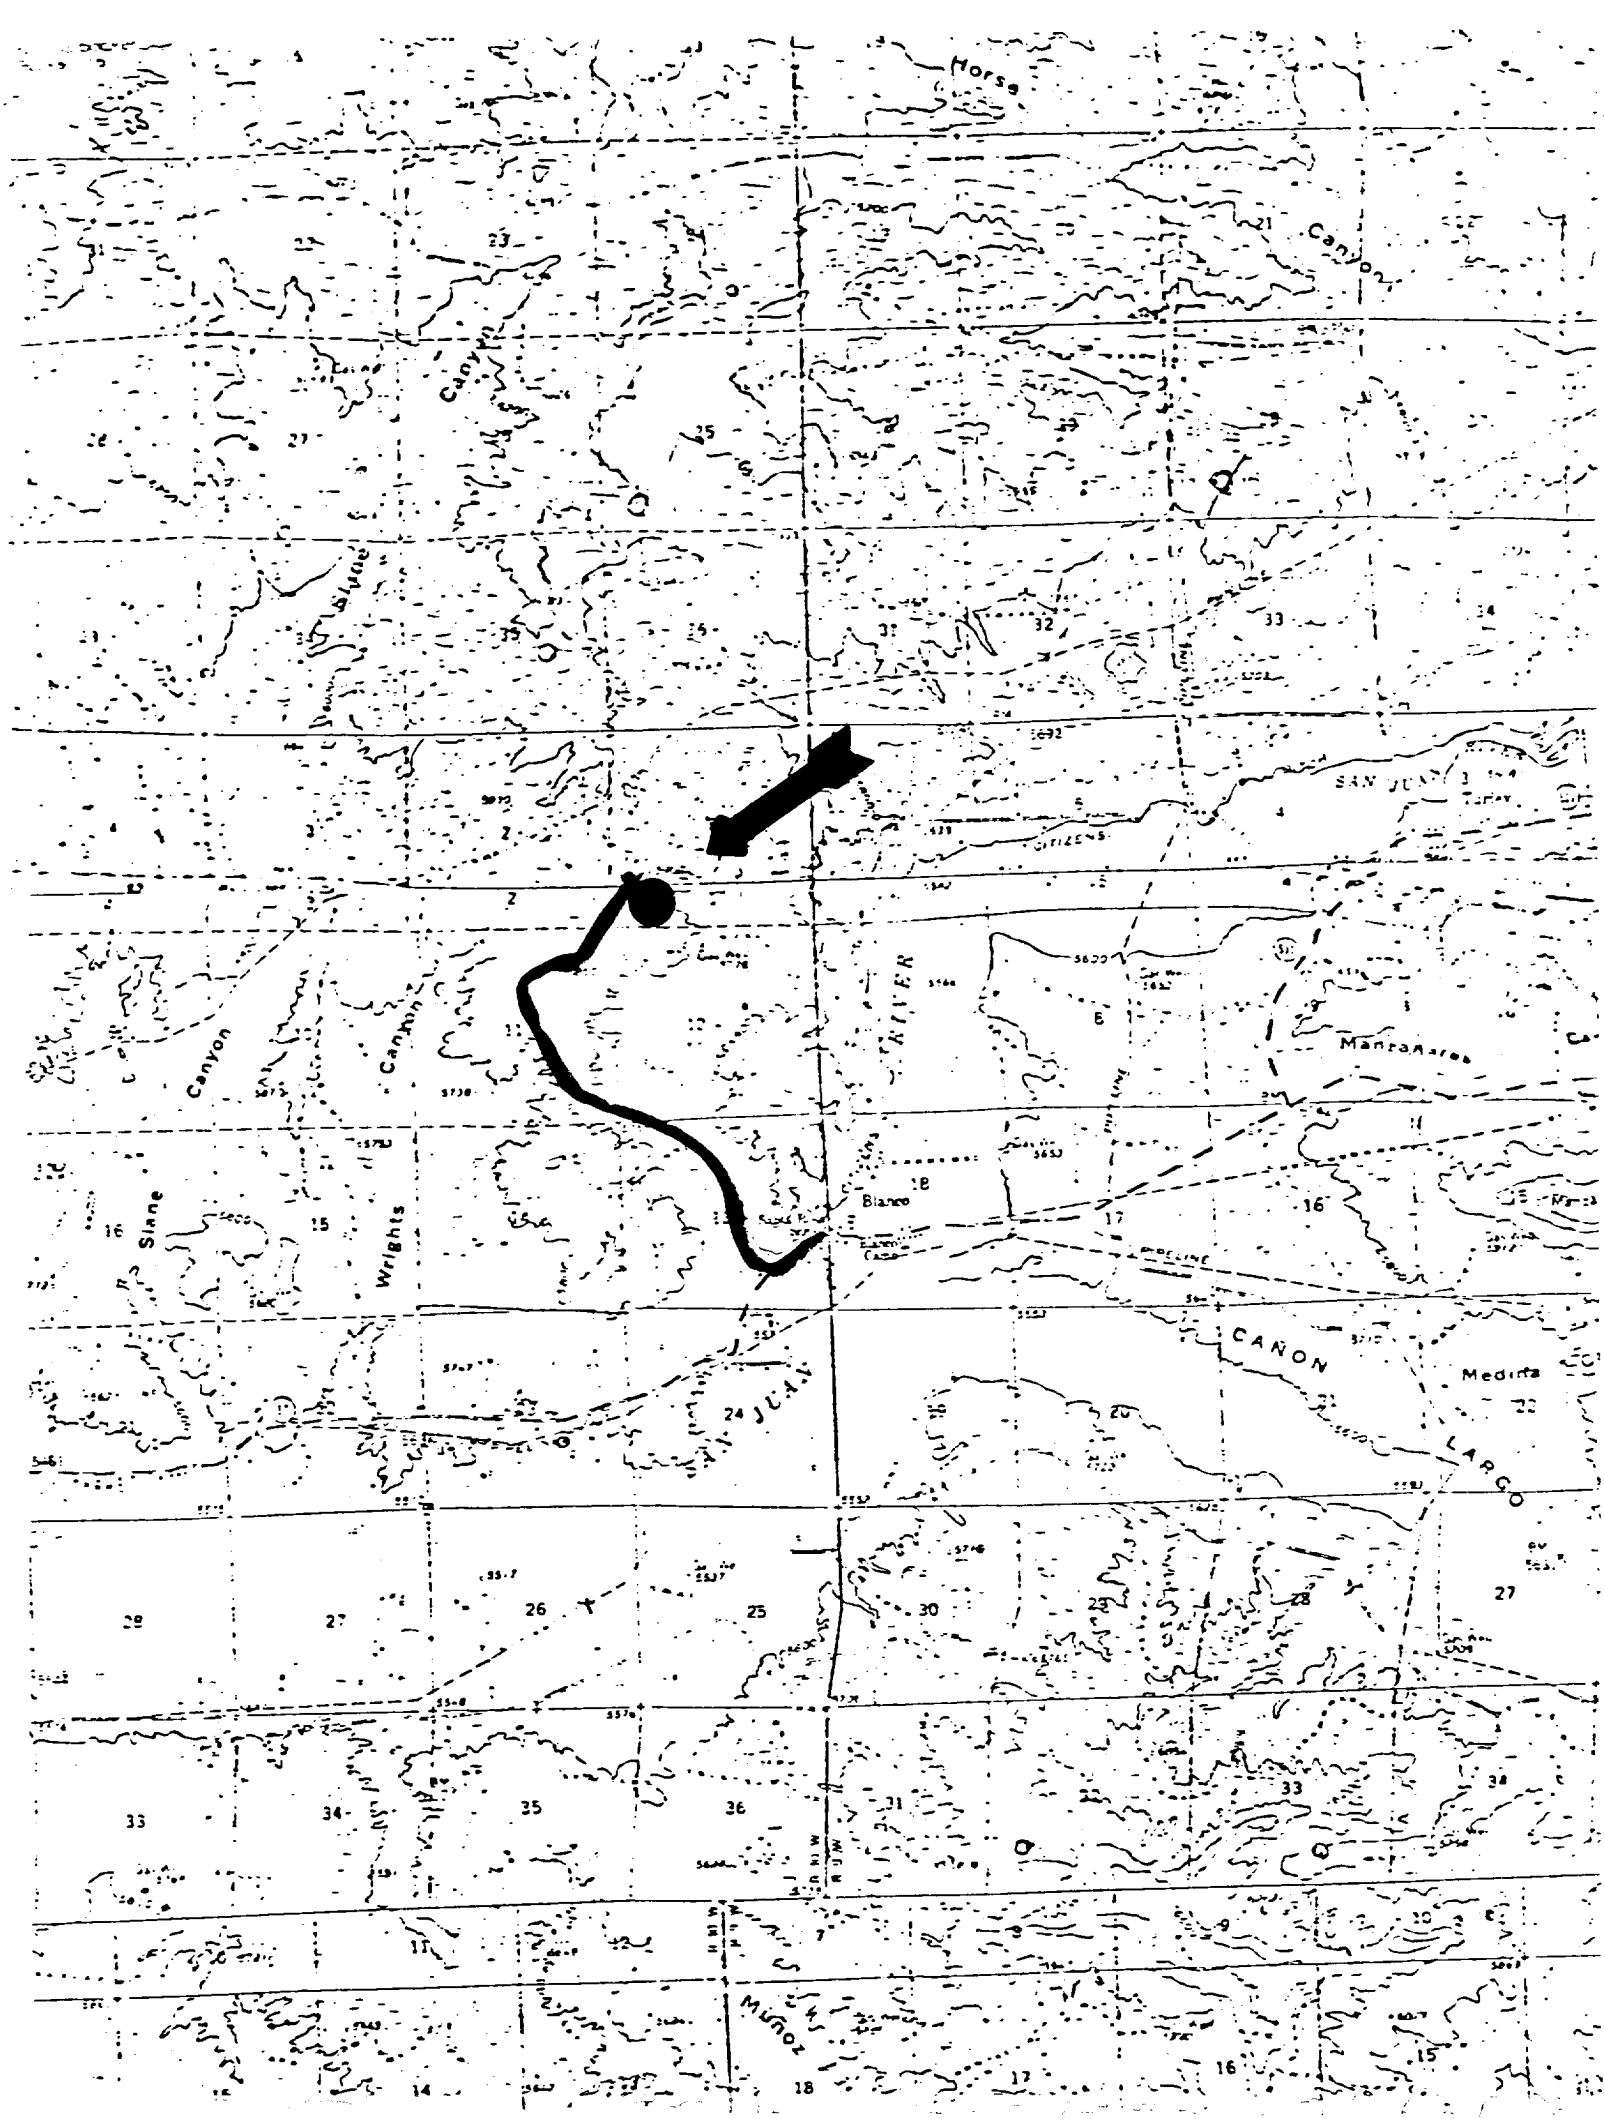


EXHIBIT II

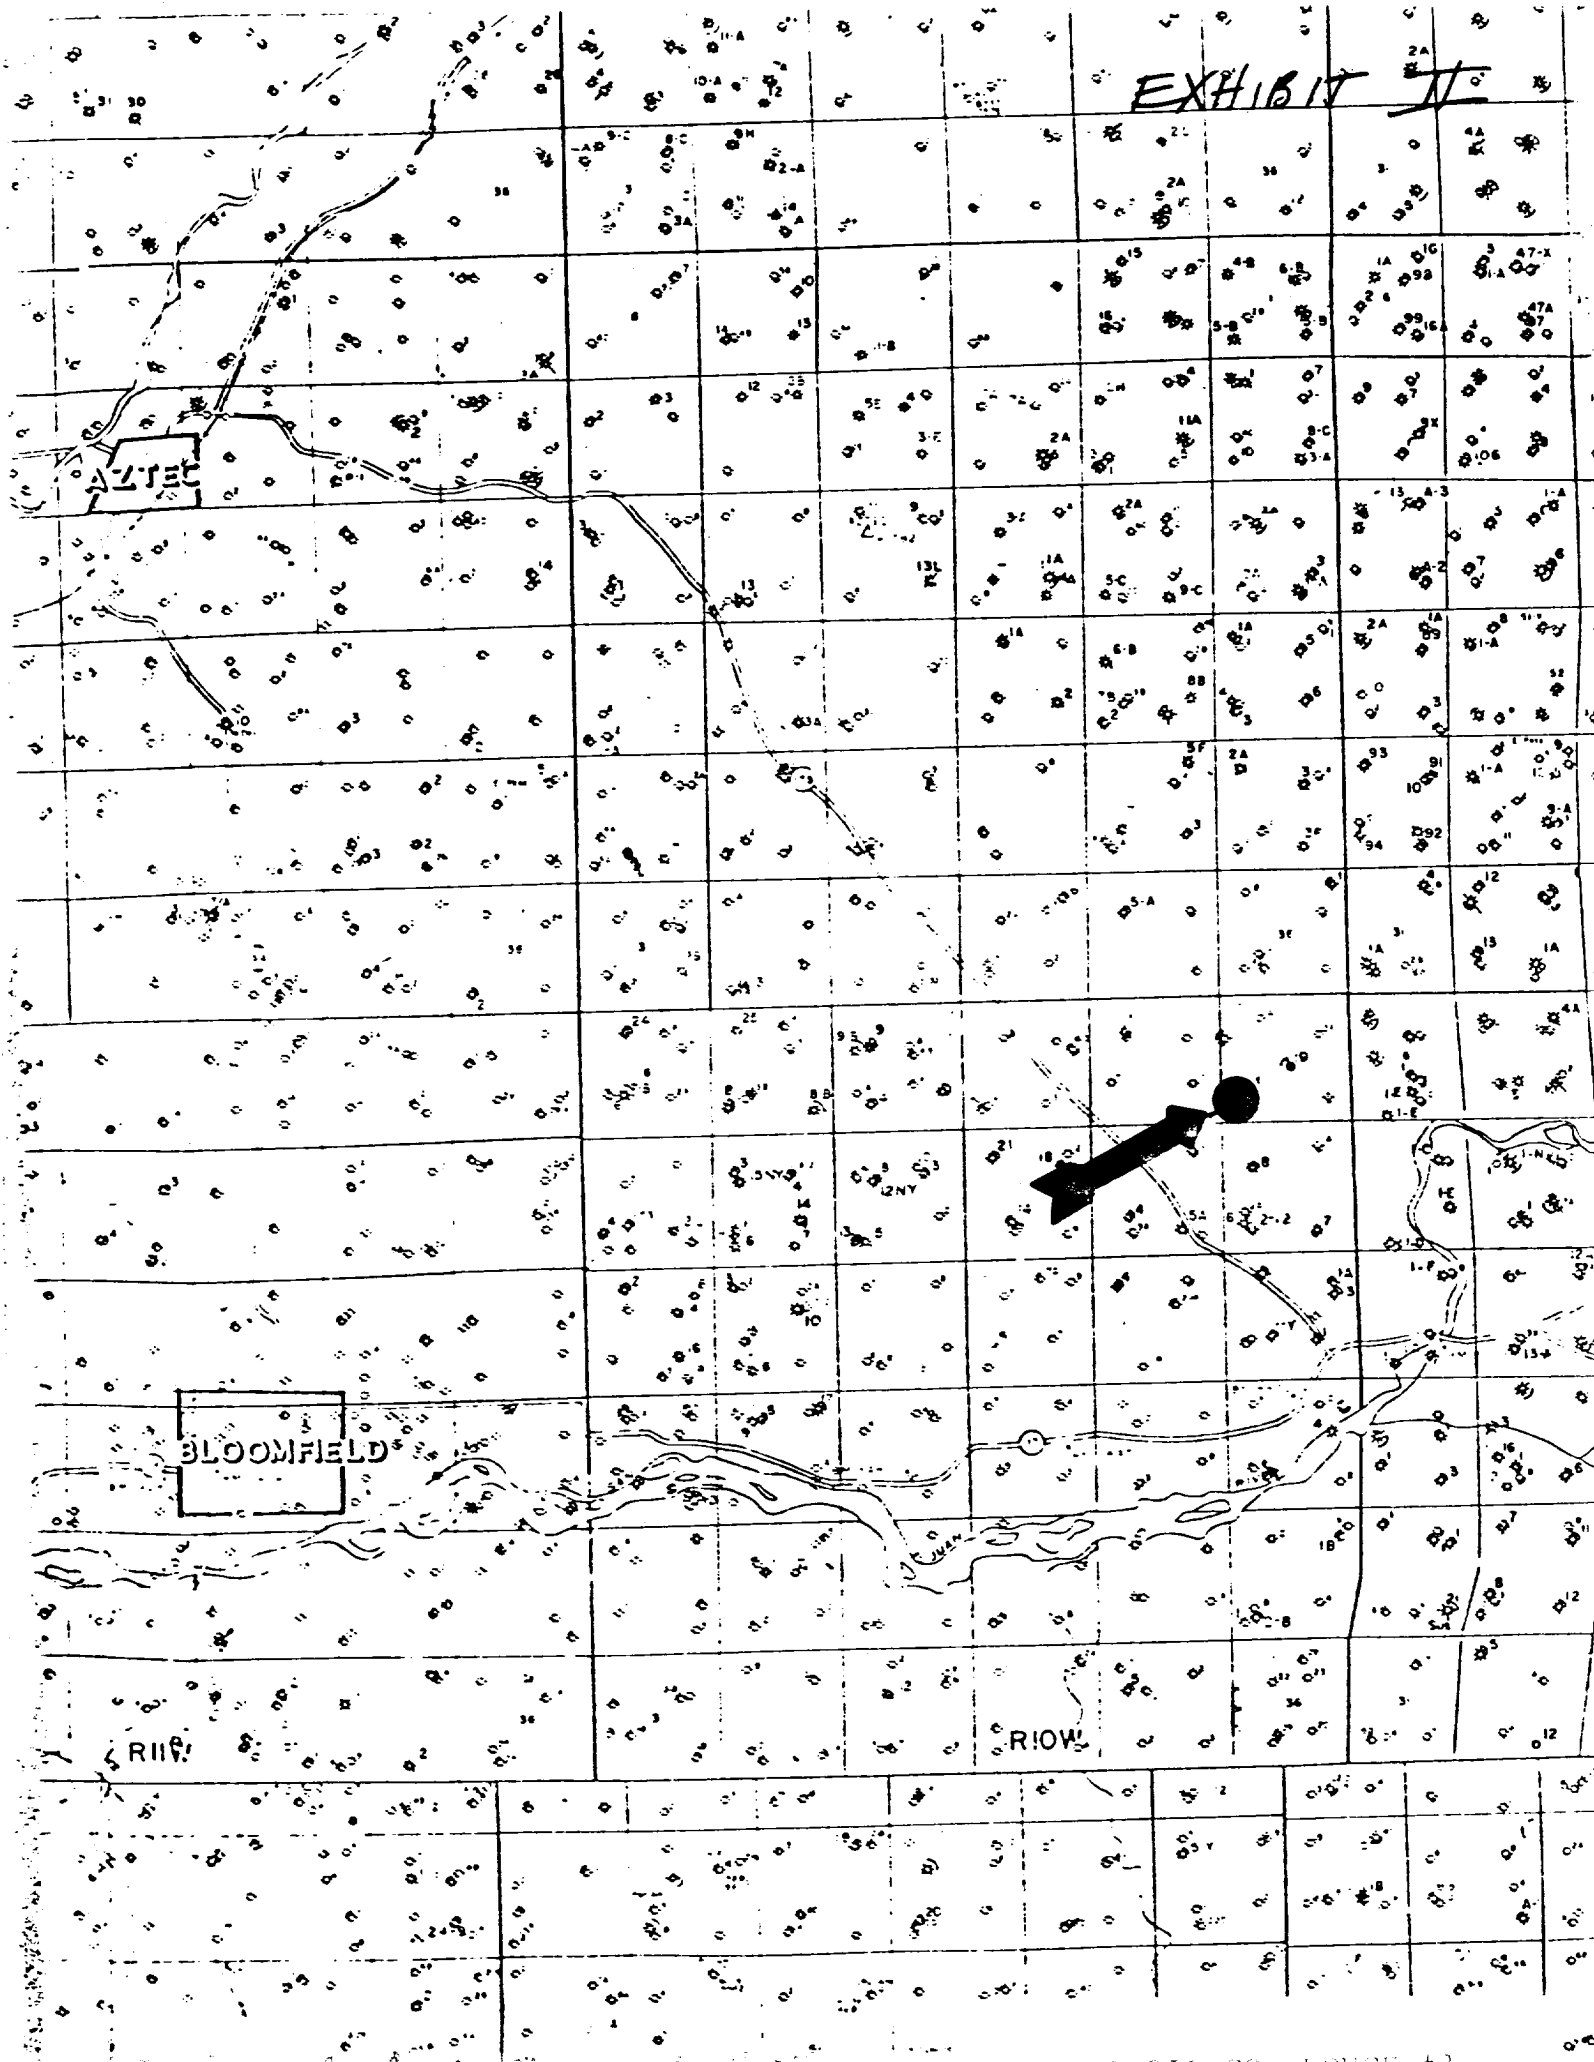

TENNECO OIL COMPANY

CALCULATION SHEET

EXHIBIT III

COMPANY

SUBJECT *Drilling Well Site Layout* HOUCK #1

LOCATION SW/SW SEC. 1, T 29N, R 10W, San Juan BY

