



ADA
3/13/02

NEW MEXICO STATE 36-2

CURRENT COMPLETION

LOCATION:


970' FNL & 1275' FEL
Sec.36, T30N, R10W
San Juan County, NM

SPUD DATE: 6/29/2001

ELEVATION: 5858' GL
5872' KB

FRUITLAND PERFORATIONS:

Perforate 4 SPF (2394'-2406'),
(2348'-2354'), (2332'-2338'),
(2311'-2330'), (2290'-2302') ; Delta Frac
149,517 Gal. and 275,000 # of 20/40
sand using sandwedge.

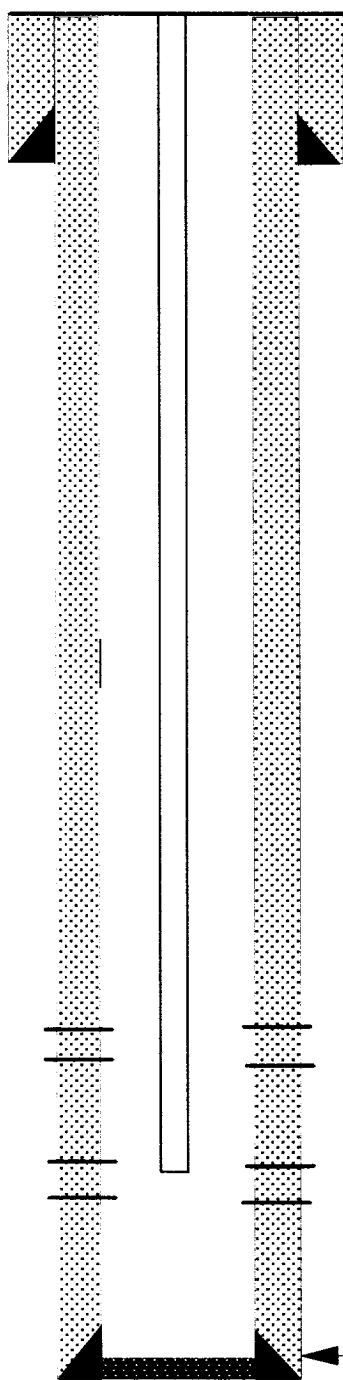

8 5/8", 24 #, K-55 ST&C CSG.
Set @ 362' in 12 1/4" Hole
w/ 240 SX Class G CMT
Circ. 70 bbls. of Cement to
Surface.

79 JOINTS 2-3/8" EUE J-55 tubing
EOT 2449'



5 1/2", 17#, J-55, LT&C CSG
Set @ 2553' in 7 7/8" Hole
Float Collar at 2479'. CMT w/ 440
SX Class G Cement. Circulate 7
bbls. of cement to surface

TD - 2553'
