



ADA  
3/13/02

## NEW MEXICO STATE 32-2

### CURRENT COMPLETION

#### LOCATION:

905' FNL & 1830' FWL  
Sec. 32, T30N, R11W  
San Juan County, NM

SPUD DATE: 6/21/2001

ELEVATION: 5906' GL  
5919' KB


8 5/8", 24 #, K-55 ST&C CSG.  
Set @ 368' in 12 1/4" Hole  
w/ 240 SX Class G CMT  
Circ. 10 bbls. of Cement to  
Surface.



75 Joints 2-3/8" EUE J-55 tubing  
EOT 2202'

#### FRUITLAND PERFORATIONS:

Perforate 4 SPF  
(2118'-2140'), (2059'-2069'),  
(2026'-2034'), (1942'-1946') ; Delta Frac  
w/ 123,625 Gal. and 225,000 # of 20/40  
sand using sandwedge.

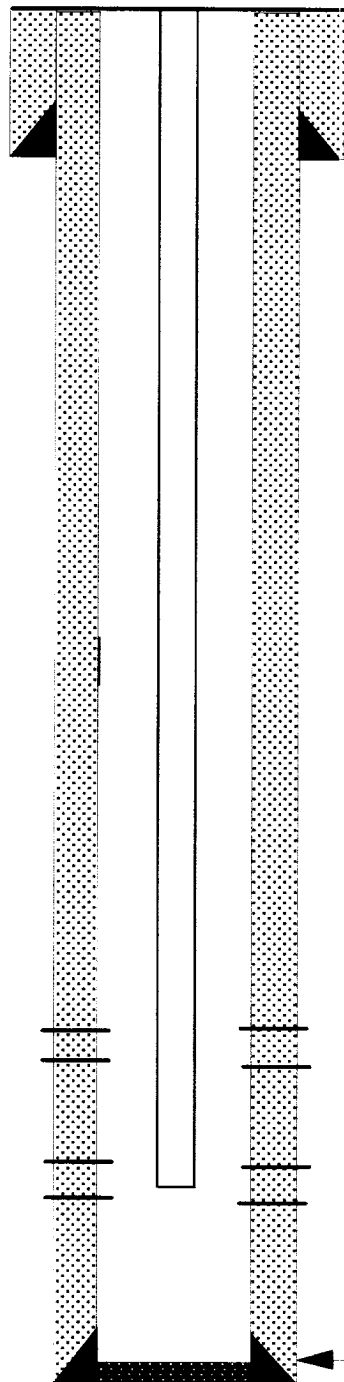

TD - 2310'

5 1/2", 17#, J-55, LT&C CSG  
Set @ 2310' in 7 7/8" Hole  
Float Collar at 2220'. CMT w/ 380  
SX Class G Cement. Circulate 3  
bbls. of cement to surface
