

State of New Mexico  
Energy, Minerals and Natural Resources Department  
Oil Conservation Division

Sundry Notices and Reports on Wells

<p>1. Type of Well GAS</p> <hr/> <p>2. Name of Operator <b>BURLINGTON RESOURCES</b> OIL &amp; GAS COMPANY</p> <hr/> <p>3. Address &amp; Phone No. of Operator PO Box 4289, Farmington, NM 87499 (505) 326-9700</p> <hr/> <p>4. Location of Well, Footage, Sec., T, R, M 790' FSL, 1595' FWL, Sec. 12, T-32-N, R-7-W, NMPM, San Juan County, NM</p>	<p>API # (assigned by OCD) 30-045-27175</p> <p>5. Lease Number FEE</p> <p>6. State Oil&amp;Gas Lease #</p> <p>7. Lease Name/Unit Name Allison Unit</p> <p>8. Well No. #125</p> <p>9. Pool Name or Wildcat Basin Fruitland Coal</p> <p>10. Elevation:</p>
--	--

Type of Submission	Type of Action	
<input checked="" type="checkbox"/> Notice of Intent	<input type="checkbox"/> Abandonment	<input type="checkbox"/> Change of Plans
<input type="checkbox"/> Subsequent Report	<input type="checkbox"/> Recompletion	<input type="checkbox"/> New Construction
<input type="checkbox"/> Final Abandonment	<input type="checkbox"/> Plugging Back	<input type="checkbox"/> Non-Routine Fracturing
	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> Water Shut off
	<input type="checkbox"/> Altering Casing	<input type="checkbox"/> Conversion to Injection
	<input checked="" type="checkbox"/> Other - Pump Installation	

13. Describe Proposed or Completed Operations

It is intended to install a pump on the subject well according to the attached procedure and wellbore diagram.

**RECEIVED**  
MAY 10 1999  
OIL CON. DIV  
DIST. 3

SIGNATURE *Charlie T. Perrin* Regulatory Administrator \_\_\_\_\_ May 6, 1999 \_\_\_\_\_

trc

(This space for State Use)

ORIGINAL SIGNED BY CHARLIE T. PERRIN


DEPUTY OIL & GAS INSPECTOR, DIST. #3

Approved by \_\_\_\_\_ Title \_\_\_\_\_ Date MAY 10 1999

## Allison #125

Basin Fruitland Coal  
Unit N, Section 12, T32N, R7W, San Juan, New Mexico

Completed: 1/24/89

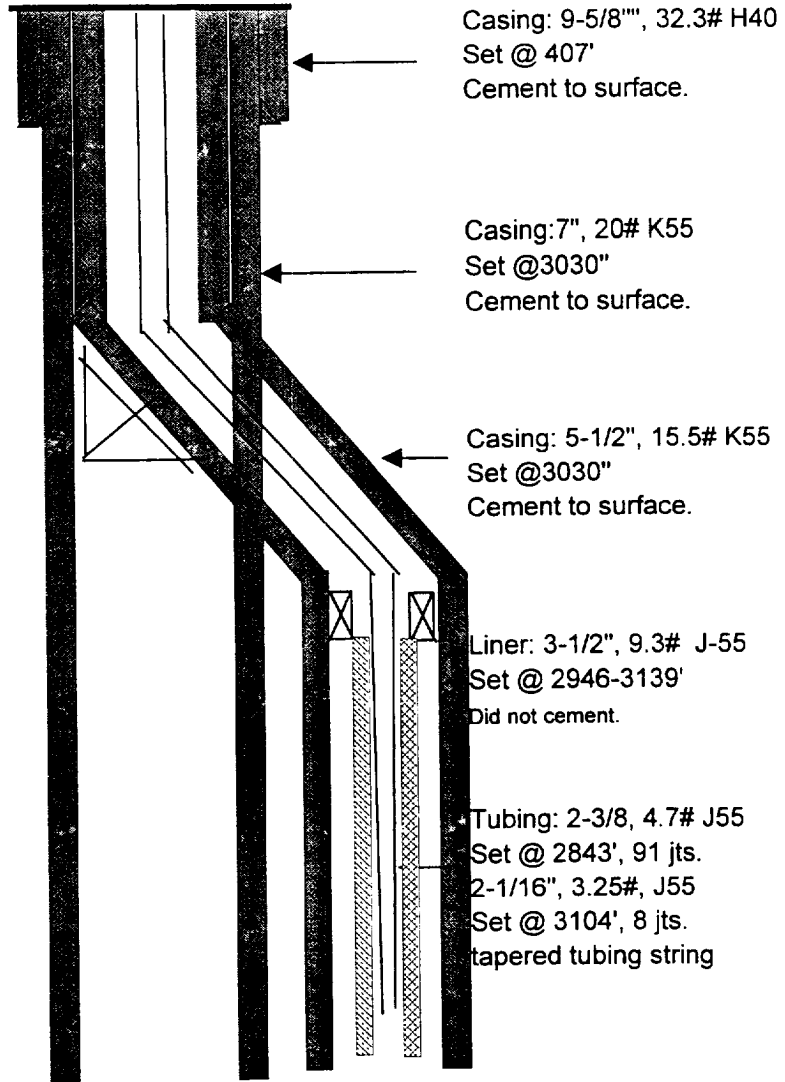

### Workover History:

4/93 Install PCP

5/97 Remove rods & PCP rotor

6/97 RU for recav.,

pull 5-1/2" liner, 7" csg. collapsed @ 1013' during recav., run 2-3/8" tbgr. to 855', return well to production

6/98 Pull tbgr. & sidetracked out of 7" w/6-1/4" hole to 3030', tbgr. to 3104', return well to production
