

WELL CASING
CATHODIC PROTECTION CONSTRUCTION REPORT
DAILY LOG

Drilling Log (Attach Hereto). ☐

Completion Date 5/10/78

Well Name <u>FIELDS #7A</u>		Location <u>NW 34-32-11</u>		C.P.C. No. <u>1219W</u>	
Type & Size Bit Used <u>6 3/4"</u>				Work Order No. <u>57141-21</u>	
Anode Hole Depth <u>240-240 T.D.</u>	Total Drilling Rig Time	Total Lbs. Coke Used	Lost Circulation Mat'l Used	Hrs. Sacks Mud Used	
Anode Depth					
# 1 <u>210'</u>	# 2 <u>195'</u>	# 3 <u>185'</u>	# 4 <u>175'</u>	# 5 <u>165'</u>	# 6 <u>155'</u>
# 7 <u>145'</u>	# 8 <u>110'</u>	# 9 <u>100'</u>	# 10 <u>85'</u>		
Anode Output (Amps)					
# 1 <u>3.0</u>	# 2 <u>2.4</u>	# 3 <u>3.3</u>	# 4 <u>2.8</u>	# 5 <u>3.2</u>	# 6 <u>3.8</u>
# 7 <u>3.6</u>	# 8 <u>2.9</u>	# 9 <u>2.7</u>	# 10 <u>4.0</u>		
Anode Depth					
# 11	# 12	# 13	# 14	# 15	# 16
# 17	# 18	# 19	# 20		
Anode Output (Amps)					
# 11	# 12	# 13	# 14	# 15	# 16
# 17	# 18	# 19	# 20		
Total Circuit Resistance		Hrs. 8 C.P.C. Cable Used		Hrs. 2 C.P.C. Cable Used	
Volts <u>12.5V</u>	Amps <u>9.5A</u>	Ohms <u>1.3</u>			


Remarks: STATIC 600' WEST = .85V DRILLER SAID WATER AT 55', DRILLED
TO 180' HOLE CAVED IN. MOVED OVER STARTED IN, DRILLED 240', LOGGED
240'. INSTALLED 240' OF 1" P.V.C. VENT PERFORATED 240'.
WATER AT 55' APPROX 4 TO 5 GAL./MIN.
PITCH & CABLE = 356'
EXTRA CABLE = 60'
Stub Pole + 40/16 RECT.

All Construction Completed

JE Stath
(Signature)

Gnd. Rod

GROUND BED LAYOUT SKETCH

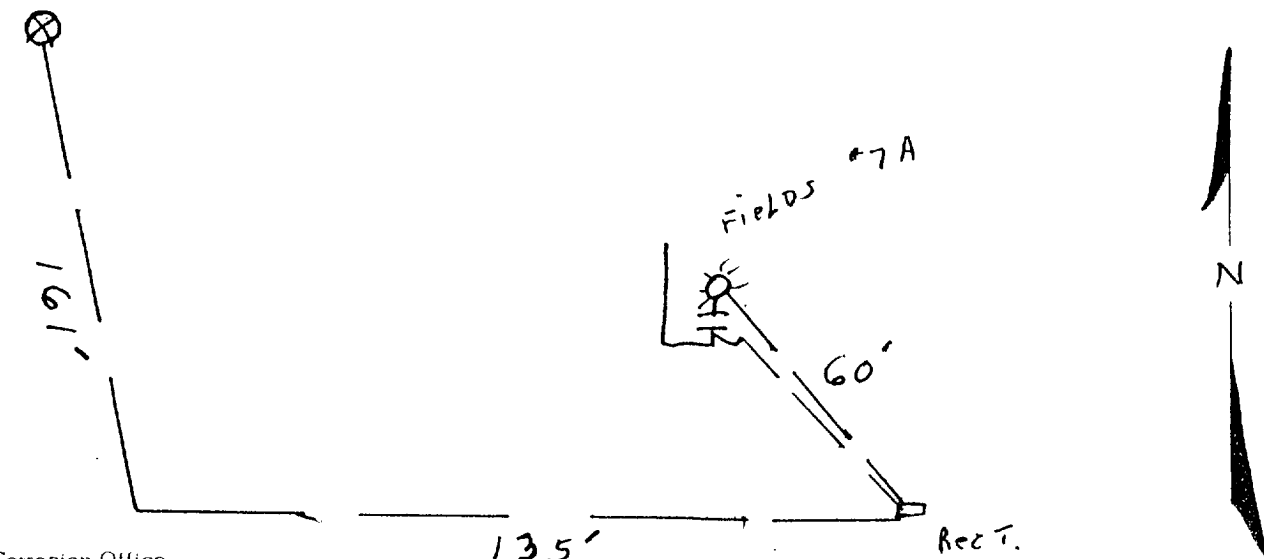

DISTRIBUTION:

WHITE - Division Corrosion Office
 YELLOW - Area Corrosion Office
 PINK - Originator File
