


10/21/14 Cloudy, Windy
+ Warm 55°

Survey boat is outside
at the SWD to
install Super Hob +
Sample, inside the
Bank Berm

Installed six Super
holes to the depth of
one foot. Field tested
Samples 2 + 4

Sample	CT	Time
SP-2	1260 ppm	0830
SP-4	4600 ppm	0855

Mapped out the site
using the Trimble
JUNO 3D, SITE, Banks
+ Sample points!

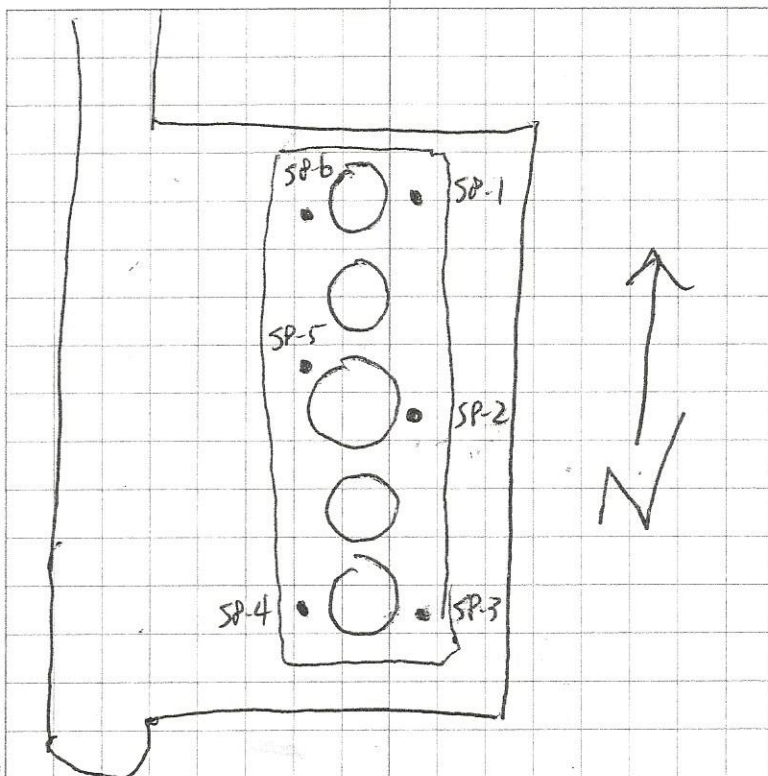

TOOK PHOTOS of
SWD

Samples were properly
preserved + taken to
Cardinal Lab. to be
analyzed for BTEX, TPH
+ Chlorides

Rite in the Rain
