

District I
1625 N. French Dr., Hobbs, NM 88240
District II
811 S. First St., Artesia, NM 88210
District III
1000 Rio Brazos Rd., Aztec, NM 87410
District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505

Submit one copy to appropriate District Office

Oil Conservation Division
1220 South St. Francis Dr.

☐ AMENDED REPORT

I. REQUEST FOR ALLOWABLE MINERAL AUTHORIZATION TO TRANSPORT

¹ Operator name and Address EOG RESOURCES INC PO BOX 2267 MIDLAND, TEXAS 79702		² OGRID Number 7377	
		³ Reason for Filing Code/ Effective Date NW 3/21/2021	
⁴ API Number 30 - 025-47856	⁵ Pool Name WC025 G09 S253309P; UPPER WOLFCAMP		⁶ Pool Code 98180
⁷ Property Code 329310	⁸ Property Name RESOLUTE 12 FED COM		⁹ Well Number 751H

II. ¹⁰ Surface Location

UI or lot no. O	Section 12	Township 25S	Range 32E	Lot Idn	Feet from the 284'	North/South Line SOUTH	Feet from the 1697'	East/West line EAST	County LEA
--------------------	---------------	-----------------	--------------	---------	-----------------------	---------------------------	------------------------	------------------------	---------------

¹¹ Bottom Hole Location

UL or lot no. B	Section 1	Township 25S	Range 32E	Lot Idn	Feet from the 109'	North/South line NORTH	Feet from the 958'	East/West line EAST	County LEA
¹² Lse Code	¹³ Producing Method Code FLOWING	¹⁴ Gas Connection Date	¹⁵ C-129 Permit Number		¹⁶ C-129 Effective Date		¹⁷ C-129 Expiration Date		

III. Oil and Gas Transporters

¹⁸ Transporter OGRID	¹⁹ Transporter Name and Address	²⁰ O/G/W
372812	EOGRM	OIL
151618	ENTERPRISE FIELD SERVICES	GAS
298751	REGENCY FIELD SERVICES	GAS
36785	DCP MIDSTREAM	GAS

IV. Well Completion Data

²¹ Spud Date 10/31/2020	²² Ready Date 3/21/2021	²³ TD 23,220'	²⁴ PBDT 23,198'	²⁵ Perforations 12,968'-23,141'	²⁶ DHC, MC
²⁷ Hole Size		²⁸ Casing & Tubing Size	²⁹ Depth Set		³⁰ Sacks Cement
12 1/4"		9 5/8"	1134'		710 SXS CL C/CIRC
8 3/4"		7 5/8"	12,531'		1494 SXS CL C/CIRC
6 3/4"		5 1/2"	23,198'		785 SXS CL H/CIRC

V. Well Test Data

³¹ Date New Oil 3/21/2021	³² Gas Delivery Date 3/21/2021	³³ Test Date 04/10/2021	³⁴ Test Length 24 HRS	³⁵ Tbg. Pressure	³⁶ Csg. Pressure 3378
³⁷ Choke Size 64	³⁸ Oil 2199	³⁹ Water 12,336	⁴⁰ Gas 13,900		⁴¹ Test Method
⁴² I hereby certify that the rules of the Oil Conservation Division have been complied with and that the information given above is true and complete to the best of my knowledge and belief. Signature: Kristina Agee			OIL CONSERVATION DIVISION		
Printed name: Kristina Agee			Approved by: KURT SIMMONS		
Title: SENIOR REGULATORY ADMINISTRATOR			Title: NMOCD, SANTA FE		
E-mail Address: kristina_agee@eogresources.com			Approval Date: 07/16/2021		
Date: 5/6/2021		Phone: 432-686-6996			

District I
1625 N. French Dr., Hobbs, NM 88240
Phone: (575) 393-6161 Fax: (575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone: (575) 748-1283 Fax: (575) 748-0720
District III
1000 Rio Brazos Road, Aztec, NM 87410
Phone: (505) 334-6178 Fax: (505) 334-6170
District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505
Phone: (505) 476-3460 Fax: (505) 476-3462

State of New Mexico
Energy, Minerals & Natural Resources
Department
OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505

FORM C-102
Revised August 1, 2011
Submit one copy to appropriate
District Office
☐ AMENDED REPORT

WELL LOCATION AND ACREAGE DEDICATION PLAT

¹ API Number 30-025-47856	² Pool Code 98180	³ Pool Name WC-025 G-09 S253309P; Upper Wolfcamp
⁴ Property Code 329310	⁵ Property Name RESOLUTE 12 FED COM	⁶ Well Number 742H
⁷ GRID No. 7377	⁸ Operator Name EOG RESOURCES, INC.	⁹ Elevation 3505'

¹⁰Surface Location


UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
0	12	25-S	32-E	-	284'	SOUTH	1697'	EAST	LEA

¹¹Bottom Hole Location If Different From Surface

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
B	1	25-S	32-E	-	109'	NORTH	958'	EAST	LEA

¹² Dedicated Acres 640.21	¹³ Joint or Infill	¹⁴ Consolidation Code	¹⁵ Order No.
--	-------------------------------	----------------------------------	-------------------------

No allowable will be assigned to this completion until all interests have been consolidated or a non-standard unit has been approved by the division.

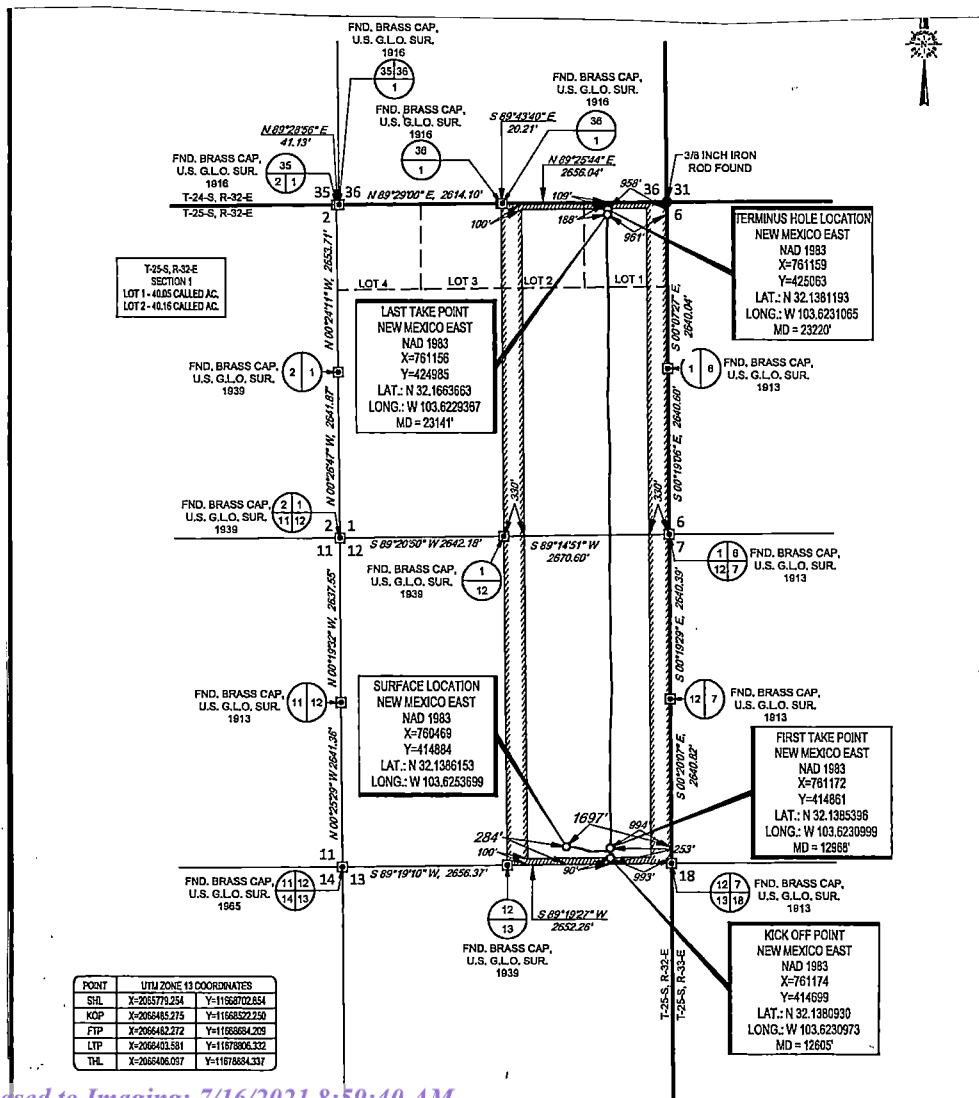¹⁷OPERATOR CERTIFICATION

I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of such a mineral or working interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division.

Kristina Agee 5/16/2021
Signature Date

Kristina Agee
Printed Name


Kristina.agee@eogresources.com
E-mail Address

¹⁸SURVEYOR CERTIFICATION


I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true to the best of my belief.

06/03/2020

Date of Survey
Signature and Seal of Professional Surveyor



Certificate Number

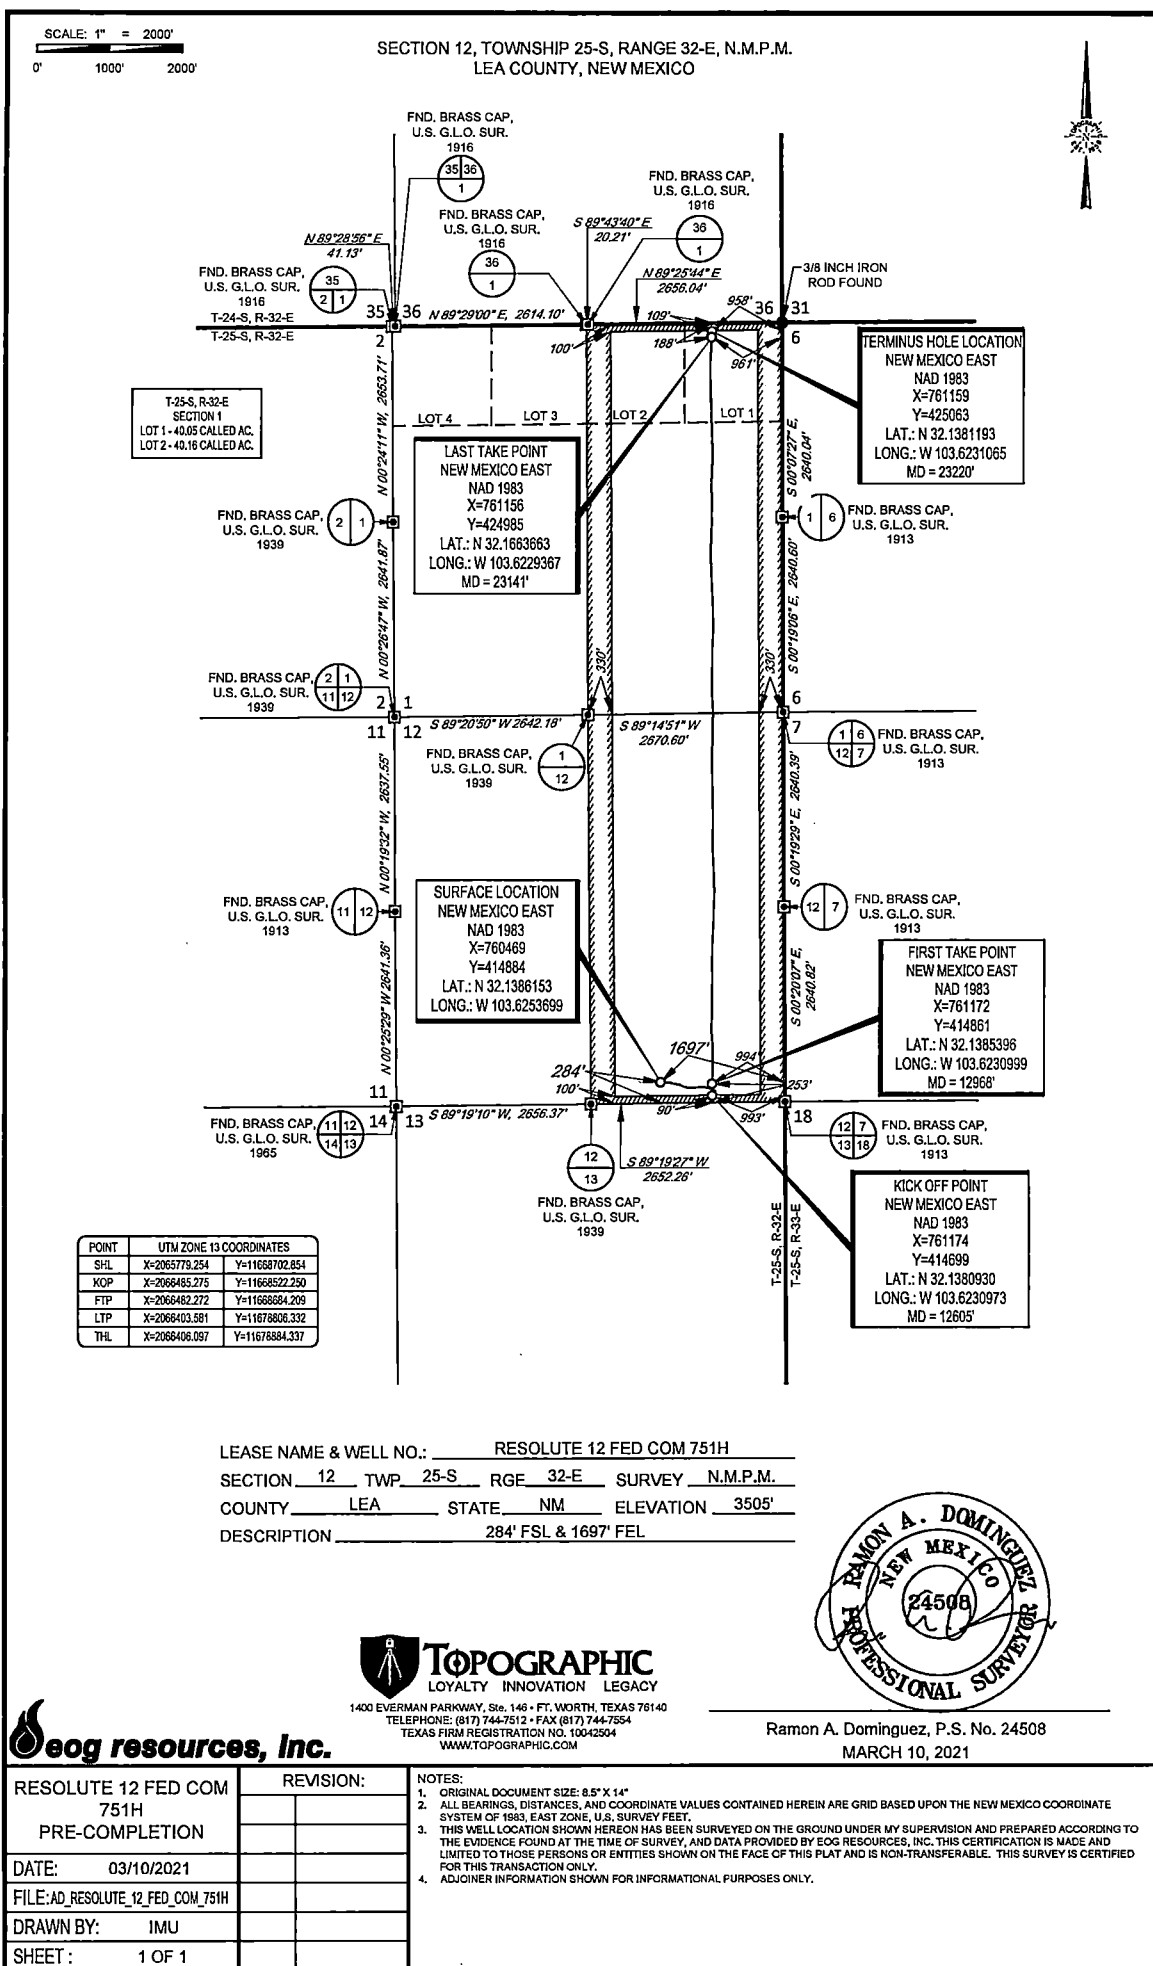



Lea County, NM (NAD 83 NME)

Resolute 12 Fed Com #751H

Plan #2

PROJECT DETAILS: Lea County, NM (NAD 83 NME)

Geodetic System: US State Plane 1983
Datum: North American Datum 1983
Ellipsoid: GRS 1980
Zone: New Mexico Eastern Zone
System Datum: Mean Sea Level

WELL DETAILS: #751H

KB = 32' @ 3537.0usft
Northing 414884.00 Easting 760469.00 Latitude 32° 8' 19.014 N Longitude 103° 37' 31.336 W

SECTION DETAILS








	MD	Inc	Azi	TVD	+N/-S	+E/-W	Dleg	TFace	VSect	Target
1	1139.0	0.22	154.77	1139.0	-0.2	-3.4	0.00	0.00	-0.4	
2	2500.0	0.22	154.77	2500.0	-5.0	-1.1	0.00	0.00	-5.0	
3	2982.7	9.79	102.40	2980.3	-14.7	39.4	2.00	-53.40	-12.0	
4	6854.8	9.79	102.40	6796.0	-156.0	682.3	0.00	0.00	-110.7	
5	7344.1	0.00	0.00	7283.0	-165.0	723.0	2.00	180.00	-116.9	
6	12625.6	0.00	0.00	12564.5	-165.0	723.0	0.00	0.00	-116.9	KOP (Resolute 12 Fed Com #751H)
7	13373.7	89.77	359.72	13042.0	310.5	720.7	12.00	359.72	357.4	TGT 1 (Resolute 12 Fed Com #751H)
8	16360.8	89.77	359.72	13054.0	3297.6	706.3	0.00	0.00	3337.0	TGT 2 (Resolute 12 Fed Com #751H)
9	16362.4	89.74	359.72	13054.0	3299.2	706.3	2.00	180.00	3338.6	
10	20722.8	89.74	359.72	13074.0	7659.5	685.2	0.00	0.00	7688.0	
11	20726.8	89.66	359.72	13074.0	7663.4	685.2	2.00	-180.00	7691.9	
12	23241.4	89.66	359.72	13089.0	10178.0	673.0	0.00	0.00	10200.2	PBHL (Resolute 12 Fed Com #751H)

CASING DETAILS

No casing data is available

WELLBORE TARGET DETAILS (MAP CO-ORDINATES)

Name	TVD	+N/-S	+E/-W	Northing	Easting
KOP (Resolute 12 Fed Com #751H)	12564.5	-165.0	723.0	414719.00	761192.00
FTP (Resolute 12 Fed Com #751H)	13042.0	-175.0	723.0	414709.00	761192.00
TGT 1 (Resolute 12 Fed Com #751H)	13054.0	3297.6	706.3	418181.60	761175.26
TGT 2 (Resolute 12 Fed Com #751H)	13074.0	7659.5	685.2	422543.50	761154.17
PBHL (Resolute 12 Fed Com #751H)	13089.0	10178.0	673.0	425062.00	761142.00

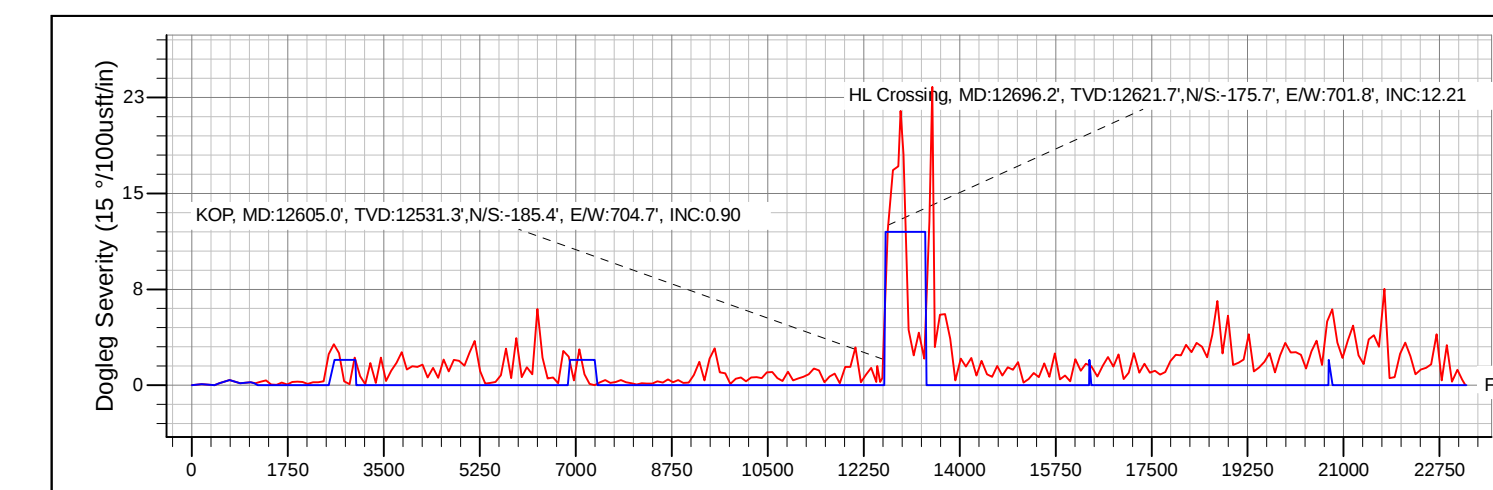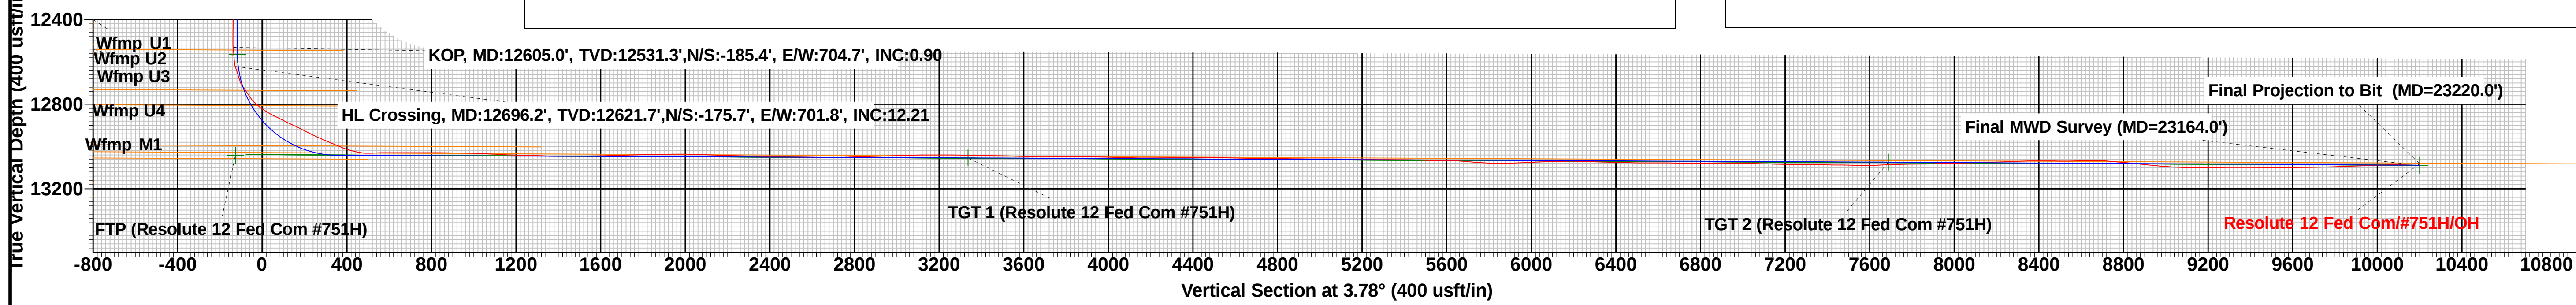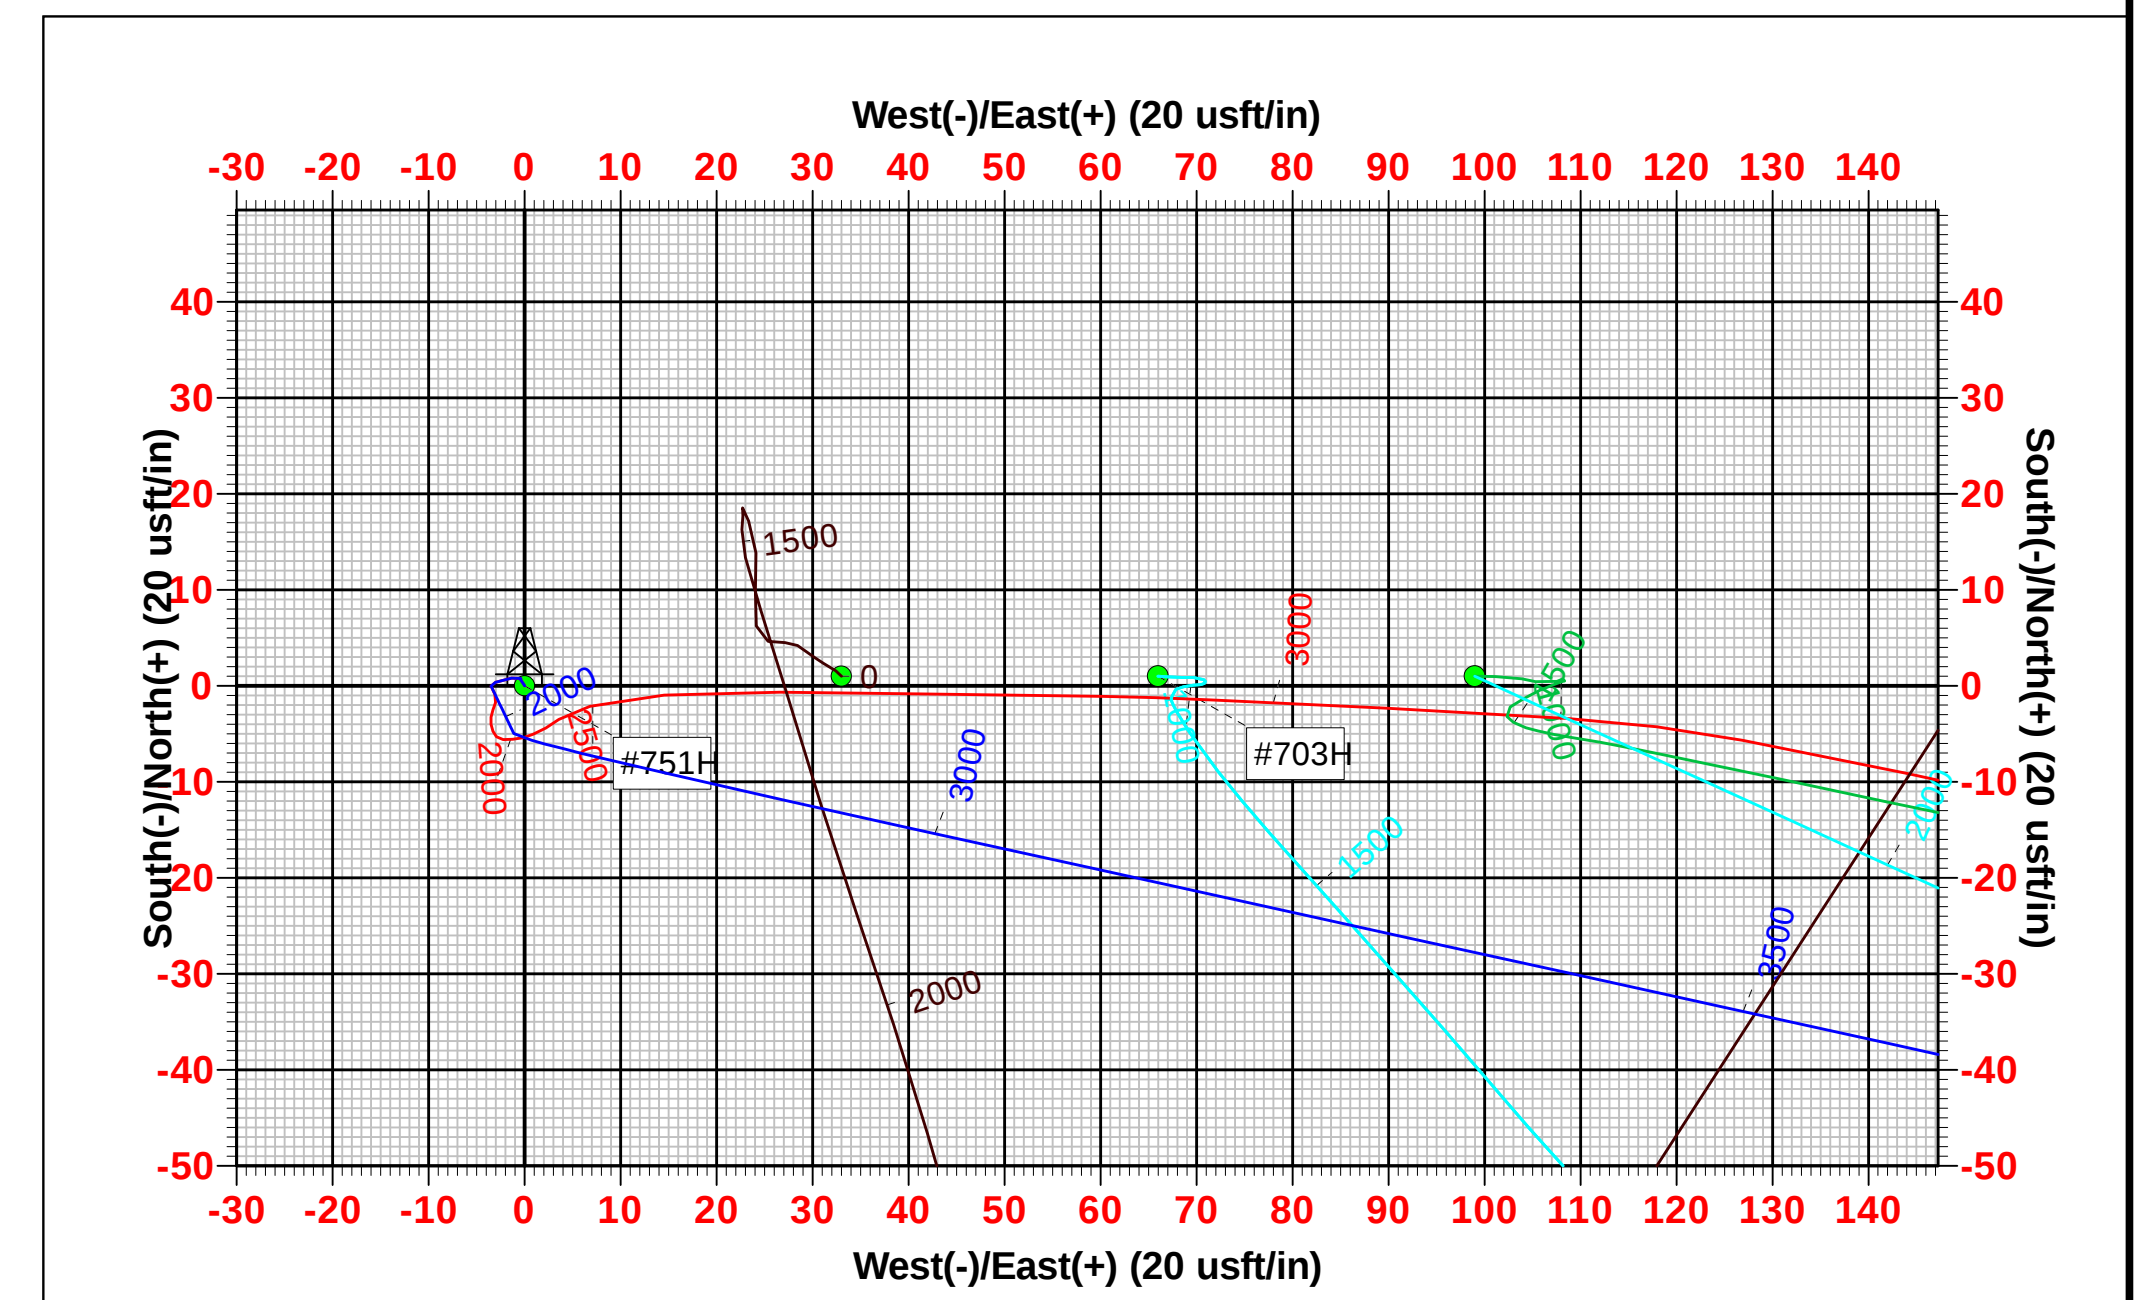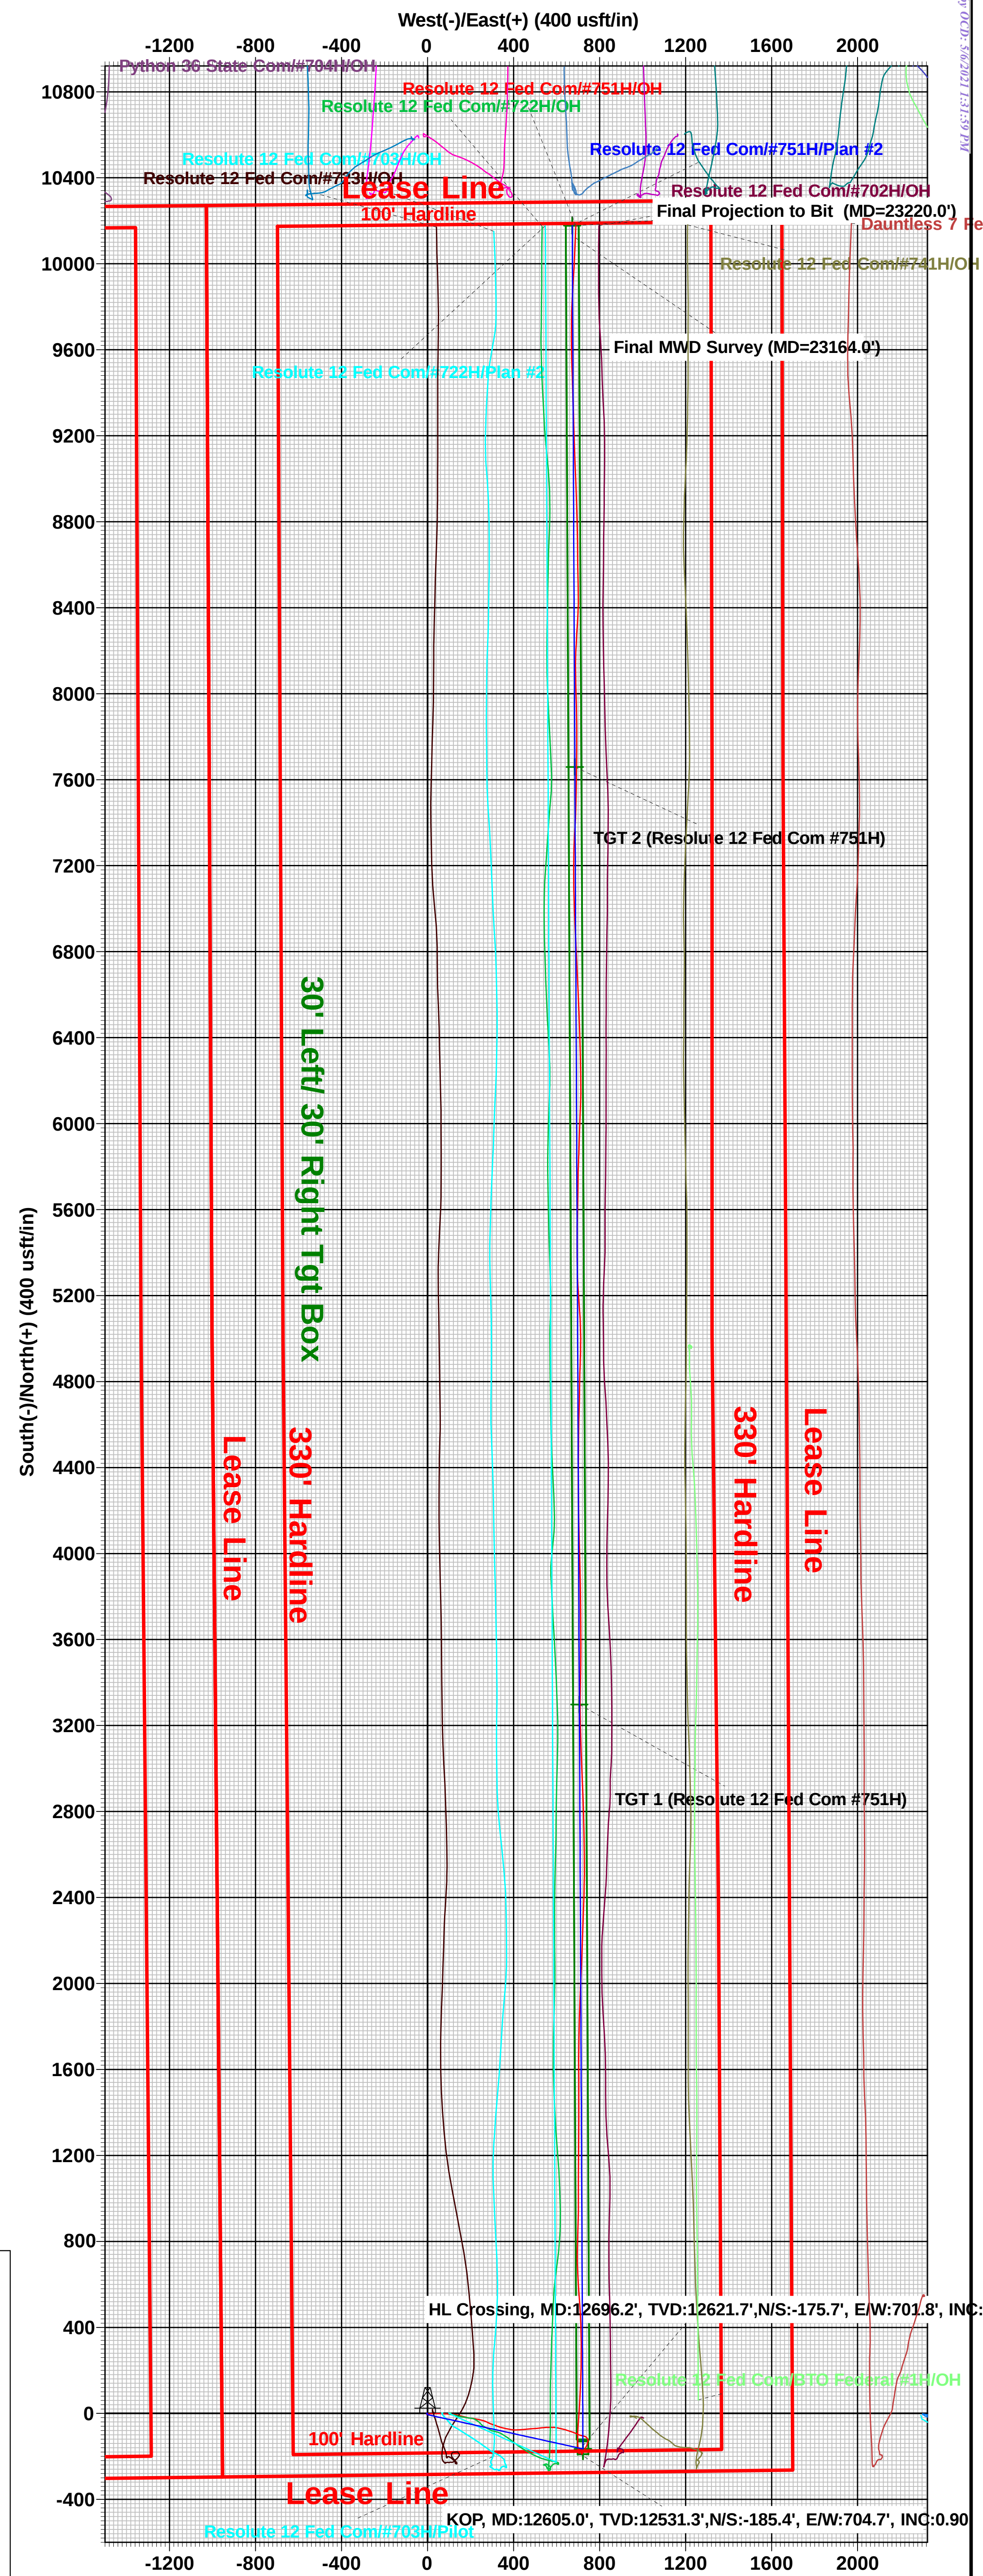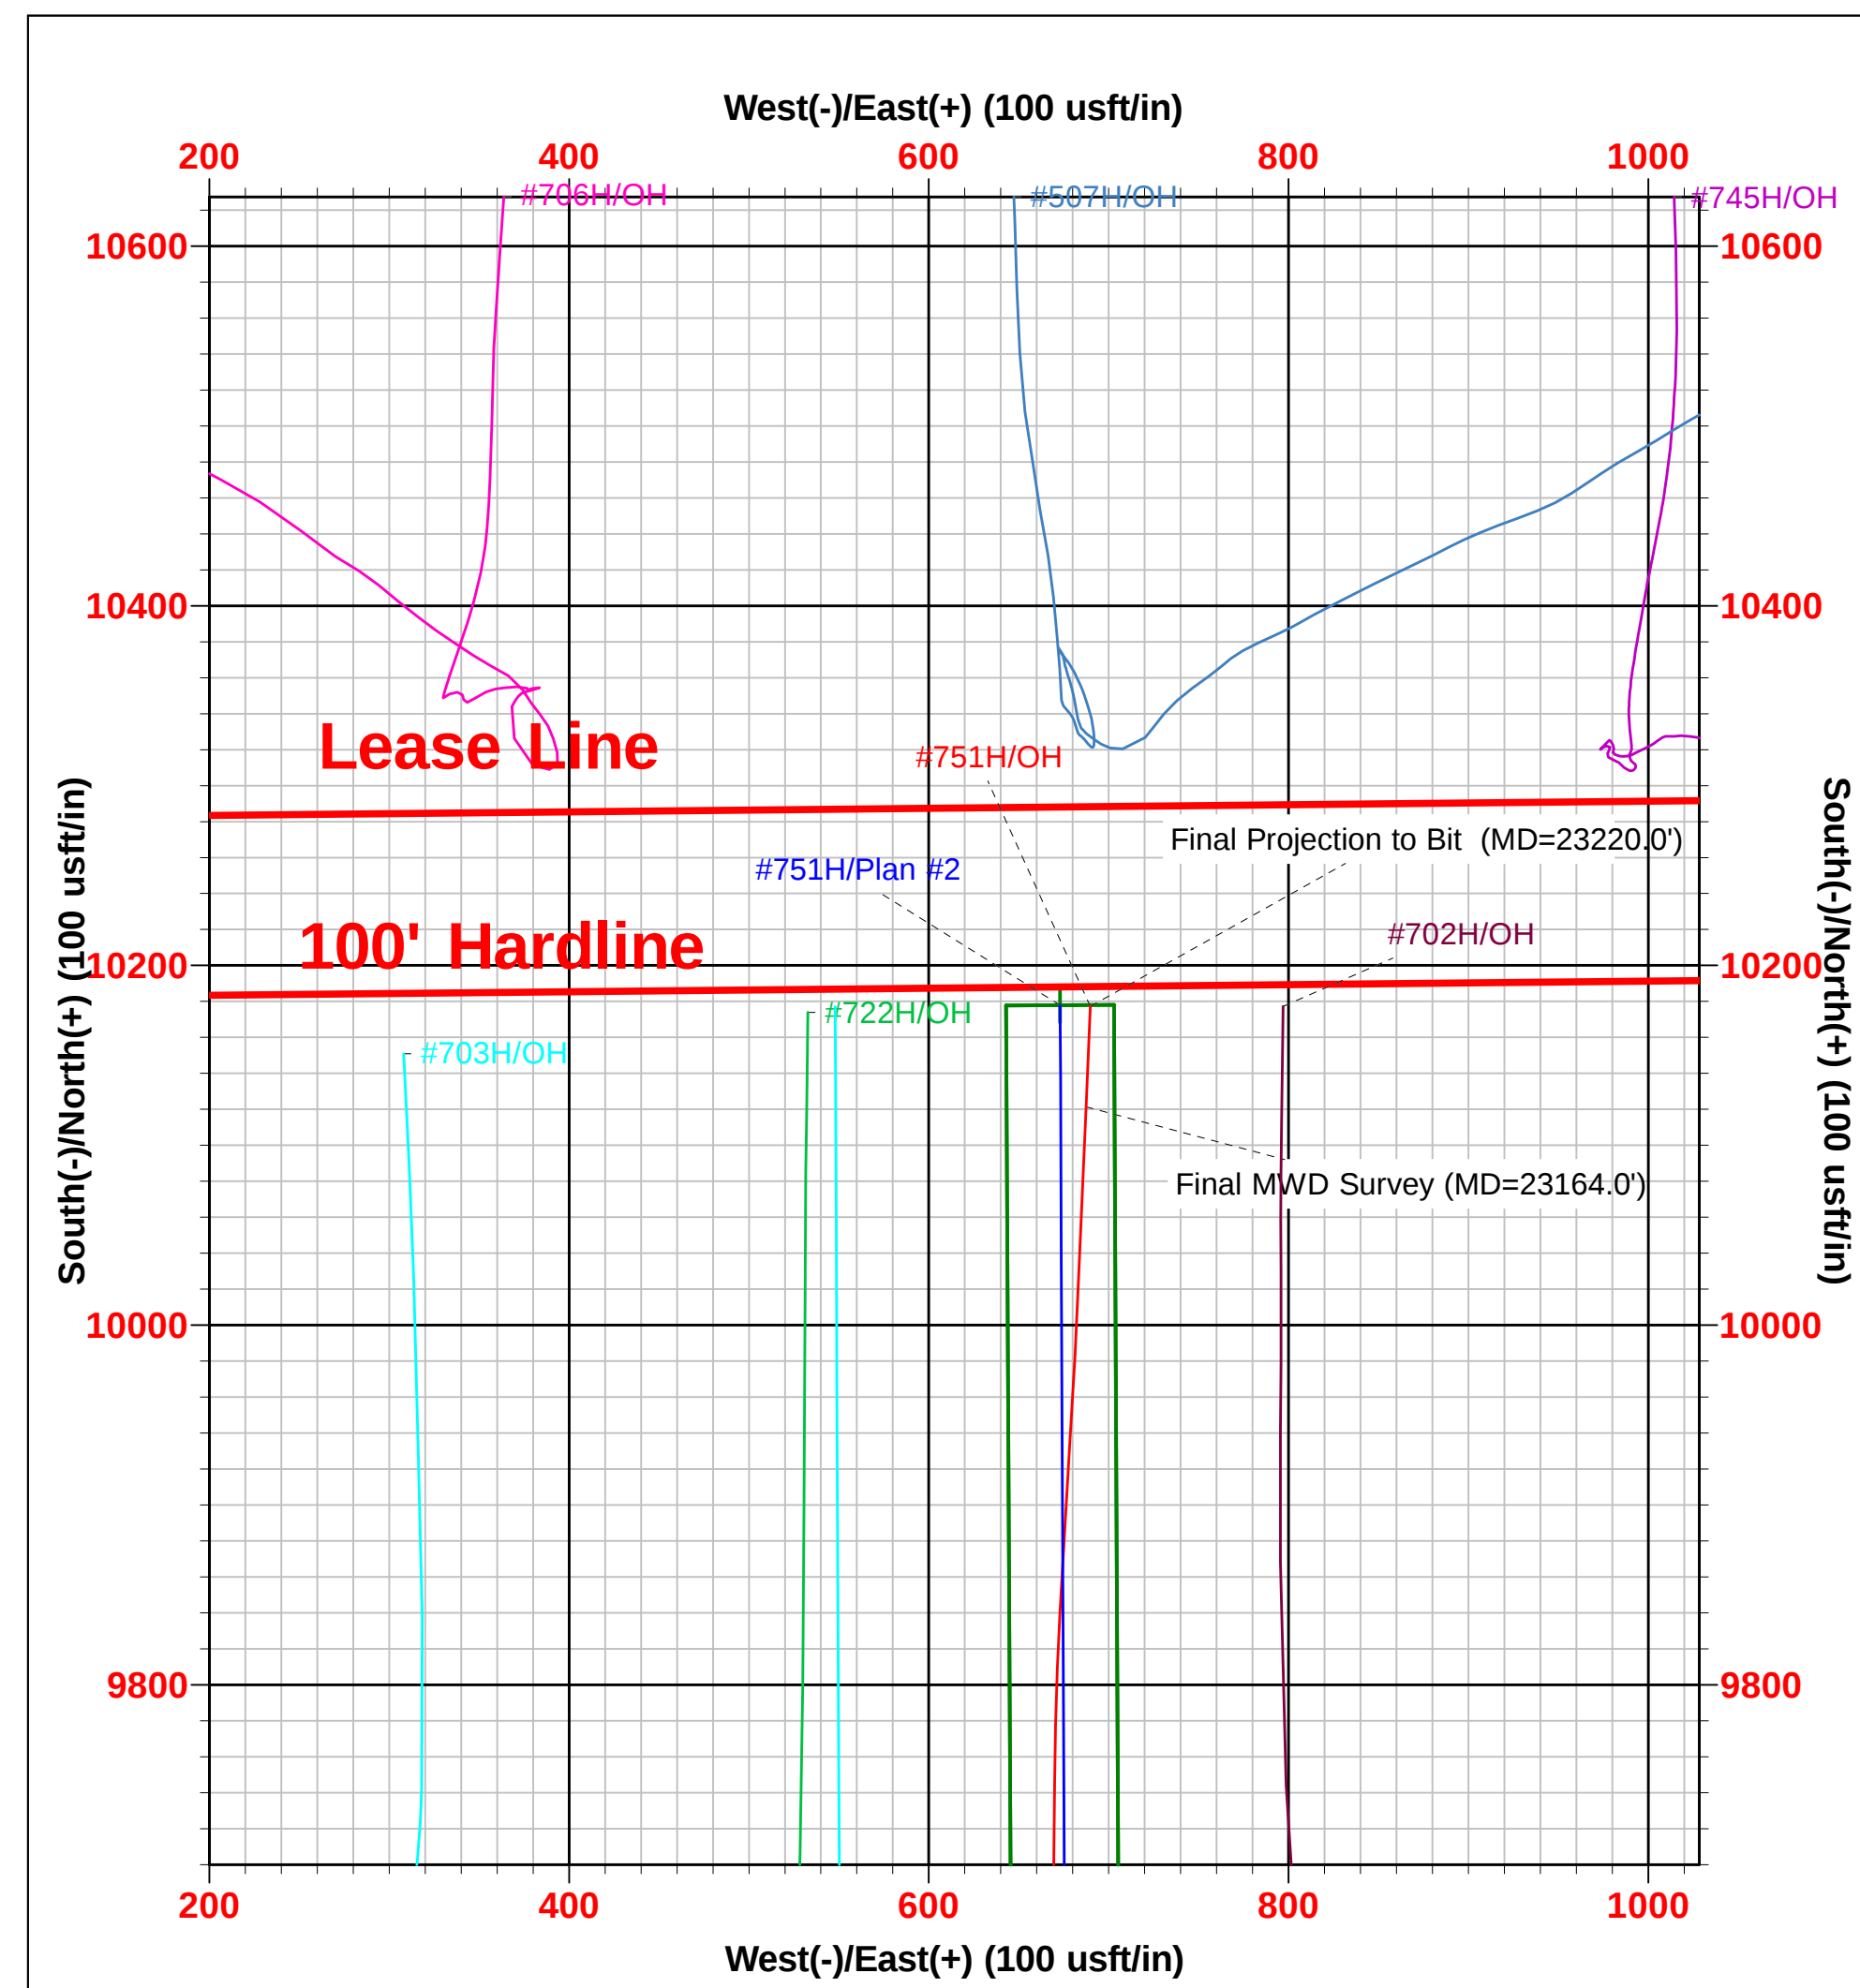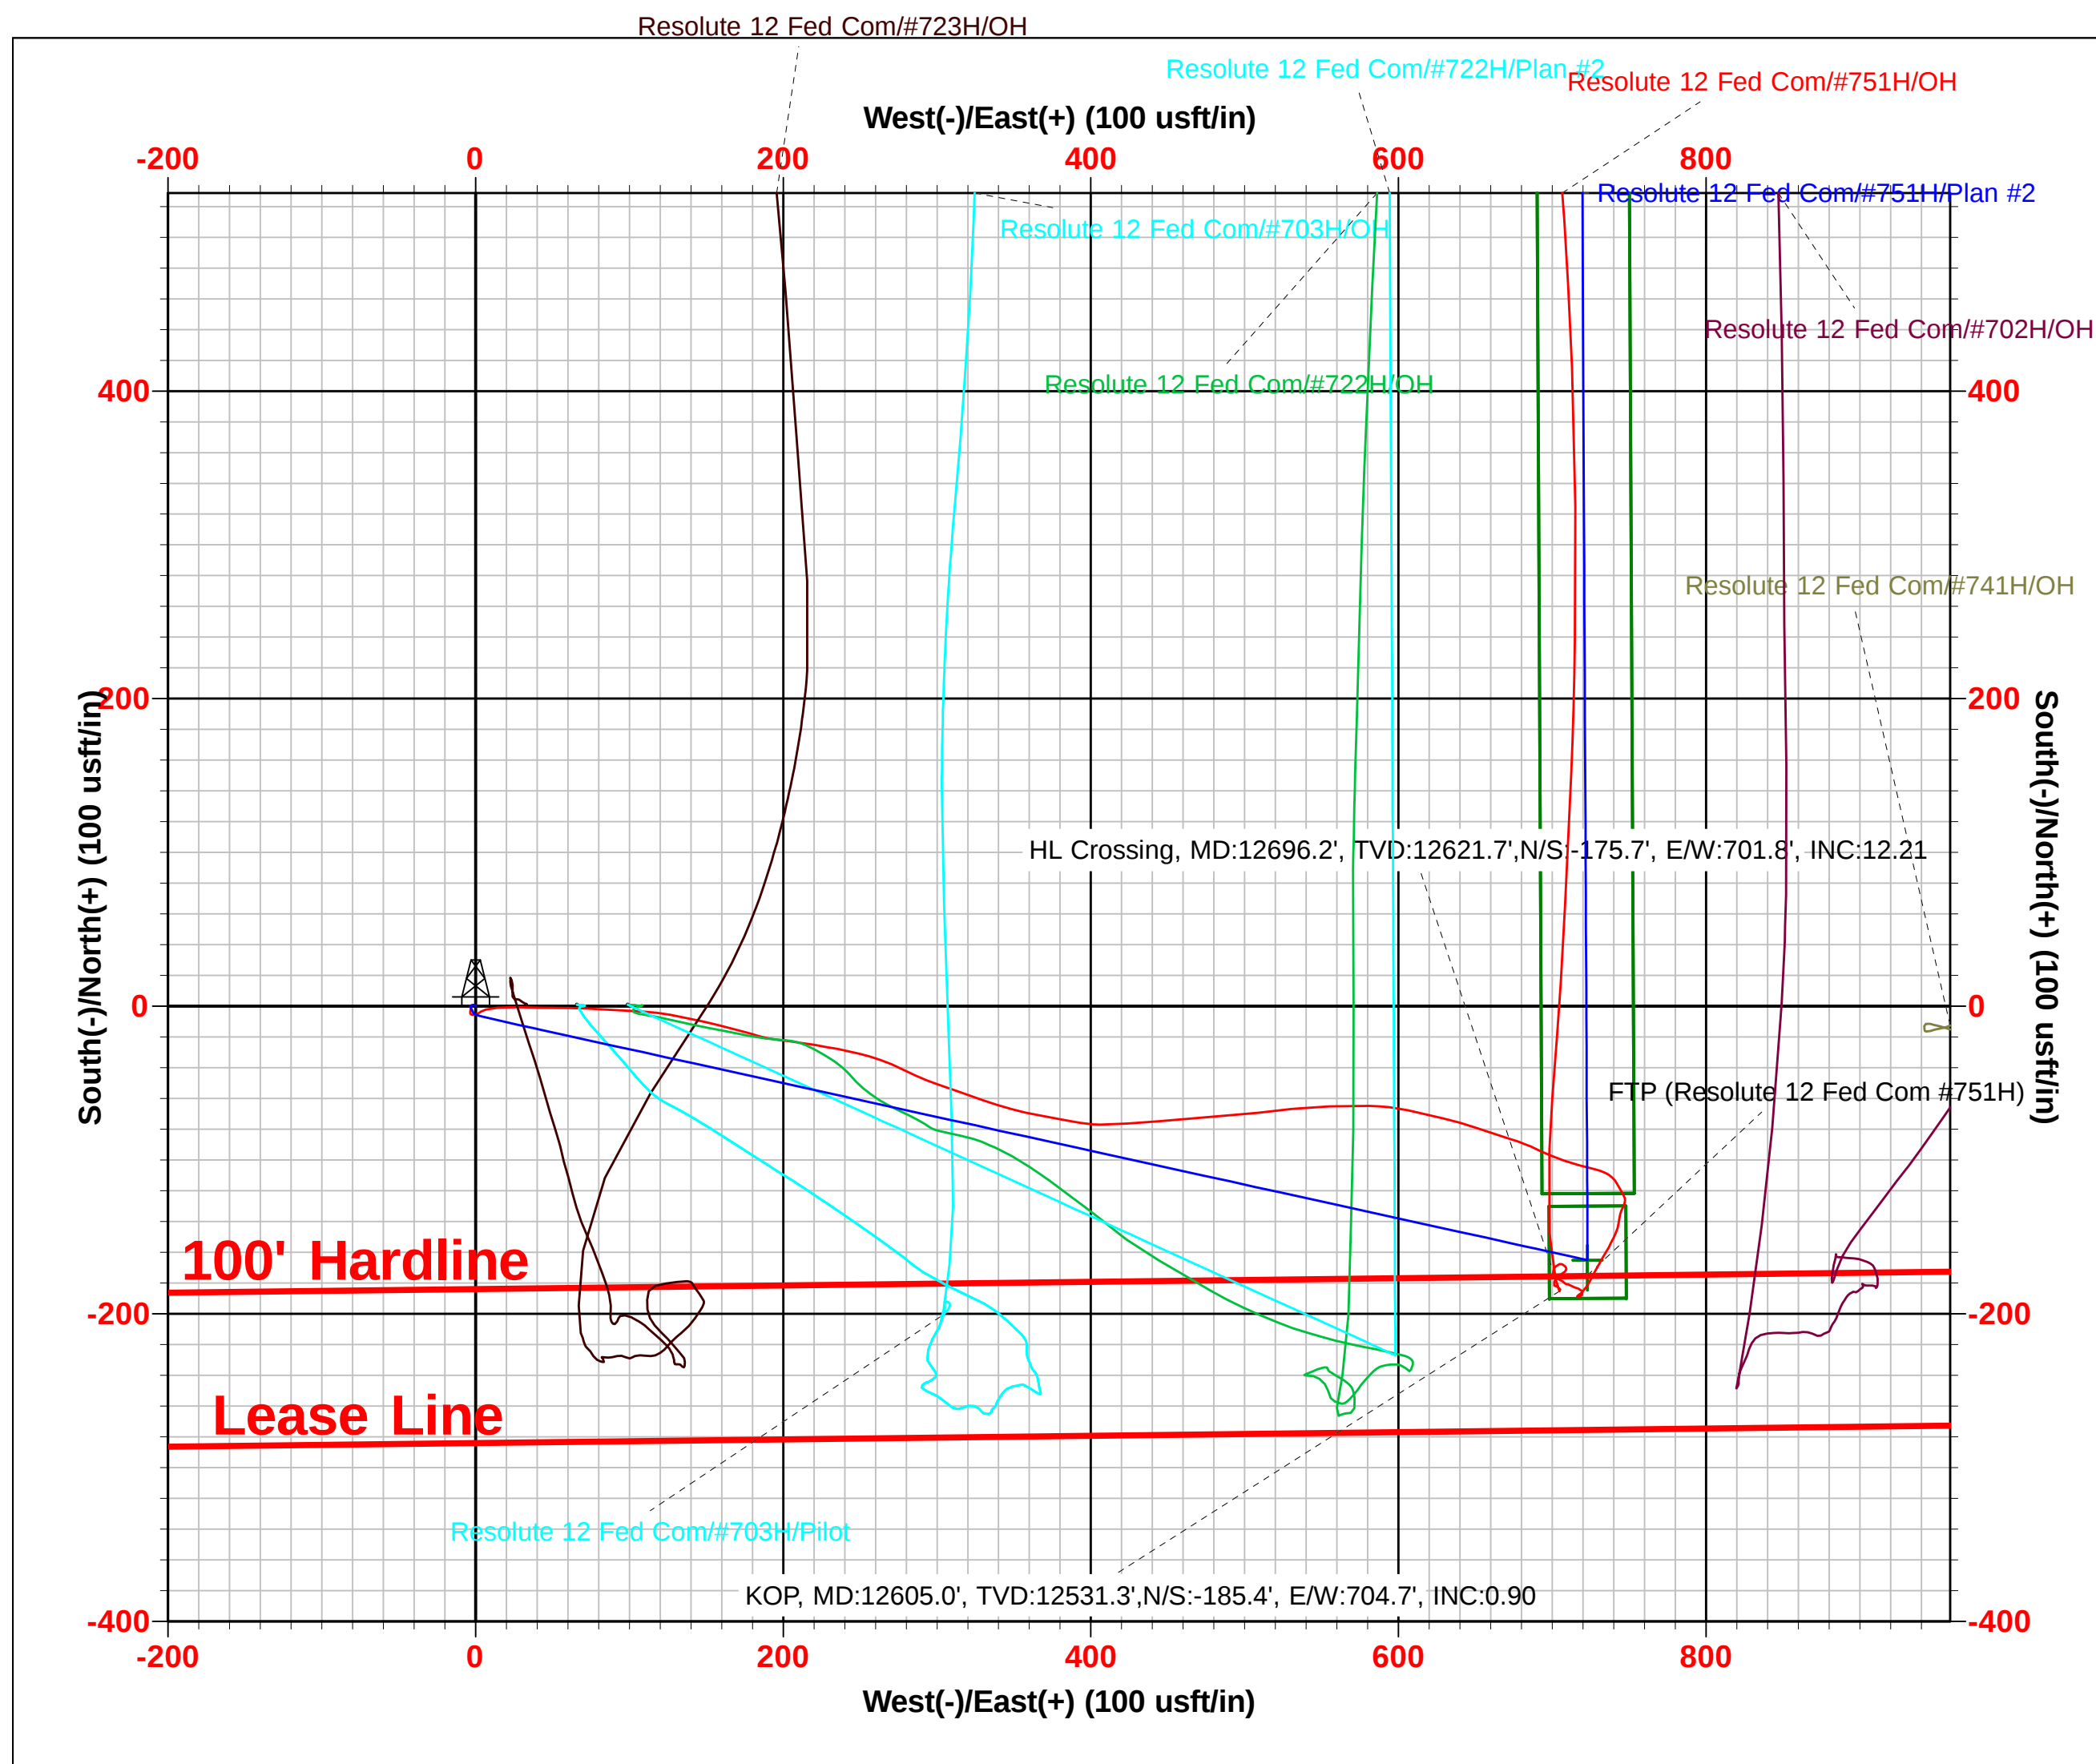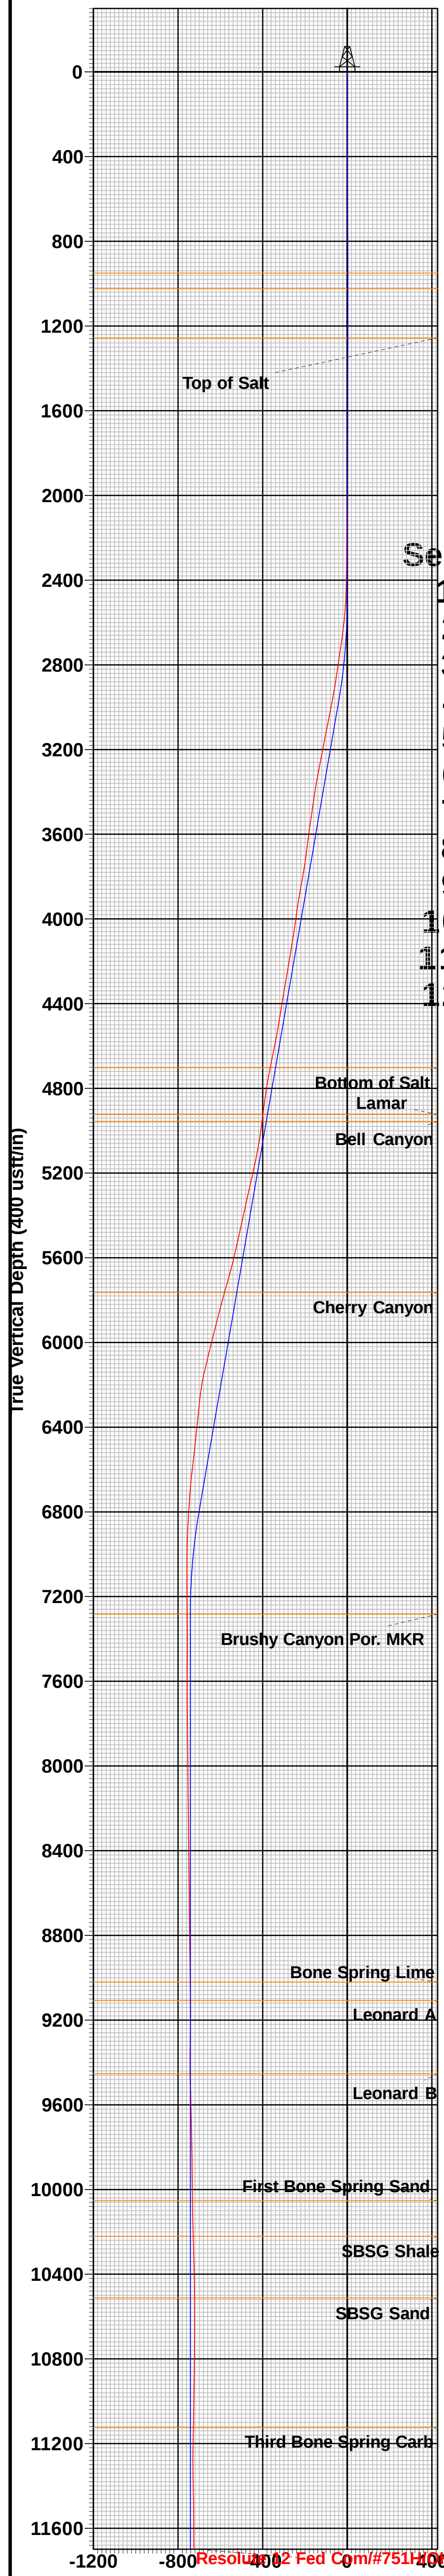

Lea County, NM (NAD 83 NME)
Resolute 12 Fed Com #751H
Plan #2
14.01, February 01, 2021



EOG Resources - Midland

Lea County, NM (NAD 83 NME)

Resolute 12 Fed Com

#751H

OH

Design: OH

Final PVA

01 February, 2021



EOG Resources

Final PVA

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #751H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 32' @ 3537.0usft
Site:	Resolute 12 Fed Com	MD Reference:	KB = 32' @ 3537.0usft
Well:	#751H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM 5000.14

Project		Lea County, NM (NAD 83 NME)	
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	New Mexico Eastern Zone		

Site		Resolute 12 Fed Com								
Site Position:		Northing:		414,863.00	usft	Latitude:	32° 8' 18.736 N			
From:	Map	Easting:		761,539.00	usft	Longitude:	103° 37' 18.893 W			
Position Uncertainty:		0.0	usft	Slot Radius:		13-3/16	"	Grid Convergence:	0.38	°

Well		#751H				
Well Position	+N/-S	0.0 usft	Northing:	414,884.00 usft	Latitude:	32° 8' 19.014 N
	+E/-W	0.0 usft	Easting:	760,469.00 usft	Longitude:	103° 37' 31.336 W
Position Uncertainty		0.0 usft	Wellhead Elevation:	usft	Ground Level:	3,505.0 usft

Wellbore	OH				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	IGRF2020	11/24/2020	6.63	59.83	47,494.98707612

Design		OH			
Audit Notes:					
Version:	1.0	Phase:	ACTUAL	Tie On Depth:	0.0
Vertical Section:	Depth From (TVD) (usft)		+N/-S (usft)	+E/-W (usft)	Direction (°)
	0.0		0.0	0.0	3.78

Survey Program		Date	2/1/2021		
From (usft)	To (usft)	Survey (Wellbore)	Tool Name	Description	
182.0	23,220.0	Pro MWD #1 (OH)	EOG MWD+IFR1	MWD + IFR1	



EOG Resources

Final PVA

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #751H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 32' @ 3537.0usft
Site:	Resolute 12 Fed Com	MD Reference:	KB = 32' @ 3537.0usft
Well:	#751H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM 5000.14

Survey											
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)	
0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.00	0.0	0.0	
182.0	0.13	326.12	182.0	0.2	-0.1	0.07	0.07	0.00	0.0	0.0	
412.0	0.13	326.12	412.0	0.6	-0.4	0.00	0.00	0.00	0.0	0.0	
503.0	0.13	31.51	503.0	0.8	-0.4	0.15	0.00	71.86	0.0	0.0	
690.0	0.66	261.70	690.0	0.8	-1.4	0.40	0.28	-69.42	0.0	0.0	
880.0	0.40	247.46	880.0	0.4	-3.1	0.15	-0.14	-7.49	0.0	0.0	
1,070.0	0.13	133.55	1,070.0	0.0	-3.5	0.25	-0.14	-59.95	0.0	0.0	
1,164.0	0.26	158.53	1,164.0	-0.3	-3.4	0.16	0.14	26.57	0.0	0.0	
1,259.0	0.53	155.94	1,259.0	-0.9	-3.1	0.28	0.28	-2.73	-0.3	0.0	
1,354.0	0.53	196.98	1,354.0	-1.7	-3.1	0.39	0.00	43.20	-0.7	0.2	
1,450.0	0.48	195.66	1,450.0	-2.5	-3.3	0.05	-0.05	-1.37	-1.3	-0.1	
1,545.0	0.44	193.64	1,545.0	-3.3	-3.5	0.05	-0.04	-2.13	-1.8	-0.3	
1,640.0	0.48	168.33	1,640.0	-4.0	-3.5	0.22	0.04	-26.64	-1.8	-1.3	
1,735.0	0.44	162.70	1,735.0	-4.7	-3.3	0.06	-0.04	-5.93	-2.1	-1.6	
1,830.0	0.40	129.66	1,830.0	-5.3	-2.9	0.25	-0.04	-34.78	-1.2	-2.5	
1,925.0	0.53	99.25	1,925.0	-5.6	-2.2	0.29	0.14	-32.01	-0.3	-2.6	
2,020.0	0.70	82.90	2,020.0	-5.6	-1.2	0.26	0.18	-17.21	-0.4	-2.4	
2,115.0	0.62	77.89	2,114.9	-5.4	-0.2	0.10	-0.08	-5.27	-1.2	-2.1	
2,210.0	0.75	64.18	2,209.9	-5.0	0.9	0.22	0.14	-14.43	-1.8	-2.1	
2,305.0	0.97	64.88	2,304.9	-4.4	2.2	0.23	0.23	0.74	-3.3	-1.7	
2,400.0	1.05	48.97	2,399.9	-3.5	3.6	0.31	0.08	-16.75	-4.4	-2.4	
2,495.0	3.25	72.79	2,494.8	-2.1	6.8	2.45	2.32	25.07	-8.4	0.3	
2,591.0	6.15	85.97	2,590.5	-1.0	14.5	3.20	3.02	13.73	-14.4	3.6	
2,686.0	8.48	90.46	2,684.7	-0.7	26.6	2.52	2.45	4.73	-21.5	6.4	
2,781.0	8.75	90.98	2,778.7	-0.8	40.8	0.30	0.28	0.55	-27.9	8.3	
2,876.0	8.79	90.46	2,872.6	-1.0	55.3	0.09	0.04	-0.55	-31.6	10.4	
2,971.0	10.81	92.39	2,966.2	-1.5	71.5	2.15	2.13	2.03	-33.4	14.3	



EOG Resources

Final PVA

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #751H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 32' @ 3537.0usft
Site:	Resolute 12 Fed Com	MD Reference:	KB = 32' @ 3537.0usft
Well:	#751H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM 5000.14

Survey											
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)	
3,066.0	11.47	93.09	3,059.4	-2.3	89.8	0.71	0.69	0.74	-35.7	17.4	
3,161.0	11.43	93.45	3,152.5	-3.4	108.7	0.09	-0.04	0.38	-38.5	20.2	
3,257.0	10.63	101.00	3,246.7	-5.7	126.8	1.72	-0.83	7.86	-37.6	26.7	
3,352.0	10.50	101.71	3,340.1	-9.1	143.9	0.19	-0.14	0.75	-38.6	27.4	
3,447.0	8.48	103.90	3,433.8	-12.5	159.2	2.16	-2.13	2.31	-37.0	28.8	
3,542.0	8.22	105.31	3,527.8	-16.0	172.5	0.35	-0.27	1.48	-33.9	29.0	
3,637.0	7.16	106.63	3,621.9	-19.5	184.8	1.13	-1.12	1.39	-29.8	28.8	
3,732.0	8.04	95.91	3,716.1	-21.9	197.0	1.75	0.93	-11.28	-31.0	23.5	
3,827.0	10.46	98.54	3,809.9	-23.8	212.2	2.59	2.55	2.77	-29.0	26.3	
3,922.0	9.32	100.39	3,903.4	-26.5	228.3	1.25	-1.20	1.95	-28.3	28.0	
4,018.0	7.91	101.62	3,998.4	-29.2	242.4	1.48	-1.47	1.28	-25.8	29.0	
4,113.0	9.14	105.57	4,092.3	-32.6	256.1	1.43	1.29	4.16	-21.7	30.2	
4,208.0	9.62	114.45	4,186.0	-37.9	270.6	1.60	0.51	9.35	-16.4	31.0	
4,303.0	10.20	114.89	4,279.6	-44.7	285.4	0.62	0.61	0.46	-16.8	27.7	
4,398.0	9.49	108.56	4,373.2	-50.8	300.5	1.36	-0.75	-6.66	-19.8	23.0	
4,493.0	9.01	110.32	4,467.0	-55.8	314.9	0.59	-0.51	1.85	-18.3	21.6	
4,588.0	10.90	108.91	4,560.6	-61.3	330.4	2.01	1.99	-1.48	-19.2	19.2	
4,683.0	11.69	105.49	4,653.7	-66.8	348.1	1.09	0.83	-3.60	-22.8	16.6	
4,779.0	10.11	99.95	4,748.0	-70.9	365.8	1.97	-1.65	-5.77	-26.1	14.1	
4,874.0	8.31	100.83	4,841.8	-73.6	380.8	1.90	-1.89	0.93	-25.0	15.1	
4,969.0	6.86	99.69	4,935.9	-75.8	393.1	1.53	-1.53	-1.20	-21.6	15.2	
5,064.0	9.01	91.51	5,030.0	-77.0	406.1	2.55	2.26	-8.61	-20.7	14.3	
5,159.0	12.09	85.45	5,123.4	-76.4	423.5	3.44	3.24	-6.38	-24.0	16.0	
5,254.0	13.14	85.27	5,216.1	-74.7	444.2	1.11	1.11	-0.19	-29.4	20.7	
5,349.0	13.27	85.27	5,308.6	-72.9	465.8	0.14	0.14	0.00	-35.8	25.4	
5,444.0	13.10	85.36	5,401.1	-71.2	487.4	0.18	-0.18	0.09	-42.1	30.2	
5,539.0	13.05	84.22	5,493.6	-69.2	508.8	0.28	-0.05	-1.20	-48.9	34.2	



EOG Resources

Final PVA

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #751H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 32' @ 3537.0usft
Site:	Resolute 12 Fed Com	MD Reference:	KB = 32' @ 3537.0usft
Well:	#751H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM 5000.14

Survey										
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
5,634.0	13.75	82.99	5,586.0	-66.7	530.7	0.80	0.74	-1.29	-56.4	38.3
5,729.0	16.04	88.61	5,677.8	-65.1	555.0	2.85	2.41	5.92	-61.2	48.7
5,824.0	16.00	90.54	5,769.2	-64.9	581.2	0.56	-0.04	2.03	-70.2	54.5
5,920.0	14.63	102.94	5,861.8	-67.7	606.3	3.69	-1.43	12.92	-66.2	70.7
6,015.0	14.02	103.11	5,953.8	-73.0	629.2	0.64	-0.64	0.18	-73.5	70.7
6,110.0	13.97	108.65	6,046.0	-79.3	651.2	1.41	-0.05	5.83	-73.5	76.7
6,205.0	13.18	107.68	6,138.3	-86.2	672.4	0.87	-0.83	-1.02	-81.2	73.8
6,300.0	7.73	116.21	6,231.7	-92.3	688.5	5.95	-5.74	8.98	-70.9	82.6
6,396.0	5.71	112.08	6,327.1	-97.0	698.7	2.16	-2.10	-4.30	-71.6	74.3
6,491.0	6.11	109.09	6,421.6	-100.4	707.9	0.53	0.42	-3.15	-69.0	68.3
6,586.0	6.46	105.05	6,516.0	-103.5	717.8	0.59	0.37	-4.25	-67.8	62.2
6,682.0	6.46	103.64	6,611.4	-106.1	728.3	0.17	0.00	-1.47	-63.8	60.0
6,777.0	4.92	124.38	6,705.9	-109.7	736.8	2.68	-1.62	21.83	-32.5	74.5
6,872.0	4.53	149.96	6,800.6	-115.2	742.1	2.24	-0.41	26.93	6.2	71.1
6,967.0	4.17	150.49	6,895.3	-121.5	745.6	0.38	-0.38	0.56	9.2	60.5
7,062.0	1.93	180.28	6,990.2	-126.1	747.3	2.81	-2.36	31.36	35.9	38.6
7,158.0	1.36	201.55	7,086.2	-128.8	746.9	0.86	-0.59	22.16	43.5	15.5
7,253.0	1.45	204.80	7,181.1	-130.9	746.0	0.13	0.09	3.42	41.0	8.3
7,348.0	1.45	205.07	7,276.1	-133.1	745.0	0.01	0.00	0.28	38.2	6.4
7,444.0	1.41	196.19	7,372.1	-135.3	744.1	0.23	-0.04	-9.25	34.4	12.0
7,539.0	1.71	186.96	7,467.0	-137.9	743.6	0.41	0.32	-9.72	29.4	17.2
7,634.0	1.89	188.46	7,562.0	-140.8	743.2	0.20	0.19	1.58	26.9	16.5
7,729.0	2.07	193.64	7,656.9	-144.0	742.6	0.27	0.19	5.45	25.0	14.1
7,824.0	2.20	203.40	7,751.9	-147.4	741.5	0.41	0.14	10.27	23.5	10.0
7,919.0	2.20	209.02	7,846.8	-150.7	739.9	0.23	0.00	5.92	20.7	7.8
8,014.0	2.11	206.03	7,941.7	-153.8	738.2	0.15	-0.09	-3.15	16.7	8.8
8,110.0	2.07	207.09	8,037.7	-156.9	736.6	0.06	-0.04	1.10	13.4	8.5



EOG Resources

Final PVA

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #751H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 32' @ 3537.0usft
Site:	Resolute 12 Fed Com	MD Reference:	KB = 32' @ 3537.0usft
Well:	#751H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM 5000.14

Survey										
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
8,205.0	2.07	211.40	8,132.6	-159.9	735.0	0.16	0.00	4.54	10.6	7.6
8,300.0	1.98	208.85	8,227.6	-162.8	733.3	0.13	-0.09	-2.68	6.8	8.0
8,395.0	2.02	212.27	8,322.5	-165.7	731.6	0.13	0.04	3.60	4.0	7.6
8,490.0	2.24	207.53	8,417.4	-168.8	729.8	0.30	0.23	-4.99	-0.2	7.8
8,586.0	2.07	210.60	8,513.4	-171.9	728.1	0.21	-0.18	3.20	-3.4	7.9
8,680.0	2.46	206.56	8,607.3	-175.2	726.3	0.45	0.41	-4.30	-7.6	7.5
8,775.0	2.24	206.56	8,702.2	-178.7	724.6	0.23	-0.23	0.00	-11.5	7.5
8,870.0	2.07	216.32	8,797.1	-181.7	722.7	0.43	-0.18	10.27	-13.6	9.7
8,965.0	1.93	219.22	8,892.1	-184.3	720.7	0.18	-0.15	3.05	-16.4	10.5
9,060.0	1.80	223.79	8,987.0	-186.6	718.7	0.21	-0.14	4.81	-18.6	11.9
9,155.0	1.27	245.32	9,082.0	-188.2	716.7	0.82	-0.56	22.66	-15.4	18.4
9,250.0	0.62	115.24	9,177.0	-188.8	716.2	1.83	-0.68	-136.93	-4.0	-24.5
9,345.0	0.88	95.82	9,272.0	-189.1	717.4	0.38	0.27	-20.44	3.1	-24.6
9,440.0	2.33	40.01	9,367.0	-187.7	719.3	2.08	1.53	-58.75	19.7	-11.8
9,535.0	1.71	315.63	9,461.9	-185.2	719.6	2.90	-0.65	-88.82	12.1	16.6
9,630.0	2.02	287.51	9,556.9	-183.7	717.0	1.00	0.33	-29.60	-0.1	19.6
9,726.0	1.14	296.39	9,652.8	-182.8	714.5	0.95	-0.92	9.25	0.3	19.7
9,821.0	1.19	291.44	9,747.8	-182.0	712.8	0.12	0.05	-5.21	-3.3	19.5
9,916.0	0.79	308.14	9,842.8	-181.2	711.3	0.51	-0.42	17.58	0.8	20.0
10,011.0	0.66	263.05	9,937.8	-180.9	710.3	0.60	-0.14	-47.46	-14.5	14.2
10,106.0	0.70	287.49	10,032.8	-180.8	709.2	0.31	0.04	25.73	-8.4	19.2
10,201.0	1.05	317.37	10,127.8	-180.0	708.0	0.59	0.37	31.45	0.9	21.1
10,296.0	1.54	300.41	10,222.7	-178.7	706.4	0.65	0.52	-17.85	-7.4	20.2
10,391.0	2.02	293.46	10,317.7	-177.4	703.7	0.55	0.51	-7.32	-12.8	19.0
10,486.0	1.58	320.97	10,412.6	-175.7	701.4	1.01	-0.46	28.96	-5.3	23.5
10,581.0	1.19	359.56	10,507.6	-173.7	700.5	1.04	-0.41	40.62	8.5	22.5
10,676.0	0.88	23.46	10,602.6	-172.0	700.8	0.55	-0.33	25.16	15.3	17.6



EOG Resources

Final PVA

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #751H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 32' @ 3537.0usft
Site:	Resolute 12 Fed Com	MD Reference:	KB = 32' @ 3537.0usft
Well:	#751H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM 5000.14

Survey											
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)	
10,771.0	1.10	10.54	10,697.6	-170.4	701.3	0.33	0.23	-13.60	9.3	20.4	
10,867.0	1.01	67.67	10,793.6	-169.2	702.2	1.05	-0.09	59.51	20.8	4.0	
10,962.0	1.01	47.55	10,888.6	-168.3	703.6	0.37	0.00	-21.18	16.6	10.6	
11,057.0	0.92	78.13	10,983.6	-167.6	705.0	0.54	-0.09	32.19	18.2	1.1	
11,152.0	1.10	113.03	11,078.5	-167.8	706.6	0.66	0.19	36.74	14.0	-9.0	
11,247.0	1.67	137.28	11,173.5	-169.2	708.3	0.85	0.60	25.53	6.9	-13.6	
11,342.0	1.01	184.66	11,268.5	-171.0	709.2	1.30	-0.69	49.87	-7.1	-13.3	
11,437.0	1.49	232.38	11,363.5	-172.6	708.2	1.16	0.51	50.23	-16.4	-3.0	
11,532.0	1.41	240.29	11,458.4	-174.0	706.2	0.23	-0.08	8.33	-19.1	-0.6	
11,627.0	0.97	216.21	11,553.4	-175.2	704.7	0.69	-0.46	-25.35	-19.0	-8.8	
11,723.0	0.35	277.82	11,649.4	-175.8	703.9	0.90	-0.65	64.18	-17.4	13.3	
11,818.0	0.40	297.51	11,744.4	-175.6	703.3	0.14	0.05	20.73	-12.6	18.5	
11,913.0	1.23	198.63	11,839.4	-176.4	702.7	1.42	0.87	-104.08	-17.3	-15.6	
12,008.0	2.59	204.52	11,934.3	-179.3	701.5	1.44	1.43	6.20	-22.0	-13.6	
12,103.0	1.05	112.94	12,029.3	-181.6	701.4	2.97	-1.62	-96.40	13.4	-23.7	
12,198.0	1.27	109.77	12,124.3	-182.3	703.2	0.24	0.23	-3.34	12.8	-23.0	
12,293.0	1.23	146.25	12,219.3	-183.5	704.7	0.82	-0.04	38.40	-5.3	-25.5	
12,388.0	0.09	275.27	12,314.3	-184.4	705.2	1.36	-1.20	135.81	-15.9	20.9	
12,483.0	0.31	231.76	12,409.3	-184.5	705.0	0.27	0.23	-45.80	-26.3	4.2	
12,496.0	0.35	198.01	12,422.3	-184.6	704.9	1.50	0.31	-259.62	-24.2	-11.1	
12,552.0	0.48	187.47	12,478.3	-185.0	704.8	0.27	0.23	-18.82	-22.2	-15.4	
12,593.0	0.70	194.32	12,519.3	-185.4	704.8	0.56	0.54	16.71	-24.3	-12.6	
12,605.0	0.90	324.37	12,531.3	-185.4	704.7	12.12	1.68	1,083.77	5.9	26.8	
KOP, MD:12605.0', TVD:12531.3', N/S:-185.4', E/W:704.7', INC:0.90											
12,639.6	5.04	342.22	12,565.8	-183.7	704.1	12.12	11.97	51.66	12.0	23.8	
KOP (Resolute 12 Fed Com #751H)											
12,688.0	10.90	344.27	12,613.7	-177.3	702.2	12.12	12.10	4.23	8.6	24.0	



EOG Resources

Final PVA

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #751H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 32' @ 3537.0usft
Site:	Resolute 12 Fed Com	MD Reference:	KB = 32' @ 3537.0usft
Well:	#751H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM 5000.14

Survey										
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
12,696.2	12.21	346.43	12,621.7	-175.7	701.8	16.81	15.97	26.30	8.7	23.9
HL Crossing, MD:12696.2', TVD:12621.7', N/S:-175.7', E/W:701.8', INC:12.21										
12,783.0	26.50	356.04	12,703.4	-147.3	698.2	16.81	16.46	11.08	1.3	24.8
12,879.0	42.54	2.46	12,782.3	-93.1	698.2	17.11	16.71	6.69	-15.9	25.4
12,924.0	52.12	4.04	12,812.8	-60.2	700.1	21.44	21.29	3.51	-27.8	24.8
12,955.9	57.87	4.27	12,831.1	-34.1	702.0	18.03	18.02	0.73	-38.4	23.8
FTP (Resolute 12 Fed Com #751H)										
12,974.0	61.13	4.39	12,840.3	-18.6	703.1	18.03	18.02	0.65	-44.9	23.1
13,069.0	65.00	2.81	12,883.3	66.0	708.4	4.33	4.07	-1.66	-74.0	16.2
13,164.0	62.80	2.46	12,925.1	151.2	712.4	2.34	-2.32	-0.37	-82.3	10.7
13,259.0	66.36	0.70	12,965.9	236.9	714.7	4.10	3.75	-1.85	-69.0	6.7
13,354.0	68.12	359.73	13,002.6	324.5	715.0	2.08	1.85	-1.02	-39.4	6.0
13,449.0	80.11	357.63	13,028.6	415.7	712.9	12.80	12.62	-2.21	-13.8	7.4
13,502.0	92.46	357.10	13,032.0	468.4	710.4	23.32	23.30	-1.00	-10.6	9.5
13,545.0	93.03	355.95	13,029.9	511.3	707.8	2.98	1.33	-2.67	-12.8	11.9
13,640.0	87.80	355.60	13,029.2	606.0	700.8	5.52	-5.51	-0.37	-14.0	18.4
13,735.0	91.49	359.38	13,029.8	700.9	696.7	5.56	3.88	3.98	-13.7	22.1
13,830.0	89.08	1.84	13,029.4	795.9	697.7	3.62	-2.54	2.59	-14.6	20.7
13,925.0	89.08	1.49	13,030.9	890.8	700.5	0.37	0.00	-0.37	-13.4	17.4
14,020.0	88.02	359.82	13,033.3	985.8	701.5	2.08	-1.12	-1.76	-11.4	15.9
14,116.0	86.75	0.44	13,037.7	1,081.7	701.8	1.47	-1.32	0.65	-7.4	15.2
14,211.0	88.77	0.35	13,041.4	1,176.6	702.4	2.13	2.13	-0.09	-4.1	14.1
14,306.0	88.07	0.44	13,044.0	1,271.5	703.1	0.74	-0.74	0.09	-1.8	13.0
14,401.0	89.87	0.26	13,045.7	1,366.5	703.7	1.90	1.89	-0.19	-0.5	11.9
14,496.0	90.66	0.00	13,045.3	1,461.5	703.9	0.88	0.83	-0.27	-1.3	11.3
14,591.0	90.75	359.38	13,044.1	1,556.5	703.4	0.66	0.09	-0.65	-2.9	11.3
14,686.0	91.89	0.26	13,041.9	1,651.5	703.1	1.52	1.20	0.93	-5.5	11.2



EOG Resources

Final PVA

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #751H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 32' @ 3537.0usft
Site:	Resolute 12 Fed Com	MD Reference:	KB = 32' @ 3537.0usft
Well:	#751H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM 5000.14

Survey										
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
14,782.0	91.71	0.96	13,038.9	1,747.4	704.1	0.75	-0.19	0.73	-8.9	9.7
14,877.0	90.57	1.67	13,037.0	1,842.4	706.3	1.41	-1.20	0.75	-11.1	7.0
14,971.0	89.87	2.55	13,036.6	1,936.3	709.7	1.20	-0.74	0.94	-11.9	3.1
15,066.0	88.20	2.19	13,038.2	2,031.2	713.6	1.80	-1.76	-0.38	-10.7	-1.3
15,161.0	88.02	2.11	13,041.4	2,126.1	717.2	0.21	-0.19	-0.08	-7.9	-5.3
15,256.0	88.20	2.55	13,044.5	2,221.0	721.1	0.50	0.19	0.46	-5.2	-9.6
15,352.0	88.46	1.67	13,047.3	2,316.9	724.6	0.96	0.27	-0.92	-2.8	-13.6
15,447.0	89.03	1.84	13,049.4	2,411.8	727.5	0.63	0.60	0.18	-1.1	-17.0
15,542.0	89.38	0.26	13,050.7	2,506.8	729.3	1.70	0.37	-1.66	-0.1	-19.2
15,637.0	89.25	359.65	13,051.8	2,601.8	729.2	0.66	-0.14	-0.64	0.6	-19.6
15,732.0	91.41	358.68	13,051.3	2,696.7	727.8	2.49	2.27	-1.02	-0.3	-18.6
15,827.0	91.76	358.42	13,048.7	2,791.7	725.4	0.46	0.37	-0.27	-3.3	-16.7
15,922.0	92.15	357.80	13,045.4	2,886.6	722.3	0.77	0.41	-0.65	-6.9	-14.0
16,017.0	91.85	357.80	13,042.1	2,981.4	718.6	0.32	-0.32	0.00	-10.6	-10.8
16,112.0	89.96	357.45	13,040.6	3,076.3	714.7	2.02	-1.99	-0.37	-12.5	-7.3
16,207.0	90.13	358.50	13,040.5	3,171.3	711.3	1.12	0.18	1.11	-13.0	-4.4
16,302.0	89.12	359.73	13,041.2	3,266.3	709.9	1.68	-1.06	1.29	-12.7	-3.4
16,333.5	89.19	0.19	13,041.6	3,297.7	709.8	1.49	0.23	1.47	-12.4	-3.6
TGT 1 (Resolute 12 Fed Com #751H)										
16,398.0	89.34	1.14	13,042.4	3,362.2	710.6	1.49	0.23	1.47	-11.9	-4.6
16,514.0	88.64	0.79	13,044.5	3,478.2	712.5	0.67	-0.60	-0.30	-10.3	-7.1
16,609.0	87.71	359.65	13,047.5	3,573.2	712.9	1.55	-0.98	-1.20	-7.7	-8.0
16,704.0	89.78	359.38	13,049.6	3,668.1	712.1	2.20	2.18	-0.28	-6.1	-7.6
16,799.0	90.97	0.09	13,049.0	3,763.1	711.7	1.46	1.25	0.75	-7.2	-7.6
16,894.0	89.12	358.77	13,048.9	3,858.1	710.7	2.39	-1.95	-1.39	-7.7	-7.2
16,989.0	88.95	358.33	13,050.5	3,953.1	708.3	0.50	-0.18	-0.46	-6.5	-5.2
17,084.0	88.02	358.50	13,053.0	4,048.0	705.7	1.00	-0.98	0.18	-4.4	-3.1



EOG Resources

Final PVA

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #751H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 32' @ 3537.0usft
Site:	Resolute 12 Fed Com	MD Reference:	KB = 32' @ 3537.0usft
Well:	#751H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM 5000.14

Survey										
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
17,179.0	90.26	359.30	13,054.4	4,143.0	703.9	2.50	2.36	0.84	-3.4	-1.7
17,274.0	90.88	358.59	13,053.5	4,237.9	702.1	0.99	0.65	-0.75	-4.8	-0.4
17,369.0	90.35	0.09	13,052.5	4,332.9	701.0	1.67	-0.56	1.58	-6.3	0.2
17,464.0	89.65	0.70	13,052.5	4,427.9	701.7	0.98	-0.74	0.64	-6.7	-0.9
17,560.0	88.59	0.52	13,053.9	4,523.9	702.7	1.12	-1.10	-0.19	-5.7	-2.4
17,655.0	89.17	1.05	13,055.8	4,618.9	704.0	0.83	0.61	0.56	-4.3	-4.1
17,750.0	90.00	1.58	13,056.5	4,713.8	706.2	1.04	0.87	0.56	-4.0	-6.8
17,845.0	88.51	0.61	13,057.7	4,808.8	708.0	1.87	-1.57	-1.02	-3.2	-9.0
17,940.0	90.13	2.19	13,058.9	4,903.8	710.3	2.38	1.71	1.66	-2.5	-11.8
18,036.0	89.74	0.00	13,059.0	4,999.8	712.1	2.32	-0.41	-2.28	-2.8	-14.1
18,131.0	89.74	357.01	13,059.4	5,094.7	709.7	3.15	0.00	-3.15	-2.8	-12.1
18,226.0	88.11	355.16	13,061.2	5,189.5	703.2	2.60	-1.72	-1.95	-1.5	-6.1
18,321.0	90.18	357.54	13,062.6	5,284.2	697.1	3.32	2.18	2.51	-0.5	-0.5
18,416.0	89.34	0.26	13,063.0	5,379.2	695.3	3.00	-0.88	2.86	-0.6	0.9
18,511.0	87.28	0.09	13,065.8	5,474.2	695.6	2.18	-2.17	-0.18	1.8	0.1
18,606.0	90.70	1.58	13,067.5	5,569.1	697.0	3.93	3.60	1.57	3.1	-1.7
18,701.0	84.51	0.70	13,071.4	5,664.0	698.9	6.58	-6.52	-0.93	6.6	-4.1
18,797.0	86.84	1.14	13,078.7	5,759.7	700.4	2.47	2.43	0.46	13.4	-6.1
18,892.0	91.89	2.28	13,079.7	5,854.6	703.2	5.45	5.32	1.20	14.0	-9.3
18,987.0	93.16	1.49	13,075.5	5,949.5	706.4	1.57	1.34	-0.83	9.4	-12.9
19,082.0	91.80	2.46	13,071.4	6,044.3	709.6	1.76	-1.43	1.02	4.9	-16.7
19,177.0	90.22	1.40	13,069.8	6,139.2	712.8	2.00	-1.66	-1.12	2.7	-20.3
19,272.0	87.80	358.50	13,071.4	6,234.2	712.8	3.98	-2.55	-3.05	4.0	-20.7
19,367.0	88.73	358.94	13,074.3	6,329.1	710.6	1.08	0.98	0.46	6.4	-19.0
19,462.0	88.68	357.63	13,076.4	6,424.1	707.8	1.38	-0.05	-1.38	8.1	-16.6
19,557.0	90.13	358.59	13,077.4	6,519.0	704.7	1.83	1.53	1.01	8.6	-14.0
19,652.0	89.21	356.39	13,078.0	6,613.9	700.5	2.51	-0.97	-2.32	8.8	-10.3



EOG Resources

Final PVA

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #751H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 32' @ 3537.0usft
Site:	Resolute 12 Fed Com	MD Reference:	KB = 32' @ 3537.0usft
Well:	#751H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM 5000.14

Survey										
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
19,747.0	89.12	357.36	13,079.3	6,708.8	695.3	1.03	-0.09	1.02	9.7	-5.5
19,843.0	91.32	357.80	13,079.0	6,804.7	691.3	2.34	2.29	0.46	8.9	-2.0
19,938.0	88.33	356.83	13,079.3	6,899.6	686.8	3.31	-3.15	-1.02	8.7	2.0
20,033.0	90.09	358.50	13,080.6	6,994.5	683.0	2.55	1.85	1.76	9.6	5.4
20,128.0	87.63	358.68	13,082.5	7,089.4	680.6	2.60	-2.59	0.19	11.1	7.3
20,223.0	89.25	0.26	13,085.1	7,184.4	679.7	2.38	1.71	1.66	13.2	7.7
20,318.0	89.12	1.49	13,086.4	7,279.3	681.2	1.30	-0.14	1.29	14.1	5.8
20,413.0	89.96	3.86	13,087.2	7,374.2	685.6	2.65	0.88	2.49	14.5	0.9
20,508.0	88.33	0.96	13,088.6	7,469.1	689.6	3.50	-1.72	-3.05	15.5	-3.5
20,604.0	89.82	1.23	13,090.1	7,565.1	691.4	1.58	1.55	0.28	16.6	-5.8
20,698.9	94.47	0.44	13,086.6	7,659.9	692.8	4.98	4.91	-0.83	12.6	-7.7
TGT 2 (Resolute 12 Fed Com #751H)										
20,699.0	94.48	0.44	13,086.6	7,660.0	692.8	4.98	4.90	-0.84	12.6	-7.7
20,794.0	88.86	0.17	13,083.8	7,754.9	693.3	5.92	-5.92	-0.28	9.2	-8.6
20,889.0	92.02	0.35	13,083.1	7,849.9	693.8	3.33	3.33	0.19	7.9	-9.5
20,984.0	92.68	358.42	13,079.2	7,944.8	692.8	2.15	0.69	-2.03	3.5	-9.0
21,079.0	89.38	357.80	13,077.5	8,039.7	689.6	3.53	-3.47	-0.65	1.2	-6.3
21,174.0	92.72	0.70	13,075.7	8,134.7	688.4	4.66	3.52	3.05	-1.1	-5.5
21,269.0	92.37	2.90	13,071.5	8,229.5	691.4	2.34	-0.37	2.32	-5.9	-8.9
21,364.0	91.19	3.95	13,068.6	8,324.3	697.0	1.66	-1.24	1.11	-9.4	-15.1
21,459.0	89.03	1.32	13,068.4	8,419.2	701.4	3.58	-2.27	-2.77	-10.2	-19.9
21,554.0	90.22	357.80	13,069.0	8,514.2	700.7	3.91	1.25	-3.71	-10.1	-19.6
21,648.0	92.11	359.91	13,067.1	8,608.1	698.8	3.01	2.01	2.24	-12.6	-18.2
21,743.0	85.08	358.59	13,069.4	8,703.0	697.5	7.53	-7.40	-1.39	-10.8	-17.4
21,838.0	84.55	358.59	13,078.0	8,797.6	695.2	0.56	-0.56	0.00	-2.7	-15.6
21,933.0	83.94	358.50	13,087.5	8,892.1	692.8	0.65	-0.64	-0.09	6.2	-13.6
22,028.0	85.87	357.18	13,096.0	8,986.6	689.2	2.46	2.03	-1.39	14.1	-10.5



EOG Resources

Final PVA

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #751H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 32' @ 3537.0usft
Site:	Resolute 12 Fed Com	MD Reference:	KB = 32' @ 3537.0usft
Well:	#751H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM 5000.14

Survey											
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)	
22,123.0	88.90	358.15	13,100.3	9,081.4	685.4	3.35	3.19	1.02	17.8	-7.1	
22,218.0	91.01	358.68	13,100.4	9,176.4	682.8	2.29	2.22	0.56	17.3	-4.9	
22,313.0	90.57	357.98	13,099.1	9,271.4	680.0	0.87	-0.46	-0.74	15.5	-2.6	
22,408.0	89.43	357.71	13,099.1	9,366.3	676.4	1.23	-1.20	-0.28	14.9	0.5	
22,503.0	90.04	358.86	13,099.5	9,461.2	673.6	1.37	0.64	1.21	14.8	2.9	
22,598.0	89.65	357.36	13,099.8	9,556.2	670.4	1.63	-0.41	-1.58	14.5	5.6	
22,693.0	91.23	0.79	13,099.0	9,651.2	668.9	3.97	1.66	3.61	13.2	6.6	
22,788.0	91.32	0.44	13,096.9	9,746.1	669.9	0.38	0.09	-0.37	10.5	5.2	
22,883.0	92.29	3.25	13,093.9	9,841.0	673.0	3.13	1.02	2.96	6.9	1.6	
22,978.0	92.20	3.51	13,090.2	9,935.8	678.6	0.29	-0.09	0.27	2.7	-4.4	
23,073.0	91.76	2.46	13,086.9	10,030.6	683.5	1.20	-0.46	-1.11	-1.2	-9.8	
23,164.0	92.15	2.46	13,083.8	10,121.5	687.4	0.43	0.43	0.00	-4.8	-14.2	
Final MWD Survey (MD=23164.0')											
23,219.6	92.15	2.46	13,081.7	10,177.0	689.8	0.00	0.00	0.00	-7.2	-16.8	
PBHL (Resolute 12 Fed Com #751H)											
23,220.0	92.15	2.46	13,081.7	10,177.4	689.8	0.00	0.00	0.00	-7.3	-16.8	
Final Projection to Bit (MD=23220.0')											

Design Annotations					
Measured Depth (usft)	Vertical Depth (usft)	Local Coordinates		Comment	
		+N/-S (usft)	+E/-W (usft)		
12,605.0	12,531.3	-185.4	704.7	KOP, MD:12605.0', TVD:12531.3', N/S:-185.4', E/W:704.7', INC:0.90	
12,696.2	12,621.7	-175.7	701.8	HL Crossing, MD:12696.2', TVD:12621.7', N/S:-175.7', E/W:701.8', INC:12.21	
23,164.0	13,083.8	10,121.5	687.4	Final MWD Survey (MD=23164.0')	
23,220.0	13,081.7	10,177.4	689.8	Final Projection to Bit (MD=23220.0')	

Checked By: _____ Approved By: _____ Date: _____

Intent ☐ As Drilled ☐

API #		
Operator Name:	Property Name:	Well Number

Kick Off Point (KOP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

First Take Point (FTP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

Last Take Point (LTP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

Is this well the defining well for the Horizontal Spacing Unit? ☐Is this well an infill well? ☐

If infill is yes please provide API if available, Operator Name and well number for Defining well for Horizontal Spacing Unit.

API #		
Operator Name:	Property Name:	Well Number

KZ 06/29/2018

Submit To Appropriate District Office Two Copies <u>District I</u> 1625 N. French Dr., Hobbs, NM 88240 <u>District II</u> 811 S. First St., Artesia, NM 88210 <u>District III</u> 1000 Rio Brazos Rd., Aztec, NM 87410 <u>District IV</u> 1220 S. St. Francis Dr., Santa Fe, NM 87505		State of New Mexico Energy, Minerals and Natural Resources Oil Conservation Division 1220 South St. Francis Dr. Santa Fe, NM 87505			Form C-105 Revised August 1, 2011					
WELL COMPLETION OR RECOMPLETION REPORT AND LOG										
4. Reason for filing: ☒ COMPLETION REPORT (Fill in boxes #1 through #31 for State and Fee wells only) ☐ C-144 CLOSURE ATTACHMENT (Fill in boxes #1 through #9, #15 Date Rig Released and #32 and/or #33; attach this and the plat to the C-144 closure report in accordance with 19.15.17.13.K NMAC)								1. WELL API NO. 30-025-47856		
								2. Type of Lease ☐ STATE ☐ FEE ☒ FED/INDIAN 3. State Oil & Gas Lease No. NMNM110835		
5. Lease Name or Unit Agreement Name RESOLUTE 12 FED COM								6. Well Number: 751H		
7. Type of Completion: ☒ NEW WELL ☐ WORKOVER ☐ DEEPENING ☐ PLUGBACK ☐ DIFFERENT RESERVOIR ☐ OTHER _____										
8. Name of Operator EOG RESOURCES INC								9. OGRID 7377		
10. Address of Operator PO BOX 2267 MIDLAND, TEXAS 79702								11. Pool name or Wildcat WC025 G09 S253309P; UPPER WOLFCAMP		
12. Location	Unit Ltr	Section	Township	Range	Lot	Feet from the	N/S Line	Feet from the	E/W Line	County
Surface:	O	12	25S	32E		284'	SOUTH	1697'	EAST	LEA
BH:	B	1	25S	32E		109'	NORTH	958'	EAST	LEA
13. Date Spudded 10/31/2020	14. Date T.D. Reached 01/24/2021		15. Date Rig Released 1/29/2021			16. Date Completed (Ready to Produce) 3/21/2021		17. Elevations (DF and RKB, RT, GR, etc.) 3496GL		
18. Total Measured Depth of Well MD 23,220' TVD 13,081'			19. Plug Back Measured Depth MD 23,198' TVD 13,081'			20. Was Directional Survey Made? YES		21. Type Electric and Other Logs Run None		
22. Producing Interval(s), of this completion - Top, Bottom, Name WOLFCAMP - 12,383'-22,615'										
23. CASING RECORD (Report all strings set in well)										
CASING SIZE		WEIGHT LB./FT.		DEPTH SET		HOLE SIZE		CEMENTING RECORD		AMOUNT PULLED
9 5/8"		40# J-55		1134'		12 1/4"		710 CL C/CIRC		
7 5/8"		29.7# ICP 110		12,531'		8 3/4"		1494 C/CIRC		
5 1/2"		20# HCP 110		23,198'		6 3/4"		785CL H/CIRC		
24. LINER RECORD						25. TUBING RECORD				
SIZE	TOP	BOTTOM	SACKS CEMENT	SCREEN	SIZE	DEPTH SET	PACKER SET			
26. Perforation record (interval, size, and number) 12,968'-23,141' 3 1/8", 2100 holes						27. ACID, SHOT, FRACTURE, CEMENT, SQUEEZE, ETC.				
						DEPTH INTERVAL		AMOUNT AND KIND MATERIAL USED		
						12,968'-23,141'		FRAC W/20,231,316 lbs proppant, 481,698 bbls load fld		
28. PRODUCTION										
Date First Production 3/21/2021		Production Method (<i>Flowing, gas lift, pumping - Size and type pump</i>) Flowing				Well Status (<i>Prod. or Shut-in</i>) Producing				
Date of Test 4/10/2021	Hours Tested 24	Choke Size 64	Prod'n For Test Period	Oil - Bbl 2199	Gas - MCF 13,900	Water - Bbl. 12,336	Gas - Oil Ratio 6320			
Flow Tubing Press.	Casing Pressure 3378	Calculated 24-Hour Rate	Oil - Bbl.	Gas - MCF	Water - Bbl.	Oil Gravity - API - (<i>Corr.</i>) 49				
29. Disposition of Gas (<i>Sold, used for fuel, vented, etc.</i>) SOLD								30. Test Witnessed By		
31. List Attachments C-102, C-104, C-103, Directional Survey, H spacing,										
32. If a temporary pit was used at the well, attach a plat with the location of the temporary pit.										
33. If an on-site burial was used at the well, report the exact location of the on-site burial:										
Latitude _____ Longitude _____ NAD 1927 1983										
I hereby certify that the information shown on both sides of this form is true and complete to the best of my knowledge and belief										
Signature Kristina Agee			Printed Name Kristina Agee		Title Senior Regulatory Administrator			Date 5/6/2021		
E-mail Address kristina_agee@eogresources.com										

This form is to be filed with the appropriate District Office of the Division not later than 20 days after the completion of any newly-drilled or deepened well and not later than 60 days after completion of closure. When submitted as a completion report, this shall be accompanied by one copy of all electrical and radio-activity logs run on the well and a summary of all special tests conducted, including drill stem tests. All depths reported shall be measured depths. In the case of directionally drilled wells, true vertical depths shall also be reported. For multiple completions, items 11, 12 and 26-31 shall be reported for each zone.

Southeastern New Mexico		Northwestern New Mexico	
T. Anhy Rustler 950'	T. Canyon Brushy 7,283'	T. Ojo Alamo	T. Penn A "
T. Salt 1256'	T. Strawn	T. Kirtland	T. Penn. "B"
B. Salt 4,703'	T. Atoka	T. Fruitland	T. Penn. "C"
T. Yates	T. Miss	T. Pictured Cliffs	T. Penn. "D"
T. 7 Rivers	T. Devonian	T. Cliff House	T. Leadville
T. Queen	T. Silurian	T. Menefee	T. Madison
T. Grayburg	T. Montoya	T. Point Lookout	T. Elbert
T. San Andres	T. Simpson	T. Mancos	T. McCracken
T. Glorieta	T. McKee	T. Gallup	T. Ignacio Otzte
T. Paddock	T. Ellenburger	Base Greenhorn	T. Granite
T. Blinebry	T. Gr. Wash	T. Dakota	
T. Tubb	T. Delaware Sand	T. Morrison	
T. Drinkard	T. Bone Springs	T. Todilto	
T. Abo	T. 1st BS Sand 10,053'	T. Entrada	
T. Wolfcamp 12,240'	T. 2nd BS Sand 10,512'	T. Wingate	
T. Penn	T.	T. Chinle	
T. Cisco (Bough C)	T.	T. Permian	

No. 1, from.....to.....
No. 2, from.....to.....
No. 3, from.....to.....
No. 4, from.....to.....

Include data on rate of water inflow and elevation to which water rose in hole.

No. 1, from.....to.....feet.....
 No. 2, from.....to.....feet.....
 No. 3, from.....to.....feet.....

From	To	Thickness In Feet	Lithology

From	To	Thickness In Feet	Lithology

District I

1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720

District II

811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720

District III

1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170

District IV

1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

ACKNOWLEDGMENTS

Action 27183

ACKNOWLEDGMENTS

Operator: EOG RESOURCES INC P.O. Box 2267 Midland, TX 79702	OGRID: 7377
	Action Number: 27183
	Action Type: [C-104] Completion Packet (C-104C)

ACKNOWLEDGMENTS

☐	I hereby certify that the required Water Use Report has been, or will be, submitted for this wells completion.
☐	I hereby certify that the required FracFocus disclosure has been, or will be, submitted for this wells completion.

District I
1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720
District III
1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170
District IV
1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 27183

CONDITIONS

Operator: EOG RESOURCES INC P.O. Box 2267 Midland, TX 79702	OGRID: 7377
	Action Number: 27183
	Action Type: [C-104] Completion Packet (C-104C)

CONDITIONS

Created By	Condition	Condition Date
ksimmons	None	7/16/2021
