

District I
1625 N. French Dr., Hobbs, NM 88240
District II
811 S. First St., Artesia, NM 88210
District III
1000 Rio Brazos Rd., Aztec, NM 87410
District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505

State of New Mexico
Energy, Minerals & Natural
Resources

Form C-104
Revised August 1, 2011

Submit one copy to appropriate District Office

Oil Conservation Division
1220 South St. Francis Dr.

☐ AMENDED REPORT

I. REQUEST FOR ALLOWABLE MINERAL AUTHORIZATION TO TRANSPORT

¹ Operator name and Address EOG RESOURCES INC PO BOX 2267 MIDLAND, TEXAS 79702		² OGRID Number 7377
		³ Reason for Filing Code/ Effective Date NW 07/16/2021
⁴ API Number 30 - 025-47672	⁵ Pool Name WC025 G09 S253309P; UPPER WOLFCAMP	⁶ Pool Code 98180
⁷ Property Code 328894	⁸ Property Name MERCILESS 13 FED COM	⁹ Well Number 705H

II. ¹⁰ Surface Location

Ul or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South Line	Feet from the	East/West line	County
B	13	25S	32E		289'	NORTH	2192'	EAST	LEA

¹¹ Bottom Hole Location

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
G	24	25S	32E		2530'	NORTH	2294'	EAST	LEA
¹² Lse Code	¹³ Producing Method Code FLOWING	¹⁴ Gas Connection Date	¹⁵ C-129 Permit Number	¹⁶ C-129 Effective Date	¹⁷ C-129 Expiration Date				

III. Oil and Gas Transporters

¹⁸ Transporter OGRID	¹⁹ Transporter Name and Address	²⁰ O/G/W
372812	EOGRM	OIL
151618	ENTERPRISE FIELD SERVICES	GAS
298751	REGENCY FIELD SERVICES	GAS
36785	DCP MIDSTREAM	GAS

IV. Well Completion Data

²¹ Spud Date 3/27/2021	²² Ready Date 08/14/2021	²³ TD 19,872	²⁴ PBTd 19,843	²⁵ Perforations 12,412 - 19,843'	²⁶ DHC, MC
²⁷ Hole Size	²⁸ Casing & Tubing Size	²⁹ Depth Set	³⁰ Sacks Cement		
13 1/2"	10 3/4"	1093'	520 SXS CL C/CIRC		
9 7/8"	8 3/4"	11,658'	1545 SXS CL C&H/191' ECHO		
7 7/8"	6"	19,852'	1265 SXS CL H TOC 6320' CBL		

V. Well Test Data

³¹ Date New Oil 08/14/2021	³² Gas Delivery Date 08/14/2021	³³ Test Date 08/24/2021	³⁴ Test Length 24 HRS	³⁵ Tbg. Pressure	³⁶ Csg. Pressure 2514
³⁷ Choke Size 64	³⁸ Oil 4392	³⁹ Water 6586	⁴⁰ Gas 8916		⁴¹ Test Method

⁴² I hereby certify that the rules of the Oil Conservation Division have been complied with and that the information given above is true and complete to the best of my knowledge and belief. Signature: Kay Maddox Printed name: Kay Maddox Title: SENIOR REGULATORY SPECIALIST E-mail Address: kay_maddox@eogresources.com Date: 08/26/2021	Phone: 432-638-8475	OIL CONSERVATION DIVISION
		Approved by: PATRICIA MARTINEZ
		Title: PETROLEUM SPECIALIST
		Approval Date: 10/27/2021

District I
1625 N. French Dr., Hobbs, NM 88240
Phone: (575) 393-6161 Fax: (575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone: (575) 748-1283 Fax: (575) 748-9720
District III
1000 Rio Brazos Road, Aztec, NM 87410
Phone: (505) 334-6178 Fax: (505) 334-6170
District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505
Phone: (505) 476-3460 Fax: (505) 476-3462

State of New Mexico
Energy, Minerals & Natural Resources
Department
OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505

FORM C-102

Revised August 1, 2011

Submit one copy to appropriate

District Office

☐ AMENDED REPORT

WELL LOCATION AND ACREAGE DEDICATION PLAT

¹ API Number 30-025-47672	² Pool Code 98180	³ Pool Name WC025 G09 S253309P; UPPER WOLFCAMP
⁴ Property Code 328894	⁵ Property Name MERCILESS 13 FED COM	⁶ Well Number 705H
⁷ GRID No. 7377	⁸ Operator Name EOG RESOURCES, INC.	⁹ Elevation 3497'

¹⁰Surface Location


UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
B	13	25-S	32-E	-	289'	NORTH	2192'	EAST	LEA

¹¹Bottom Hole Location If Different From Surface

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
G	24	25-S	32-E	-	2530'	NORTH	2294'	EAST	LEA

¹² Dedicated Acres 480.00	¹³ Joint or Infill	¹⁴ Consolidation Code	¹⁵ Order No.
---	-------------------------------	----------------------------------	-------------------------

No allowable will be assigned to this completion until all interests have been consolidated or a non-standard unit has been approved by the division.

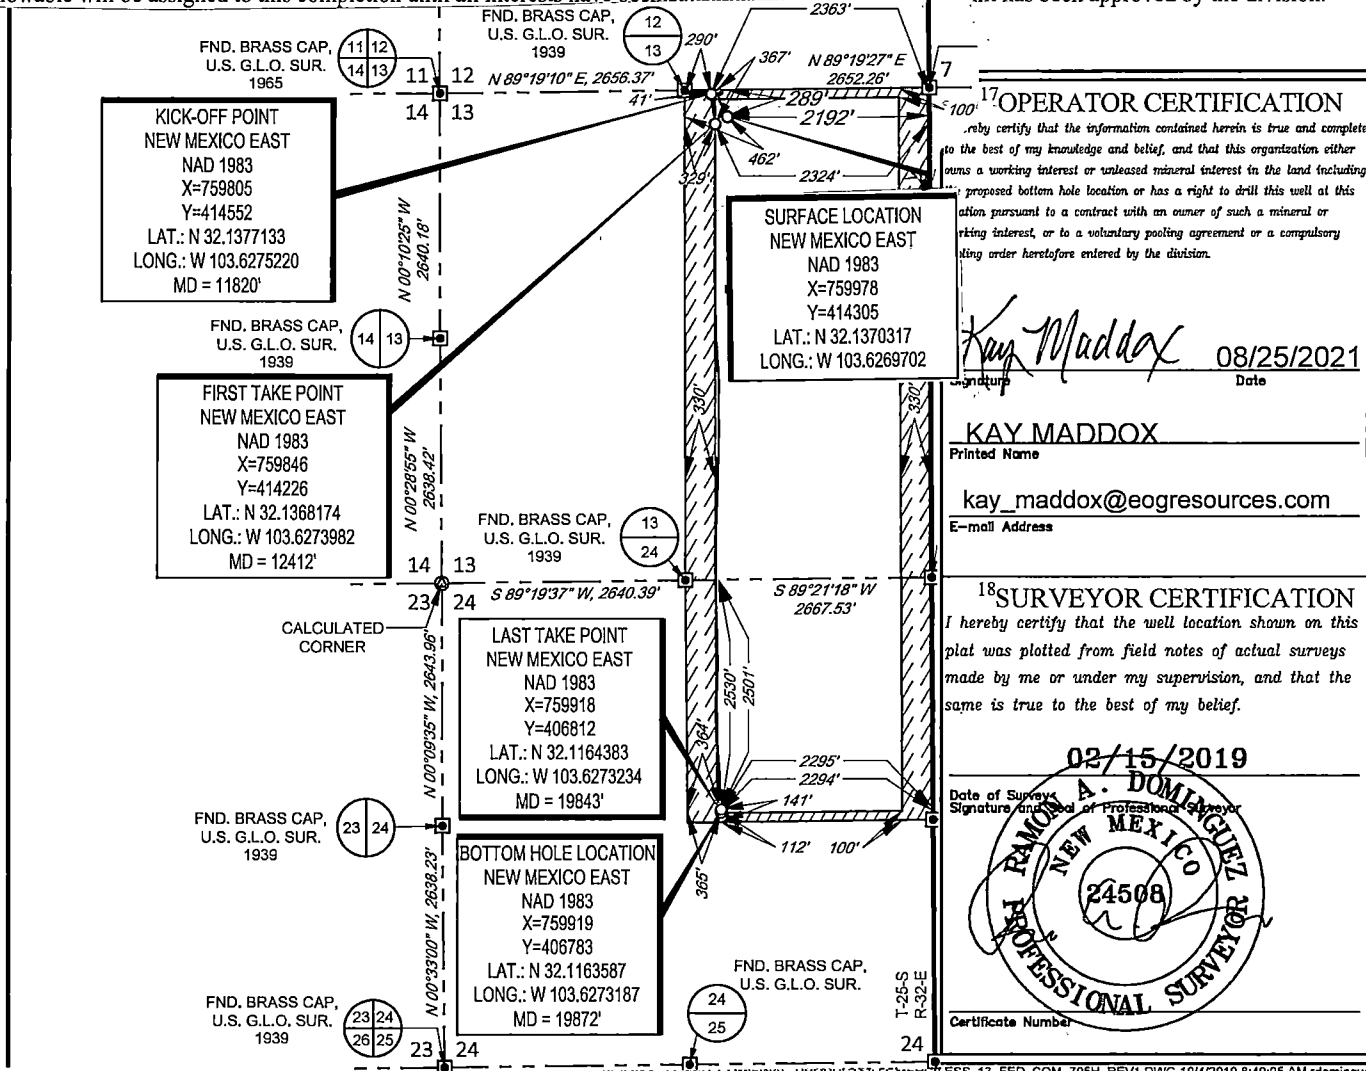¹⁷OPERATOR CERTIFICATION

I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and that this organization either owns a working interest or unleased mineral interest in the land including proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of such a mineral or working interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division.

Kay Maddox 08/25/2021
Signature Date

KAY MADDOX

Printed Name


kay_maddox@egoresources.com

E-mail Address


¹⁸SURVEYOR CERTIFICATION

I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true to the best of my belief.

02/15/2019
Date of Survey
Signature and Seal of Professional Surveyor



Certificate Number

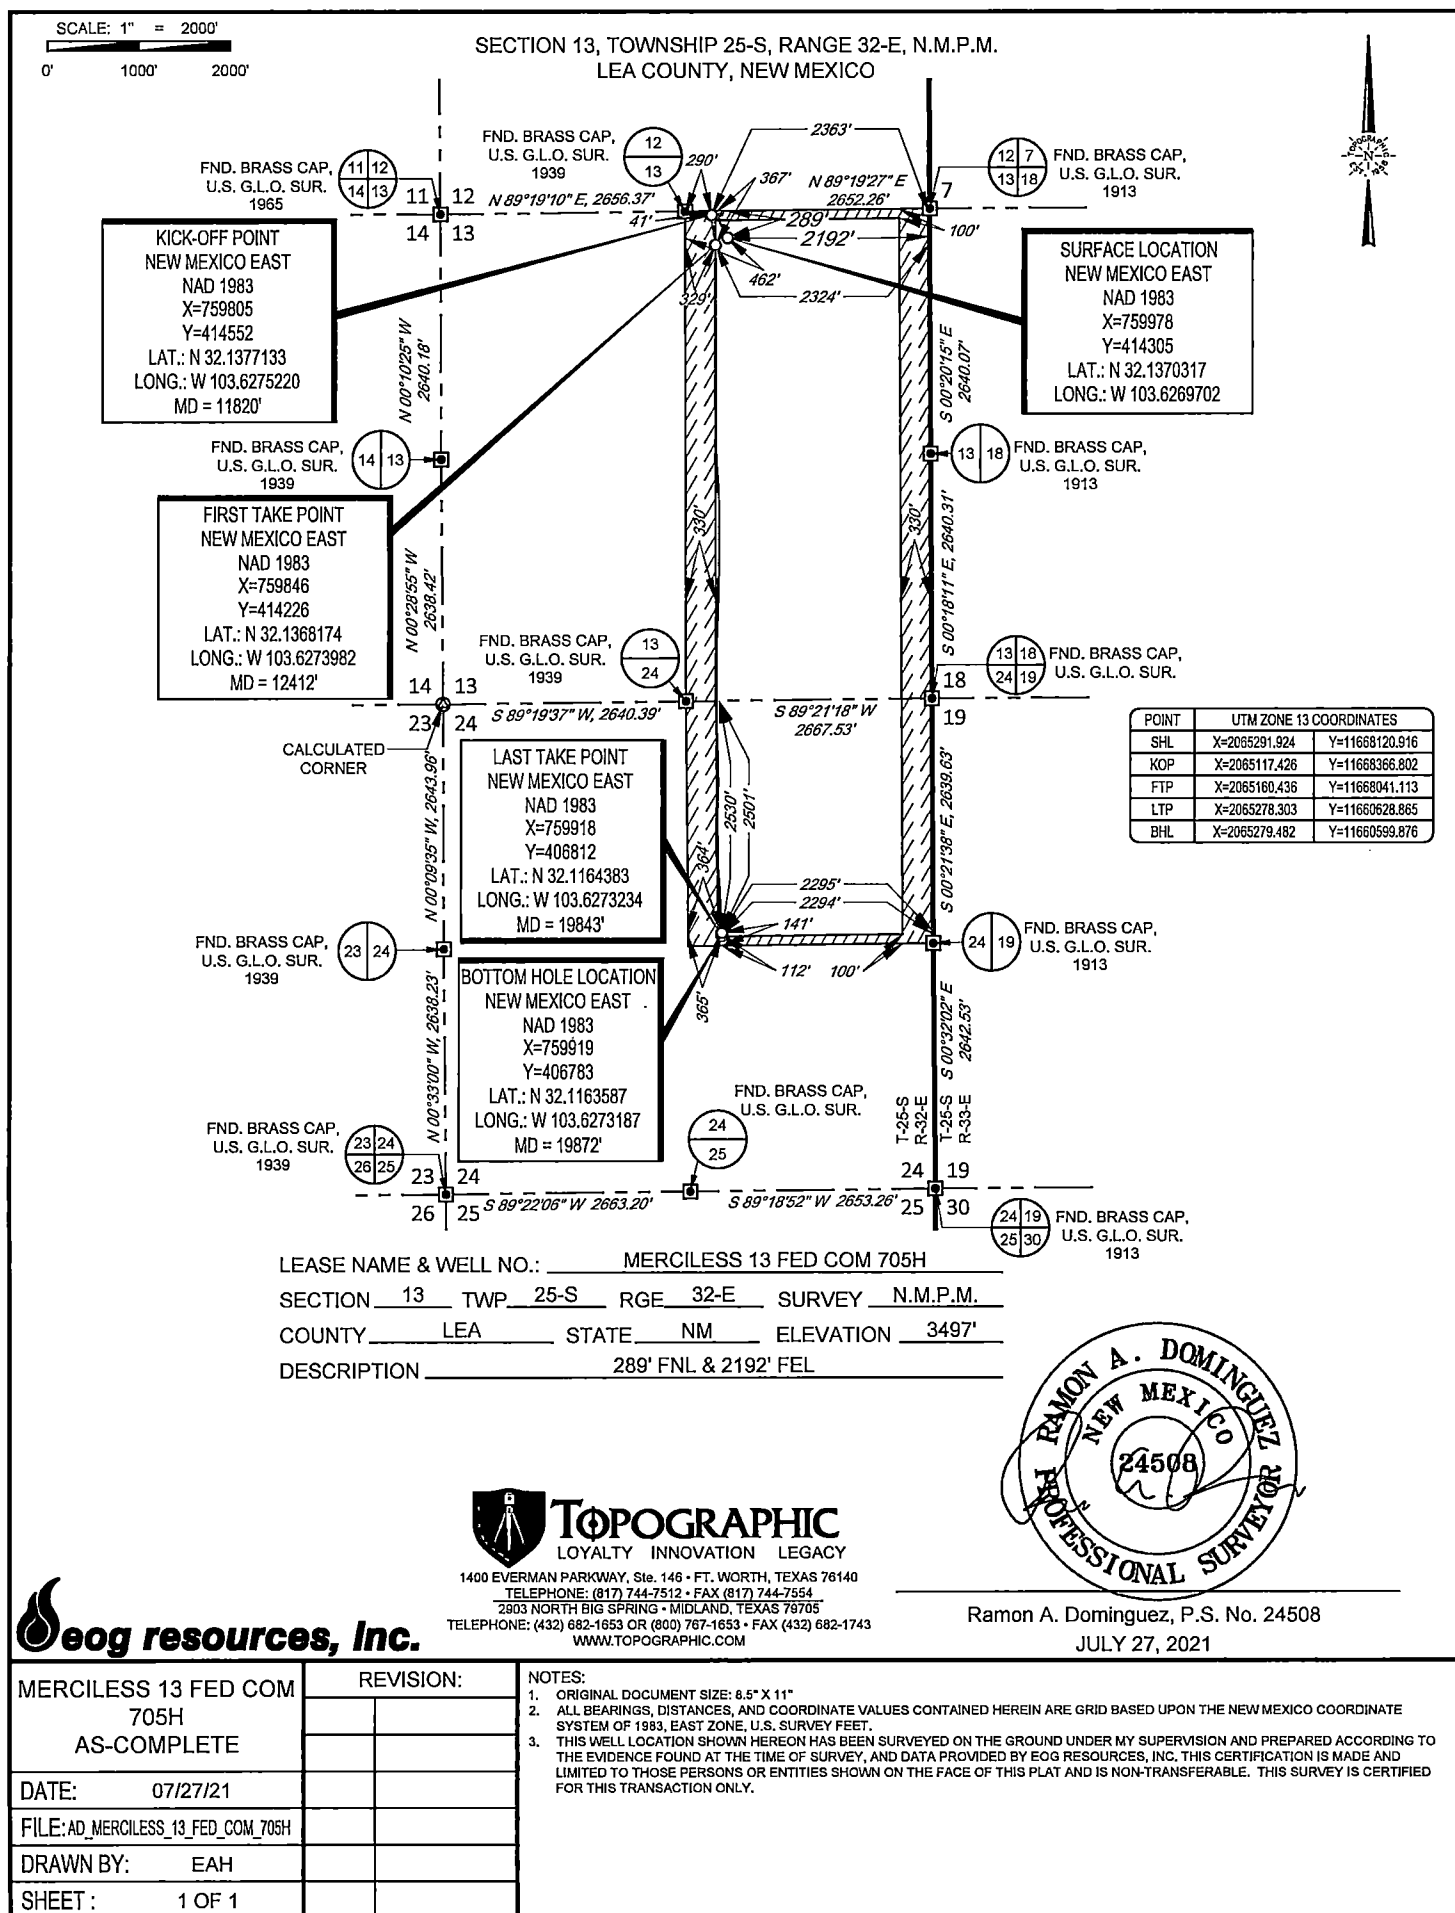



EOG Resources - Midland

Lea County, NM (NAD 83 NME)

Merciless 13 Fed Com

#705H

OH

Design: OH

Midland PVA

09 May, 2021



EOG Resources

Midland PVA

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #705H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 26' @ 3523.0usft
Site:	Merciless 13 Fed Com	MD Reference:	KB = 26' @ 3523.0usft
Well:	#705H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM

Project	Lea County, NM (NAD 83 NME)		
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	New Mexico Eastern Zone		

Site	Merciless 13 Fed Com		
Site Position:		Northing:	414,304.00 usft
From:	Map	Easting:	757,406.00 usft
Position Uncertainty:	0.0 usft	Slot Radius:	13-3/16 "
		Latitude:	32° 8' 13.472 N
		Longitude:	103° 38' 7.002 W
		Grid Convergence:	0.37 °

Well		#705H				
Well Position	+N/-S	0.0 usft	Northing:	414,305.00 usft	Latitude:	32° 8' 13.316 N
	+E/-W	0.0 usft	Easting:	759,978.00 usft	Longitude:	103° 37' 37.090 W
Position Uncertainty		0.0 usft	Wellhead Elevation:	usft	Ground Level:	3,497.0 usft

Wellbore	OH				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	IGRF2020	4/26/2020	6.70	59.85	47,554.46034702

Design	OH			
Audit Notes:				
Version:	1.0	Phase:	ACTUAL	Tie On Depth: 0.0
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)	Direction (°)
	0.0	0.0	0.0	180.72

Survey Program	Date	5/9/2021		
From (usft)	To (usft)	Survey (Wellbore)	Tool Name	Description
199.0	19,872.0	Gordon MWD (OH)	EOG MWD+IFR1	MWD + IFR1



EOG Resources

Midland PVA

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #705H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 26' @ 3523.0usft
Site:	Merciless 13 Fed Com	MD Reference:	KB = 26' @ 3523.0usft
Well:	#705H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM

Survey											
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)	
0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.00	0.0	0.0	
199.0	1.19	347.04	199.0	2.0	-0.5	0.60	0.60	0.00	-2.1	0.0	
300.0	1.06	345.38	300.0	3.9	-0.9	0.13	-0.13	-1.64	-4.0	-0.1	
389.0	0.97	355.68	389.0	5.5	-1.2	0.23	-0.10	11.57	-5.6	0.8	
479.0	0.73	356.58	478.9	6.8	-1.3	0.27	-0.27	1.00	-6.9	0.9	
568.0	0.60	2.81	567.9	7.9	-1.3	0.17	-0.15	7.00	-7.8	1.7	
662.0	0.47	6.49	661.9	8.7	-1.2	0.14	-0.14	3.91	-8.5	2.2	
756.0	0.22	37.33	755.9	9.3	-1.1	0.32	-0.27	32.81	-6.7	6.5	
850.0	0.20	50.57	849.9	9.5	-0.8	0.06	-0.02	14.09	-5.4	7.9	
1,037.0	0.12	307.63	1,036.9	9.8	-0.7	0.14	-0.04	-55.05	-6.6	-7.3	
1,121.0	0.51	353.89	1,120.9	10.3	-0.9	0.52	0.46	55.07	-10.3	-0.2	
1,215.0	3.52	348.40	1,214.9	13.5	-1.5	3.21	3.20	-5.84	-12.8	-1.5	
1,309.0	4.82	348.67	1,308.6	20.2	-2.8	1.38	1.38	0.29	-16.1	-2.5	
1,403.0	4.78	349.40	1,402.3	27.9	-4.3	0.08	-0.04	0.78	-17.9	-4.3	
1,497.0	4.67	350.54	1,496.0	35.5	-5.7	0.15	-0.12	1.21	-19.1	-6.3	
1,591.0	5.48	332.13	1,589.6	43.3	-8.4	1.92	0.86	-19.59	-17.3	-13.3	
1,685.0	6.21	328.36	1,683.1	51.6	-13.2	0.88	0.78	-4.01	-18.9	-14.4	
1,779.0	6.03	326.91	1,776.6	60.0	-18.5	0.25	-0.19	-1.54	-21.6	-14.5	
1,874.0	6.12	324.28	1,871.0	68.3	-24.2	0.31	0.09	-2.77	-23.9	-14.9	
1,968.0	5.97	326.17	1,964.5	76.5	-29.9	0.27	-0.16	2.01	-27.3	-13.3	
2,062.0	6.05	327.58	2,058.0	84.7	-35.2	0.18	0.09	1.50	-30.5	-12.1	
2,157.0	6.02	328.57	2,152.5	93.2	-40.5	0.11	-0.03	1.04	-33.6	-11.2	
2,251.0	6.26	331.84	2,245.9	101.9	-45.5	0.45	0.26	3.48	-37.2	-9.1	
2,345.0	6.37	335.15	2,339.4	111.2	-50.1	0.40	0.12	3.52	-41.0	-7.1	
2,440.0	6.56	337.74	2,433.8	121.0	-54.4	0.37	0.20	2.73	-45.0	-5.9	
2,534.0	5.37	330.66	2,527.2	129.8	-58.6	1.49	-1.27	-7.53	-46.6	-12.0	
2,628.0	4.86	323.78	2,620.9	136.8	-63.1	0.85	-0.54	-7.32	-46.3	-17.1	



EOG Resources

Midland PVA

Company: EOG Resources - Midland
Project: Lea County, NM (NAD 83 NME)
Site: Merciless 13 Fed Com
Well: #705H
Wellbore: OH
Design: OH

Local Co-ordinate Reference: Well #705H
TVD Reference: KB = 26' @ 3523.0usft
MD Reference: KB = 26' @ 3523.0usft
North Reference: Grid
Survey Calculation Method: Minimum Curvature
Database: EDM

Survey											
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)	
2,722.0	4.90	323.41	2,714.5	143.3	-67.8	0.05	0.04	-0.39	-47.2	-16.5	
2,817.0	5.05	327.35	2,809.2	150.0	-72.5	0.39	0.16	4.15	-49.4	-12.5	
2,911.0	5.06	330.84	2,902.8	157.1	-76.8	0.33	0.01	3.71	-51.3	-9.2	
3,006.0	5.01	335.08	2,997.4	164.6	-80.6	0.40	-0.05	4.46	-53.1	-5.6	
3,100.0	5.05	339.66	3,091.1	172.2	-83.7	0.43	0.04	4.87	-54.7	-2.1	
3,194.0	4.89	342.39	3,184.7	179.9	-86.4	0.30	-0.17	2.90	-56.0	-0.7	
3,288.0	4.62	344.64	3,278.4	187.3	-88.6	0.35	-0.29	2.39	-56.9	0.0	
3,383.0	5.29	347.41	3,373.1	195.3	-90.6	0.75	0.71	2.92	-58.3	0.9	
3,477.0	5.30	347.25	3,466.7	203.7	-92.5	0.02	0.01	-0.17	-60.2	-1.2	
3,572.0	4.68	343.71	3,561.3	211.7	-94.5	0.73	-0.65	-3.73	-61.4	-6.7	
3,666.0	4.12	346.38	3,655.0	218.7	-96.4	0.63	-0.60	2.84	-62.0	-5.6	
3,760.0	3.78	359.63	3,748.8	225.1	-97.2	1.03	-0.36	14.10	-61.9	6.2	
3,854.0	3.36	356.31	3,842.6	230.9	-97.4	0.50	-0.45	-3.53	-61.6	-0.6	
3,949.0	2.83	352.89	3,937.5	236.0	-97.9	0.59	-0.56	-3.60	-60.0	-7.1	
4,043.0	1.83	350.86	4,031.4	239.8	-98.4	1.07	-1.06	-2.16	-57.0	-11.7	
4,137.0	1.54	356.37	4,125.4	242.6	-98.7	0.35	-0.31	5.86	-54.2	-9.0	
4,232.0	1.26	49.94	4,220.3	244.5	-98.0	1.35	-0.29	56.39	-39.9	32.3	
4,326.0	1.61	86.22	4,314.3	245.3	-95.9	1.01	0.37	38.60	-18.2	43.9	
4,420.0	1.64	96.35	4,408.3	245.2	-93.2	0.31	0.03	10.78	-16.9	40.9	
4,514.0	2.87	121.80	4,502.2	243.8	-89.9	1.66	1.31	27.07	-7.3	41.4	
4,608.0	2.50	118.91	4,596.1	241.6	-86.1	0.42	-0.39	-3.07	-19.6	37.1	
4,702.0	1.73	97.58	4,690.0	240.4	-82.9	1.16	-0.82	-22.69	-39.3	21.1	
4,796.0	1.57	91.49	4,784.0	240.2	-80.2	0.25	-0.17	-6.48	-47.6	10.6	
4,890.0	1.45	80.38	4,878.0	240.4	-77.7	0.34	-0.13	-11.82	-53.0	-4.3	
4,985.0	1.29	74.83	4,972.9	240.8	-75.5	0.22	-0.17	-5.84	-55.2	-11.9	
5,079.0	1.36	61.37	5,066.9	241.6	-73.5	0.34	0.07	-14.32	-53.1	-24.8	
5,267.0	1.39	56.65	5,254.8	244.0	-69.7	0.06	0.02	-2.51	-55.4	-29.3	



EOG Resources

Midland PVA

Company: EOG Resources - Midland
Project: Lea County, NM (NAD 83 NME)
Site: Merciless 13 Fed Com
Well: #705H
Wellbore: OH
Design: OH

Local Co-ordinate Reference: Well #705H
TVD Reference: KB = 26' @ 3523.0usft
MD Reference: KB = 26' @ 3523.0usft
North Reference: Grid
Survey Calculation Method: Minimum Curvature
Database: EDM

Survey										
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
5,361.0	1.54	50.59	5,348.8	245.4	-67.7	0.23	0.16	-6.45	-54.3	-35.1
5,455.0	1.17	56.02	5,442.8	246.7	-66.0	0.42	-0.39	5.78	-59.6	-29.7
5,550.0	1.16	47.34	5,537.8	247.9	-64.4	0.19	-0.01	-9.14	-56.4	-38.5
5,738.0	1.51	39.19	5,725.7	251.1	-61.5	0.21	0.19	-4.34	-54.7	-46.4
5,832.0	1.44	33.05	5,819.7	253.1	-60.1	0.18	-0.07	-6.53	-51.9	-52.1
5,926.0	1.29	21.61	5,913.7	255.1	-59.0	0.33	-0.16	-12.17	-42.7	-61.6
6,020.0	1.27	21.41	6,007.6	257.0	-58.3	0.02	-0.02	-0.21	-44.6	-61.7
6,115.0	1.03	16.98	6,102.6	258.8	-57.6	0.27	-0.25	-4.66	-41.6	-65.1
6,209.0	1.06	4.49	6,196.6	260.5	-57.3	0.24	0.03	-13.29	-28.3	-72.7
6,397.0	1.23	4.00	6,384.6	264.2	-57.0	0.09	0.09	-0.26	-31.4	-73.0
6,491.0	1.32	7.77	6,478.5	266.3	-56.8	0.13	0.10	4.01	-38.2	-70.7
6,585.0	1.09	0.40	6,572.5	268.3	-56.7	0.29	-0.24	-7.84	-30.8	-75.1
6,774.0	1.04	17.28	6,761.5	271.7	-56.1	0.17	-0.03	8.93	-54.7	-62.4
6,868.0	0.99	12.96	6,855.5	273.3	-55.7	0.10	-0.05	-4.60	-51.5	-66.4
6,962.0	1.11	10.17	6,949.5	275.0	-55.4	0.14	0.13	-2.97	-50.0	-68.9
7,057.0	1.13	5.58	7,044.4	276.8	-55.1	0.10	0.02	-4.83	-46.1	-72.8
7,151.0	0.94	331.48	7,138.4	278.4	-55.4	0.67	-0.20	-36.28	1.0	-86.6
7,246.0	0.88	264.88	7,233.4	279.1	-56.5	1.05	-0.06	-70.11	78.9	-34.2
7,340.0	1.01	272.41	7,327.4	279.0	-58.0	0.19	0.14	8.01	72.2	-44.1
7,435.0	1.28	272.79	7,422.4	279.1	-59.9	0.28	0.28	0.40	70.0	-44.6
7,529.0	1.22	271.50	7,516.4	279.2	-62.0	0.07	-0.06	-1.37	68.9	-43.0
7,623.0	1.27	259.80	7,610.3	279.0	-64.0	0.28	0.05	-12.45	74.2	-28.4
7,717.0	1.46	263.11	7,704.3	278.7	-66.2	0.22	0.20	3.52	70.2	-32.5
7,812.0	1.46	257.95	7,799.3	278.3	-68.6	0.14	0.00	-5.43	70.4	-26.2
7,906.0	1.52	243.03	7,893.2	277.5	-70.9	0.42	0.06	-15.87	72.4	-7.5
8,000.0	1.58	240.02	7,987.2	276.3	-73.1	0.11	0.06	-3.20	70.1	-3.7
8,094.0	1.33	234.62	8,081.2	275.0	-75.1	0.30	-0.27	-5.74	67.8	2.8



EOG Resources

Midland PVA

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #705H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 26' @ 3523.0usft
Site:	Merciless 13 Fed Com	MD Reference:	KB = 26' @ 3523.0usft
Well:	#705H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM

Survey											
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)	
8,189.0	0.95	235.41	8,176.2	273.9	-76.7	0.40	-0.40	0.83	65.9	1.8	
8,283.0	1.12	224.55	8,270.2	272.8	-78.0	0.28	0.18	-11.55	62.7	14.1	
8,377.0	1.31	219.37	8,364.1	271.3	-79.3	0.23	0.20	-5.51	59.2	19.6	
8,472.0	1.63	223.66	8,459.1	269.5	-80.9	0.36	0.34	4.52	58.1	15.2	
8,566.0	1.69	222.47	8,553.1	267.5	-82.8	0.07	0.06	-1.27	55.0	16.4	
8,660.0	1.70	229.75	8,647.0	265.6	-84.8	0.23	0.01	7.74	53.9	9.4	
8,754.0	1.90	226.93	8,741.0	263.6	-87.0	0.23	0.21	-3.00	50.4	12.0	
8,942.0	1.78	232.20	8,928.9	259.7	-91.6	0.11	-0.06	2.80	45.3	7.6	
9,037.0	1.74	231.90	9,023.8	257.9	-93.9	0.04	-0.04	-0.32	42.3	7.9	
9,131.0	1.79	237.08	9,117.8	256.3	-96.2	0.18	0.05	5.51	40.0	4.1	
9,225.0	1.54	230.73	9,211.7	254.7	-98.4	0.33	-0.27	-6.76	36.5	8.4	
9,319.0	1.18	229.79	9,305.7	253.2	-100.1	0.38	-0.38	-1.00	34.2	8.9	
9,414.0	1.60	234.66	9,400.7	251.8	-102.0	0.46	0.44	5.13	32.5	6.1	
9,508.0	2.12	243.08	9,494.6	250.3	-104.6	0.62	0.55	8.96	30.0	1.5	
9,602.0	1.82	244.87	9,588.6	248.9	-107.5	0.33	-0.32	1.90	26.8	0.6	
9,696.0	1.80	261.34	9,682.5	248.0	-110.3	0.55	-0.02	17.52	23.0	-6.6	
9,791.0	2.44	283.22	9,777.5	248.2	-113.7	1.07	0.67	23.03	15.4	-14.2	
9,885.0	2.95	279.43	9,871.4	249.1	-118.1	0.57	0.54	-4.03	11.9	-13.2	
9,979.0	3.00	276.92	9,965.2	249.8	-122.9	0.15	0.05	-2.67	7.6	-12.8	
10,074.0	3.00	272.78	10,060.1	250.2	-127.9	0.23	0.00	-4.36	3.5	-12.4	
10,168.0	2.52	275.15	10,154.0	250.5	-132.4	0.52	-0.51	2.52	-1.5	-12.4	
10,262.0	2.67	279.06	10,247.9	251.1	-136.6	0.25	0.16	4.16	-6.6	-12.2	
10,356.0	2.49	278.64	10,341.8	251.7	-140.8	0.19	-0.19	-0.45	-10.7	-12.2	
10,451.0	1.88	279.00	10,436.7	252.3	-144.4	0.64	-0.64	0.38	-14.4	-12.2	
10,545.0	2.59	276.94	10,530.7	252.8	-148.0	0.76	0.76	-2.19	-17.6	-12.7	
10,639.0	2.80	273.56	10,624.6	253.2	-152.4	0.28	0.22	-3.60	-21.3	-13.9	
10,733.0	1.68	264.44	10,718.5	253.2	-156.0	1.25	-1.19	-9.70	-22.5	-17.4	



EOG Resources

Midland PVA

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #705H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 26' @ 3523.0usft
Site:	Merciless 13 Fed Com	MD Reference:	KB = 26' @ 3523.0usft
Well:	#705H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM

Survey										
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
10,827.0	0.97	279.30	10,812.5	253.2	-158.2	0.83	-0.76	15.81	-28.3	-10.7
10,922.0	0.61	240.02	10,907.5	253.0	-159.4	0.66	-0.38	-41.35	-16.2	-26.7
11,016.0	0.59	172.40	11,001.5	252.3	-159.8	0.71	-0.02	-71.94	17.9	-25.7
11,110.0	0.89	196.34	11,095.4	251.1	-159.9	0.45	0.32	25.47	4.7	-30.5
11,204.0	0.25	229.31	11,189.4	250.3	-160.3	0.74	-0.68	35.07	-13.4	-27.8
11,298.0	0.84	288.55	11,283.4	250.4	-161.1	0.79	0.63	63.02	-31.5	-2.5
11,393.0	1.63	260.90	11,378.4	250.4	-163.1	1.02	0.83	-29.11	-28.8	-17.2
11,487.0	1.20	278.27	11,472.4	250.3	-165.4	0.64	-0.46	18.48	-34.8	-7.4
11,581.0	1.46	259.80	11,566.4	250.2	-167.6	0.53	0.28	-19.65	-32.8	-18.4
11,753.0	1.20	258.43	11,738.3	249.5	-171.5	0.15	-0.15	-0.80	-36.4	-19.2
11,820.0	4.38	185.97	11,805.2	246.8	-172.4	6.23	4.74	-108.15	4.5	-41.1
KOP, MD:11820.0', TVD:11805.2', N/S:246.8', E/W:-172.4', INC:4.38										
11,847.0	6.01	181.56	11,832.1	244.4	-172.6	6.23	6.05	-16.34	5.2	-40.7
11,941.0	16.86	181.34	11,924.1	225.8	-173.0	11.54	11.54	-0.23	-6.8	-40.9
12,035.0	30.14	175.40	12,010.1	188.4	-171.4	14.33	14.13	-6.32	-16.6	-41.0
12,037.5	30.39	175.20	12,012.3	187.2	-171.3	10.99	10.19	-8.15	-16.9	-41.0
FTP Crossing, MD:12037.5', TVD:12012.3', N/S:187.2', E/W:-171.3', INC:30.39										
12,130.0	39.99	169.33	12,087.8	134.5	-163.9	10.99	10.37	-6.34	-27.7	-36.8
12,224.0	46.65	170.28	12,156.2	71.1	-152.5	7.12	7.09	1.01	-36.9	-25.6
12,318.0	53.65	170.63	12,216.4	0.0	-140.5	7.45	7.45	0.37	-36.7	-12.9
12,412.0	60.00	176.68	12,267.8	-78.2	-132.0	8.64	6.76	6.44	-27.2	-2.1
12,507.0	70.88	180.52	12,307.3	-164.4	-130.0	12.03	11.45	4.04	-11.6	0.0
12,601.0	84.33	180.76	12,327.4	-256.0	-131.1	14.31	14.31	0.26	2.5	-1.5
12,695.0	89.94	183.26	12,332.1	-349.8	-134.3	6.53	5.97	2.66	7.4	-5.2
12,789.0	91.68	179.77	12,330.8	-443.7	-136.8	4.15	1.85	-3.71	6.2	-8.2
12,884.0	90.56	179.54	12,328.9	-538.7	-136.3	1.20	-1.18	-0.24	4.6	-8.1
12,978.0	90.31	179.25	12,328.2	-632.7	-135.3	0.41	-0.27	-0.31	4.1	-7.5



EOG Resources

Midland PVA

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #705H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 26' @ 3523.0usft
Site:	Merciless 13 Fed Com	MD Reference:	KB = 26' @ 3523.0usft
Well:	#705H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM

Survey										
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
13,073.0	90.92	179.94	12,327.2	-727.7	-134.6	0.97	0.64	0.73	3.3	-7.3
13,167.0	91.12	179.95	12,325.5	-821.6	-134.5	0.21	0.21	0.01	1.8	-7.7
13,261.0	90.45	180.38	12,324.2	-915.6	-134.8	0.85	-0.71	0.46	0.7	-8.4
13,355.0	89.02	179.56	12,324.6	-1,009.6	-134.7	1.75	-1.52	-0.87	1.4	-8.8
13,450.0	90.22	180.49	12,325.3	-1,104.6	-134.8	1.60	1.26	0.98	2.2	-9.3
13,544.0	90.25	180.08	12,324.9	-1,198.6	-135.2	0.44	0.03	-0.44	2.0	-10.3
13,639.0	88.99	179.27	12,325.5	-1,293.6	-134.7	1.58	-1.33	-0.85	2.9	-10.2
13,733.0	88.68	179.81	12,327.4	-1,387.6	-133.9	0.66	-0.33	0.57	5.0	-9.9
13,827.0	93.05	180.56	12,326.0	-1,481.6	-134.2	4.72	4.65	0.80	3.8	-10.7
13,922.0	92.41	180.27	12,321.5	-1,576.4	-134.9	0.74	-0.67	-0.31	-0.5	-11.8
14,016.0	91.51	179.86	12,318.3	-1,670.4	-135.0	1.05	-0.96	-0.44	-3.5	-12.4
14,126.0	90.10	178.42	12,316.7	-1,780.4	-133.4	1.83	-1.28	-1.31	-4.9	-11.3
14,205.0	89.66	178.59	12,316.9	-1,859.3	-131.3	0.60	-0.56	0.22	-4.5	-9.6
14,299.0	89.58	178.98	12,317.5	-1,953.3	-129.3	0.42	-0.09	0.41	-3.7	-8.1
14,393.0	89.83	179.69	12,318.0	-2,047.3	-128.2	0.80	0.27	0.76	-3.0	-7.4
14,488.0	89.72	179.41	12,318.4	-2,142.3	-127.5	0.32	-0.12	-0.29	-2.4	-7.2
14,582.0	89.02	178.58	12,319.4	-2,236.3	-125.8	1.16	-0.74	-0.88	-1.2	-6.0
14,676.0	88.80	177.22	12,321.2	-2,330.2	-122.4	1.47	-0.23	-1.45	0.8	-3.0
14,770.0	88.35	176.12	12,323.5	-2,424.0	-116.9	1.26	-0.48	-1.17	3.4	2.0
14,864.0	88.57	176.03	12,326.1	-2,517.8	-110.5	0.25	0.23	-0.10	6.1	8.0
14,958.0	88.21	174.76	12,328.7	-2,611.4	-103.0	1.40	-0.38	-1.35	8.9	15.1
15,053.0	89.61	177.28	12,330.5	-2,706.2	-96.4	3.03	1.47	2.65	10.9	21.2
15,181.0	92.21	179.30	12,328.5	-2,834.1	-92.6	2.57	2.03	1.58	9.1	24.4
15,241.0	92.55	179.81	12,326.0	-2,894.0	-92.1	1.02	0.57	0.85	6.8	24.6
15,335.0	90.00	180.51	12,323.9	-2,988.0	-92.4	2.81	-2.71	0.74	4.9	23.8
15,429.0	89.83	180.16	12,324.0	-3,082.0	-92.9	0.41	-0.18	-0.37	5.2	22.8
15,523.0	90.36	179.80	12,323.9	-3,176.0	-92.9	0.68	0.56	-0.38	5.2	22.4



EOG Resources

Midland PVA

Company: EOG Resources - Midland
Project: Lea County, NM (NAD 83 NME)
Site: Merciless 13 Fed Com
Well: #705H
Wellbore: OH
Design: OH

Local Co-ordinate Reference: Well #705H
TVD Reference: KB = 26' @ 3523.0usft
MD Reference: KB = 26' @ 3523.0usft
North Reference: Grid
Survey Calculation Method: Minimum Curvature
Database: EDM

Survey											
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)	
15,617.0	90.81	178.81	12,322.9	-3,270.0	-91.7	1.16	0.48	-1.05	4.5	23.1	
15,711.0	90.14	180.59	12,322.1	-3,364.0	-91.2	2.02	-0.71	1.89	3.9	23.1	
15,805.0	88.23	180.88	12,323.5	-3,457.9	-92.4	2.06	-2.03	0.31	5.4	21.5	
15,899.0	86.30	180.99	12,328.0	-3,551.8	-94.0	2.06	-2.05	0.12	10.1	19.5	
15,994.0	88.57	180.76	12,332.2	-3,646.7	-95.4	2.40	2.39	-0.24	14.5	17.5	
16,088.0	89.44	181.23	12,333.8	-3,740.7	-97.1	1.05	0.93	0.50	16.3	15.5	
16,182.0	90.34	181.70	12,334.0	-3,834.6	-99.5	1.08	0.96	0.50	16.7	12.6	
16,276.0	90.48	181.59	12,333.4	-3,928.6	-102.2	0.19	0.15	-0.12	16.2	9.4	
16,370.0	91.15	181.93	12,332.0	-4,022.5	-105.0	0.80	0.71	0.36	15.0	6.1	
16,464.0	91.06	181.97	12,330.2	-4,116.5	-108.2	0.10	-0.10	0.04	13.4	2.4	
16,558.0	90.11	181.32	12,329.2	-4,210.4	-110.9	1.22	-1.01	-0.69	12.6	-0.7	
16,653.0	91.46	182.40	12,327.9	-4,305.4	-114.0	1.82	1.42	1.14	11.5	-4.3	
16,747.0	91.51	182.62	12,325.5	-4,399.2	-118.1	0.24	0.05	0.23	9.3	-8.8	
16,841.0	91.62	182.47	12,322.9	-4,493.1	-122.3	0.20	0.12	-0.16	6.9	-13.5	
16,935.0	90.25	180.53	12,321.4	-4,587.1	-124.8	2.53	-1.46	-2.06	5.6	-16.4	
17,029.0	90.81	180.42	12,320.5	-4,681.0	-125.6	0.61	0.60	-0.12	4.9	-17.6	
17,123.0	88.32	179.63	12,321.2	-4,775.0	-125.6	2.78	-2.65	-0.84	5.8	-18.1	
17,218.0	87.65	179.67	12,324.6	-4,870.0	-125.0	0.71	-0.71	0.04	9.3	-18.0	
17,312.0	86.83	179.70	12,329.1	-4,963.9	-124.5	0.87	-0.87	0.03	14.0	-18.0	
17,406.0	89.61	178.40	12,332.0	-5,057.8	-122.9	3.26	2.96	-1.38	17.1	-16.9	
17,501.0	89.52	178.71	12,332.8	-5,152.8	-120.5	0.34	-0.09	0.33	18.0	-14.9	
17,595.0	89.13	177.95	12,333.9	-5,246.7	-117.8	0.91	-0.41	-0.81	19.3	-12.7	
17,689.0	89.78	177.75	12,334.8	-5,340.6	-114.3	0.72	0.69	-0.21	20.4	-9.6	
17,783.0	91.99	178.91	12,333.3	-5,434.6	-111.5	2.66	2.35	1.23	19.1	-7.3	
17,877.0	91.04	178.20	12,330.8	-5,528.5	-109.2	1.26	-1.01	-0.76	16.8	-5.4	
17,972.0	90.76	178.22	12,329.3	-5,623.5	-106.2	0.30	-0.29	0.02	15.5	-2.9	
18,066.0	91.06	178.40	12,327.8	-5,717.4	-103.4	0.37	0.32	0.19	14.2	-0.6	



EOG Resources

Midland PVA

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #705H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 26' @ 3523.0usft
Site:	Merciless 13 Fed Com	MD Reference:	KB = 26' @ 3523.0usft
Well:	#705H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM

Survey										
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
18,160.0	92.46	178.88	12,324.9	-5,811.3	-101.2	1.57	1.49	0.51	11.5	1.2
18,254.0	90.95	179.68	12,322.1	-5,905.3	-100.0	1.82	-1.61	0.85	8.9	1.9
18,348.0	90.34	183.81	12,321.1	-5,999.2	-102.9	4.44	-0.65	4.39	8.1	-1.4
18,442.0	88.52	185.57	12,322.0	-6,092.9	-110.6	2.69	-1.94	1.87	9.2	-9.6
18,537.0	87.59	182.30	12,325.3	-6,187.6	-117.1	3.58	-0.98	-3.44	12.6	-16.6
18,631.0	85.82	181.28	12,330.7	-6,281.4	-120.0	2.17	-1.88	-1.09	18.1	-20.0
18,725.0	88.04	179.87	12,335.7	-6,375.2	-121.0	2.80	2.36	-1.50	23.4	-21.3
18,820.0	89.94	179.07	12,337.4	-6,470.2	-120.1	2.17	2.00	-0.84	25.3	-20.9
18,915.0	90.42	177.78	12,337.1	-6,565.2	-117.5	1.45	0.51	-1.36	25.2	-18.8
19,009.0	89.69	176.37	12,337.0	-6,659.1	-112.7	1.69	-0.78	-1.50	25.3	-14.4
19,103.0	89.94	177.05	12,337.3	-6,752.9	-107.3	0.77	0.27	0.72	25.7	-9.5
19,223.0	92.33	174.22	12,334.9	-6,872.5	-98.1	3.09	1.99	-2.36	23.6	-1.0
19,291.0	93.87	174.70	12,331.2	-6,940.1	-91.6	2.37	2.26	0.71	20.1	5.2
19,385.0	92.16	177.15	12,326.3	-7,033.7	-84.9	3.18	-1.82	2.61	15.3	11.5
19,479.0	92.38	177.23	12,322.6	-7,127.5	-80.3	0.25	0.23	0.09	11.8	15.6
19,573.0	91.04	177.04	12,319.7	-7,221.4	-75.6	1.44	-1.43	-0.20	9.2	19.8
19,673.0	90.39	176.69	12,318.5	-7,321.2	-70.2	0.74	-0.65	-0.35	8.1	24.8
Last MWD Survey (MD=19673.0')										
19,872.0	90.39	176.69	12,317.1	-7,519.9	-58.7	0.00	0.00	0.00	7.2	35.3
Projection to Bit (MD=19872.0')										



EOG Resources

Midland PVA

Company: EOG Resources - Midland
Project: Lea County, NM (NAD 83 NME)
Site: Merciless 13 Fed Com
Well: #705H
Wellbore: OH
Design: OH

Local Co-ordinate Reference: Well #705H
TVD Reference: KB = 26' @ 3523.0usft
MD Reference: KB = 26' @ 3523.0usft
North Reference: Grid
Survey Calculation Method: Minimum Curvature
Database: EDM

Design Annotations

Measured Depth (usft)	Vertical Depth (usft)	Local Coordinates		Comment
		+N/-S (usft)	+E/-W (usft)	
11,820.0	11,805.2	246.8	-172.4	KOP, MD:11820.0', TVD:11805.2',N/S:246.8', E/W:-172.4', INC:4.38
12,037.5	12,012.3	187.2	-171.3	FTP Crossing, MD:12037.5', TVD:12012.3',N/S:187.2', E/W:-171.3', INC:30.39
19,673.0	12,318.5	-7,321.2	-70.2	Last MWD Survey (MD=19673.0')
19,872.0	12,317.1	-7,519.9	-58.7	Projection to Bit (MD=19872.0')

Checked By: _____ Approved By: _____ Date: _____

I CERTIFY THIS SURVEY TO BE TRUE AND CORRECT TO THE BEST OF MY BELIEF AND KNOWLEDGE
 KAY MADDOX 08/25/2021

Intent ☐ As Drilled ☐

API #		
Operator Name:	Property Name:	Well Number

Kick Off Point (KOP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

First Take Point (FTP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

Last Take Point (LTP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

Is this well the defining well for the Horizontal Spacing Unit? ☐Is this well an infill well? ☐

If infill is yes please provide API if available, Operator Name and well number for Defining well for Horizontal Spacing Unit.

API #		
Operator Name:	Property Name:	Well Number

KZ 06/29/2018

Submit To Appropriate District Office Two Copies <u>District I</u> 1625 N. French Dr., Hobbs, NM 88240 <u>District II</u> 811 S. First St., Artesia, NM 88210 <u>District III</u> 1000 Rio Brazos Rd., Aztec, NM 87410 <u>District IV</u> 1220 S. St. Francis Dr., Santa Fe, NM 87505		State of New Mexico Energy, Minerals and Natural Resources Oil Conservation Division 1220 South St. Francis Dr. Santa Fe, NM 87505			Form C-105 Revised August 1, 2011					
WELL COMPLETION OR RECOMPLETION REPORT AND LOG										
4. Reason for filing: ☒ COMPLETION REPORT (Fill in boxes #1 through #31 for State and Fee wells only) ☐ C-144 CLOSURE ATTACHMENT (Fill in boxes #1 through #9, #15 Date Rig Released and #32 and/or #33; attach this and the plat to the C-144 closure report in accordance with 19.15.17.13.K NMAC)								5. Lease Name or Unit Agreement Name MERCILESS 13 FED COM		
								6. Well Number: 705H		
7. Type of Completion: ☒ NEW WELL ☐ WORKOVER ☐ DEEPENING ☐ PLUGBACK ☐ DIFFERENT RESERVOIR ☐ OTHER _____										
8. Name of Operator EOG RESOURCES INC							9. OGRID 7377			
10. Address of Operator PO BOX 2267 MIDLAND, TEXAS 79702							11. Pool name or Wildcat WC025 G09 S253309P; UPPER WOLFCAMP			
12. Location	Unit Ltr	Section	Township	Range	Lot	Feet from the	N/S Line	Feet from the	E/W Line	County
Surface:	B	13	25S	32E		289	NORTH	2192	EAST	LEA
BH:	G	24	25S	32E		2530	NORTH	2294	EAST	LEA
13. Date Spudded 03/27/2021	14. Date T.D. Reached 05/04/2021		15. Date Rig Released 05/05/2021			16. Date Completed (Ready to Produce) 08/14/2021		17. Elevations (DF and RKB, RT, GR, etc.) 3497' GL		
18. Total Measured Depth of Well MD 19,872' TVD 12,317'			19. Plug Back Measured Depth MD 19,843' 12,317'			20. Was Directional Survey Made? YES		21. Type Electric and Other Logs Run None		
22. Producing Interval(s), of this completion - Top, Bottom, Name WOLFCAMP 12,412 - 19,843'										
23. CASING RECORD (Report all strings set in well)										
CASING SIZE		WEIGHT LB./FT.		DEPTH SET		HOLE SIZE		CEMENTING RECORD		AMOUNT PULLED
10 3/4"		40.5# J-55		1093'		13 1/2"		520 CL C/CIRC		
8 3/4"		38.5# ECP 110		11,658'		9 7/8"		1545 CL C & H/191' ECHO		
6"		24.5 # ECP 110		19,852'		7 7/8"		1265 CL H TOC 6320' CBL		
24. LINER RECORD						25. TUBING RECORD				
SIZE	TOP	BOTTOM	SACKS CEMENT	SCREEN		SIZE	DEPTH SET		PACKER SET	
26. Perforation record (interval, size, and number) 12,412 - 19,843' 3 1/8", 1500 holes						27. ACID, SHOT, FRACTURE, CEMENT, SQUEEZE, ETC.				
						DEPTH INTERVAL		AMOUNT AND KIND MATERIAL USED		
						12,412 - 19,843'		FRAC W/18,402,240 lbs proppant, 280,791 bbls load fld		
28. PRODUCTION										
Date First Production 08/14/2021		Production Method (<i>Flowing, gas lift, pumping - Size and type pump</i>) Flowing				Well Status (<i>Prod. or Shut-in</i>) Producing				
Date of Test 08/24/2021	Hours Tested 24	Choke Size 64	Prod'n For Test Period	Oil - Bbl 4392	Gas - MCF 8916	Water - Bbl. 6586	Gas - Oil Ratio 2030			
Flow Tubing Press.	Casing Pressure 2514	Calculated 24-Hour Rate	Oil - Bbl.	Gas - MCF	Water - Bbl.	Oil Gravity - API - (<i>Corr.</i>) 50				
29. Disposition of Gas (<i>Sold, used for fuel, vented, etc.</i>) SOLD									30. Test Witnessed By	
31. List Attachments C-102, C-104, C-103, Directional Survey, H spacing										
32. If a temporary pit was used at the well, attach a plat with the location of the temporary pit.										
33. If an on-site burial was used at the well, report the exact location of the on-site burial:										
Latitude _____ Longitude _____ NAD 1927 1983										
I hereby certify that the information shown on both sides of this form is true and complete to the best of my knowledge and belief Printed Signature Kay Maddox Name Kay Maddox Title Senior Regulatory Specialist Date 08/26/2021 E-mail Address kay_maddox@eogresources.com										

This form is to be filed with the appropriate District Office of the Division not later than 20 days after the completion of any newly-drilled or deepened well and not later than 60 days after completion of closure. When submitted as a completion report, this shall be accompanied by one copy of all electrical and radio-activity logs run on the well and a summary of all special tests conducted, including drill stem tests. All depths reported shall be measured depths. In the case of directionally drilled wells, true vertical depths shall also be reported. For multiple completions, items 11, 12 and 26-31 shall be reported for each zone.

Southeastern New Mexico			Northwestern New Mexico				
T. Anhy	Rustler	946'	T. Canyon	Brushy	7536'	T. Ojo Alamo	T. Penn A "
T. Salt		1275'	T. Strawn			T. Kirtland	T. Penn. "B"
B. Salt		4670'	T. Atoka			T. Fruitland	T. Penn. "C"
T. Yates			T. Miss			T. Pictured Cliffs	T. Penn. "D"
T. 7 Rivers			T. Devonian			T. Cliff House	T. Leadville
T. Queen			T. Silurian			T. Menefee	T. Madison
T. Grayburg			T. Montoya			T. Point Lookout	T. Elbert
T. San Andres			T. Simpson			T. Mancos	T. McCracken
T. Glorieta			T. McKee			T. Gallup	T. Ignacio Otzte
T. Paddock			T. Ellenburger			Base Greenhorn	T. Granite
T. Blinebry			T. Gr. Wash			T. Dakota	
T. Tubb			T. Delaware Sand			T. Morrison	
T. Drinkard			T. Bone Springs			T. Todilto	
T. Abo			T. 1st BS Sand	10,025'		T. Entrada	
T. Wolfcamp	12,206'		T. 2nd BS Sand	10,487'		T. Wingate	
T. Penn			T. 3rd BS Sand	11,733'		T. Chinle	
T. Cisco (Bough C)			T.			T. Permian	

No. 1, from.....to.....

No. 2, from.....to.....

No. 3, from.....to.....

No. 4, from.....to.....

Include data on rate of water inflow and elevation to which water rose in hole.

No. 1, from.....to.....feet.....
 No. 2, from.....to.....feet.....
 No. 3, from.....to.....feet.....

From	To	Thickness In Feet	Lithology

From	To	Thickness In Feet	Lithology

District I

1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720

District II

811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720

District III

1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170

District IV

1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

ACKNOWLEDGMENTS

Action 44742

ACKNOWLEDGMENTS

Operator: EOG RESOURCES INC P.O. Box 2267 Midland, TX 79702	OGRID: 7377
	Action Number: 44742
	Action Type: [C-104] Completion Packet (C-104C)

ACKNOWLEDGMENTS

☒	I hereby certify that the required Water Use Report has been, or will be, submitted for this wells completion.
☒	I hereby certify that the required FracFocus disclosure has been, or will be, submitted for this wells completion.

District I
1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720
District III
1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170
District IV
1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 44742

CONDITIONS

Operator: EOG RESOURCES INC P.O. Box 2267 Midland, TX 79702	OGRID: 7377
	Action Number: 44742
	Action Type: [C-104] Completion Packet (C-104C)

CONDITIONS

Created By	Condition	Condition Date
plmartinez	File 3160-4 Completion Report within 10 days to NMOCD after BLM approval.	10/27/2021
